

Citizens' Bond Oversight Committee (CBOC)

Meeting on April 19th, 2023

March 31st, 2023 Report

9 Months - FY 2022-23

BOND CAPITAL CONSTRUCTION REPORTS

District Management is responsible for the preparation and fair presentation of the statement of expenditures and bond proceeds in accordance with U.S. generally accepted accounting principles; this includes the design, implementation, and maintenance of internal control relevant to the preparation and fair presentation of the statement of expenditures of bond proceeds that is free from material misstatement, whether due to fraud or error.

This report is prepared in accordance with these requirements and all bond expenditures were made in compliance with all applicable laws.


U-B Er U-C Pr U-D Pl U-E Rr U-F Sf U-G Sf U-H Tr U-I Er U-K Er U-L Sr U-M N U-Q In U-R Rr S-1 Ar S-1A Ar S-10 Pi	Project Name Furchase of BAE Airport Site Furchase of 1738 Pearl Street Furchase of BAE Airport Street Furchase of 1738 Pearl Street Furcha	Measure U Budget \$30,280,878 \$8,909,940 \$749,208 \$2,797,033 \$1,458,690 \$4,170,264	Measure S Budget	Measure AA Budget	Measure V Budget	Interest		Other Funding Pending **	Total Budget \$30,280,878	Estimate at Completion	Status Completed	Bond Funds Remaining
U-B Er U-C Pr U-D Pl U-E Rr U-F Sf U-G Sf U-H Tr U-I Er U-K Er U-L Sr U-M N U-Q In U-R Rr S-1 Ar S-1A Ar S-10 Pi	meritus College Facility Furchase of 1738 Pearl Street E Temp. Bldg. Replacement Emodel Library Village for Math M Airport Campus Site Improvements M Airport Campus West Building Theater Arts Renovation	\$30,280,878 \$8,909,940 \$749,208 \$2,797,033 \$1,458,690 \$4,170,264	Budget	Buuget	Budget		Received	Pending	\$20,200,070		Commissed	Remaining
U-B Er U-C Pr U-D Pl U-E Rr U-F Sf U-G Sf U-H Tr U-I Er U-K Er U-L Sr U-M N U-Q In U-R Rr S-1 Ar S-1A Ar S-10 Pi	meritus College Facility Furchase of 1738 Pearl Street E Temp. Bldg. Replacement Emodel Library Village for Math M Airport Campus Site Improvements M Airport Campus West Building Theater Arts Renovation	\$8,909,940 \$749,208 \$2,797,033 \$1,458,690 \$4,170,264							ココリ・とのし、6/6	\$30,280,878	Completea	SO
U-C PI U-D PI U-E Ri U-F SI U-G SI U-H Th U-I Ea U-K Ea U-L Sh U-M N U-Q In U-R Ri S-1 Ai S-1A Ai	Purchase of 1738 Pearl Street E Temp. Bldg. Replacement Elemodel Library Village for Math M Airport Campus Site Improvements M Airport Campus West Building Theater Arts Renovation	\$749,208 \$2,797,033 \$1,458,690 \$4,170,264					\$693,842		\$9,603,782	\$9,603,782	Completed	\$(
U-E Ro U-F SI U-G SI U-H Th U-I Ea U-K Ea U-L Sh U-M N U-Q In U-R Ro S-1 Aa S-1A Aa S-10 Pi S-13 Aa	Remodel Library Village for Math M Airport Campus Site Improvements M Airport Campus West Building Theater Arts Renovation	\$1,458,690 \$4,170,264					+ /		\$749,208	\$749,208	Completed	\$(
U-E Ro U-F SI U-G SI U-H Th U-I Ea U-K Ea U-L Sh U-M N U-Q In U-R Ro S-1 Aa S-1A Aa S-10 Pi S-13 Aa	Remodel Library Village for Math M Airport Campus Site Improvements M Airport Campus West Building Theater Arts Renovation	\$4,170,264							\$2,797,033	\$2,797,033	Completed	\$(
U-G SI U-H Th U-I Ea U-K Ea U-L Sh U-M N U-Q In U-R Ro S-1 Aa S-1A Aa S-10 Pi S-13 Aa	M Airport Campus West Building heater Arts Renovation								\$1,458,690	\$1,458,690	Completed	\$0
U-H Th U-I Ea U-K Ea U-L Sh U-M N U-Q In U-R Re S-1 Ar S-1A Ar S-10 Pi S-13 Ar	heater Arts Renovation								\$4,170,264	\$4,170,264	Completed	\$0
U-I Ea U-K Ea U-L Sh U-M N U-Q In U-R Ro S-1 An S-1A An S-10 Pi		\$19,709,741							\$19,709,741	\$19,709,741	Completed	\$0
U-K Ea U-L Sh U-M N U-Q In U-R Ro S-1 An S-1A An S-10 Pi S-13 An		\$19,544,314							\$19,544,314	\$19,544,314	Completed	\$0
U-L Sh U-M N U-Q In U-R Re S-1 Ar S-1A Ar S-10 Pi S-13 Ar	arthquake Rpl. Liberal Arts North	\$6,011,584					\$6,496,141		\$12,507,725	\$12,507,725	Completed	\$0
U-M N U-Q In U-R R S-1 A S-1A A S-10 Pi S-13 A	arthquake Rpl. Liberal Arts South	\$6,108,150					\$10,625,070		\$16,733,220	\$16,733,220	Completed	\$0
U-Q In U-R Re S-1 Ar S-1A Ar S-10 Pr S-13 Ar	huttle Replacement Parking	\$18,969,509							\$18,969,509	\$18,969,509	Completed	\$0
U-R Ro S-1 Ar S-1A Ar S-10 Pi S-13 Ar	lorth Quad Plaza	\$11,388,463							\$11,388,463	\$11,388,463	Completed	\$0
S-1 A ¹ S-1A A ² S-10 Pi S-13 A ³	nfrastructure & Safety	\$4,003,084							\$4,003,084	\$4,003,084	Completed	\$0
S-1A A ¹ S-10 Pi S-13 A ¹	Restroom Improvements	\$17,501							\$17,501	\$17,501	Completed	\$0
S-10 Pi S-13 A	thletic Fields Phase I, Corsair Field		\$4,372,535				\$67,530		\$4,440,065	\$4,440,065	Completed	\$0
S-13 A	thletic Fields Phase I, John Adams		\$2,969,807						\$2,969,807	\$2,969,807	Completed	\$0
	rico Promenade Improvements, Phase I		\$1,018,009						\$1,018,009	\$1,018,009	Completed	\$0
ΔΔ-11/1	dv. Architecture Related Exp for AA		\$0						\$0	\$0	Completed	\$0
	Community Classroom & Facility Projects			\$3,162,183					\$3,162,183	\$3,162,183	Completed	\$0
	4th and Pico Project	\$319,242							\$319,242	\$319,242	Completed	\$0
	etters & Sci Demo/Restore	\$0							\$0	\$0	Completed	\$0
	enovation of Corsair Stadium			\$1,035,299					\$1,035,299	\$1,035,299	In Design	\$995,400
	erforming Arts Complex		\$37,697,625				\$2,992,576		\$40,690,201	\$40,690,201	Completed	\$0
	Ausic Complex	\$2,011,371					\$2,618,113		\$4,629,484	\$4,629,484	Completed	\$0
	Career Opportunity Center			\$0					\$0	\$0	Completed	\$0
	nfrastructure & Technology - Utility			\$27,753					\$27,753	\$27,753	Completed	\$0
	susiness & Facilities Infrastructure			\$1,968,124					\$1,968,124	\$1,968,124	Completed	\$0
	nfrastructure & Technology - Technology			\$2,434,417					\$2,434,417	\$2,434,417	Completed	\$0
·	nergy Efficiency Projects		\$293,361	\$3,016,773			\$708,637		\$4,018,771	\$4,018,771	Completed	\$0
	ignage Safety/Information		\$706,713						\$706,713	\$706,713	Completed	\$0
	nfrastructure & Technology - Information Technology Relocation			\$23,140,771			\$19,798		\$23,160,569	\$23,160,569	Completed	\$0
	atellite Campus Parking Facilities and Roadway		\$3,891,747	\$2,130,670					\$6,022,417	\$6,022,417	Completed	\$0
	Madison East Wing Seismic Upgrade			\$30,161,852					\$30,161,852	\$30,161,852	Completed	\$0
· ·	teplacement Health/PE/Fitness Central Plant Building		\$11,603,383	\$44,428,222			\$208,847		\$56,240,452	\$56,240,452	Completed	\$0
	nvironmental Performance - Central Plant Connections		4	\$10,767,251					\$10,767,251	\$10,767,251	Completed	\$0
	leal Property Acquisition		\$45,597				45.00=.001		\$24,683,983	\$24,683,983	Completed	\$0
	Media and Technology Complex - Academy Site			\$124,669,502			\$6,835,391		\$131,504,893	\$131,504,893	Completed	\$1,165,385
	mergency Lighting, Fire Alarm, and Security System	624 424 425	¢45 505 333	\$11,515,614		¢24 604 200	Ć4 224 000		\$11,515,614	\$11,515,614	Completed	\$0
	tudent Services Building	\$21,131,135	\$45,595,322	\$6,870,490	\$33,624,909	\$21,681,308	\$1,321,000		\$130,224,164	\$130,224,164	Completed	\$9,017,016
,	arly Childhood Development/Childcare		\$8,858,656		\$15,405,517	42.224.724	\$6,661,598		\$30,925,771	\$30,925,771	Completed	\$2,325,022
	Malibu Center and Site Acquisition	62.440.420	\$25,132,568	<u> </u>	\$34,287,482	\$2,294,791			\$61,714,841	\$61,714,841	Completed	\$9,058,582
I-S, S-11, AA-112, V-109 N	·	\$2,110,430	\$716,428	\$834,697	\$1,000,000		Ć45 450 530	624 020 472	\$4,661,555	\$4,661,555	In Design	\$253,442
	Replacement Math and Science Extension Building	\$308,336		\$2,244,008	\$82,317,992		\$15,159,528	\$24,928,472	\$124,958,336	. , ,	In Construction	\$29,891,275
·	Orescher - Academic Modernization, Bookstore, Pico Promenade II			\$5,082	\$13,000,000		¢200.000	640.644.00	\$13,005,082	\$13,005,082	In Planning	\$13,000,000
	Art Building Replacement				\$24,000,000		\$286,093	. , ,	\$34,901,000	\$34,901,000	In Design	\$22,198,335
	Business Building Renovation				\$12,547,000			\$12,470,000	\$25,017,000	\$25,017,000	In Planning	\$12,543,600
	ir Conditioning				\$10,777,654				\$10,777,654	. , ,	In Construction	\$646,917
	NDA				\$4,000,000				\$4,000,000	\$4,000,000	In Planning	\$4,000,000
	Outdoor Classroom				\$321,723				\$321,723	\$321,723	Completed	\$0
	ohn Adams MS Auditorium (SMMUSD)				\$20,000,000				\$20,000,000	\$20,000,000	Completed	\$0
	City of Santa Monica				\$20,000,000				\$20,000,000	\$20,000,000	In Planning	\$20,000,000
	Classrooms Relocation				\$7,400,000				\$7,400,000	\$7,400,000	Completed	\$113,281
	Parking Structure 3 Improvement Project				\$1,500,000				\$1,500,000	\$1,500,000	In Design	\$1,493,134
	Gender Neutral Bathrooms				\$3,500,000				\$3,500,000	\$3,500,000	In Design	\$3,500,000
	Athletic Facilities		6476 606		\$5,000,000				\$5,000,000	\$5,000,000	In Planning	\$4,998,265
·	Other Bond Related Expenses		\$476,636		\$300,000				\$776,636	\$776,636	In Planning	\$55,446
	BD Sant of Lancaca and		4440	4400 000	\$39,717,723				\$39,717,723	\$39,717,723	In Planning	\$39,717,723
	Cost of Issuance		\$119,470			ĆC 452 000			\$1,417,496	\$1,417,496	In Planning	\$55,848
·	Nanagement Reserve	** -=-	An	\$1,446,709	\$15,500,000	\$6,152,892			\$23,099,601	\$23,099,601	In Planning	\$16,946,709
-U, S-17, AA-123, V-123 U		\$1,127		· · · · · · · · · · · · · · · · · · ·	.	1	A	4	\$7,441	\$7,441	On-Going	\$0
Pı	roject Totals	\$160,000,000	\$143,500,000	\$295,000,000	\$345,000,000	\$30,128,991	\$54,694,164	\$48,013,379	\$1,076,336,534	\$1,076,336,534		\$191,975,380
	City of SM: \$14,647,889; FEMA: \$2,456,388; State: \$8,363,000; Prop T: \$2,618,113 29,858,053	3; DWP: \$86,245; S	SCE: \$844,284; Gas	Co.: \$106,262; Ma	dison Foundation: \$	52,992,576; KCRW: \$	6,803,412; Emerit	us College Foundation	on: \$693,842; Bond In	terest and Cost of Iss	uance Refund:	

SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of March 31, 2023

Total Bond Program (AA and V)	\$640,000,000
Total Bonds Issued	\$639,995,829
Total Expenses as of 3-31-23	\$448,020,448
Total Available Remaining	\$191,975,381
Total Unsold Bond	\$4,171

Measure AA Bond \$295,000,000	
Bond Issue Date	Amount
2010	\$100,000,000
2014	\$144,995,829
2017	\$50,000,000
Total Available	\$294,995,829
Expenses as of 3-31-23	\$291,148,510
Total Available Remaining	\$3,847,319
Unsold Bond Amount	\$4,171
Total Available as of 4-1-2023	\$3,851,490

Measure V Bond \$345,000,000	
Bond Issue Date	Amount
2018	\$180,000,000
2022	\$165,000,000
Total Available	\$345,000,000
Expenses as of 3-31-23	\$156,871,938
Total Available Remaining	\$188,128,062
Unsold Bond Amount	\$0
Total Available as of 4-1-2023	\$188,128,062

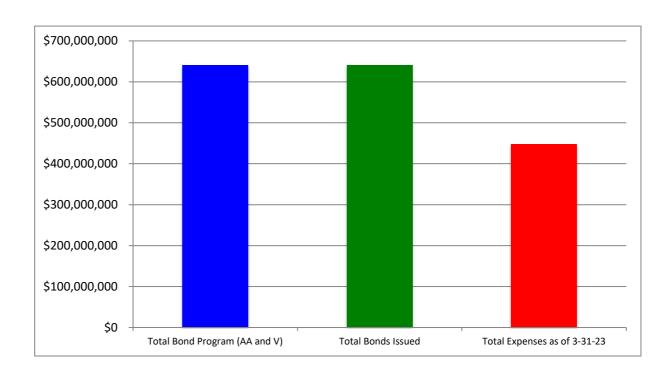


Interest	Measure AA	Measure V
As of 6-30-22	\$6,978,496	\$8,737,900
Expenditure / Arbitrage as of 6-30-22	\$5,192,948	\$0
Available Interest as of 7-1-22	\$1,785,548	\$8,737,900

(1) Original Bond \$135,000,000, refunding on 2-15-07 received additional \$8,500,000

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget As of March 31, 2023

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 3/31/23	Measure AA Expenditures as of 12/31/22	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant Connections	Completed	\$10,767,251	\$10,767,251	\$0	\$10,767,251	\$10,767,251	\$0	\$0
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$23,160,569	\$23,140,771	\$19,798	\$23,140,771	\$23,140,771	\$0	\$0
103	Media and Technology Complex - Academy Site	Completed	\$131,504,893	\$124,669,502	\$6,835,391	\$123,504,117	\$123,489,790	\$14,327	\$1,165,385
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$56,240,452	\$44,428,222	\$11,812,230	\$44,428,222	\$44,428,222	\$0	\$0
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	Completed	\$13,005,082	\$5,082	\$13,000,000	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	July 2024	\$124,958,336	\$2,244,008	\$122,714,328	\$2,004,184	\$2,004,184	\$0	\$239,824
107	Madison East Wing Seismic Upgrade	Completed	\$30,161,852	\$30,161,852	\$0	\$30,161,852	\$30,161,852	\$0	\$0
108	Renovation of Corsair Stadium	June 2024	\$1,035,299	\$1,035,299	\$0	\$39,899	\$39,899	\$0	\$995,400
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
110	Malibu Center	Completed	\$61,582,273	\$0	\$61,582,273	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$1,968,124	\$1,968,124	\$0	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	Completed	\$834,697	\$834,697	\$0	\$834,697	\$834,697	\$0	\$0
113	Energy Efficiency Projects	Completed	\$3,508,088	\$3,016,773	\$491,315	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$3,162,183	\$3,162,183	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$24,638,386	\$24,638,386	\$0	\$24,638,386	\$24,638,386	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$7,022,417	\$2,130,670	\$4,891,747	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$2,434,417	\$2,434,417	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$27,753	\$27,753	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	Completed	\$11,515,614	\$11,515,614	\$0	\$11,515,614	\$11,515,614	\$0	\$0
120	Student Services	Completed	\$130,224,164	\$6,870,490	\$123,353,674	\$6,870,490	\$6,870,490	\$0	\$0
121	Cost of Issuance	Completed	\$498,026	\$498,026	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$1,446,709	\$1,446,709	\$0	\$0	\$0	\$0	\$1,446,709
123	Unissuable Bond	Completed	\$4,171	\$4,171	\$0	\$0	\$0	\$0	\$4,171
	Project Totals		\$638,249,876	\$295,000,000	\$344,700,756	\$291,148,511	\$291,134,184	\$14,327	\$3,851,489

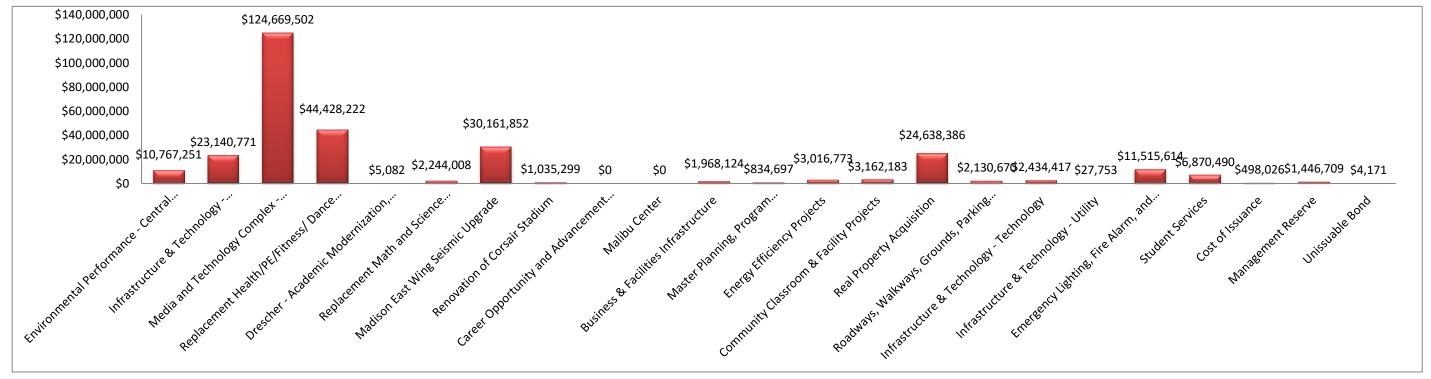

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget History as of March 31, 2023


			Preliminary	Measure AA	Measure AA		Measure AA
	Project Name	Completion	Measure AA	Budget as of	Budget as of	Variance	Remaining as
			Budget	12/31/22	3/31/23		of 3/31/23
101	Environmental Performance - Central Plant Connections	Completed	\$12,034,042	\$10,767,251	\$10,767,251	\$0	\$0
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$13,287,218	\$23,140,771	\$23,140,771	\$0	\$0
103	Media and Technology Complex - Academy Site	Completed	\$57,480,824	\$124,669,502	\$124,669,502	\$0	\$1,165,385
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$29,232,317	\$44,428,222	\$44,428,222	\$0	\$0
105	Drescher - Academic Modernization, Bookstore, Pico Promenade II	Completed	\$34,026,480	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	July 2024	\$68,259,000	\$2,244,008	\$2,244,008	\$0	\$239,824
107	Madison East Wing Seismic Upgrade	Completed	\$6,146,000	\$30,161,852	\$30,161,852	\$0	\$0
108	Renovation of Corsair Stadium	June 2024	\$11,203,000	\$1,035,299	\$1,035,299	\$0	\$995,400
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$32,384,000	\$0	\$0	\$0	\$0
110	Malibu Center	Completed	\$6,069,031	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$17,506,952	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	Completed	\$2,000,000	\$834,697	\$834,697	\$0	\$0
113	Energy Efficiency Projects	Completed	\$5,371,136	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$0	\$24,638,386	\$24,638,386	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$0	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$0	\$27 <i>,</i> 753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	Completed	\$0	\$11,515,614	\$11,515,614	\$0	\$0
120	Student Services	Completed	\$0	\$6,870,490	\$6,870,490	\$0	
121	Cost of Issuance	Completed	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$0	\$1,446,709	\$1,446,709	\$0	
123	Unissuable Bond	Completed	\$0		\$4,171	\$0	
	Project Totals		\$295,000,000	\$295,000,000	\$295,000,000	\$0	

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure AA Project Schedule As of March 31, 2023

102 In	Environmental Performance - Central Plant Connections nfrastructure & Technology - Information Technology Relocation	Completed								24
	nfrastructure & Technology - Information Technology Relocati									
103 M		Completed								
	Media and Technology Complex - Academy Site	Completed								
104 Re	Replacement Health/PE/Fitness/Dance Building with Central Pla	Completed								
105 D	Prescher - Academic Modernization, Bookstore, Pico Promenad	Completed								
106 R	Replacement Math and Science Extension Building	July 2024								
107 M	Madison East Wing Seismic Upgrade	Completed								
108 R	Renovation of Corsair Stadium	June 2024								
109 Ca	Career Opportunity and Advancement Center (Bundy)	Completed								
110 M	1alibu Center	Completed								
111 Bı	Business & Facilities Infrastructure	Completed								
112 M	Master Planning, Program Management, Overhead	Completed								
113 Er	nergy Efficiency Projects	Completed								
114 C	Community Classroom & Facility Projects	Completed								
115 R	Real Property Acquisition	Completed								
116 R	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed								
117 Ir	nfrastructure & Technology - Technology	Completed								
118 Ir	nfrastructure & Technology - Utility	Completed								
119 Er	mergency Lighting, Fire Alarm, and Security System	Completed								
120 St	Student Services	Completed								
121 C	Cost of Issuance	Completed								
122 M	lanagement Reserve	On-Going								
123 U	Inissuable Bond	Completed						T		\top
			In P				ruct	Ī		

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
·			<u> </u>						<u> </u>		•		•	<u> </u>		
AA 7100062																
Environmental Performance - Central	Plant Connect	ions (101)														
Legal		\$0		\$0		\$0		\$0				\$0			\$0	
Other Contract Services		\$0		\$49,837	\$16,239	\$0		\$0			\$0	\$0			\$0	\$75,996
Consultants		\$0	\$0	\$0	\$0	\$28		\$0			\$0	\$0			\$0	\$28
Building & Additions		\$0	\$0	\$0	\$361	\$729	\$640	\$1,328,592	\$6,934,044	\$446,861	\$0	\$0	\$0	\$0	\$0	\$8,711,229
Architect		\$0	\$385	\$148,311	\$176,897	\$36,256	\$0	\$0	\$0	\$0	\$15,699	\$0			\$0	\$377,547
Engineering		\$48,500	\$0	\$4,000	\$0	\$152,010	\$39,638	\$66,918	\$138,887	\$62,883	\$0	\$0			\$0	\$512,836
Inspection & Testing		\$0	\$0	\$7,688	\$0			\$7,310	\$137,150	\$4,382	\$0	\$0			\$0	
Project Management		\$0	\$17,263	\$55,116	\$48,685	\$61,908	\$19,313	\$104,575	\$526,072	\$99,840	\$190	\$0			\$0	
Cap Equipment		\$0		\$0					\$0			\$0			\$0	\$(
Non-Cap Equipment		\$0	\$0	\$0	\$0			\$0	\$0	\$0		\$0			\$0	
Total		\$48,500	\$17,648	\$264,951	\$242,307	\$250,931	\$59,591	\$1,507,396	\$7,736,152	\$623,886	\$15,889	\$0	\$0	\$0	\$0	\$10,767,25°
Project Budget			-			-					•		•			,
Less Other Funding	\$0															
	\$10,767,251															
Actual Measure AA Expenditures	\$10,767,251															
Running Balance	\$0															
AA 7100063																
Infrastructure & Technology - IT Relo	cation (102)															
Supplies		\$0	\$0	\$965	\$8,442	\$3,137	\$2,600	\$0			\$0	\$0	\$0	\$0	\$0	\$15,14
Consultants		\$0	\$0	\$0	\$0		\$0	\$7,800	\$0		\$0	\$0	\$0		\$0	\$8,20
Maintenance Contract		\$0	\$0	\$0	\$0		\$0	\$77,074	\$79		\$0	\$0	\$0	\$0	\$0	\$184,54
Legal		\$0	\$0	\$0	\$1,363	\$50	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,41
Printing		\$0	\$0	\$0	\$0	\$1,624	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$1,62
Postage		\$0	\$0	\$0	\$0		\$0	\$0	\$0			\$0			\$0	\$1,56
Other Contract Services		\$0	\$0	\$2,163	\$15,259	\$23,356	\$0	\$19,050	\$4,500			\$0			\$0	
Moving		\$0		\$0	\$577	\$266	\$27,655	\$22,618	\$0			\$0			\$0	\$51,110
Site Improvement		\$0	\$0	\$0				\$0	\$0			\$0			\$0	
Building & Additions		\$0	\$0	\$0		\$9,667,362	\$4,288,987	\$1,203,916	\$165,229	-\$19,798	\$0	\$0			\$0	
Architect		\$105,049	\$482,261	\$505,580	\$183,181	\$287,201	\$236,860	\$120,091	\$0			\$0			\$0	\$1,920,223
Engineering		\$0	\$0	\$10,037	\$11,065	\$17,147	\$19,512	\$25,994	\$1,956			\$0			\$0	\$85,712
Inspection & Testing		\$10,291	\$8,793	\$21,449	\$137,523	\$499,982	\$200,262	\$568	\$0	\$0		\$0	\$0	\$0	\$0	\$878,868
Project Management		\$33,460	\$76,290	\$84,991	\$331,754	\$431,730	\$297,951	\$22,978	\$1,500	\$0	\$0	\$0	\$0	\$0	\$0	\$1,280,65
Cap Equipment		\$0	\$0	\$0		\$645,830	-\$29,090	\$589,604	\$9,811	\$0	\$0	\$0	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$18,344	\$10,852	\$277,219	\$1,891	\$20,689	\$0	\$0	\$0	\$0	\$0	\$0	\$328,994
Total		\$148,800				\$11,697,901									\$0	\$23,140,77°
Project Budget	\$23,160,569	Received	•		. , - ,	. , - ,	, , , , , , , , , , , , , , , , , , , ,	. , - ,-						, , ,		<u> </u>
Less Other Funding		\$19,798	* Other Fundii	ng Source:												
	\$23,140,771	. , -	1) Edison \$19		d											
Actual Measure AA Expenditures			.,	,. 22 . 30000	=-											
Running Balance																

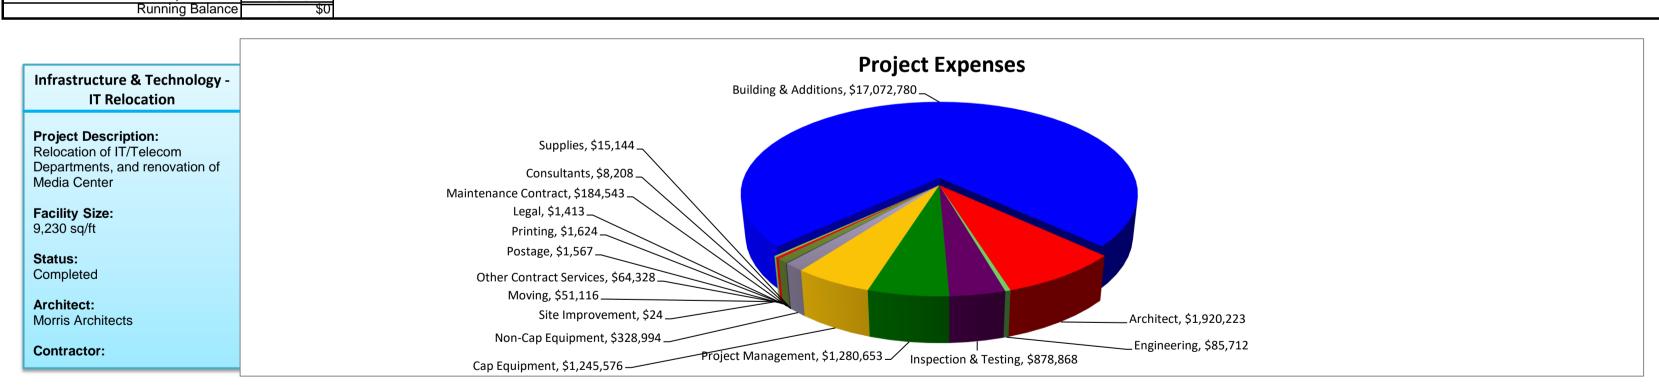

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
•	<u> </u>	•		•	•	<u> </u>				•				•		
AA 7100061						I										
Media and Technology Complex - Aca	ademy Site (103	3)														
Consultants		\$0	\$0	\$20,675	\$12,576	\$9,488	\$7,789	\$2,102	\$0		\$0	\$0	\$0		\$0	\$65,551
Supplies		\$0	\$0	\$0	\$19,481	\$1,048	\$289	\$0	\$9,251	\$40,519	\$937	\$0	\$0	\$0	\$0	\$71,525
Maintenance Contract		\$0	\$0		\$0	\$0	\$0	\$0	\$15,922	\$23,561	\$0	\$0	\$0	Ŧ -	\$0	\$39,483
Legal		\$16,903	\$0	\$7,958	\$43,363	\$5,066	\$26,186	\$49,155	\$15,435	\$36,221	\$26,991	\$121,256	\$100,053	\$200,783	\$166,191	\$815,559
Software Support		\$0	\$0	\$0	\$1,982	\$0	\$0	\$0	\$6,548	\$6,975	\$0	\$0	\$0	¥ -	\$0	\$15,505
Service Fee		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$17,000	\$0	\$0	\$0	\$0		\$0	\$17,000
Other Contract Services		\$3,993	\$5,763	\$13,456	\$39,188	\$0	\$0	\$5,853	\$22,622		\$7,690	\$7,550	\$0		\$0	\$124,743
Moving Expenses		\$0	\$0	\$0	\$38,756	\$0	\$0	¥ •	\$0	\$97,543	\$17,556	\$0	\$0		\$0	\$153,855
Site Improvement		\$0	\$0	\$0	\$100,505	\$664	\$606	\$476	\$622	\$526	\$0	\$526	\$0		\$0	\$103,925
Building & Additions		\$0	\$538	\$1,498,660	\$3,543,657	\$11,820,615	\$17,734,534	\$23,465,347	\$16,267,550	\$25,548,089	\$219,234	\$626,512	-\$67,164		\$0	\$100,657,570
Architect		\$2,097,553		\$295,753	\$265,481	\$778,015	\$517,794	\$1,048,935	\$991,386	\$869,801	\$151,886	\$43,416	\$90,690	\$240,094	-\$1,327,000	\$8,572,392
Engineering		\$16,459	\$29,293	\$9,102	\$29,223	\$8,203	\$72,993	\$118,368	\$72,786	\$51,971	\$37,259	\$0	\$0		\$0	\$445,657
Inspection & Testing		\$64,905	\$27,527	\$123,842	\$235,287	\$563,746	\$1,381,801		\$525,264		\$27,210	\$1,212	\$0		\$0	\$3,800,005
Project Management		\$121,786	\$233,826	\$269,249	\$506,917	\$800,315	\$930,115	\$1,207,850	\$1,121,670	\$859,779	\$50,681	\$27,825	\$2,450		\$2,188	\$6,134,649
Cap Equipment		\$0	\$0	\$0	\$186,301	\$0	\$0	\$0	\$0	\$1,458,273	\$6,604	\$0	\$0		\$0	\$1,651,178
Non-Cap Equipment		\$0	\$0	\$0	\$10,782	\$0	\$0	\$0	\$326,845		\$7,167	\$0	\$0	T -	\$0	\$835,520
Total		\$2,321,599	\$2,805,534	\$2,238,694	\$5,033,499	\$13,987,159	\$20,672,105	\$26,540,059	\$19,392,902	\$29,722,772	\$553,215	\$828,296	\$126,029	\$440,877	-\$1,158,622	\$123,504,117
	\$131,504,893	Received														
Less Other Funding*		\$6,835,391	* Other Fund													
	\$124,669,502				3,412 received	1										
Actual Measure AA Expenditures			2) Edison \$3	1,979.48 recei	ved											
Running Balance	\$1,165,385															



Renovation and new extension to the existing building, new building for KCRW, and a new parking structure

Facility Size: Building - 116,000 sq/ft Parking Structure - 450 spaces


Status: Completed

Architect:


Clive Wilkinson Architects

Contractor:

H.B. Parkco Construction

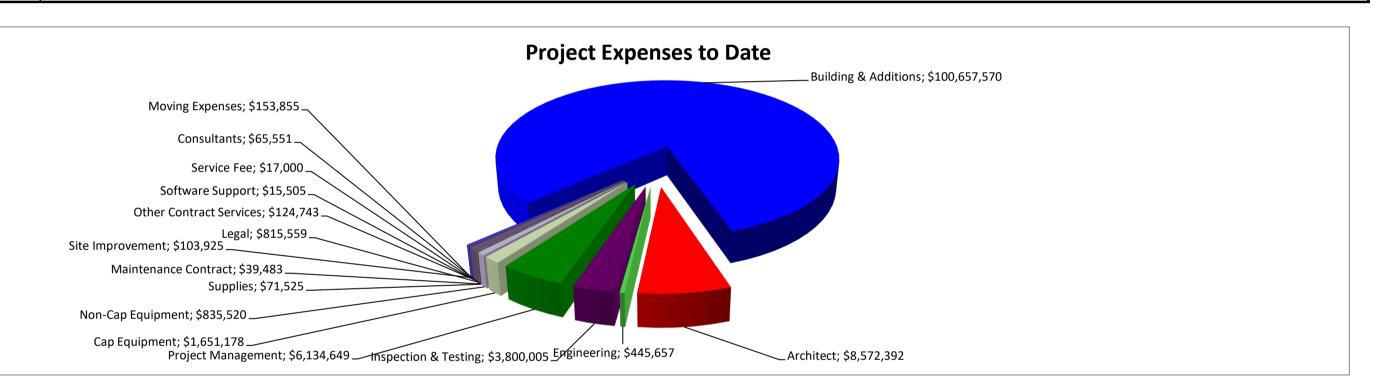

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
·		<u> </u>		•	<u> </u>	•				•				•		<u> </u>
AA 7100060					I											
Repl. Health/PE/Fitness/Dance Building	ng with Central	Plant (104)														
Consultants		\$0	\$0	\$0	\$14	\$62	\$2,304	\$184	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,564
Supplies		\$0	\$0	\$0	\$0	\$7,089	\$195	\$484	\$20,947	\$0	\$0	\$0	\$0	\$0	\$0	\$28,715
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$663	\$80	\$0	\$0	\$0	\$0	\$0	\$(\$742
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0		\$0	
Site Improvement		\$0	\$0	\$0	\$0	\$0	\$559	\$440	\$575	\$0	\$0	\$0	\$0		\$0	\$1,574
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$2,165	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Postage		\$0	\$0	\$0	\$0	\$0	\$1,505	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$(
Other Contract Services		\$120	\$38	\$112	\$32,634	\$0	\$1,019	\$581	\$0	\$2,644	\$0	\$0	\$0		\$0	\$37,147
Building & Additions		\$0	\$0	\$0	\$817	\$4,188	\$1,623	\$13,783,023	\$14,880,829	\$5,315,393	-\$148,184	\$0	\$0	\$0	\$0	\$33,837,688
Architect		\$256,076	\$1,568,564	\$1,790,207	\$518,973	\$177,583	\$364,853	\$585,900	\$373,345	\$210,312	\$108,264	\$0	\$0	\$0	\$0	\$5,954,078
Engineering		\$0	\$8,507	\$31,650	\$7,871	\$6,529	\$9,276	\$76,712	\$51,025	\$11,318	\$2,900	\$0	\$0	\$0	\$0	
Inspection & Testing		\$36,892	\$490	\$21,150	\$1,285	\$360	\$133,756	\$846,765	\$358,724	\$60,826	\$1,330	\$0	\$0	\$0	\$0	\$1,461,579
Project Management		\$34,968	\$113,379	\$118,783	\$94,768	\$108,528	\$463,418	\$564,240	\$487,065	\$312,539	\$20,242	\$0	\$0		\$0	\$2,317,928
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$164,793	\$68,425	\$0	\$0	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$9,015	\$0	\$206,229	\$127,078	\$0	\$0	\$0	\$0	\$0	\$342,322
Total		\$328,056	\$1,690,978	\$1,961,901	\$656,362	\$304,338	\$989,689	\$15,858,991	\$16,544,820	\$6,108,535	-\$15,448	\$0	\$0	\$0	\$(\$44,428,222
	\$56,240,452				_											
Less Other Funding*	\$11,812,230		* Other Fund													
	\$44,428,222			5 - \$11,603,38												
Actual Measure AA Expenditures	\$44,428,222		SCE \$190	,847.28, Gas (Co. \$18,000 red	eived										
Running Balance	\$0															

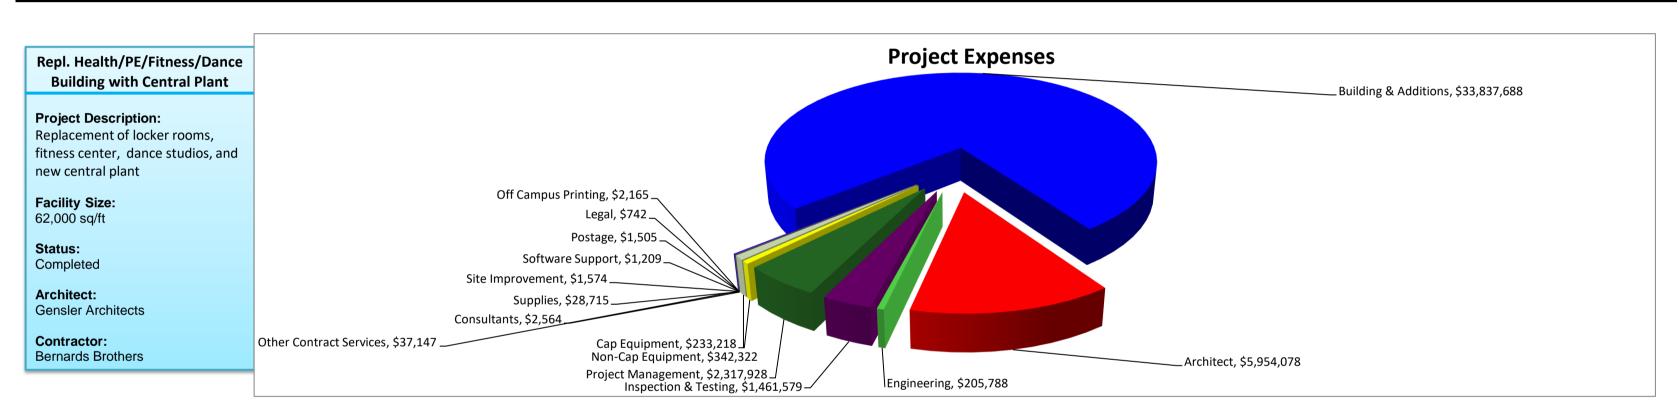


Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
AA 7100065																
Drescher - Academic Modernization, E	Bookstore, Picc	o Promenade (1	05)													
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0
Site Acquisition		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$5,082
Total		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,082
Project Budget	\$13,005,082															
Less Other Funding	\$13,000,000		* Other Fund	ing Source:												
Net			1) Measure V	′ 13,000,000 a	allocated											
Actual Measure AA Expenditures	\$5,082															
Running Balance	\$0															

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
AA 7100090																
Replacement Math and Science Exter	nsion Building ((106)														
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,525	\$0	\$0	\$0	\$0	\$0	\$1,525
Site Acquisition		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$4,796
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,787,824	-\$94,695	\$0	\$0	\$0	\$0	\$1,693,130
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	, ,	\$0	\$0	\$0	\$0	\$0	\$70,223
Project Management		\$0	\$0	\$0	\$0	\$4,950		\$0	\$800		\$0	\$0	\$0		\$0	\$234,510
Total		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$800	\$2,093,128	-\$94,695	\$0	\$0	\$0	\$0	\$2,004,184
Project Budget	\$124,958,336	Received														
Less Other Funding		\$17,743,528														
Net	\$2,244,008		1) Measure U	J \$308,336 2)	Measure V \$	82,317,992 allo	cated									
Actual Measure AA Expenditures	\$2,004,184		State of C	alifornia \$40.0	88,000 allocat	ed										

Running Balance

AA 7100047															
Madison East Wing Seismic Upgrade (10	7)														
Supplies		\$0 \$0	\$0	\$0	\$0	\$0	\$0	\$6,197	\$0	\$0	\$0	\$0	\$0	\$0	\$6,197
Consultants		\$0 \$0	\$0	\$0	\$135	\$28		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$163
Off Campus Printing		\$0 \$0	\$0	\$0	\$0	\$285	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$285
Maintenance Contract		\$0 \$0	\$0	\$0	\$0	\$0	\$0	\$357	\$0	\$0	\$0	\$0	\$0	\$0	\$357
Legal		\$0 \$0	\$0	\$0	\$0	\$0	\$0	\$7,579	\$11,822	\$8,263	\$950	\$0	\$0	\$0	\$28,613
Software Support		\$0 \$0	\$0	\$0	\$0	\$0	\$0	\$806	\$0	\$0	\$0	\$0	\$0	\$0	\$806
Other Contract Services		\$0 \$364	\$997	\$0	\$0	\$1,328	\$711	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,400
Building & Additions		\$0 \$656	\$312,643	\$0	\$4,248	\$6,030,371	\$8,829,626	\$4,949,223	\$3,967,591	\$0	\$0	\$0	\$0	\$0	\$24,094,358
Architect	\$76,0	73 \$398,050	\$550,589	\$65,444	\$57,480	\$199,100	\$404,764	\$122,764	\$103,824	\$0	\$0	\$0	\$0	\$0	\$1,978,088
Engineering		\$0 \$0	\$10,707	\$778	\$0	\$13,792	\$33,184	\$37,491	\$90	\$0	\$0	\$0	\$0	\$0	\$96,042
Inspection & Testing		\$0 \$19,848	\$16,752	\$3,036	\$5,851	\$676,323	\$405,443	\$112,876	\$4,703	\$0	\$0	\$0	\$0	\$0	\$1,244,832
Project Management	\$5,5	57 \$128,878	\$112,573	\$67,447	\$118,242	\$494,874	\$481,165	\$322,379	\$31,230	\$11,286	\$0	\$0	\$0	\$0	\$1,773,629
Cap Equipment		\$0 \$0	\$30,603	\$0	\$0	\$0	\$0	\$537,627	\$0	\$0	\$0	\$0	\$0	\$0	\$568,230
Non-Cap Equipment		\$0 \$0	\$71,827	\$9,788	\$0	\$0	\$0	\$285,236	\$0	\$0	\$0	\$0	\$0	\$0	\$366,851
Total	\$81,6	30 \$547,796	\$1,106,691		\$185,956	\$7,416,101	\$10,154,894	\$6,382,534	\$4,119,259	\$19,549	\$950	\$0	\$0	\$0	\$30,161,852
Project Budget	30,161,852	•								•		•	•	•	
Less Other Funding	\$0														
Net S	30,161,852														
	30,161,852														

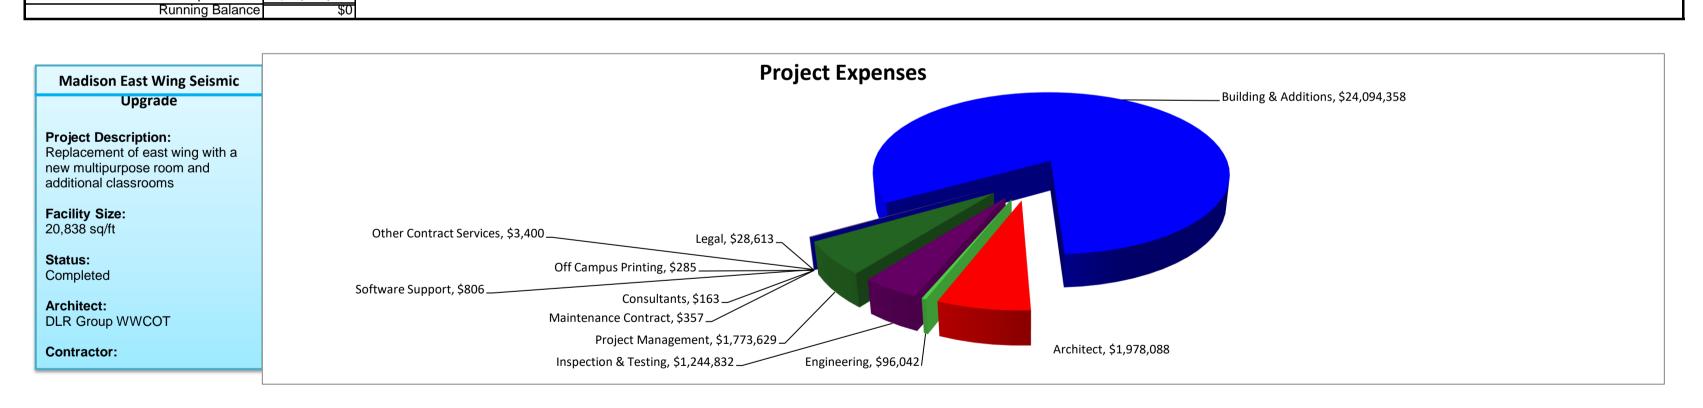

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
AA 7100068																
Renovation to Corsair Stadium (108)																
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$30,759	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$30,759
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$4,540	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,600	\$9,140
Total		\$0	\$35,299	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,600	
Project Budget	\$1,035,299			_	_											
Less Other Funding	\$0															
Net	\$1,035,299															
Actual Measure AA Expenditures	\$39,899															
Running Balance	\$995,400															

AA 7100067, 7100152, 7100155, 7100157 Business & Facilities Infrastructure (111)																
)	40	Φ0	Φ0	¢4.402	¢4 040	CO	Φ0	C O	PO	C O	C O	CO	Φ0	<u> </u>	Φ0.00
Supplies		\$0	\$0	\$0	\$1,493	\$4,840	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,33
Service Fee		\$0	\$0	\$0	\$12,885	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,88
Consultants		\$0	\$0	\$0	\$0	\$14	\$8	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2
Maintenance Contract		\$0	\$0	\$0	\$0	\$1,366	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,36
Legal		\$0	\$0	\$75	\$0	\$0	\$0	\$1,105	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,18
Software License		\$0	\$0	\$0	\$0	\$375	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$37
Other Contract Services		\$0	\$6,289	\$6,988	\$750	\$0	\$2,209	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,23
Moving Services		\$0	\$0	\$0	\$395	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$39
Building & Additions		\$0	\$34,672	\$198,667	\$200,585	\$284,668	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$718,59
Architect		\$0	\$0	\$80,626	\$170,132	\$37,906	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$288,66
Engineering		\$0	\$0	\$0	\$3,705	\$9,735	\$6,840	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,28
Inspection & Testing		\$0	\$0	\$8,142	\$10,938	\$10,500	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$29,58
Project Management		\$0	\$3,073	\$154,904	\$87,291	\$139,821	\$3,571	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$388,65
Cap Equipment		\$0	\$0	\$0	\$35,892	\$80,090	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$115,98
Non-Cap Equipment		\$0	\$89,204	\$0	\$84,590	\$193,782	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$367,57
Total		\$0	\$133,238	\$449,401	\$608,656	\$763,095	\$12,628	\$1,105	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,968,12
Project Budget	\$1,968,124	•	•			•		•		•	· •	· ·	•	•		V 1,000,100
Less Other Funding	\$0															
Net	\$1,968,124															
	\$1,968,124															
Running Balance	<u>\$0</u>															

AA 7100004																
Master Planning, Program Manageme	nt, Overhead (1	12)														
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$139,302	\$187,927	\$245,329		\$0	\$0	\$0	\$0	\$573,828
Project Management		\$0	\$0	\$0	\$0	\$76,015	\$150	\$0	\$49,170	\$135,533	\$0	\$0	\$0	\$0	\$0	\$260,868
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	T -	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$76,015	\$150	\$139,302	\$237,097	\$380,863	\$1,270	\$0	\$0	\$0	\$0	\$834,697
Project Budget																
Less Other Funding	•															
Net	\$834,697															
Actual Measure AA Expenditures																
Running Balance	\$0															

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
AA 7100154																
Energy Efficiency Projects (113)																
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$(\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$(\$0
Building & Additions		\$0	\$0	\$189	\$2,108,853	\$990,389	-\$97,621	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$(\$3,001,810
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$(
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$(\$0
Inspection & Testing		\$0	\$0	\$0	\$4,020	\$0	\$10,118	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$(\$14,138
Project Management		\$0	\$0	\$0	\$0	\$0	\$825	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$(\$0
Total		\$0	\$0	\$189	\$2,112,873	\$990,389	-\$86,678	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$(\$3,016,773
Project Budget	\$3,508,088					•		•		•				•		
Less Other Funding	\$491,315		* Other Fund	ing Source:												
Net	\$3,016,773		1) DWP \$18.	715.00 receive	ed											
Actual Measure AA Expenditures				,519.77 receiv												
Running Balance			3) Gas Co. \$	26,080 receive	ed											

A A 7400004																
AA 7100064																
Community Classroom & Facility Projects	(114)															
Supplies		\$0	\$0	\$0	\$124	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$124
Legal		\$0	\$0	\$1,867	\$1,418	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,285
Other Contract Services		\$0	\$3,720	\$1,869	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,588
Building & Additions		\$0	\$434,578	\$1,369,441	\$408,696	-\$1,003	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,211,712
Architect		\$0	\$263,833	\$48,120	\$1,318	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$313,272
Engineering		\$0	\$3,220	\$3,143	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,363
Inspection & Testing		\$0	\$41,002	\$80,885	\$1,495	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$123,382
Project Management		\$135	\$117,247	\$143,780	\$27,570	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$288,732
Non-Cap Equipment		\$0	\$0	\$209,726	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$209,726
Total		\$135	\$863,599	\$1,858,831	\$440,621	-\$1,003	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,162,183
	3,162,183	·		-			<u> </u>	·			-	,				
Less Other Funding	\$0															
Net \$	3,162,183															
Actual Measure AA Expenditures \$	3,162,183															
Running Balance	\$0															

AA 7100057															I	
Real Property Acquisition (115)																
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$659	\$0	\$0	\$0	\$0	\$0	\$659
Other Contract Services		\$0	\$39	\$7,000	\$0	\$15,800	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$22,839
Site Acquisition		\$1,739,979	\$4,001,204	\$9,022,207	\$0	\$0	\$0	\$0	\$5,013,226	\$4,821,600	\$0	\$0	\$0	\$0	\$0	\$24,598,214
Inspection & Testing		\$8,689	\$7,986	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,674
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total			\$4,009,228	\$9,029,207	\$0	\$15,800	\$0	\$0	\$5,013,226	\$4,822,259	\$0	\$0	\$0	\$0	\$0	\$24,638,386
Project Budget	\$24,638,386								,							
Less Other Funding																
Net																
Actual Measure AA Expenditures																
Running Balance	\$0															

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
AA 7100058, 7100151, 7100156, 7100	059															1
Roadways, Walkways, Grounds, Parl		Sarages (116)												 		
Supplies		\$0	\$0	\$0	\$0	\$4,616	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$(\$4,616
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$(\$125
Consultants		\$0	\$0	\$0	\$48,090	\$5,018	\$0	\$0	\$0			\$0	\$0		\$0	\$53,108
Other Contract Services		\$218	\$770	\$122	\$25,249	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Building & Additions		\$185,345	\$6,731	\$113,784	\$321,603	\$975,401	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,602,864
Architect		\$0	\$0	\$0	\$103,569	\$19,225	\$1,240	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$124,035
Engineering		\$0	\$0	\$0	\$1,095	\$1,445	\$0	\$0	\$0	\$0		\$0	\$0		\$0	
Inspection & Testing		\$13,380		\$13,553	\$20,126	\$42,865	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	40.1.0.
Project Management		\$24,404		\$21,945	\$54,095	\$104,943	\$1,411	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$219,237
Total		\$223,347	\$27,804	\$149,403	\$573,951	\$1,153,512	\$2,652	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,130,670
Project Budget	+ /- /			_												
Less Other Funding	+ 1,1,		* Other Fund													
Net	+-,,		1) Measure S	S: \$3,891,747												
Actual Measure AA Expenditures			2) Measure \	': \$1,000,000	allocated											
Running Balance	\$0															

AA 7100069		I												Ī	T	
Infrastructure & Technology - Technol	logy (117)															
Software		\$0	\$0	\$0	\$0	\$0	\$218	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$218
Supplies		\$0	\$0	\$13,646	\$7,587	\$0	\$16,966	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$38,200
Maintenance Contract		\$0	\$9,472	\$46,300	\$210,581	\$18,944	\$42,415	\$9,472	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$337,186
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$49,589	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$49,589
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$207,423	\$33,063	\$576,294	\$0	\$1,145,668	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,962,449
Non-Cap Equipment		\$0	\$0	\$42,827	\$500	\$0	\$3,447	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$46,775
Total		\$0	\$216,896	\$135,838	\$794,963	\$18,944	\$1,258,304	\$9,472	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,434,417
Project Budget	\$2,434,417					,		,	,							
Less Other Funding	\$0															
Net	\$2,434,417															
Actual Measure AA Expenditures	\$2,434,417															
Running Balance	\$0															

AA 7100150																
Infrastructure & Technology - Utility (118)															
Software License		\$0	\$12,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,000
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$4,979	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,979
Project Management		\$0	\$3,240	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,240
Cap Equipment		\$0	\$0	\$7,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,534
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$20,219	\$7,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,753
Project Budget	\$27,753			-									_	-		
Less Other Funding	\$0															
Net	\$27,753															
Actual Measure AA Expenditures																
Running Balance	\$0															

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
AA 7100153																
Emergency Lighting, Fire Alarm, and	Security Syste	m (119)														
Supplies		\$0	\$0	\$0	\$0	\$2,348	\$0	\$0	\$2,671	\$0	\$0	\$0	\$0	\$0	\$0	\$5,020
Consultants/Legal		\$0	\$0	\$0	\$0	\$0	\$16	\$0	\$0	\$0	\$442	\$0	\$0	\$0	\$0	\$458
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$800	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$800
Maintenance Contract		\$0	\$0	\$648	\$0	\$39,700	\$0	\$2,700	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$43,048
Software Support		\$0	\$0	\$24,765	\$0	\$106,367	\$0	\$2,232	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$133,365
Other Contract Services		\$0	\$0	\$0	\$0	\$47,695	\$0	\$4,643	\$1,560	\$0	\$0	\$0	\$0	\$0	\$0	
Building & Additions		\$0	\$0	\$0	\$0	\$110	\$2,648,866	\$4,129,145	\$1,308,230	\$763,170	\$26,375	\$79,172	\$0	\$0	\$0	
Architect		\$0	\$0	\$0	\$0	\$0	\$18,925	\$0	\$0	\$5,047	\$0	\$0	\$0	\$0	\$0	
Engineering		\$0	\$0	\$0	\$0	\$211,030	\$389,013	\$156,247	\$255,798	\$358,560	\$114,585	\$0	\$0	\$0	\$0	\$1,485,233
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$58,831	\$4,800	\$0	\$0	\$0	\$0	\$0	\$0	
Project Management		\$0	\$0	\$0	\$0	\$51,008	\$52,044	\$79,285	\$16,500	\$49,738	\$240	\$0	\$0	\$0	\$0	
Cap Equipment		\$0	\$0	\$0	\$0	\$89,415	\$0	\$5,871	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$6,087	\$0	\$392,586	\$8,348	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$407,022
Total		\$0	\$0	\$31,500	\$0	\$940,259	\$3,118,012	\$4,438,953	\$1,589,560	\$1,176,515	\$141,642	\$79,172	\$0	\$0	\$0	\$11,515,614
	\$11,515,614			•	•	,					•					
Less Other Funding	\$0]														
Net	\$11,515,614	1														
Actual Measure AA Expenditures	\$11,515,614]														
Running Balance	\$0	1														

A A 7400440											, , , , , , , , , , , , , , , , , , ,					
AA 7100142																
Student Services (120)																
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0	
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	9
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	9
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	9
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	(
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	(
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,165,626	\$3,704,864	\$0	\$0	\$0	\$0	\$6,870,49
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	(
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	Ç
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	9
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	9
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	9
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	9
Total		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,165,626	\$3,704,864	\$0	\$0	\$0	\$0	\$6,870,49
Project Budget	\$6,870,490	•		•	•	•	•								•	,
Less Other Funding	90	* (Other Fundi	na Source:												

Total		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Budget	\$6,870,490							,
Less Other Funding	\$0		* Other Fund	ing Source:				
Net	\$6,870,490				1,000 received			
Actual Measure AA Expenditures	\$6,870,490		2) Measure L	J \$21,131,135	, Measure S \$4	5,595,322, Mea	asure V \$33,624	,909 allocated
Running Balance	\$0		3) Measure L	J. S & AA intei	ests \$21.681.3	08 allocated		

Cost of Issuance (121)																
Cost of Issuance		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026		\$0	\$0	\$0	\$0	\$0	\$498,026
Total		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$0	\$0	\$0	\$0	\$0	\$0	\$498,026
Project Budget	\$498,026															
Less Other Funding	\$0]														
Net	\$498,026	1														
Actual Measure AA Expenditures	\$498,026															
Running Balance	\$0															


Grand Total	$$4.900.734 \ 10.935.584 \ 17.864.407 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.113.759 \ 13.$	11 148 510

Measure AA Interest		18/19 Final
Parking Garage and Grounds - Stude	nt Services (9)	
Site Improvement		\$0
Building & Additions		\$5,192,948
Architect		\$0
Engineering		\$0
Inspection & Testing		\$0
Project Management		\$0
Total		\$5,192,948
Project Budget		
ctual Measure AA Interest Expenditures		•
Running Balance	\$0	

Measure V Bond Budget

As of March 31, 2023

	Project Name	Completion	Project Budget	Measure V Allocation	Other Funding	Measure V Expenditures as of 3/31/23	Measure V Expenditures as of 12/31/22	Measure V Expenditures Last Period	Total Measure V Remaining
101	Replacement Math and Science Extension Building	July 2024	\$124,958,336	\$82,317,992	\$42,640,344	\$52,666,542	\$46,282,515	\$6,384,027	\$29,651,450
102	Student Services	Completed	\$130,224,164	\$33,624,909	\$96,599,255	\$24,607,893	\$24,613,145	-\$5,252	\$9,017,016
103	Malibu Center	Completed	\$61,714,841	\$34,558,420	\$27,156,421	\$25,228,900	\$22,995,169	\$2,233,731	\$9,329,520
104	Early Childhood Development/Childcare	Completed	\$30,925,771	\$15,405,517	\$15,520,254	\$13,080,495	\$12,995,353	\$85,142	\$2,325,022
105	Art Building Replacement	August 2025	\$34,901,000	\$24,000,000	\$10,901,000	\$1,801,665	\$1,679,440	\$122,225	\$22,198,335
106	Business Building Renovation	December 2026	\$25,017,000	\$12,547,000	\$12,470,000	\$3,400	\$3,400	\$0	\$12,543,600
107	Air Conditioning	Completed	\$10,777,654	\$10,777,654	\$0	\$10,130,737	\$10,127,362	\$3,375	\$646,917
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$0	\$0	\$0	\$0	\$4,000,000
109	Master Planning	March 2023	\$1,000,000	\$1,000,000	\$0	\$746,558	\$746,558	\$0	\$253,442
110	Drescher Hall Modernization	On-Going	\$13,005,082	\$13,000,000	\$5,082	\$0	\$0	\$0	\$13,000,000
111	Outdoor Classroom	On-Going	\$321,723	\$321,723	\$0	\$321,723	\$321,723	\$0	\$0
112	John Adams MS Auditorium (SMMUSD)	Completed	\$20,000,000	\$20,000,000	\$0	\$20,000,000	\$20,000,000	\$0	\$0
113	City of Santa Monica	On-Going	\$20,000,000	\$20,000,000	\$0	\$0	\$0	\$0	\$20,000,000
114	Classrooms Relocation	Completed	\$7,400,000	\$7,400,000	\$0	\$7,286,719	\$7,286,719	\$0	\$113,281
124	Parking Structure 3 Improvement Project	June 2024	\$1,500,000	\$1,500,000	\$0	\$6,866	\$4,045	\$2,821	\$1,493,134
125	Gender Neutral Bathrooms	June 2025	\$3,500,000	\$3,500,000	\$0	\$0	\$0	\$0	\$3,500,000
126	Athletic Facilities	June 2026	\$5,000,000	\$5,000,000	\$0	\$1,735	\$0	\$1,735	\$4,998,265
115	TBD	On-Going	\$39,446,785	\$39,446,785	\$0	\$0	\$0	\$0	\$39,446,785
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$0	\$244,554	\$244,554	\$0	\$55,446
121	Cost of Issuance	On-Going	\$800,000	\$800,000	\$0	\$744,152	\$744,152	\$0	\$55,848
122	Management Reserve	On-Going	\$15,500,000	\$15,500,000		\$0	\$0	\$0	
	Unissuable Bond	On-Going	\$0	\$0	·	·	·	\$0	
	Project Totals		\$550,292,356	\$345,000,000	\$205,292,356	\$156,871,939	\$148,044,135	\$8,827,804	\$188,128,061

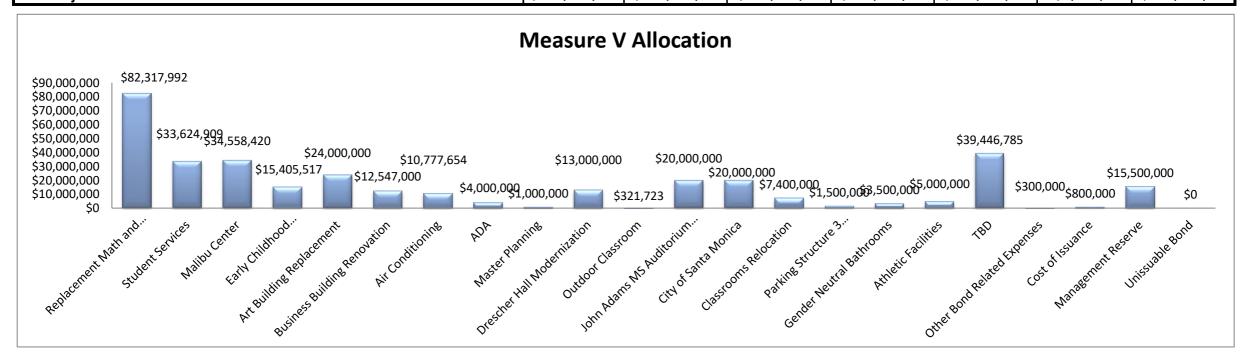

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure V Bond Budget History as of March 31, 2023

	Project Name	Completion	Preliminary Measure V	Measure V Budget as of	Measure V Budget as of	Variance	Measure V Remaining as
			Budget	12/31/22	3/31/23		of 3/31/23
101	Replacement Math and Science Extension Building	July 2024	\$82,317,992	\$82,317,992	\$82,317,992	\$0	\$29,651,450
102	Student Services	Completed	\$21,130,252	\$33,624,909	\$33,624,909	\$0	\$9,017,016
103	Malibu Center	Completed	\$25,000,000	\$34,558,420	\$34,558,420	\$0	\$9,329,520
104	Early Childhood Development/Childcare	Completed	\$15,405,517	\$15,405,517	\$15,405,517	\$0	\$2,325,022
105	Art Building Replacement	August 2025	\$24,000,000	\$24,000,000	\$24,000,000	\$0	\$22,198,335
106	Business Building Renovation	December 2026	\$12,547,000	\$12,547,000	\$12,547,000	\$0	\$12,543,600
107	Air Conditioning	Completed	\$10,777,654	\$10,777,654	\$10,777,654	\$0	\$646,917
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$4,000,000	\$0	\$4,000,000
109	Master Planning	March 2023	\$450,000	\$1,000,000	\$1,000,000	\$0	\$253,442
110	Drescher Hall Modernization	On-Going	\$13,000,000	\$13,000,000	\$13,000,000	\$0	\$13,000,000
111	Outdoor Classroom	On-Going	\$10,000,000	\$321,723	\$321,723	\$0	\$0
112	John Adams MS Auditorium (SMMUSD)	Completed	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$0
113	City of Santa Monica	On-Going	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$20,000,000
114	Classrooms Relocation	Completed	\$0	\$7,400,000	\$7,400,000	\$0	\$113,281
124	Parking Structure 3 Improvement Project	June 2024	\$0	\$1,500,000	\$1,500,000	\$0	\$1,493,134
125	Gender Neutral Bathrooms	June 2025	\$0	\$0	\$3,500,000	\$3,500,000	\$3,500,000
126	Athletic Facilities	June 2026	\$0	\$0	\$5,000,000	\$5,000,000	\$4,998,265
115	TBD	On-Going	\$57,271,585	\$39,446,785	\$39,446,785	\$0	\$39,446,785
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$300,000	\$0	\$55,446
121	Cost of Issuance	On-Going	\$800,000	\$800,000	\$800,000	\$0	\$55,848
122	Management Reserve	On-Going	\$28,000,000	\$24,000,000	\$15,500,000	-\$8,500,000	\$15,500,000
123	Unissuable Bond	On-Going	\$0	\$0	\$0	\$0	\$0
	Project Totals		\$345,000,000	\$345,000,000	\$345,000,000	\$0	\$188,128,061

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure V Project Schedule As of March 31, 2023

	Project Name	Completion	2020		20)21	20	22	2	023	2	024	2	025	;	2026	
101	Replacement Math and Science Extension Building	July 2024															1
102	Student Services	Completed															
103	Malibu Center	Completed															
104	Early Childhood Development/Childcare	Completed															
105	Art Building Replacement	August 2025															
106	Business Building Renovation	December 2026															
107	Air Conditioning	Completed															
108	ADA	On-Going															
109	Master Planning	March 2023						,									1
110	Drescher Hall Modernization	On-Going															1
111	Outdoor Classroom	On-Going															1
112	John Adams SMMUSD	Completed			<u> </u>			,									
113	City of Santa Monica	On-Going														\Box	1
114	Classrooms Relocation	Completed			<u> </u>			,									
124	Parking Structure 3 Improvement Project	June 2024														\Box	1
125	Gender Neutral Bathrooms	June 2025															
126	Athletic Facilities	June 2026															
115	TBD	On-Going															
120	Other Bond Related Expenses	On-Going															1
121	Cost of Issuance	On-Going															1
122	Management Reserve	On-Going															1
123	Unissuable Bond	On-Going														11	1
																	1
			In Pla	anni	ng	lr	Const	ructic	n								

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
V 7100090	. 5 (404)							
Replacement Math and Science Extensi	ion Building (101)	4.0	40	40	4.0	4.0	4.0	
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$67,242	\$0	\$0	\$0	\$67,242
Building & Additions		\$675	\$12,987	\$2,633	\$3,697,529	\$13,243,628	\$27,118,257	\$44,075,710
Architect		\$2,047,911	\$14,446	\$229,267	\$653,770	\$552,565	\$486,661	\$3,984,621
Engineering		\$0	\$0	\$19,622	\$6,966	\$10,940	, \$0	\$37,529
Inspection & Testing		\$30,804	\$44,077	\$60,666	\$225,542	\$919,688	\$416,969	
Project Management		\$130,874	\$617,805	\$347,350	\$474,483	\$866,097	\$277,800	\$2,714,409
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$89,286	\$89,286
Total		\$2,210,264	\$689,315	\$726,781	\$5,058,290	\$15,592,919	\$28,388,974	\$52,666,542
Project Budget	\$124,958,336	Received						
Less Other Funding	\$42,640,344	\$17,711,872 <u>*</u>	Other Funding Sour	<u>ce:</u>				
Net	\$82,317,992	1)) Measure U \$308,336 2	2) Measure AA \$2,244,0	08 allocated			
Actual Measure V Expenditures	\$52,666,542	3)) State of California \$40	,088,000 allocated				
Running Balance	\$29,651,451							
	1 -, , -							
V 7100142								
Student Services Building (102)								
Supplies		\$0	\$71,445	\$38,162	\$0	\$0	\$0	\$109,607
Other Contract Services		\$0	\$0	\$59,784	\$6,935	\$0	\$0	\$66,719
Consultants		\$0	\$0	\$687	\$0	\$0	\$0	\$687
Software Support		\$0	\$189,120	\$0	\$0	\$0	\$0	\$189,120
Moving Services		\$0	\$55,062	\$9,056	\$0	\$0	\$0	\$64,118
Building & Additions		\$0	\$12,355,060	\$4,201,966	\$355,441	\$0	-\$10,731	\$16,901,735
Architect		\$0	\$419,829	\$530,797	\$186,296	\$27,836	\$7,378	\$1,172,135
Engineering		\$0	\$140,458	\$67,481	\$0	\$0	\$0	\$207,939
Inspection & Testing		\$55,202	\$296,732	\$131,128	\$21,146	\$0	\$3,050	\$507,258
Project Management		\$0	\$900,333	\$219,425	\$85,310	\$13,020	\$0	\$1,218,088
Cap Equipment		\$0	\$1,565,928	\$90,915	\$0	\$0	\$0	\$1,656,844
Non-Cap Equipment		\$0	\$2,279,541	\$196,313	\$37,790	\$0	\$0	\$2,513,644
Total		\$55,202	\$18,273,508	\$5,545,714	\$692,918	•	-\$304	
Project Budget	\$130,224,164		Other Funding Sour	<u> </u>	,	, -,	¥ = 0 =	, ,== ,===
Less Other Funding	\$96,599,255) State of California \$1,3					
Net	\$33,624,909) Measure U \$21,131,13		5.322.			
Actual Measure V Expenditures	\$24,607,893) Measure AA \$6,870,49		-,- <u></u> ,			
Running Balance	\$9,017,016				cated			
Nullilling balance	\$2,017,010	٥,) Measure U, S & AA int	CICS13 741,001,300 dll0	cateu			

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
V 7100015					1			
V 7100015)\							
Malibu Site Acquisition and Center (103	5)	ćo	ćo	ćo	ćo	ćo	¢10.077	¢10.077
Supplies Software Support		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$10,977 \$7,716	\$10,977 \$7,716
Software Support		\$0	\$0 \$0	\$0	\$0	\$0 \$0	\$41,004	
Legal Other Contract Services		\$0	\$0 \$0	\$2,713	\$38,163	\$0 \$0	\$107,734	\$41,004 \$148,610
Consultants		\$0	\$0 \$0	\$0	\$38,103	\$0	\$32,582	\$32,582
Moving Services		\$0	\$0 \$0	\$0	\$0	\$0	\$11,936	\$11,936
Building & Additions		\$0	\$0	\$2,642,861	\$3,388,666	\$8,734,478	\$6,147,792	\$20,913,796
Architect		\$0	\$0	\$2,042,881	\$155,448	\$493,355	\$214,156	\$862,959
Engineering		\$0	\$0	\$8,482	\$0	\$15,268	\$8,641	\$32,392
Inspection & Testing		\$0	\$0	\$51,754	\$633,723	\$511,002	\$129,567	\$1,326,045
Project Management		\$0	\$0	\$49,588	\$581,175	\$626,405	\$289,610	\$1,546,778
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$35,447	\$35,447
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$12,015	\$246,643	\$258,658
Total		\$0	\$0	\$2,755,398	\$4,797,174	\$10,392,522	\$7,283,805	
Project Budget	\$61,714,841	7-1	*-1	Ψ=,: = =,====	¥ -,,	+	¥-,=-,	+,,
Less Other Funding	\$27,427,359	*	Other Funding Source	e:				
Net	\$34,287,482) Measure S \$25,132,56					
Actual Measure V Expenditures	\$25,228,900) Interest Allocated \$2,2					
Running Balance	\$9,058,582	_	, meerese / mocated φ2)2	3 1,7 3 1				
Nullilling Balance	73,030,302							
V 7100104								
Early Childhood Development/Childcare	e (104)							
Supplies		\$0	\$0	\$35,150	\$5,332	-\$500	-\$96	\$39,886
Other Contract Services		\$0	\$0	\$35,344	\$15,128	\$0	\$0	\$50,472
Consultants		\$0	\$0	\$16	\$0	\$0	\$0	\$16
Software Support		\$0	\$0	\$6,158	\$0	\$5,677	\$5,677	\$17,513
Legal		\$0	\$0	\$96	\$0	\$0	\$0	\$96
Building & Additions		\$0	\$0	\$8,879,770	\$1,603,432	\$0	\$73,242	\$10,556,444
Architect		\$0	\$0	\$262,660	\$275,924	\$105,158	\$15,112	\$658,854
Engineering		\$0	\$0	\$19,448	\$0	\$15,550	\$3,149	\$38,146
Inspection & Testing		\$0	\$0	\$349,661	\$135,767	\$3,700	\$5,200	\$494,328
Project Management		\$0	\$0	\$384,279	\$384,714	\$2,144	\$0	\$771,137
Cap Equipment		\$0	\$0	\$32,448	\$0	\$0	\$0	\$32,448
Non-Cap Equipment		\$0	\$0	\$328,242	\$92,913	\$0	\$0	\$421,155
Total		\$0	\$0	\$10,333,272	\$2,513,210	\$131,730	\$102,284	\$13,080,495
Project Budget	\$30,925,771	Received						
Less Other Funding	\$15,520,254	\$6,661,598	* (Other Funding Soul	rce:			
Net	\$15,405,517		1)	City of Santa Monica \$	\$6,661,598 committed			
Net Actual Measure V Expenditures			·					

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
			1	Ţ	Ţ	ı		
V 7100240								
Art Complex (105)		40	40	444044	40	40	40	444.044
Legal		\$0	\$0	\$14,811	\$0	\$0	\$0	\$14,811
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$20,991	\$40,710	\$1,344	\$0	\$63,045
Moving Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$184	\$407,369	\$3,040	\$0	\$1,791	\$0	\$412,200
Architect		\$0	\$0	\$39,542	\$569,178	\$28,572	\$53,340	\$690,632
Engineering		\$0	\$0	\$0	\$0	\$40,750	\$0	\$40,750
Inspection & Testing		\$0	\$35,495	\$25,052	\$43,653	\$45,227	\$1,400	\$150,827
Project Management		\$0	\$1,600	\$85,708	\$85,978	\$184,706	\$71,225	\$429,217
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$184	\$444,464	\$189,143	\$739,518	\$302,390	\$125,965	\$1,801,665
Project Budget	\$34,901,000	Received						
Less Other Funding	\$10,901,000	\$506,957 <u>*</u>	Other Funding Soul	<u>ce:</u>				
Net	\$24,000,000	1) State of California \$10	0,901,000 pending				
Actual Measure V Expenditures	\$1,801,665			•				
Running Balance	\$22,198,335							
V 7100243								
Business Building Replacement (106)								
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$3,400	\$0	\$0	\$0	\$3,400
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	
Total		\$0	\$0	\$3,400	\$0		\$0	
Project Budget	\$25,017,000	, , , , , , , , , , , , , , , , , , ,	, , ,	Ţ-, Z-	7-1		*-	, , , , ,
Less Other Funding	\$12,470,000	*	Other Funding Soul	ce:				
Net	\$12,547,000	_) State Funding \$12,47					
Actual Measure V Expenditures	\$3,400	_	, Juice Fullating 712,47	0,000				
·								
Running Balance	\$12,543,600							

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
V 7100188				T				
Air Conditioning (107)								
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$2,451	\$7,537,201	\$733,457	\$0	\$8,273,110
Architect		\$0	\$79,000	\$0	\$0	\$39,872	\$3,280	\$122,152
Engineering		\$417,960	\$217,966	\$26,992	\$81,868	\$109,823	\$3,375	\$857,984
Inspection & Testing		\$0	\$54,810	\$776	\$253,936	\$125,639	\$0	\$435,160
Project Management		\$4,370	\$4,570	\$35,700	\$365,350	\$32,340	\$0	\$442,330
Total		\$422,330	\$356,346	\$65,919	\$8,238,355	\$1,041,132	\$6,655	\$10,130,737
Project Budget	\$10,777,654	Ψ :==,σσσ	+ + + + + + + + + + + + + + + + + + + 		+0,200,000	4.,0.1,10	ψο,οοο	410,100,101
Less Other Funding	\$0							
Net	\$10,777,654							
Actual Measure V Expenditures	\$10,130,737							
Running Balance	\$646,917							
Nullilling Balance	5040,917							
V 7100004								
Master Plan (109)								
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$48,000	\$0	\$48,000
Advertising		\$0	\$641	\$0	\$0	\$0	\$0	\$641
Architect		\$0	\$112,073	\$528,182	\$37,861	\$0	\$14,900	\$693,016
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$3,800	\$1,100	\$0	\$0	\$0	\$4,900
Total		\$0	\$116,515	\$529,282	\$37,861	\$48,000	\$14,900	\$746,558
Project Budget	\$1,000,000	•	,	-	•	•		
Less Other Funding	\$0							
Net	\$1,000,000							
Actual Measure V Expenditures	\$746,558							
Running Balance	\$253,442							
<u> </u>	, , ,							
V 7100237								
Outdoor Classroom (111)								
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$100,000	\$102,023	\$102,495	\$0	\$0	\$0	\$304,518
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$17,205	\$0	\$0	\$0	\$0	\$17,205
Total		\$100,000	\$119,228	\$102,495	\$0	\$0	\$0	\$321,723
	\$321,723							
Project Budget	3321,723							
Project Budget Less Other Funding	\$0							
Less Other Funding	\$0							

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
V 74003C0								
V 7100268								
Parking Structure 3 Imp Project (124)		ćo	ćo	ćo	ćo	ćo	ćo	ćo
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	'
Architect		\$0	\$0	\$0	\$0	\$0	\$6,866	
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0 \$0	\$0	\$0	\$0	\$0	\$0	\$U *c occ
Total	¢4 500 000	\$0	\$0	\$0	\$0	\$0	\$6,866	\$6,866
Project Budget	\$1,500,000							
Less Other Funding	\$0							
Net	\$1,500,000							
Actual Measure V Expenditures	\$6,866							
Running Balance	\$1,493,134							
V 7100270								
Gender Neutral Bathroom Project (125)								
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0 \$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0 \$0	·
Engineering		\$0 \$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0 \$0	\$0	\$0	\$0		<u> </u>	
Project Management		\$0 \$0	\$0	\$0	\$0	\$0	\$0	
Total		\$0 \$0	\$0	\$0	\$0		\$ 0	
Project Budget	\$3,500,000	ΨΟ	ΨΟ	ΨΟ	ΨΟ	ΨΟ	ΨΟ	ΨΟ
Less Other Funding	\$3,500,000							
	· ·							
Net Na saura V Fura raditura a	\$3,500,000							
Actual Measure V Expenditures	\$0							
Running Balance	\$3,500,000							
V 7100271			I			Ī		
Athletic Facilities (126)								
Legal		\$0	\$0	\$0	\$0	\$0	\$1,735	\$1,735
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	·
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0		\$0	
Total		\$0	\$0	\$0	\$0		\$1,735	-
Project Budget	\$5,000,000	+-	+3	+•	4.0	Ψ*	Ţ.,. 30	1 7.,
Less Other Funding	\$0							
Net	\$5,000,000							
Actual Measure V Expenditures	\$3,000,000							
Running Balance	\$4,998,265							

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
V 7100242						1		
V 7100243 Classrooms Relocation (114)								
Supplies		\$0	\$0	\$0	\$0	\$11,963	\$0	\$11,963
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	
Building & Additions		\$0	\$3,467	\$5,709,329	\$391,967	\$0	\$0	\$6,104,763
Supplies		\$0	\$0	\$4,982	\$0	\$0	\$0	
Architect		\$0	\$184,434	\$78,179	\$92,082	\$0	\$0	
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	
Inspection & Testing		\$0	\$16,795	\$115,194	\$25,996	\$0	\$0	
Project Management		\$0	\$61,520	\$476,831	\$55,650	\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$58,331	\$0	\$0	\$0	
Total		\$0	\$266,216	\$6,442,846	\$565,695	\$11,963	\$0	
Project Budget	\$7,400,000	<u>.</u>						
Less Other Funding	\$0							
Net	\$7,400,000							
Actual Measure V Expenditures	\$7,286,719							
Running Balance	\$113,281							
V 7100255								
John Adams MS Auditorium - SMMUSI	D (112)							
Building and Additions		\$0	\$0	\$0	\$15,000,000	\$5,000,000	\$0	\$20,000,000
Total		\$0	\$0	\$0	\$15,000,000	\$5,000,000	\$0	\$20,000,000
Project Budget	\$20,000,000							
Less Other Funding	\$0							
Net	\$20,000,000							
Actual Measure V Expenditures	\$20,000,000							
Running Balance	\$0							

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
S7100048								
Other Bond Related Expenses (116)								
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Lease/Rental		\$0	\$13,590	\$18,171	\$6,814	\$0	\$0	\$38,576
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Software License		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Advertising		\$0	\$0	\$0	\$770	\$900	\$0	\$1,670
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$184	\$191,065	\$0	\$0		\$0	\$191,249
Inspection & Testing		\$0	\$13,060	\$0	\$0	\$0	\$0	\$13,060
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$184	\$217,715	\$18,171	\$7,584	\$900	\$0	\$244,554
		Ψ.σ.	Ψ=11,110	Ψ.Θ,	Ψ1,00+	ψοσο	ΨΟ	Ψ 244,334
Project Budget	\$300,000	Ψ.σ.	Ψ211,110	ψ·ο,····	Ψ1,004	Ψ000	Ψ0	Ψ244,334
	\$300,000 \$0	****		Ψ.Θ,	Ψ1,00-1	Ψσσσ	\$ 0	Ψ244,334
Project Budget		****	4211,1110	Ψ.Θ,	Ψ1,00-1	Ψσσσ	Ψ 0	Ψ244,334
Project Budget Less Other Funding	\$0	*	4211,110	Ψ.Θ,	Ψ1,00-1	 	Ψ0	Ψ244,334
Project Budget Less Other Funding Net	\$0 \$300,000	****	4211,1110	Ψ.Θ,	Ψ1,00-1	Ψσσσ	Ψ0	Ψ 244, 334
Project Budget Less Other Funding Net Actual Measure V Expenditures Running Balance	\$0 \$300,000 \$244,554	****	42.11,1.10	Ψ.Θ,	Ψ1,001	4000	•••	Ψ 244, 334
Project Budget Less Other Funding Net Actual Measure V Expenditures Running Balance Cost of Issuance (117)	\$0 \$300,000 \$244,554							
Project Budget Less Other Funding Net Actual Measure V Expenditures Running Balance Cost of Issuance (117) Cost of Issuance	\$0 \$300,000 \$244,554	\$291,277	\$0	\$0	\$0	\$452,875	\$0	\$744,152
Project Budget Less Other Funding Net Actual Measure V Expenditures Running Balance Cost of Issuance (117) Cost of Issuance Total	\$0 \$300,000 \$244,554 \$55,446					\$452,875		\$744,152
Project Budget Less Other Funding Net Actual Measure V Expenditures Running Balance Cost of Issuance (117) Cost of Issuance Total Project Budget	\$0 \$300,000 \$244,554 \$55,446 \$800,000	\$291,277	\$0	\$0	\$0	\$452,875	\$0	\$744,152
Project Budget Less Other Funding Net Actual Measure V Expenditures Running Balance Cost of Issuance (117) Cost of Issuance Total Project Budget Less Other Funding	\$0 \$300,000 \$244,554 \$55,446 \$800,000 \$0	\$291,277	\$0	\$0	\$0	\$452,875	\$0	\$744,152
Project Budget Less Other Funding Net Actual Measure V Expenditures Running Balance Cost of Issuance (117) Cost of Issuance Total Project Budget Less Other Funding Net	\$0 \$300,000 \$244,554 \$55,446 \$800,000 \$0 \$800,000	\$291,277	\$0	\$0	\$0	\$452,875	\$0	\$744,152
Project Budget Less Other Funding Net Actual Measure V Expenditures Running Balance Cost of Issuance (117) Cost of Issuance Total Project Budget Less Other Funding	\$0 \$300,000 \$244,554 \$55,446 \$800,000 \$0	\$291,277	\$0	\$0	\$0	\$452,875	\$0	\$744,152

Grand Total	\$3,079,439	\$20,483,307	\$26,712,421	\$37,650,605	\$33,015,286	\$35,930,880	\$156,871,938

SMC Bond Program (Measure AA and V) Bond Contractor List as of 3-31-2023

Student Services (Measure U #0, Measure S #9, Measure AA #120, Measure V #102):

Architect - Steinberg Architects, Morris Architects, SVA Architects

Contractor - Minco, Bernards Brothers, Spinitar

Engineering - IVA, Cogent Energy Engineering, XL Fire

Inspection & Testing – Geo Labs, BTC Labs - Vertical V, Peak Survey, LPI Rango Inc., Twining, AGE

Project Management - LPI, YNL, Vanir

Replacement Health/PE/Fitness/Dance Building (Measure S #4, Measure AA #104):

Architect - Gensler Architects

Contractor - Bernards Brothers

Engineering – IVA, Glumac

Inspection & Testing – GeoLabs, Ellis Environmental, Twining, Rango

Inspection, AGE

Project Management - LPI

Early Childhood Development (Measure S #5, Measure V #104):

Architect - Carde Ten Architects, SVA Architects

Consultant - Child Educational Center

Contractor - The Nazerian Group

Engineering – Jacobs

Inspection & Testing - Geo Labs, Rango Inspection, Twining

Project Management - LPI, Vanir, YNL

Malibu Site (Measure S #6, Measure AA #110, Measure V #103):

Architect - Quatro Design Group

Contractor - Master Contracting, Icon West

Consultant – m2 Strategic, Parker Environmental, M6 Consultants

Engineering – Ensitu Services, Jacobs, CNA

Inspection & Testing – Peak Surveys, Ellis Environmental, JL Inspection, Ninyo

& Moore, GeoLabs, Twining

Project Management - LPI, m6 Strategic, Vanir, YNL

Energy Efficiency Projects (Measure S #7, Measure AA #113):

Architect - N/A

Contractor – Compass Energy Solutions, Johnson Controls

Engineering - Compass Energy Solutions, Johnson Controls

Inspection & Testing - Ellis Environmental

Environmental Performance (Measure AA #101):

Architect - Kishimoto Architects

Contractor – SJ Amoroso Construction

Engineering – P2S Engineering

Inspection & Testing – Cannon, Peak Surveys

Project Management - LPI

Information Technology Relocation (Measure AA #102):

Architect - Morris Architects

Contractor - Minco, Bernards Brothers, Eidim AV Technology

Engineering – IVA, P2S Engineering

Inspection & Testing - Cannon, Peak Surveys, Geo Labs, Ellis Environmental,

Twining, JL Inspection, Rango Inc.

Project Management - LPI, CCS Presentation

Media and Technology Complex (Measure AA #103):

Architect - Clive Wilkinson Architects, Morris Architects

Contractor – H.B. Parkco Construction, Fast Track Construction, CW Driver, Dimension Data, Key Code Media, Omega

Construction

Consultant - EEG Services

Engineering – IVA, P2S Engineering

Inspection & Testing - Twining, Geo Labs, BTC Labs - Vertical V,

JL Inspection, EEG Services, Ellis Environmental, Rango

Inc., Cannon

Project Management – LPI

Madison East Wing Seismic Upgrade (Measure AA #107):

Architect - DLR Group - WWCOT, LPI

Contractor - Trimax, Bernards Brothers, Dimension Data

Engineering – IVA, Glumac

Inspection & Testing - Twining, Peak Surveys, LPI, All Group Engineering, EEG

Services, Ellis Environmental

Project Management - LPI

Business & Facilities Infrastructure (Measure AA #111):

Architect - LPI, Gwynne Pugh Urban Studio

Contractor - REC+S, Inc., Omega Construction,

Concept Consultant, Inc.

Engineering – N/A

Inspection & Testing - Ellis Environmental, JL Inspection

Project Management – LPI

Community Classroom & Facility Project (Measure AA #114)

Architect - Morris Architects

Contractor – Waisman Construction, Spinitar, Trimax

Engineering – IVA

Inspection & Testing – LPI, Twining

Project Management - LPI

Roadways, walkways, Grounds, Parking Lots, and Garages (Measure AA #116)

Architect - LPI, DLR Group - WWCOT

Contractor – Trimax, Pub Construction

Consultant - Walker Parking

Engineering – MK Engineering

Inspection & Testing - Ellis Environmental, Peak Surveys, LPI

Project Management – LPI

Emergency Lighting, Fire Alarm, and Security System (Measure AA #119)

Contractor – Red Hawk Fire and Security, Nexus

Engineering - MDC Engineers

Inspection & Testing - Rango Inc.

Project Management - LPI

Math and Science Addition (Measure AA #106/Measure V #101)

Architect - Cannon Design

Contractor – Icon West, The Nazerian Group

Consultant – N/A

Engineering – Arup

Inspection & Testing – AGE

Project Management - Vanir, YNL

Classrooms Relocation (Measure V #114)

Architect – Gwynne Pugh

Contractor - The Nazerian Group

Inspection & Testing – AGE

Project Management - Vanir, YNL

Art Building Replacement (Measure V #105)

Architect – Little Architects

Contractor – N/A

Engineering – tk1sc

Inspection & Testing – B2 Environmental, Geolabs, CNA

Project Management – Vanir, YNL

Air Conditioning (Measure V #107)

Architect - P2S

Contractor – A&B Construction, Inc

Engineering – tk1sc, P2S

Inspection & Testing - Rango Inc., Koury, B2 Environmental

Project Management - Vanir, YNL

Parking Structure 3 Improvement Project (Measure V #124)

Architect – SVA Architects

Gender Neutral Bathrooms (Measure V #125)

Architect - TSK Architects

Athletic Facilities (Measure V #126)

Architect - TBD



Paid Vendors List

(Vendors that Received Payments from Bond Funds)

For the 9 month period July 1, 2022 to March 31, 2023 (FY 2022-23)

Adaptive Building Group All Group Engineering (AGE)

ARC Printing B2 Environmental Cannon Design

Charter Communications
Chris Nelson and Associates

Dell Computer Dick Blick Art

Division of State Architect (DSA)

DLR Architects

Fagen Friedman and Fulfrost (FFF)

GeoLabs Grainger Inc

Harding Larmore Kutcher

Icon West Construction Company

ITSavvy

Jacobs Engineering JH Technologies

JL Inspection
Little Architects

LPI

M6 Consulting McMurray Stern

P2S

Pacific Office Design QDG Architecture Rango Inspection School Health Corp School Outfitters Shade Structures Inc Suttles Plumbing SVA Architects

tk1sc Twining

Vanir Construction Management

Virco Manufacturing Williams Scotsman
