



Citizens' Bond Oversight Committee (CBOC)

Meeting on July 16th, 2025

June 30th, 2025 Report

12 Months - FY 2024-25 (Preliminary)

BOND CAPITAL CONSTRUCTION REPORTS

District Management is responsible for the preparation and fair presentation of the statement of expenditures and bond proceeds in accordance with U.S. generally accepted accounting principles; this includes the design, implementation, and maintenance of internal control relevant to the preparation and fair presentation of the statement of expenditures of bond proceeds that is free from material misstatement, whether due to fraud or error.

This report is prepared in accordance with these requirements and all bond expenditures were made in compliance with all applicable laws.

Santa Monica College - Bond Capital Construction Budget Summary - 6-30-2025												
Project Number	Project Name	Measure U Budget	Measure S Budget	Measure AA Budget	Measure V Budget	Interest	Other Funding Received *	Other Funding Pending **	Total Budget	Estimate at Completion	Status	Bond Funds Remaining
U-A	Purchase of BAE Airport Site	\$30,280,878							\$30,280,878	\$30,280,878	Completed	\$0
U-B	Emeritus College Facility	\$8,909,940					\$693,842		\$9,603,782	\$9,603,782	Completed	\$0
U-C	Purchase of 1738 Pearl Street	\$749,208							\$749,208	\$749,208	Completed	\$0
U-D	PE Temp. Bldg. Replacement	\$2,797,033							\$2,797,033	\$2,797,033	Completed	\$0
U-E	Remodel Library Village for Math	\$1,458,690							\$1,458,690	\$1,458,690	Completed	\$0
U-F	SM Airport Campus Site Improvements	\$4,170,264							\$4,170,264	\$4,170,264	Completed	\$0
U-G	SM Airport Campus West Building	\$19,709,741							\$19,709,741	\$19,709,741	Completed	\$0
U-H	Theater Arts Renovation	\$19,544,314							\$19,544,314	\$19,544,314	Completed	\$0
U-I	Earthquake Rpl. Liberal Arts North	\$6,011,584					\$6,496,141		\$12,507,725	\$12,507,725	Completed	\$0
U-K	Earthquake Rpl. Liberal Arts South	\$6,108,150					\$10,625,070		\$16,733,220	\$16,733,220	Completed	\$0
U-L	Shuttle Replacement Parking	\$18,969,509							\$18,969,509	\$18,969,509	Completed	\$0
U-M	North Quad Plaza	\$11,388,463							\$11,388,463	\$11,388,463	Completed	\$0
U-Q	Infrastructure & Safety	\$4,003,084							\$4,003,084	\$4,003,084	Completed	\$0
U-R	Restroom Improvements	\$17,501							\$17,501	\$17,501	Completed	\$0
S-1	Athletic Fields Phase I, Corsair Field		\$4,372,535				\$67,530		\$4,440,065	\$4,440,065	Completed	\$0
S-1A	Athletic Fields Phase I, John Adams		\$2,969,807						\$2,969,807	\$2,969,807	Completed	\$0
S-10	Pico Promenade Improvements, Phase I		\$1,018,009						\$1,018,009	\$1,018,009	Completed	\$0
S-13	Adv. Architecture Related Exp for AA		\$0						\$0	\$0	Completed	\$0
AA-114	Community Classroom & Facility Projects			\$3,162,183					\$3,162,183	\$3,162,183	Completed	\$0
U-T	14th and Pico Project	\$319,242							\$319,242	\$319,242	Completed	\$0
U-N	Letters & Sci Demo/Restore	\$0							\$0	\$0	Completed	\$0
AA-108	Renovation of Corsair Stadium and Field			\$3,882,204		\$2,149,609			\$6,031,813	\$6,031,813	In Construction	\$3,017,525
S-2	Performing Arts Complex		\$37,697,625				\$2,992,576		\$40,690,201	\$40,690,201	Completed	\$0
U-J	Music Complex	\$2,011,371					\$2,618,113		\$4,629,484	\$4,629,484	Completed	\$0
S-3, AA-109	Career Opportunity Center			\$0					\$0	\$0	Completed	\$0
AA-118	Infrastructure & Technology - Utility			\$27,753					\$27,753	\$27,753	Completed	\$0
AA-111	Business & Facilities Infrastructure			\$1,968,124					\$1,968,124	\$1,968,124	Completed	\$0
AA-117	Infrastructure & Technology - Technology			\$2,434,417					\$2,434,417	\$2,434,417	Completed	\$0
S-7, AA-113	Energy Efficiency Projects		\$293,361	\$3,016,773			\$708,637		\$4,018,771	\$4,018,771	Completed	\$0
S-15	Signage Safety/Information		\$706,713						\$706,713	\$706,713	Completed	\$0
AA-102	Infrastructure & Technology - Information Technology Relocation			\$23,140,771			\$19,798		\$23,160,569	\$23,160,569	Completed	\$0
S-8, AA-116	Satellite Campus Parking Facilities and Roadway		\$3,891,747	\$2,130,670					\$6,022,417	\$6,022,417	Completed	\$0
AA-107	Madison East Wing Seismic Upgrade			\$30,161,852					\$30,161,852	\$30,161,852	Completed	\$0
S-4, AA-104	Replacement Health/PE/Fitness Central Plant Building		\$11,603,383	\$44,428,222			\$208,847		\$56,240,452	\$56,240,452	Completed	\$0
AA-101	Environmental Performance - Central Plant Connections			\$10,767,251					\$10,767,251	\$10,767,251	Completed	\$0
S-14, AA-115	Real Property Acquisition		\$45,597	\$24,638,386				\$24,683,983	\$24,683,983	\$24,683,983	Completed	\$0
AA-103	Media and Technology Complex - Academy Site			\$123,509,130			\$6,835,391		\$130,344,521	\$130,344,521	Completed	\$0
AA-119	Emergency Lighting, Fire Alarm, and Security System			\$11,515,614					\$11,515,614	\$11,515,614	Completed	\$0
15004829	Student Services Building	\$21,131,135	\$45,595,322	\$6,870,490	\$27,773,115	\$22,070,112	\$1,321,000		\$124,761,174	\$124,761,174	Completed	\$2,499,658
S-5, V-104	Early Childhood Development/Childcare		\$8,858,656		\$15,405,517		\$6,661,598		\$30,925,771	\$30,925,771	Completed	\$2,175,389
S-6, AA-110, V-103	Malibu Center and Site Acquisition		\$25,132,568		\$34,558,420	\$2,294,791			\$61,985,779	\$61,985,779	Completed	\$5,532,211
U-S, S-11, AA-112, V-109	Master Planning	\$2,110,430	\$716,428	\$834,697	\$1,000,000				\$4,661,555	\$4,661,555	In Design	\$29,778
U-P, AA-106, V-101	Replacement Math and Science Extension Building	\$308,336		\$2,004,184	\$82,317,992		\$39,615,000		\$124,245,512	\$124,245,512	Completed	\$14,496,630
AA-105, V-110	Drescher - Academic Modernization, Bookstore, Pico Promenade II			\$5,082	\$13,000,000				\$13,005,082	\$13,005,082	In Planning	\$12,995,038
V-105	Art Building Replacement				\$52,532,040		\$8,039,870	\$2,861,130	\$63,433,040	\$63,433,040	In Construction	\$31,584,468
V-106	Business Building Renovation				\$12,547,000	\$12,470,000			\$25,017,000	\$25,017,000	In Planning	\$12,543,600
V-107	Air Conditioning				\$10,130,737				\$10,130,737	\$10,130,737	Completed	\$0
V-108	ADA				\$4,000,000				\$4,000,000	\$4,000,000	In Planning	\$4,000,000
V-111	Outdoor Classroom				\$321,723				\$321,723	\$321,723	Completed	\$0
V-112	John Adams MS Auditorium (SMMUSD)				\$20,000,000				\$20,000,000	\$20,000,000	Completed	\$0
V-113	Memorial Park Project				\$20,000,000				\$20,000,000	\$20,000,000	In Planning	\$19,996,519
V-114	Classrooms Relocation				\$7,286,719				\$7,286,719	\$7,286,719	Completed	\$0
V-124	Parking Structure 3 Improvement Project				\$6,000,000				\$6,000,000	\$6,000,000	In Design	\$5,847,667
V-125	Gender Neutral Bathrooms				\$6,057,602				\$6,057,602	\$6,057,602	In Design	\$5,826,631
V-126	Athletic Facilities				\$20,325,749				\$20,325,749	\$20,325,749	In Design	\$16,926,363
S-12, V-120	Other Bond Related Expenses		\$476,636		\$300,000				\$776,636	\$776,636	In Planning	\$55,446
V-115	TBD				\$0				\$0	\$0	Completed	\$0
S-16, AA-121, V-121	Cost of Issuance		\$119,470	\$498,026	\$744,152				\$1,361,648	\$1,361,648	Completed	\$0
AA-122, V-122	Management Reserve			\$0	\$10,699,234	\$10,134,488			\$20,833,722	\$20,833,722	In Planning	\$10,699,234
U-U, S-17, AA-123, V-123	Unissuable	\$1,127	\$2,143	\$4,171					\$7,441	\$7,441	On-Going	\$0
	Project Totals	\$160,000,000	\$143,500,000	\$295,000,000	\$345,000,000	\$49,119,000	\$86,903,413	\$2,861,130	\$1,082,383,543	\$1,082,383,543		\$148,226,157
	* SOURCES RECEIVED: City of SM: \$16,868,421; FEMA: \$2,456,388; State: \$50,849,870; Prop T: \$2,618,113; DWP: \$86,245; SCE: \$844,284; Gas Co.: \$106,262; Madison Foundation: \$2,992,576; KCRW: \$6,803,412; Emeritus College Foundation: \$693,842.											
	** SOURCES PENDING: State: \$2,861,130											

6/30/2025

SANTA MONICA COMMUNITY COLLEGE DISTRICT


Bond Sales / Expenses Report

As of June 30, 2025

Total Bond Program (AA and V)	\$640,000,000
Total Bonds Issued	\$639,995,829
Total Expenses as of 6-30-2025	\$491,769,672
Total Available Remaining	\$148,226,157
Total Unsold Bond	\$4,171

Measure AA Bond \$295,000,000	
Bond Issue Date	Amount
2010	\$100,000,000
2014	\$144,995,829
2017	\$50,000,000
Total Available	\$294,995,829
Total Expenses as of 6-30-2025	\$291,978,304
Total Available Remaining	\$3,017,525
Unsold Bond Amount	\$4,171
Total Available as of 7-1-2025	\$3,021,696

Measure V Bond \$345,000,000	
Bond Issue Date	Amount
2018	\$180,000,000
2022	\$165,000,000
Total Available	\$345,000,000
Total Expenses as of 6-30-2025	\$199,791,368
Total Available Remaining	\$145,208,632
Unsold Bond Amount	\$0
Total Available as of 7-1-2025	\$145,208,632

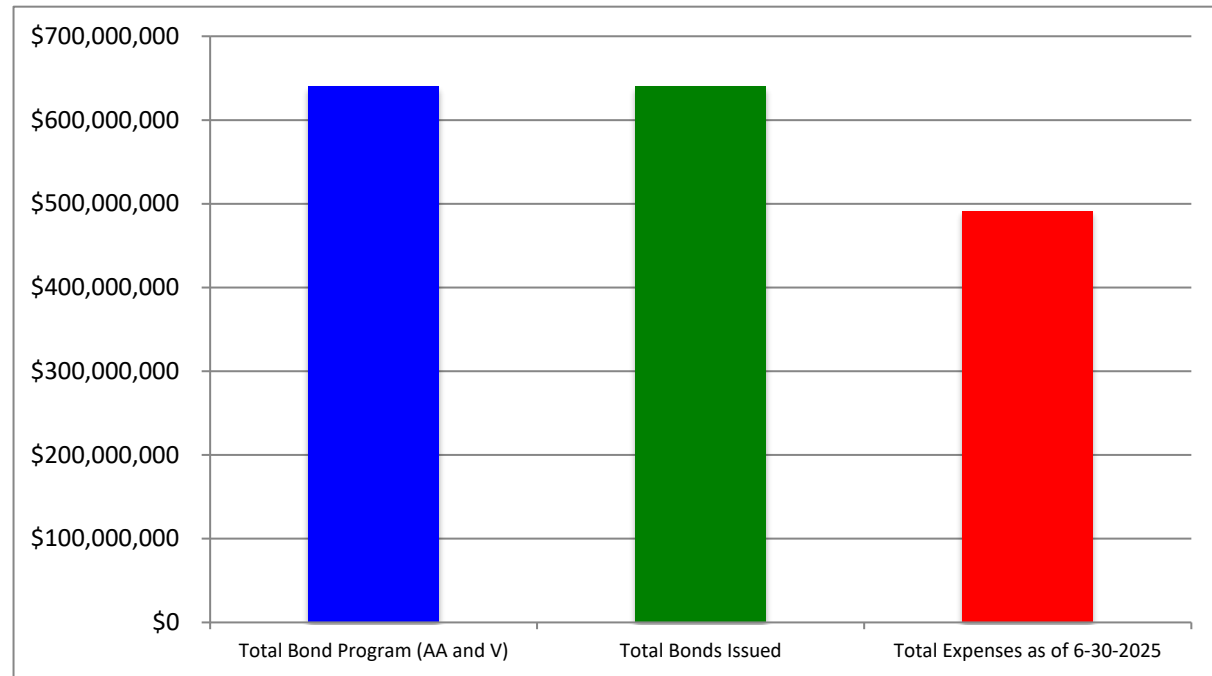


Interest	Measure U	Measure S	Measure AA	Measure V
As of 6-30-24	\$7,034,106	\$12,137,849	\$7,342,557	\$22,604,488
Expenditure / Arbitrage as of 6-30-24	\$7,034,106	\$12,137,849	\$5,192,948	\$0
Available Interest as of 7-1-24	\$0	\$0	\$2,149,609	\$22,604,488

INTEREST TOTALS
\$49,119,000
\$24,364,903
\$24,754,097

SANTA MONICA COMMUNITY COLLEGE DISTRICT
Measure AA Bond Budget
As of June 30, 2025

MEASURE AA

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 6/30/25	Measure AA Expenditures as of 3/31/25	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant Connections	Completed	\$10,767,251	\$10,767,251	\$0	\$10,767,251	\$10,767,251	\$0	\$0
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$23,160,569	\$23,140,771	\$19,798	\$23,140,771	\$23,140,771	\$0	\$0
103	Media and Technology Complex - Academy Site	Completed	\$130,344,521	\$123,509,130	\$6,835,391	\$123,509,130	\$123,509,130	\$0	\$0
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$56,240,452	\$44,428,222	\$11,812,230	\$44,428,222	\$44,428,222	\$0	\$0
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	Completed	\$13,005,082	\$5,082	\$13,000,000	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	Completed	\$124,245,512	\$2,004,184	\$122,241,328	\$2,004,184	\$2,004,184	\$0	\$0
107	Madison East Wing Seismic Upgrade	Completed	\$30,161,852	\$30,161,852	\$0	\$30,161,852	\$30,161,852	\$0	\$0
108	Renovation of Corsair Stadium and Field	June 2026	\$6,031,813	\$3,882,204	\$2,149,609	\$864,679	\$383,144	\$481,535	\$3,017,525
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
110	Malibu Center	Completed	\$61,985,779	\$0	\$61,985,779	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$1,968,124	\$1,968,124	\$0	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	Completed	\$834,697	\$834,697	\$0	\$834,697	\$834,697	\$0	\$0
113	Energy Efficiency Projects	Completed	\$3,508,088	\$3,016,773	\$491,315	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$3,162,183	\$3,162,183	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$24,638,386	\$24,638,386	\$0	\$24,638,386	\$24,638,386	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$7,022,417	\$2,130,670	\$4,891,747	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$2,434,417	\$2,434,417	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$27,753	\$27,753	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	Completed	\$11,515,614	\$11,515,614	\$0	\$11,515,614	\$11,515,614	\$0	\$0
120	Student Services	Completed	\$130,224,164	\$6,870,490	\$123,353,674	\$6,870,490	\$6,870,490	\$0	\$0
121	Cost of Issuance	Completed	\$498,026	\$498,026	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
123	Unissuable Bond	Completed	\$4,171	\$4,171	\$0	\$0	\$0	\$0	\$4,171
	Project Totals		\$641,776,700	\$295,000,000	\$346,780,871	\$291,978,304	\$291,496,769	\$481,535	\$3,021,696

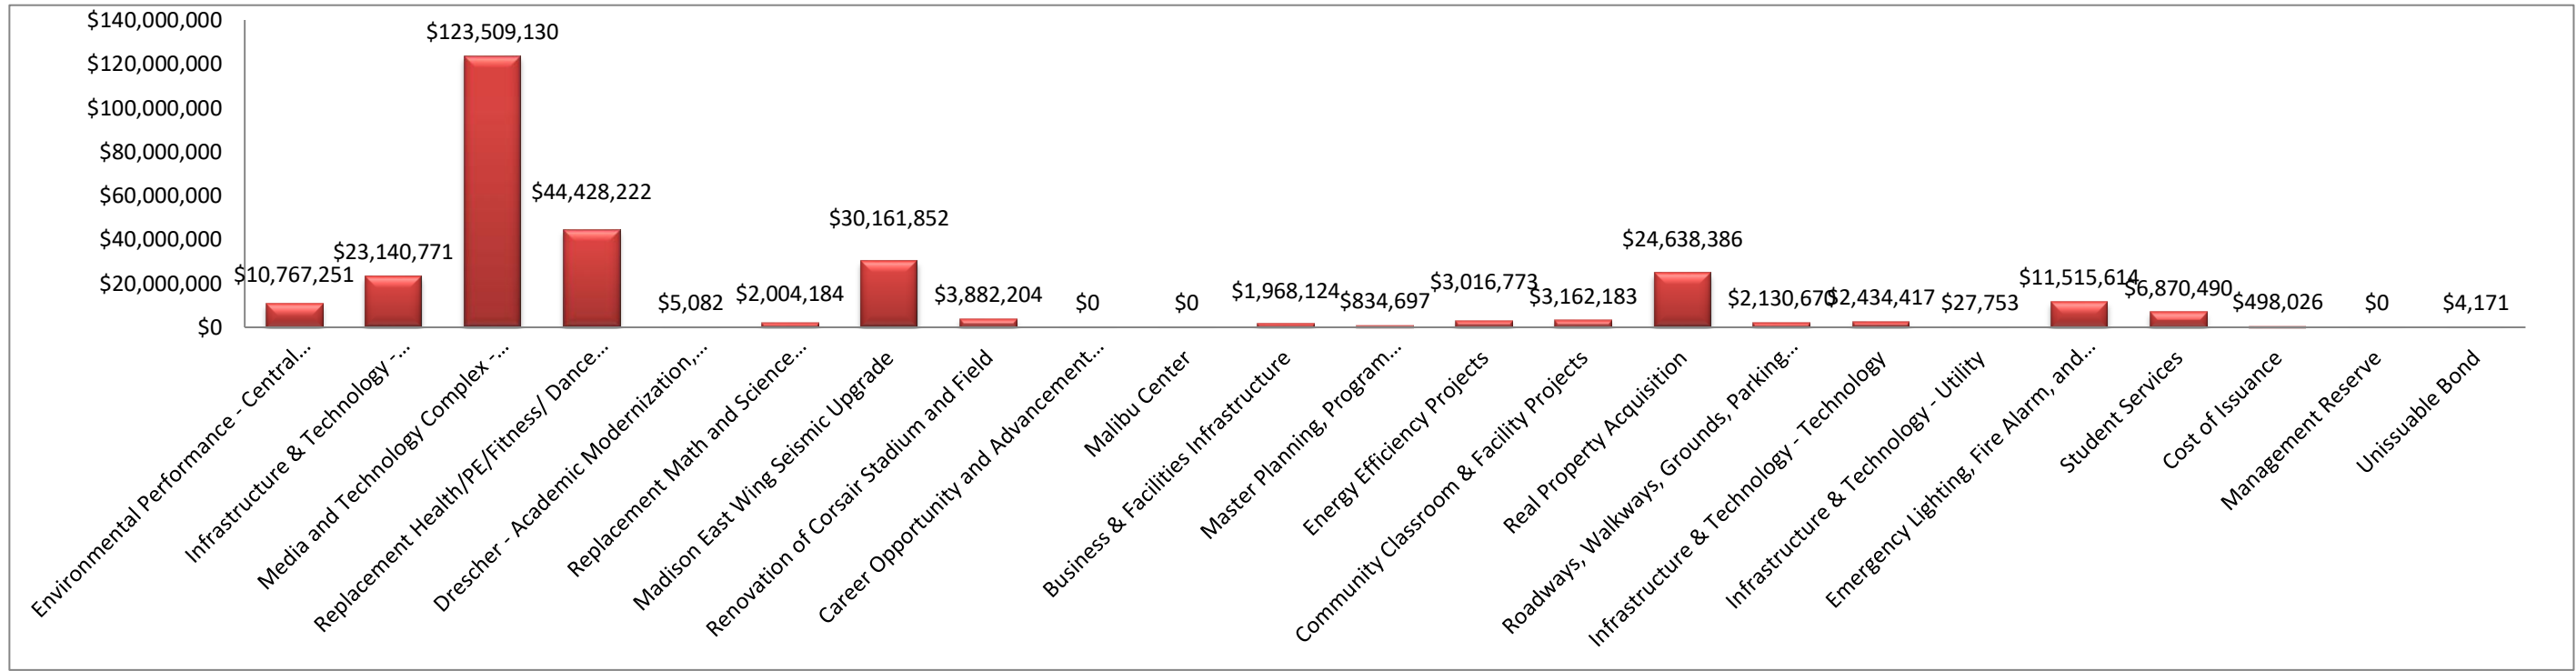

SANTA MONICA COMMUNITY COLLEGE DISTRICT
Measure AA Bond Budget History
as of June 30, 2025

MEASURE AA

	Project Name	Completion	Preliminary Measure AA Budget	Measure AA Budget as of 3/31/25	Measure AA Budget as of 6/30/25	Variance	Measure AA Remaining as of 6/30/25
101	Environmental Performance - Central Plant Connections	Completed	\$12,034,042	\$10,767,251	\$10,767,251	\$0	\$0
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$13,287,218	\$23,140,771	\$23,140,771	\$0	\$0
103	Media and Technology Complex - Academy Site	Completed	\$57,480,824	\$123,509,130	\$123,509,130	\$0	\$0
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$29,232,317	\$44,428,222	\$44,428,222	\$0	\$0
105	Drescher - Academic Modernization, Bookstore, Pico Promenade II	Completed	\$34,026,480	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	Completed	\$68,259,000	\$2,004,184	\$2,004,184	\$0	\$0
107	Madison East Wing Seismic Upgrade	Completed	\$6,146,000	\$30,161,852	\$30,161,852	\$0	\$0
108	Renovation of Corsair Stadium and Field	June 2026	\$11,203,000	\$3,882,204	\$3,882,204	\$0	\$3,017,525
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$32,384,000	\$0	\$0	\$0	\$0
110	Malibu Center	Completed	\$6,069,031	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$17,506,952	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	Completed	\$2,000,000	\$834,697	\$834,697	\$0	\$0
113	Energy Efficiency Projects	Completed	\$5,371,136	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$0	\$24,638,386	\$24,638,386	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$0	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	Completed	\$0	\$11,515,614	\$11,515,614	\$0	\$0
120	Student Services	Completed	\$0	\$6,870,490	\$6,870,490	\$0	\$0
121	Cost of Issuance	Completed	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$0	\$0	\$0	\$0	\$0
123	Unissuable Bond	Completed	\$0	\$4,171	\$4,171	\$0	\$4,171
	Project Totals		\$295,000,000	\$295,000,000	\$295,000,000	\$0	\$3,021,696

MEASURE AA

Page 6

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
AA 7100062																		
Environmental Performance - Central Plant Connections (101)																		
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$125
Other Contract Services		\$0	\$0	\$49,837	\$16,239	\$0	\$0	\$0	\$0	\$9,920	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$75,996
Consultants		\$0	\$0	\$0	\$0	\$28	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$28
Building & Additions		\$0	\$0	\$0	\$361	\$729	\$640	\$1,328,592	\$6,934,044	\$446,861	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$8,711,229
Architect		\$0	\$385	\$148,311	\$176,897	\$36,256	\$0	\$0	\$0	\$0	\$15,699	\$0	\$0	\$0	\$0	\$0	\$0	\$377,547
Engineering		\$48,500	\$0	\$4,000	\$0	\$152,010	\$39,638	\$66,918	\$138,887	\$62,883	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$512,836
Inspection & Testing		\$0	\$0	\$7,688	\$0	\$0	\$0	\$7,310	\$137,150	\$4,382	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$156,529
Project Management		\$0	\$17,263	\$55,116	\$48,685	\$61,908	\$19,313	\$104,575	\$526,072	\$99,840	\$190	\$0	\$0	\$0	\$0	\$0	\$0	\$932,961
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$48,500	\$17,648	\$264,951	\$242,307	\$250,931	\$59,591	\$1,507,396	\$7,736,152	\$623,886	\$15,889	\$0	\$0	\$0	\$0	\$0	\$0	\$10,767,251
Project Budget	\$10,767,251																	
Less Other Funding	\$0																	
Net	\$10,767,251																	
Actual Measure AA Expenditures	\$10,767,251																	
Running Balance	\$0																	

AA 7100063																		
Infrastructure & Technology - IT Relocation (102)																		
Supplies		\$0	\$0	\$965	\$8,442	\$3,137	\$2,600	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$15,144
Consultants		\$0	\$0	\$0	\$0	\$408	\$0	\$7,800	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$8,208
Maintenance Contract		\$0	\$0	\$0	\$0	\$107,390	\$0	\$77,074	\$79	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$184,543
Legal		\$0	\$0	\$0	\$1,363	\$50	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,413
Printing		\$0	\$0	\$0	\$0	\$1,624	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,624
Postage		\$0	\$0	\$0	\$0	\$1,567	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,567
Other Contract Services		\$0	\$0	\$2,163	\$15,259	\$23,356	\$0	\$19,050	\$4,500	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$64,328
Moving		\$0	\$0	\$0	\$577	\$266	\$27,655	\$22,618	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$51,116
Site Improvement		\$0	\$0	\$0	\$24	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$24
Building & Additions		\$0	\$0	\$0	\$1,767,083	\$9,667,362	\$4,288,987	\$1,203,916	\$165,229	-\$19,798	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$17,072,780
Architect		\$105,049	\$482,261	\$505,580	\$183,181	\$287,201	\$236,860	\$120,091	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,920,223
Engineering		\$0	\$0	\$10,037	\$11,065	\$17,147	\$19,512	\$25,994	\$1,956	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$85,712
Inspection & Testing		\$10,291	\$8,793	\$21,449	\$137,523	\$499,982	\$200,262	\$568	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$878,868
Project Management		\$33,460	\$76,290	\$84,991	\$331,754	\$431,730	\$297,951	\$22,978	\$1,500	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,280,653
Cap Equipment		\$0	\$0	\$0	\$29,422	\$645,830	-\$29,090	\$589,604	\$9,811	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,245,576
Non-Cap Equipment		\$0	\$0	\$0	\$18,344	\$10,852	\$277,219	\$1,891	\$20,689	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$328,994
Total		\$148,800	\$567,344	\$625,185	\$2,504,035	\$11,697,901	\$5,321,956	\$2,091,584	\$203,764	-\$19,798	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$23,140,771
Project Budget	\$23,160,569	Received																
Less Other Funding	\$19,798	\$19,798																
Net	\$23,140,771																	
Actual Measure AA Expenditures	\$23,140,771																	
Running Balance	\$0																	

Infrastructure & Technology - IT Relocation


Project Description:
Relocation of IT/Telecom Departments, and renovation of Media Center

Facility Size:
9,230 sq/ft


Status:
Completed

Architect:
Morris Architects


Contractor:
Minco, Bernards Brothers

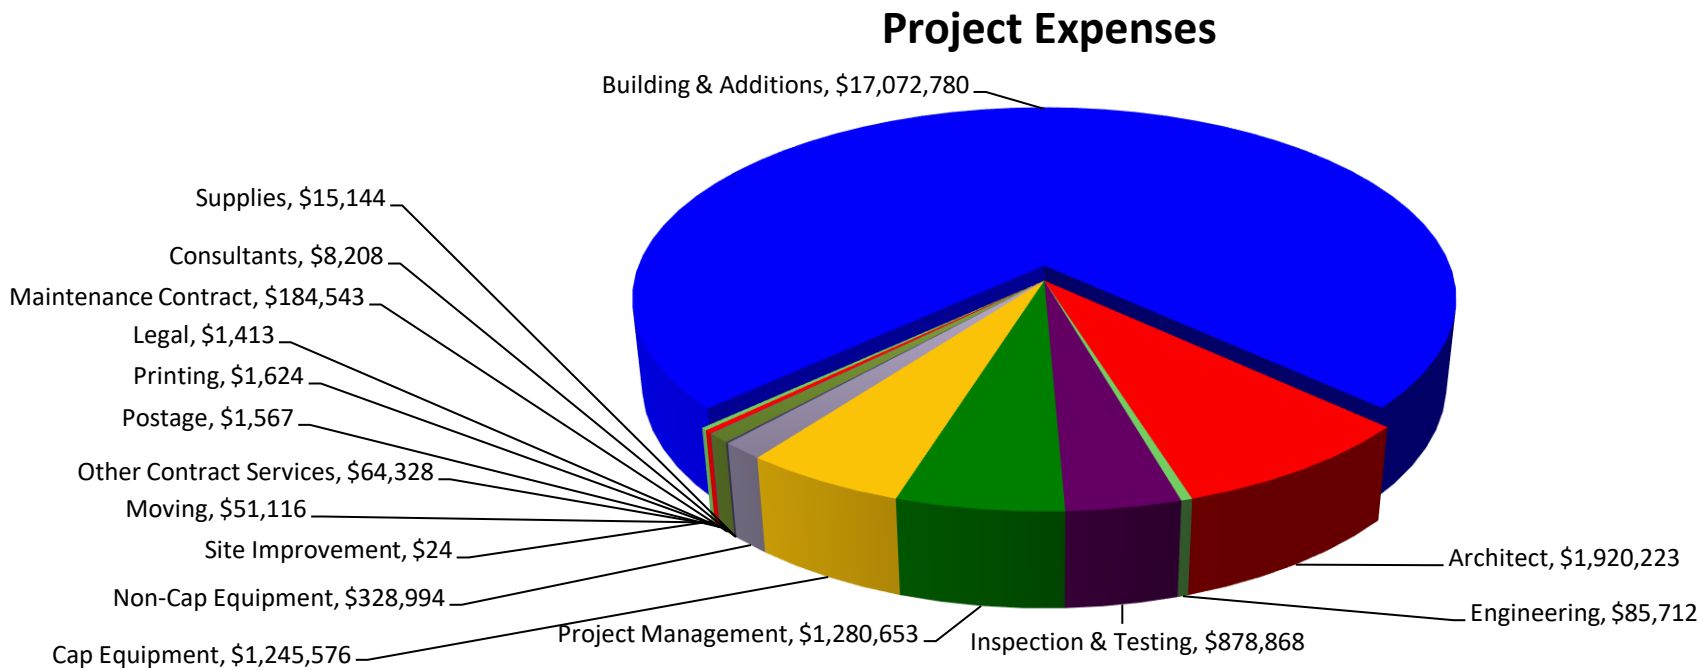

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
AA 7100061																		
Media and Technology Complex - Academy Site (103)																		
Consultants		\$0	\$0	\$20,675	\$12,576	\$9,488	\$7,789	\$2,102	\$0	\$12,922	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$65,551
Supplies		\$0	\$0	\$0	\$19,481	\$1,048	\$289	\$0	\$9,251	\$40,519	\$937	\$0	\$0	\$0	\$0	\$0	\$0	\$71,525
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$15,922	\$23,561	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$39,483
Legal		\$16,903	\$0	\$7,958	\$43,363	\$5,066	\$26,186	\$49,155	\$15,435	\$36,221	\$26,991	\$121,256	\$100,053	\$200,783	\$169,704	\$1,500	\$0	\$820,572
Software Support		\$0	\$0	\$0	\$1,982	\$0	\$0	\$0	\$6,548	\$6,975	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$15,505
Service Fee		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$17,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$17,000
Other Contract Services		\$3,993	\$5,763	\$13,456	\$39,188	\$0	\$0	\$5,853	\$22,622	\$18,628	\$7,690	\$7,550	\$0	\$0	\$0	\$0	\$0	\$124,743
Moving Expenses		\$0	\$0	\$0	\$38,756	\$0	\$0	\$0	\$0	\$97,543	\$17,556	\$0	\$0	\$0	\$0	\$0	\$0	\$153,855
Site Improvement		\$0	\$0	\$0	\$100,505	\$664	\$606	\$476	\$622	\$526	\$0	\$526	\$0	\$0	\$0	\$0	\$0	\$103,925
Building & Additions		\$0	\$538	\$1,498,660	\$3,543,657	\$11,820,615	\$17,734,534	\$23,465,347	\$16,267,550	\$25,548,089	\$219,234	\$626,512	-\$67,164	\$0	\$0	\$0	\$0	\$100,657,570
Architect		\$2,097,553	\$2,508,588	\$295,753	\$265,481	\$778,015	\$517,794	\$1,048,935	\$991,386	\$869,801	\$151,886	\$43,416	\$90,690	\$240,094	-\$1,327,000	\$0	\$0	\$8,572,392
Engineering		\$16,459	\$29,293	\$9,102	\$29,223	\$8,203	\$72,993	\$118,368	\$72,786	\$51,971	\$37,259	\$0	\$0	\$0	\$0	\$0	\$0	\$445,657
Inspection & Testing		\$64,905	\$27,527	\$123,842	\$235,287	\$563,746	\$1,381,801	\$641,972	\$525,264	\$207,240	\$27,210	\$1,212	\$0	\$0	\$0	\$0	\$0	\$3,800,005
Project Management		\$121,786	\$233,826	\$269,249	\$506,917	\$800,315	\$930,115	\$1,207,850	\$1,121,670	\$859,779	\$50,681	\$27,825	\$2,450	\$0	\$2,188	\$0	\$0	\$6,134,649
Cap Equipment		\$0	\$0	\$0	\$186,301	\$0	\$0	\$0	\$0	\$1,458,273	\$6,604	\$0	\$0	\$0	\$0	\$0	\$0	\$1,651,178
Non-Cap Equipment		\$0	\$0	\$0	\$10,782	\$0	\$0	\$0	\$326,845	\$490,727	\$7,167	\$0	\$0	\$0	\$0	\$0	\$0	\$835,520
Total		\$2,321,599	\$2,805,534	\$2,238,694	\$5,033,499	\$13,987,159	\$20,672,105	\$26,540,059	\$19,392,902	\$29,722,772	\$553,215	\$828,296	\$126,029	\$440,877	-\$1,155,109	\$1,500	\$0	\$123,509,130
Project Budget	\$130,344,521	Received																
Less Other Funding*	\$6,835,391	\$6,835,391	* Other Funding Source:															
Net	\$123,509,130		1) KCRW Foundation \$6,803,412 received															
Actual Measure AA Expenditures	\$123,509,130		2) Edison \$31,979.48 received															
Running Balance	\$0																	

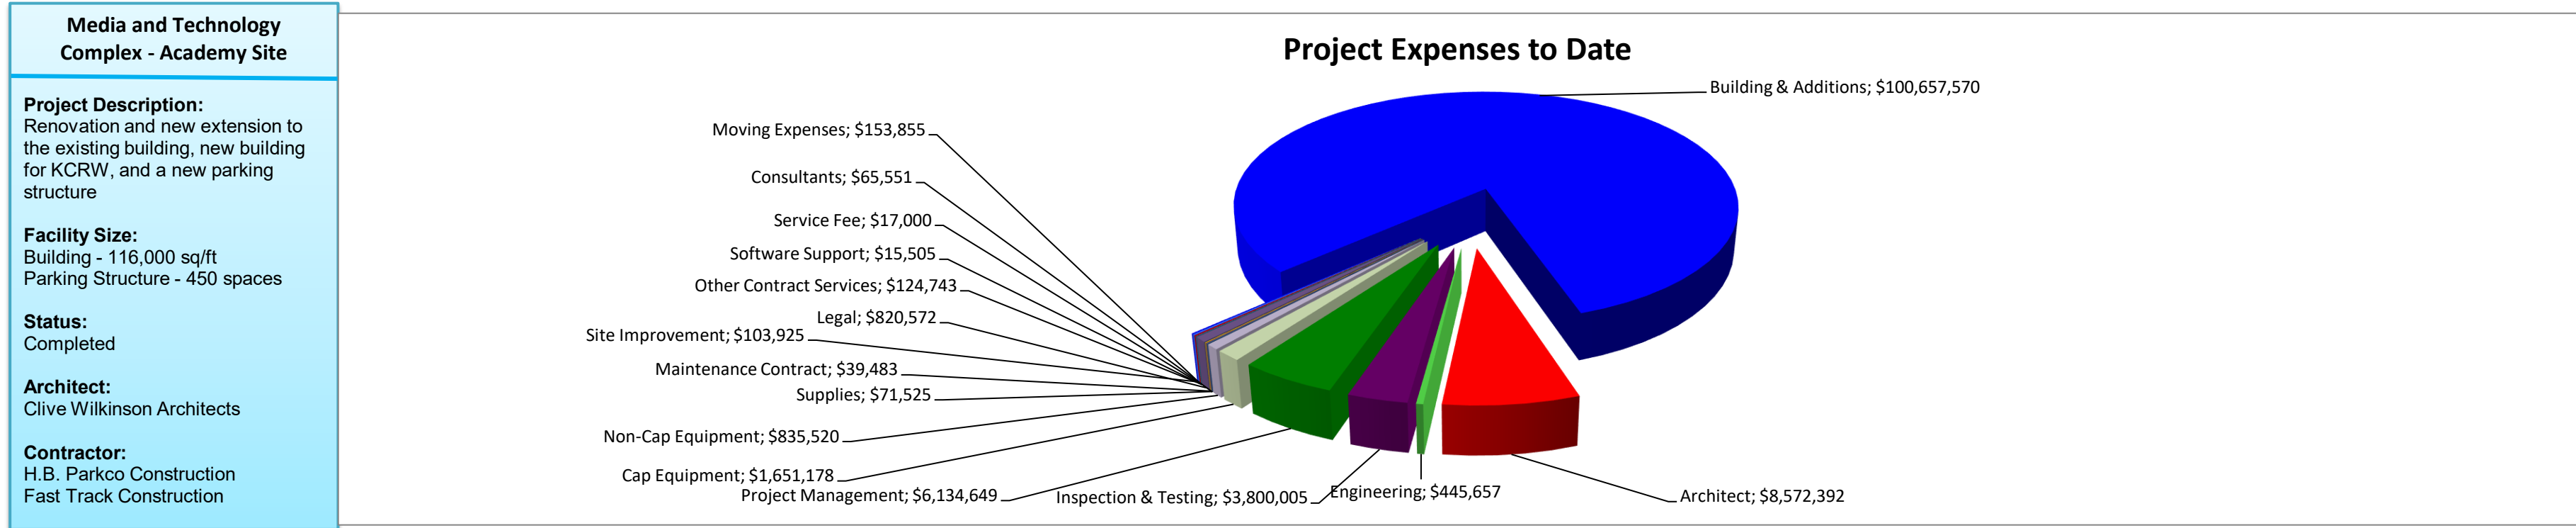


Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
AA 7100060																		
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)																		
Consultants		\$0	\$0	\$0	\$14	\$62	\$2,304	\$184	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,564
Supplies		\$0	\$0	\$0	\$0	\$7,089	\$195	\$484	\$20,947	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$28,715
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$663	\$80	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$742
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,209	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,209
Site Improvement		\$0	\$0	\$0	\$0	\$0	\$559	\$440	\$575	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,574
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$2,165	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,165
Postage		\$0	\$0	\$0	\$0	\$0	\$1,505	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,505
Other Contract Services		\$120	\$38	\$112	\$32,634	\$0	\$1,019	\$581	\$0	\$2,644	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$37,147
Building & Additions		\$0	\$0	\$0	\$817	\$4,188	\$1,623	\$13,783,023	\$14,880,829	\$5,315,393	-\$148,184	\$0	\$0	\$0	\$0	\$0	\$0	\$33,837,688
Architect		\$256,076	\$1,568,564	\$1,790,207	\$518,973	\$177,583	\$364,853	\$585,900	\$373,345	\$210,312	\$108,264	\$0	\$0	\$0	\$0	\$0	\$0	\$5,954,078
Engineering		\$0	\$8,507	\$31,650	\$7,871	\$6,529	\$9,276	\$76,712	\$51,025	\$11,318	\$2,900	\$0	\$0	\$0	\$0	\$0	\$0	\$205,788
Inspection & Testing		\$36,892	\$490	\$21,150	\$1,285	\$360	\$133,756	\$846,765	\$358,724	\$60,826	\$1,330	\$0	\$0	\$0	\$0	\$0	\$0	\$1,461,579
Project Management		\$34,968	\$113,379	\$118,783	\$94,768	\$108,528	\$463,418	\$564,240	\$487,065	\$312,539	\$20,242	\$0	\$0	\$0	\$0	\$0	\$0	\$2,317,928
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$164,793	\$68,425	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$233,218
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$9,015	\$0	\$206,229	\$127,078	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$342,322
Total		\$328,056	\$1,690,978	\$1,961,901	\$656,362	\$304,338	\$989,689	\$15,858,991	\$16,544,820	\$6,108,535	-\$15,448	\$0	\$0	\$0	\$0	\$0	\$0	\$44,428,222
Project Budget	\$56,240,452																	
Less Other Funding*	\$11,812,230																	
Net	\$44,428,222																	
Actual Measure AA Expenditures	\$44,428,222																	
Running Balance	\$0																	
* Other Funding Source: 1) Measure S - \$11,603,383 allocated 2) SCE \$190,847.28, Gas Co. \$18,000 received																		

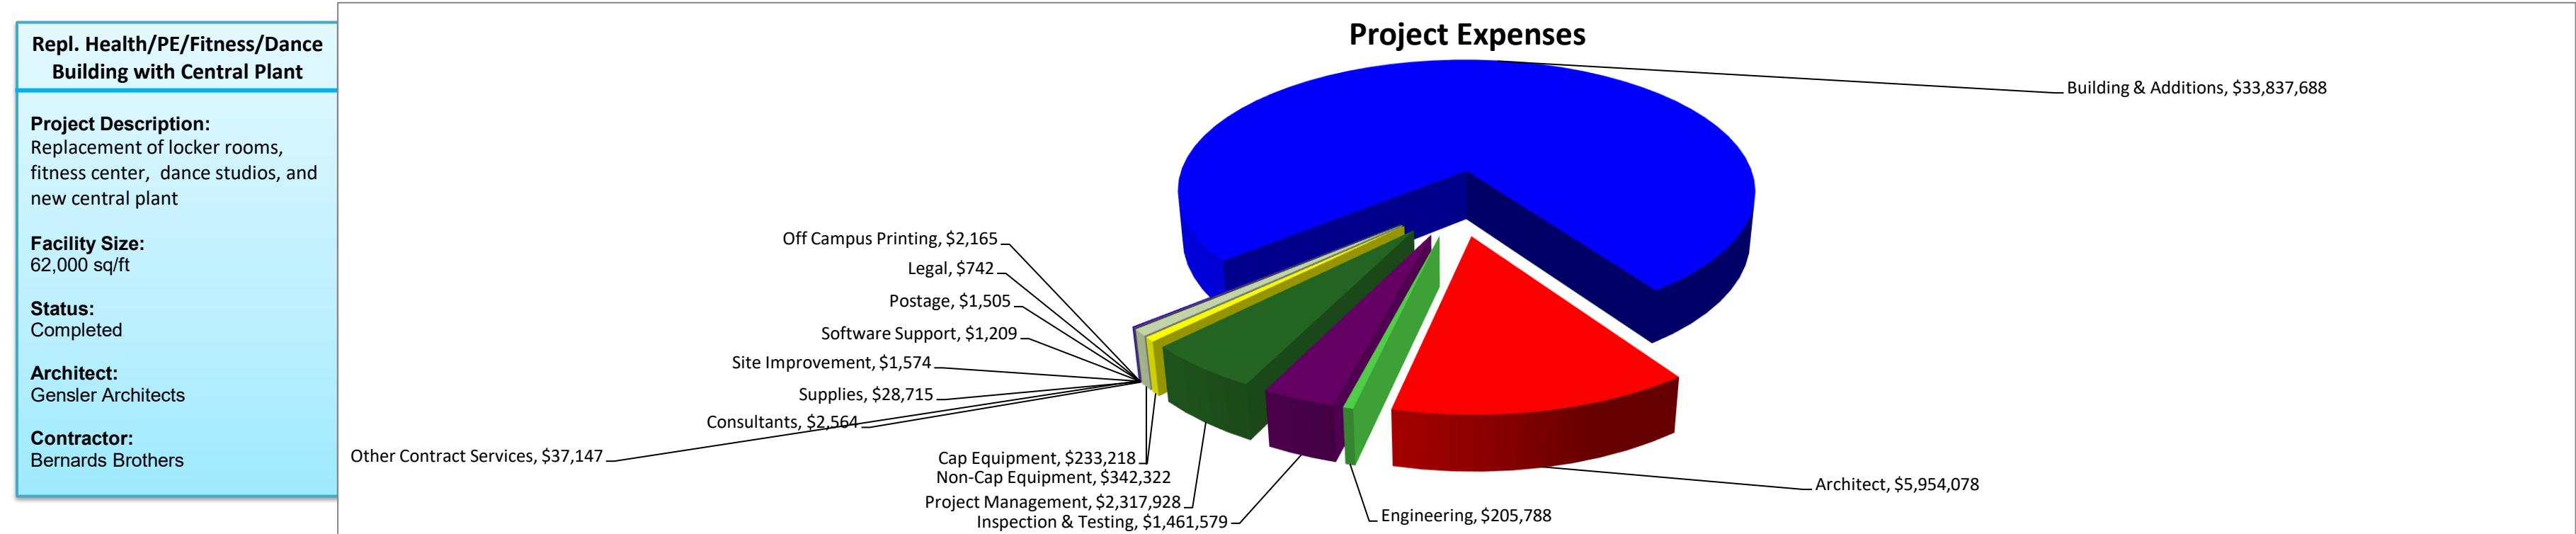

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23			Combined Totals
AA 7100065																		
Drescher - Academic Modernization, Bookstore, Pico Promenade (105)																		
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Site Acquisition		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,082
Total		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,082
Project Budget	\$13,005,082																	
Less Other Funding	\$13,000,000																	
Net	\$5,082																	
Actual Measure AA Expenditures	\$5,082																	
Running Balance	\$0																	
* Other Funding Source: 1) Measure V 13,000,000 allocated																		

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
AA 7100090																		
Replacement Math and Science Extension Building (106)																		
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,525	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,525
Site Acquisition		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,796	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,796
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,787,824	-\$94,695	\$0	\$0	\$0	\$0	\$0	\$0	\$1,693,130
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$70,223	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$70,223
Project Management		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$800	\$228,760	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$234,510
Total		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$800	\$2,093,128	-\$94,695	\$0	\$0	\$0	\$0	\$0	\$0	\$2,004,184
Project Budget	\$124,245,512	Received																
Less Other Funding	\$122,241,328	\$122,241,328	* Other Funding Source:															
Net	\$2,004,184	1) Measure U \$308,336 2) Measure V \$82,317,992 allocated																
Actual Measure AA Expenditures	\$2,004,184	3) State of California \$39,615,000																
Running Balance	\$0																	

AA 7100047																		
Madison East Wing Seismic Upgrade (107)																		
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$6,197	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,197
Consultants		\$0	\$0	\$0	\$0	\$135	\$28	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$163
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$285	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$285
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$357	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$357
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$7,579	\$11,822	\$8,263	\$950	\$0	\$0	\$0	\$0	\$0	\$0	\$28,613
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$806	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$806
Other Contract Services		\$0	\$364	\$997	\$0	\$0	\$1,328	\$711	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,400
Building & Additions		\$0	\$656	\$312,643	\$0	\$4,248	\$6,030,371	\$8,829,626	\$4,949,223	\$3,967,591	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$24,094,358
Architect		\$76,073	\$398,050	\$550,589	\$65,444	\$57,480	\$199,100	\$404,764	\$122,764	\$103,824	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,978,088
Engineering		\$0	\$0	\$10,707	\$778	\$0	\$13,792	\$33,184	\$37,491	\$90	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$96,042
Inspection & Testing		\$0	\$19,848	\$16,752	\$3,036	\$5,851	\$676,323	\$405,443	\$112,876	\$4,703	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,244,832
Project Management		\$5,557	\$128,878	\$112,573	\$67,447	\$118,242	\$494,874	\$481,165	\$322,379	\$31,230	\$11,286	\$0	\$0	\$0	\$0	\$0	\$0	\$1,773,629
Cap Equipment		\$0	\$0	\$30,603	\$0	\$0	\$0	\$537,627	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$568,230
Non-Cap Equipment		\$0	\$0	\$71,827	\$9,788	\$0	\$0	\$285,236	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$366,851
Total		\$81,630	\$547,796	\$1,106,691	\$146,492	\$185,956	\$7,416,101	\$10,154,894	\$6,382,534	\$4,119,259	\$19,549	\$950	\$0	\$0	\$0	\$0	\$0	\$30,161,852
Project Budget	\$30,161,852																	
Less Other Funding	\$0																	
Net	\$30,161,852																	
Actual Measure AA Expenditures	\$30,161,852																	
Running Balance	\$0																	

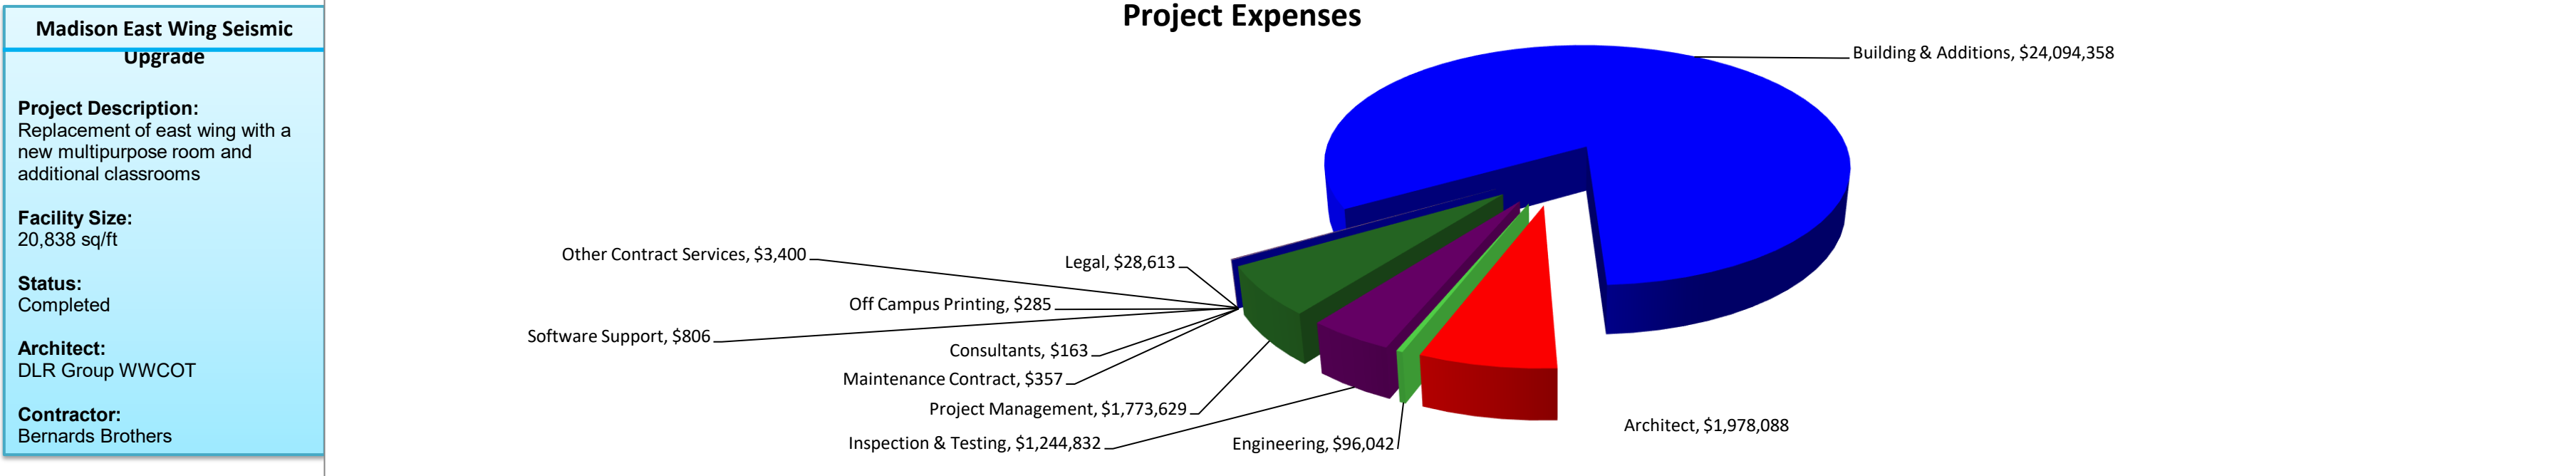

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
AA 7100068, 7100019																		
Corsair Stadium and Field Projects (108)																		
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$458,035	\$458,035
Architect		\$0	\$30,759	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$23,000	\$41,758	\$297,042	\$392,559
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$9,545	\$9,545
Project Management		\$0	\$4,540	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,540
Total		\$0	\$35,299	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$23,000	\$41,758	\$764,622	\$864,679
Project Budget	\$6,031,813																	
Less Other Funding	\$2,149,609																	
Net	\$3,882,204																	
Actual Measure AA Expenditures	\$864,679																	
Running Balance	\$3,017,525																	
* Other Funding Source: Measure AA Interest - \$2,149,609 Allocated																		

AA 7100067, 7100152, 7100155, 7100157																		
Business & Facilities Infrastructure (111)																		
Supplies		\$0	\$0	\$0	\$1,493	\$4,840	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,333
Service Fee		\$0	\$0	\$0	\$12,885	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,885
Consultants		\$0	\$0	\$0	\$0	\$14	\$8	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$22
Maintenance Contract		\$0	\$0	\$0	\$0	\$1,366	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,366
Legal		\$0	\$0	\$75	\$0	\$0	\$0	\$1,105	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,180
Software License		\$0	\$0	\$0	\$0	\$375	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$375
Other Contract Services		\$0	\$6,289	\$6,988	\$750	\$0	\$2,209	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,236
Moving Services		\$0	\$0	\$0	\$395	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$395
Building & Additions		\$0	\$34,672	\$198,667	\$200,585	\$284,668	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$718,592
Architect		\$0	\$0	\$80,626	\$170,132	\$37,906	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$288,664
Engineering		\$0	\$0	\$0	\$3,705	\$9,735	\$6,840	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,280
Inspection & Testing		\$0	\$0	\$8,142	\$10,938	\$10,500	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$29,580
Project Management		\$0	\$3,073	\$154,904	\$87,291	\$139,821	\$3,571	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$388,659
Cap Equipment		\$0	\$0	\$0	\$35,892	\$80,090	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$115,982
Non-Cap Equipment		\$0	\$89,204	\$0	\$84,590	\$193,782	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$367,576
Total		\$0	\$133,238	\$449,401	\$608,656	\$763,095	\$12,628	\$1,105	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,968,124
Project Budget	\$1,968,124																	
Less Other Funding	\$0																	
Net	\$1,968,124																	
Actual Measure AA Expenditures	\$1,968,124																	
Running Balance	\$0																	

AA 7100004																		
Master Planning, Program Management, Overhead (112)																		
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$139,302	\$187,927	\$245,329	\$1,270	\$0	\$0	\$0	\$0	\$0	\$0	\$573,828
Project Management		\$0	\$0	\$0	\$0	\$76,015	\$150	\$0	\$49,170	\$135,533	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$260,868
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$76,015	\$150	\$139,302	\$237,097	\$380,863	\$1,270	\$0	\$0	\$0	\$0	\$0	\$0	\$834,697
Project Budget	\$834,697																	
Less Other Funding	\$0																	
Net	\$834,697																	
Actual Measure AA Expenditures	\$834,697																	
Running Balance	\$0																	

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
AA 7100154																		
Energy Efficiency Projects (113)																		
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$189	\$2,108,853	\$990,389	-\$97,621	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,001,810
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$4,020	\$0	\$10,118	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14,138
Project Management		\$0	\$0	\$0	\$0	\$0	\$825	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$825
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$189	\$2,112,873	\$990,389	-\$86,678	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,016,773
Project Budget	\$3,508,088																	
Less Other Funding	\$491,315																	
Net	\$3,016,773																	
Actual Measure AA Expenditures	\$3,016,773																	
Running Balance	\$0																	
* Other Funding Source: 1) DWP \$18,715.00 received 2) SCE \$446,519.77 received 3) Gas Co. \$26,080 received																		

AA 7100064																		
Community Classroom & Facility Projects (114)																		
Supplies		\$0	\$0	\$0	\$124	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$124
Legal		\$0	\$0	\$1,867	\$1,418	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,285
Other Contract Services		\$0	\$3,720	\$1,869	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,588
Building & Additions		\$0	\$434,578	\$1,369,441	\$408,696	-\$1,003	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,211,712
Architect		\$0	\$263,833	\$48,120	\$1,318	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$313,272
Engineering		\$0	\$3,220	\$3,143	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,363
Inspection & Testing		\$0	\$41,002	\$80,885	\$1,495	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$123,382
Project Management		\$135	\$117,247	\$143,780	\$27,570	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$288,732
Non-Cap Equipment		\$0	\$0	\$209,726	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$209,726
Total		\$135	\$863,599	\$1,858,831	\$440,621	-\$1,003	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,162,183
Project Budget	\$3,162,183																	
Less Other Funding	\$0																	
Net	\$3,162,183																	
Actual Measure AA Expenditures	\$3,162,183																	
Running Balance	\$0																	

AA 7100057																		
Real Property Acquisition (115)																		
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$659	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$659
Other Contract Services		\$0	\$39	\$7,000	\$0	\$15,800	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$22,839
Site Acquisition		\$1,739,979	\$4,001,204	\$9,022,207	\$0	\$0	\$0	\$5,013,226	\$4,821,600	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$24,598,214
Inspection & Testing		\$8,689	\$7,986	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,674
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$1,748,667	\$4,009,228	\$9,029,207	\$0	\$15,800	\$0	\$5,013,226	\$4,822,259	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$24,638,386
Project Budget	\$24,638,386																	
Less Other Funding	\$0																	
Net	\$24,638,386																	
Actual Measure AA Expenditures	\$24,638,386																	
Running Balance	\$0																	

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
AA 7100058, 7100151, 7100156, 7100059																		
Roadways, Walkways, Grounds, Parking Lots, and Garages (116)																		
Supplies		\$0	\$0	\$0	\$0	\$4,616	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,616
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$125
Consultants		\$0	\$0	\$0	\$48,090	\$5,018	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$53,108
Other Contract Services		\$218	\$770	\$122	\$25,249	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$26,358
Building & Additions		\$185,345	\$6,731	\$113,784	\$321,603	\$975,401	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,602,864
Architect		\$0	\$0	\$0	\$103,569	\$19,225	\$1,240	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$124,035
Engineering		\$0	\$0	\$0	\$1,095	\$1,445	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,540
Inspection & Testing		\$13,380	\$7,865	\$13,553	\$20,126	\$42,865	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$97,787
Project Management		\$24,404	\$12,439	\$21,945	\$54,095	\$104,943	\$1,411	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$219,237
Total		\$223,347	\$27,804	\$149,403	\$573,951	\$1,153,512	\$2,652	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,130,670
Project Budget	\$7,022,417	* Other Funding Source: 1) Measure S: \$3,891,747 2) Measure V: \$1,000,000 allocated																
Less Other Funding	\$4,891,747																	
Net	\$2,130,670																	
Actual Measure AA Expenditures	\$2,130,670																	
Running Balance	\$0																	

AA 7100069																		
Infrastructure & Technology - Technology (117)																		
Software		\$0	\$0	\$0	\$0	\$0	\$218	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$218
Supplies		\$0	\$0	\$13,646	\$7,587	\$0	\$16,966	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$38,200
Maintenance Contract		\$0	\$9,472	\$46,300	\$210,581	\$18,944	\$42,415	\$9,472	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$337,186
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$49,589	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$49,589
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$207,423	\$33,063	\$576,294	\$0	\$1,145,668	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,962,449
Non-Cap Equipment		\$0	\$0	\$42,827	\$500	\$0	\$3,447	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$46,775
Total		\$0	\$216,896	\$135,838	\$794,963	\$18,944	\$1,258,304	\$9,472	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,434,417
Project Budget	\$2,434,417																	
Less Other Funding	\$0																	
Net	\$2,434,417																	
Actual Measure AA Expenditures	\$2,434,417																	
Running Balance	\$0																	

AA 7100150																		
Infrastructure & Technology - Utility (118)																		
Software License		\$0	\$12,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,000
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$4,979	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,979
Project Management		\$0	\$3,240	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,240
Cap Equipment		\$0	\$0	\$7,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,534
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$20,219	\$7,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,753
Project Budget	\$27,753																	
Less Other Funding	\$0																	
Net	\$27,753																	
Actual Measure AA Expenditures	\$27,753																	
Running Balance	\$0																	

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
AA 7100153																		
Emergency Lighting, Fire Alarm, and Security System (119)																		
Supplies		\$0	\$0	\$0	\$0	\$2,348	\$0	\$0	\$2,671	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,020
Consultants/Legal		\$0	\$0	\$0	\$0	\$0	\$16	\$0	\$0	\$0	\$442	\$0	\$0	\$0	\$0	\$0	\$0	\$458
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$800	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$800
Maintenance Contract		\$0	\$0	\$648	\$0	\$39,700	\$0	\$2,700	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$43,048
Software Support		\$0	\$0	\$24,765	\$0	\$106,367	\$0	\$2,232	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$133,365
Other Contract Services		\$0	\$0	\$0	\$0	\$47,695	\$0	\$4,643	\$1,560	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$53,897
Building & Additions		\$0	\$0	\$0	\$0	\$110	\$2,648,866	\$4,129,145	\$1,308,230	\$763,170	\$26,375	\$79,172	\$0	\$0	\$0	\$0	\$0	\$8,955,068
Architect		\$0	\$0	\$0	\$0	\$0	\$18,925	\$0	\$0	\$5,047	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$23,972
Engineering		\$0	\$0	\$0	\$0	\$211,030	\$389,013	\$156,247	\$255,798	\$358,560	\$114,585	\$0	\$0	\$0	\$0	\$0	\$0	\$1,485,233
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$58,831	\$4,800	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$63,631
Project Management		\$0	\$0	\$0	\$0	\$51,008	\$52,044	\$79,285	\$16,500	\$49,738	\$240	\$0	\$0	\$0	\$0	\$0	\$0	\$248,814
Cap Equipment		\$0	\$0	\$0	\$0	\$89,415	\$0	\$5,871	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$95,286
Non-Cap Equipment		\$0	\$0	\$6,087	\$0	\$392,586	\$8,348	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$407,022
Total		\$0	\$0	\$31,500	\$0	\$940,259	\$3,118,012	\$4,438,953	\$1,589,560	\$1,176,515	\$141,642	\$79,172	\$0	\$0	\$0	\$0	\$0	\$11,515,614
Project Budget	\$11,515,614																	
Less Other Funding	\$0																	
Net	\$11,515,614																	
Actual Measure AA Expenditures	\$11,515,614																	
Running Balance	\$0																	

AA 7100142																		
Student Services (120)																		
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,165,626	\$3,704,864	\$0	\$0	\$0	\$0	\$0	\$0	\$6,870,490
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,165,626	\$3,704,864	\$0	\$0	\$0	\$0	\$0	\$0	\$6,870,490
Project Budget	\$6,870,490																	
Less Other Funding	\$0																	
Net	\$6,870,490																	
Actual Measure AA Expenditures	\$6,870,490																	
Running Balance	\$0																	
* Other Funding Source: 1) State of California \$1,321,000 received 2) Measure U \$21,131,135, Measure S \$45,595,322, Measure V \$33,624,909 allocated 3) Measure U, S & AA interests \$21,681,308 allocated																		

Cost of Issuance (121)																		
Cost of Issuance		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$498,026
Total		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$498,026
Project Budget	\$498,026																	
Less Other Funding	\$0																	
Net	\$498,026																	
Actual Measure AA Expenditures	\$498,026																	
Running Balance	\$0																	


Grand Total		\$4,900,734	\$10,935,584	\$17,864,407	\$13,113,759	\$30,388,248	\$39,049,510	\$60,741,756	\$57,313,878	\$52,193,046	\$4,326,286	\$908,418	\$126,029	\$440,877	-\$1,132,109	\$43,258	\$764,622	\$291,978,303
-------------	--	-------------	--------------	--------------	--------------	--------------	--------------	--------------	--------------	--------------	-------------	-----------	-----------	-----------	--------------	----------	-----------	---------------

Measure AA Interest		18/19 Final
Parking Garage and Grounds - Student Services (9)		
Site Improvement		\$0
Building & Additions		\$5,192,948
Architect		\$0
Engineering		\$0
Inspection & Testing		\$0
Project Management		\$0
Total		\$5,192,948
Project Budget	\$5,192,948	
Actual Measure AA Interest Expenditures	\$5,192,948	
Running Balance	\$0	

Measure V Bond Budget

As of June 30, 2025

	Project Name	Completion	Project Budget	Measure V Allocation	Other Funding	Measure V Expenditures as of 6/30/25	Measure V Expenditures as of 3/31/25	Measure V Expenditures Last Period	Total Measure V Remaining
101	Replacement Math and Science Extension Building	Completed	\$124,245,512	\$82,317,992	\$41,927,520	\$67,821,362	\$66,199,224	\$1,622,138	\$14,496,630
102	Student Services	Completed	\$124,372,370	\$27,773,115	\$96,599,255	\$25,273,457	\$25,273,457	\$0	\$2,499,658
103	Malibu Center	Completed	\$61,985,779	\$34,558,420	\$27,427,359	\$29,026,209	\$29,006,524	\$19,685	\$5,532,211
104	Early Childhood Development/Childcare	Completed	\$30,925,771	\$15,405,517	\$15,520,254	\$13,230,128	\$13,230,128	\$0	\$2,175,389
105	Art Building Replacement	March 2026	\$63,433,040	\$52,532,040	\$10,901,000	\$20,947,572	\$15,773,408	\$5,174,164	\$31,584,468
106	Business Building Renovation	On-Going	\$25,017,000	\$12,547,000	\$12,470,000	\$3,400	\$3,400	\$0	\$12,543,600
107	Air Conditioning	Completed	\$10,130,737	\$10,130,737	\$0	\$10,130,737	\$10,130,737	\$0	\$0
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$0	\$0	\$0	\$0	\$4,000,000
109	Master Planning	December 2025	\$1,000,000	\$1,000,000	\$0	\$970,222	\$945,993	\$24,229	\$29,778
110	Drescher Hall Modernization	On-Going	\$13,005,082	\$13,000,000	\$5,082	\$4,962	\$4,962	\$0	\$12,995,038
111	Outdoor Classroom	Completed	\$321,723	\$321,723	\$0	\$321,723	\$321,723	\$0	\$0
112	John Adams MS Auditorium (SMMUSD)	Completed	\$20,000,000	\$20,000,000	\$0	\$20,000,000	\$20,000,000	\$0	\$0
113	Memorial Park Project	On-Going	\$20,000,000	\$20,000,000	\$0	\$3,481	\$3,481	\$0	\$19,996,519
114	Classrooms Relocation	Completed	\$7,286,719	\$7,286,719	\$0	\$7,286,719	\$7,286,719	\$0	\$0
124	Parking Structure 3 Improvement Project	December 2025	\$6,000,000	\$6,000,000	\$0	\$152,333	\$135,250	\$17,083	\$5,847,667
125	Gender Neutral Bathrooms	December 2026	\$6,057,602	\$6,057,602	\$0	\$230,971	\$220,664	\$10,307	\$5,826,631
126	Athletic Facilities	December 2026	\$20,325,749	\$20,325,749	\$0	\$3,399,386	\$3,314,007	\$85,379	\$16,926,363
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$0	\$244,554	\$244,554	\$0	\$55,446
121	Cost of Issuance	On-Going	\$744,152	\$744,152	\$0	\$744,152	\$744,152	\$0	\$0
122	Management Reserve	On-Going	\$11,088,996	\$10,699,234	\$0	\$0	\$0	\$0	\$10,699,234
123	Unissuable Bond	On-Going	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Totals			\$550,240,232	\$345,000,000	\$204,850,470	\$199,791,368	\$192,838,383	\$6,952,985	\$145,208,632

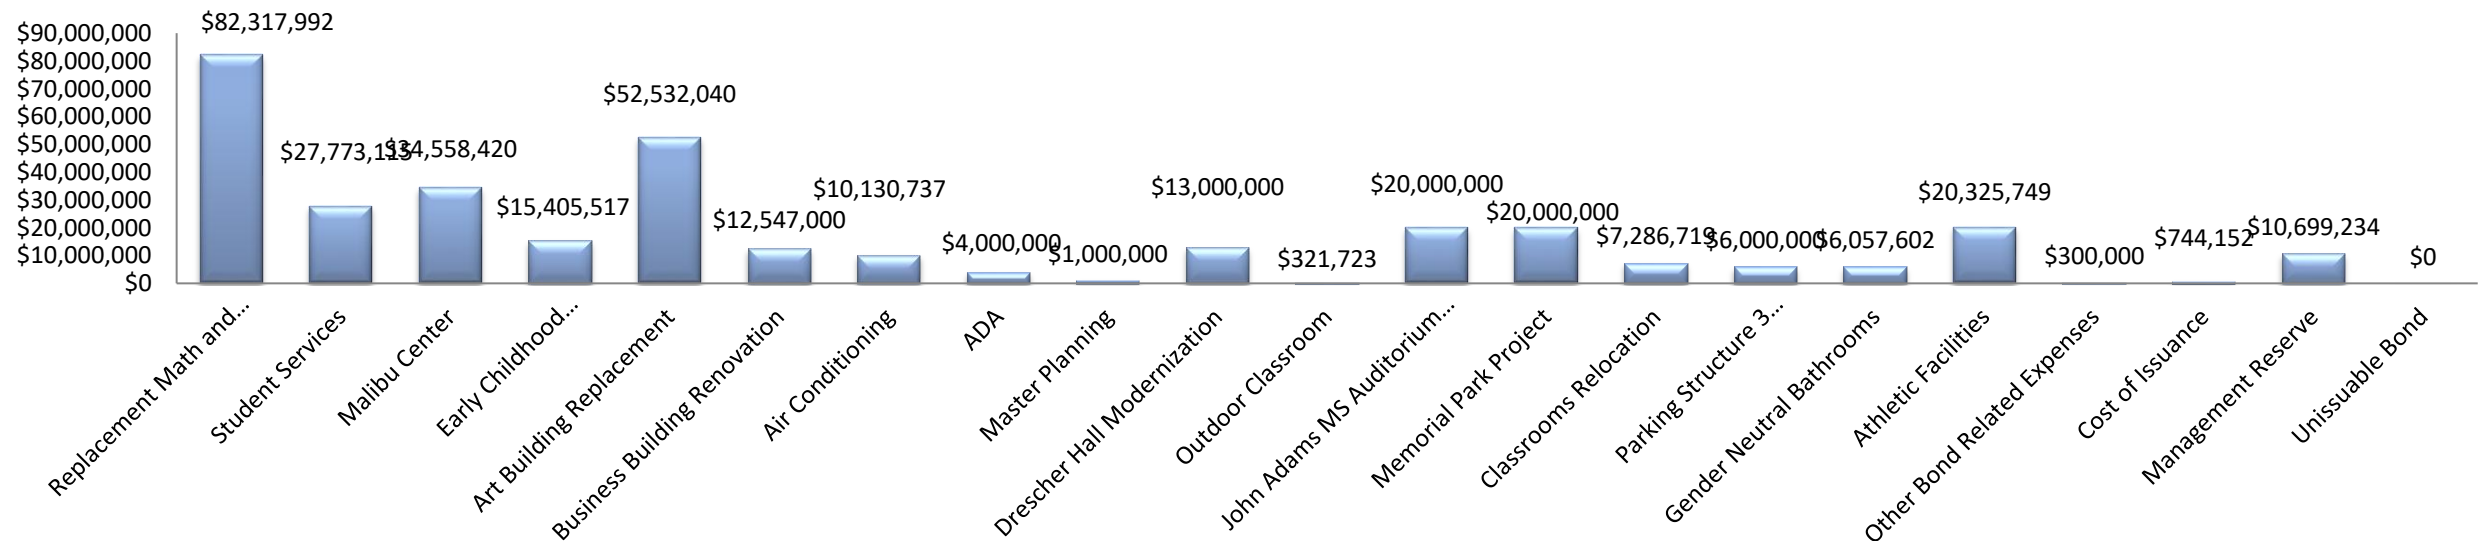Measure V Allocation

SANTA MONICA COMMUNITY COLLEGE DISTRICT
Measure V Bond Budget History
as of June 30, 2025

MEASURE V

	Project Name	Completion	Preliminary Measure V Budget	Measure V Budget as of 3/31/2025	Measure V Budget as of 6/30/2025	Variance	Measure V Remaining as of 6/30/2025
101	Replacement Math and Science Extension Building	Completed	\$82,317,992	\$82,317,992	\$82,317,992	\$0	\$14,496,630
102	Student Services	Completed	\$21,130,252	\$27,773,115	\$27,773,115	\$0	\$2,499,658
103	Malibu Center	Completed	\$25,000,000	\$34,558,420	\$34,558,420	\$0	\$5,532,211
104	Early Childhood Development/Childcare	Completed	\$15,405,517	\$15,405,517	\$15,405,517	\$0	\$2,175,389
105	Art Building Replacement	March 2026	\$24,000,000	\$52,532,040	\$52,532,040	\$0	\$31,584,468
106	Business Building Renovation	On-Going	\$12,547,000	\$12,547,000	\$12,547,000	\$0	\$12,543,600
107	Air Conditioning	Completed	\$10,777,654	\$10,130,737	\$10,130,737	\$0	\$0
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$4,000,000	\$0	\$4,000,000
109	Master Planning	December 2025	\$450,000	\$1,000,000	\$1,000,000	\$0	\$29,778
110	Drescher Hall Modernization	On-Going	\$13,000,000	\$13,000,000	\$13,000,000	\$0	\$12,995,038
111	Outdoor Classroom	Completed	\$10,000,000	\$321,723	\$321,723	\$0	\$0
112	John Adams MS Auditorium (SMMUSD)	Completed	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$0
113	Memorial Park Project	On-Going	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$19,996,519
114	Classrooms Relocation	Completed	\$0	\$7,286,719	\$7,286,719	\$0	\$0
124	Parking Structure 3 Improvement Project	December 2025	\$0	\$6,000,000	\$6,000,000	\$0	\$5,847,667
125	Gender Neutral Bathrooms	December 2026	\$0	\$6,057,602	\$6,057,602	\$0	\$5,826,631
126	Athletic Facilities	December 2026	\$0	\$20,325,749	\$20,325,749	\$0	\$16,926,363
115	TBD	On-Going	\$57,271,585	\$0	\$0	\$0	\$0
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$300,000	\$0	\$55,446
121	Cost of Issuance	Completed	\$800,000	\$744,152	\$744,152	\$0	\$0
122	Management Reserve	On-Going	\$28,000,000	\$10,699,234	\$10,699,234	\$0	\$10,699,234
123	Unissuable Bond	On-Going	\$0	\$0	\$0	\$0	\$0
	Project Totals		\$345,000,000	\$345,000,000	\$345,000,000	\$0	\$145,208,632

MEASURE V

As of June 30, 2025

Page 17

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE V EXPENDITURES - FUND 42.5
as of June 30, 2025

MEASURE V

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
V 7100090										
Replacement Math and Science Extension Building (101)										
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$45,668	\$343,876	\$389,544
Maintenance Contracts						\$0	\$0	\$0	\$2,472	\$2,472
Legal		\$0	\$0	\$0	\$0	\$0	\$2,101	\$0	\$70,887	\$72,988
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$15,799	\$39,720	\$55,519
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$15,464	\$15,464
Moving Services		\$0	\$0	\$67,242	\$0	\$0	\$0	\$32,900	\$13,419	\$113,561
Building & Additions		\$675	\$12,987	\$2,633	\$3,697,529	\$13,243,628	\$21,826,672	\$7,685,475	\$3,670,003	\$50,139,601
Architect		\$2,047,911	\$14,446	\$229,267	\$653,770	\$552,565	\$688,244	\$410,466	\$503,337	\$5,100,007
Engineering		\$0	\$0	\$19,622	\$6,966	\$10,940	\$0	\$25,926	\$10,465	\$73,920
Inspection & Testing		\$30,804	\$44,077	\$60,666	\$225,542	\$919,688	\$632,956	\$510,761	\$280,603	\$2,705,096
Project Management		\$130,874	\$617,805	\$347,350	\$474,483	\$866,097	\$503,615	\$747,805	\$672,703	\$4,360,732
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$774,548	\$427,282	\$1,201,831
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$90,431	\$1,914,731	\$1,585,465	\$3,590,627
Total		\$2,210,264	\$689,315	\$726,781	\$5,058,290	\$15,592,919	\$23,744,019	\$12,164,078	\$7,635,696	\$67,821,362
Project Budget	\$124,245,512	Received	* Other Funding Source: 1) Measure U - \$308,336 2) Measure AA - \$2,004,184 3) State of California \$39,615,000							
Less Other Funding	\$41,927,520	\$41,927,520								
Net	\$82,317,992									
Actual Measure V Expenditures	\$67,821,362									
Running Balance	\$14,496,630									

V 7100142										
Student Services Building (102)										
Supplies		\$0	\$71,445	\$38,162	\$0	\$0	\$0	\$0	\$0	\$109,607
Other Contract Services		\$0	\$0	\$59,784	\$6,935	\$0	\$0	\$0	\$0	\$66,719
Consultants		\$0	\$0	\$687	\$0	\$0	\$0	\$0	\$0	\$687
Software Support		\$0	\$189,120	\$0	\$0	\$0	\$0	\$0	\$0	\$189,120
Moving Services		\$0	\$55,062	\$9,056	\$0	\$0	\$0	\$0	\$0	\$64,118
Building & Additions		\$0	\$12,355,060	\$4,201,966	\$355,441	\$0	\$75,811	\$469,935	\$0	\$17,458,214
Architect		\$0	\$419,829	\$530,797	\$186,296	\$27,836	\$13,527	\$6,640	\$0	\$1,184,924
Engineering		\$0	\$140,458	\$67,481	\$0	\$0	\$0	\$0	\$0	\$207,939
Inspection & Testing		\$55,202	\$296,732	\$131,128	\$21,146	\$0	\$26,636	\$50,663	\$0	\$581,507
Project Management		\$0	\$900,333	\$219,425	\$85,310	\$13,020	\$0	\$21,706	\$342	\$1,240,135
Cap Equipment		\$0	\$1,565,928	\$90,915	\$0	\$0	\$0	\$0	\$0	\$1,656,844
Non-Cap Equipment		\$0	\$2,279,541	\$196,313	\$37,790	\$0	\$0	\$0	\$0	\$2,513,644
Total		\$55,202	\$18,273,508	\$5,545,714	\$692,918	\$40,856	\$115,974	\$548,944	\$342	\$25,273,457
Project Budget	\$124,372,370	Received	* Other Funding Source: 1) State of California \$1,321,000 received 2) Measure U \$21,131,135 3) Measure S 45,595,322, 4) Measure AA \$6,870,490 allocated 5) Measure U, S & AA interests \$21,681,308 allocated							
Less Other Funding	\$96,599,255	\$96,599,255								
Net	\$27,773,115									
Actual Measure V Expenditures	\$25,273,457									
Running Balance	\$2,499,658									

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE V EXPENDITURES - FUND 42.5
as of June 30, 2025

MEASURE V

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
V 7100015										
Malibu Site Acquisition and Center (103)										
Supplies		\$0	\$0	\$0	\$0	\$0	\$11,134	\$1,970	\$0	\$13,104
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$882	\$0	\$882
Software Support		\$0	\$0	\$0	\$0	\$0	\$8,281	\$8,927	\$0	\$17,207
Legal		\$0	\$0	\$0	\$0	\$0	\$181,450	\$114,381	\$53,027	\$348,858
Other Contract Services		\$0	\$0	\$2,713	\$38,163	\$0	\$136,245	\$6,123	\$739	\$183,983
Consultants		\$0	\$0	\$0	\$0	\$0	\$51,422	\$75,130	\$24,020	\$150,571
Moving Services		\$0	\$0	\$0	\$0	\$0	\$23,871	\$0	\$0	\$23,871
Building & Additions		\$0	\$0	\$2,642,861	\$3,292,435	\$8,734,478	\$7,418,550	\$1,277,493	\$12,389	\$23,378,205
Architect		\$0	\$0	\$0	\$155,448	\$493,355	\$262,129	\$182,997	-\$10,711	\$1,083,218
Engineering		\$0	\$0	\$8,482	\$0	\$15,268	\$8,641	\$0	\$0	\$32,392
Inspection & Testing		\$0	\$0	\$51,754	\$633,723	\$511,002	\$159,283	\$8,111	\$0	\$1,363,872
Project Management		\$0	\$0	\$49,588	\$581,175	\$626,405	\$406,040	\$93,407	\$2,213	\$1,758,827
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$60,513	\$12,953	\$0	\$73,466
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$12,015	\$535,594	\$27,190	\$22,956	\$597,754
Total		\$0	\$0	\$2,755,398	\$4,700,943	\$10,392,522	\$9,263,151	\$1,809,563	\$104,632	\$29,026,209
Project Budget	\$61,985,779	* Other Funding Source: 1) Measure S \$25,132,568 2) Interest Allocated \$2,294,791								
Less Other Funding	\$27,427,359									
Net	\$34,558,420									
Actual Measure V Expenditures	\$29,026,209									
Running Balance	\$5,532,211									

V 7100104										
Early Childhood Development/Childcare (104)										
Supplies		\$0	\$0	\$35,150	\$5,332	-\$500	-\$96	\$96	\$0	\$39,982
Other Contract Services		\$0	\$0	\$35,344	\$15,128	\$0	\$0	-\$3,744	\$0	\$46,728
Consultants		\$0	\$0	\$16	\$0	\$0	\$0	\$0	\$0	\$16
Software Support		\$0	\$0	\$6,158	\$0	\$5,677	\$5,677	\$1,656	\$1,656	\$20,825
Legal		\$0	\$0	\$96	\$0	\$0	\$0	\$0	\$0	\$96
Building & Additions		\$0	\$0	\$8,879,770	\$1,603,432	\$0	\$73,242	\$64,346	\$37,623	\$10,658,413
Architect		\$0	\$0	\$262,660	\$275,924	\$105,158	\$27,846	\$17,751	\$0	\$689,339
Engineering		\$0	\$0	\$19,448	\$0	\$15,550	\$3,149	\$750	\$0	\$38,896
Inspection & Testing		\$0	\$0	\$349,661	\$135,767	\$3,700	\$13,249	\$3,290	\$3,600	\$509,267
Project Management		\$0	\$0	\$384,279	\$375,643	\$2,144	\$0	\$0	\$0	\$762,066
Cap Equipment		\$0	\$0	\$32,448	\$0	\$0	\$0	\$0	\$0	\$32,448
Non-Cap Equipment		\$0	\$0	\$328,242	\$92,913	\$0	\$0	\$10,897	\$0	\$432,052
Total		\$0	\$0	\$10,333,272	\$2,504,139	\$131,730	\$123,066	\$95,042	\$42,879	\$13,230,128
Project Budget	\$30,925,771	Received	* Other Funding Source: 1) City of Santa Monica \$6,661,598 committed 2) Measure S \$8,858,656 allocated							
Less Other Funding	\$15,520,254	\$15,520,254								
Net	\$15,405,517									
Actual Measure V Expenditures	\$13,230,128									
Running Balance	\$2,175,389									

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
V 7100240										
Art Complex (105)										
Legal		\$0	\$0	\$14,811	\$0	\$0	\$11,547	\$0	\$0	\$26,359
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$1,213	\$0	\$1,213
Consultants		\$0	\$0	\$20,991	\$40,710	\$1,344	\$0	\$0	\$0	\$63,045
Moving Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$184	\$407,369	\$3,040	\$0	\$1,791	\$108,857	\$6,498,430	\$10,081,116	\$17,100,787
Architect		\$0	\$0	\$39,542	\$569,178	\$28,572	\$85,055	\$74,971	\$102,727	\$900,045
Engineering		\$0	\$0	\$0	\$0	\$40,750	\$0	\$13,630	\$4,673	\$59,053
Inspection & Testing		\$0	\$35,495	\$25,052	\$43,653	\$45,227	\$12,852	\$474,345	\$624,255	\$1,260,879
Project Management		\$0	\$1,600	\$85,708	\$85,978	\$184,706	\$117,875	\$424,477	\$635,849	\$1,536,192
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$184	\$444,464	\$189,143	\$739,518	\$302,390	\$336,186	\$7,487,066	\$11,448,620	\$20,947,572
Project Budget	\$63,433,040	Received	<div>* Other Funding Source:</div> <div>1) State of California \$10,901,000 allocated</div>							
Less Other Funding	\$10,901,000	\$8,039,870								
Net	\$52,532,040									
Actual Measure V Expenditures	\$20,947,572									
Running Balance	\$31,584,468									
V 7100243										
Business Building Replacement (106)										
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$3,400	\$0	\$0	\$0	\$0	\$0	\$3,400
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$3,400	\$0	\$0	\$0	\$0	\$0	\$3,400
Project Budget	\$25,017,000	Received	<div>* Other Funding Source:</div> <div>1. Measure V Interest - \$12,470,000 allocated</div>							
Less Other Funding	\$12,470,000	\$0								
Net	\$12,547,000									
Actual Measure V Expenditures	\$3,400									
Running Balance	\$12,543,600									

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE V EXPENDITURES - FUND 42.5
as of June 30, 2025

MEASURE V

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
<i>V 7100188</i>										
Air Conditioning (107)										
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$2,451	\$7,537,201	\$733,457	\$0	\$0	\$0	\$8,273,110
Architect		\$0	\$79,000	\$0	\$0	\$39,872	\$3,280	\$0	\$0	\$122,152
Engineering		\$417,960	\$217,966	\$26,992	\$81,868	\$109,823	\$3,375	\$0	\$0	\$857,984
Inspection & Testing		\$0	\$54,810	\$776	\$253,936	\$125,639	\$0	\$0	\$0	\$435,160
Project Management		\$4,370	\$4,570	\$35,700	\$365,350	\$32,340	\$0	\$0	\$0	\$442,330
Total		\$422,330	\$356,346	\$65,919	\$8,238,355	\$1,041,132	\$6,655	\$0	\$0	\$10,130,737
Project Budget	\$10,130,737									
Less Other Funding	\$0									
Net	\$10,130,737									
Actual Measure V Expenditures	\$10,130,737									
Running Balance	\$0									

<i>V 7100004</i>										
Master Plan (109)										
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$52,746	\$52,746
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$48,000	\$0	\$0	\$5,680	\$53,680
Advertising and Mailing		\$0	\$641	\$0	\$0	\$0	\$0	\$0	\$9,167	\$9,809
Architect		\$0	\$112,073	\$528,182	\$37,861	\$0	\$52,150	\$118,822	\$0	\$849,088
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$3,800	\$1,100	\$0	\$0	\$0	\$0	\$0	\$4,900
Total		\$0	\$116,515	\$529,282	\$37,861	\$48,000	\$52,150	\$118,822	\$67,593	\$970,222
Project Budget	\$1,000,000									
Less Other Funding	\$0									
Net	\$1,000,000									
Actual Measure V Expenditures	\$970,222									
Running Balance	\$29,778									

<i>V 7100237</i>										
Outdoor Classroom (111)										
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$100,000	\$102,023	\$102,495	\$0	\$0	\$0	\$0	\$0	\$304,518
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$17,205	\$0	\$0	\$0	\$0	\$0	\$0	\$17,205
Total		\$100,000	\$119,228	\$102,495	\$0	\$0	\$0	\$0	\$0	\$321,723
Project Budget	\$321,723									
Less Other Funding	\$0									
Net	\$321,723									
Actual Measure V Expenditures	\$321,723									
Running Balance	\$0									

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE V EXPENDITURES - FUND 42.5
as of June 30, 2025

MEASURE V

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
V 7100268										
Parking Structure 3 Imp Project (124)										
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$26,282	\$89,168	\$27,580	\$143,030
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$9,303	\$9,303
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$26,282	\$89,168	\$36,883	\$152,333
Project Budget	\$6,000,000									
Less Other Funding	\$0									
Net	\$6,000,000									
Actual Measure V Expenditures	\$152,333									
Running Balance	\$5,847,667									
V 7100270										
Gender Neutral Bathroom Project (125)										
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,827	\$4,827
Architect		\$0	\$0	\$0	\$0	\$0	\$46,298	\$124,472	\$12,442	\$183,212
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$13,490	\$19,841	\$9,600	\$42,931
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$59,788	\$144,314	\$26,869	\$230,971
Project Budget	\$6,057,602									
Less Other Funding	\$0									
Net	\$6,057,602									
Actual Measure V Expenditures	\$230,971									
Running Balance	\$5,826,631									
V 7100271										
Athletic Facilities (126)										
Consultants							\$0	\$13,455	\$0	\$13,455
Legal		\$0	\$0	\$0	\$0	\$0	\$9,431	\$34,866	\$0	\$44,297
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Land Acquisition							\$0	\$2,194,154	\$0	\$2,194,154
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27	\$27
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$583,655	\$416,346	\$1,000,002
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$47,155	\$100,297	\$147,452
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$9,431	\$2,873,286	\$516,670	\$3,399,386
Project Budget	\$20,325,749									
Less Other Funding	\$0									
Net	\$20,325,749									
Actual Measure V Expenditures	\$3,399,386									
Running Balance	\$16,926,363									

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
V 7100272										
Memorial Park Project (113)										
Legal		\$0	\$0	\$0	\$0	\$0	\$3,481	\$0	\$0	\$3,481
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$3,481	\$0	\$0	\$3,481
Project Budget	\$20,000,000									
Less Other Funding	\$0									
Net	\$20,000,000									
Actual Measure V Expenditures	\$3,481									
Running Balance	\$19,996,519									

V 7100273										
Drescher Hall Modernization Project (110)										
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$4,962	\$0	\$4,962
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$0	\$4,962	\$0	\$4,962
Project Budget	\$13,000,000									
Less Other Funding	\$0									
Net	\$13,000,000									
Actual Measure V Expenditures	\$4,962									
Running Balance	\$12,995,038									

V 7100243										
Classrooms Relocation (114)										
Supplies		\$0	\$0	\$0	\$0	\$11,963	\$0	\$0	\$0	\$11,963
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$3,467	\$5,709,329	\$391,967	\$0	\$0	\$0	\$0	\$6,104,763
Supplies		\$0	\$0	\$4,982	\$0	\$0	\$0	\$0	\$0	\$4,982
Architect		\$0	\$184,434	\$78,179	\$92,082	\$0	\$0	\$0	\$0	\$354,695
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$16,795	\$115,194	\$25,996	\$0	\$0	\$0	\$0	\$157,985
Project Management		\$0	\$61,520	\$476,831	\$55,650	\$0	\$0	\$0	\$0	\$594,001
Non-Cap Equipment		\$0	\$0	\$58,331	\$0	\$0	\$0	\$0	\$0	\$58,331
Total		\$0	\$266,216	\$6,442,846	\$565,695	\$11,963	\$0	\$0	\$0	\$7,286,719
Project Budget	\$7,286,719									
Less Other Funding	\$0									
Net	\$7,286,719									
Actual Measure V Expenditures	\$7,286,719									
Running Balance	\$0									

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Final	23/24 Final	24/25 (Prelim)	Combined Totals
V 7100255										
John Adams MS Auditorium - SMMUSD (112)										
Building and Additions		\$0	\$0	\$0	\$15,000,000	\$5,000,000	\$0	\$0	\$0	\$20,000,000
Total		\$0	\$0	\$0	\$15,000,000	\$5,000,000	\$0	\$0	\$0	\$20,000,000
Project Budget	\$20,000,000									
Less Other Funding	\$0									
Net	\$20,000,000									
Actual Measure V Expenditures	\$20,000,000									
Running Balance	\$0									
S7100048										
Other Bond Related Expenses (116)										
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Lease/Rental		\$0	\$13,590	\$18,171	\$6,814	\$0	\$0	\$0	\$0	\$38,576
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Software License		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Advertising		\$0	\$0	\$0	\$770	\$900	\$0	\$0	\$0	\$1,670
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$184	\$191,065	\$0	\$0	\$0	\$0	\$0	\$0	\$191,249
Inspection & Testing		\$0	\$13,060	\$0	\$0	\$0	\$0	\$0	\$0	\$13,060
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$184	\$217,715	\$18,171	\$7,584	\$900	\$0	\$0	\$0	\$244,554
Project Budget	\$300,000									
Less Other Funding	\$0									
Net	\$300,000									
Actual Measure V Expenditures	\$244,554									
Running Balance	\$55,446									
Cost of Issuance (117)										
Cost of Issuance		\$291,277	\$0	\$0	\$0	\$452,875	\$0	\$0	\$0	\$744,152
Total		\$291,277	\$0	\$0	\$0	\$452,875	\$0	\$0	\$0	\$744,152
Project Budget	\$744,152									
Less Other Funding	\$0									
Net	\$744,152									
Actual Measure V Expenditures	\$744,152									
Running Balance	\$0									
Grand Total		\$3,079,440	\$20,483,307	\$26,712,421	\$37,545,303	\$33,015,286	\$33,740,184	\$25,335,244	\$19,880,184	\$199,791,368

**SMC Bond Program
(Measures U, S, AA and V)
Bond Contractor List as of 6-30-2025**

Student Services (Measure U #0, Measure S #9, Measure AA #120, Measure V #102):

Architect – Steinberg Architects, Morris Architects, SVA Architects
Contractor – Minco, Bernards Brothers, Spinitar, Nazerian
Engineering – IVA, Cogent Energy Engineering, XL Fire
Inspection & Testing – Geolabs, BTC Labs - Vertical V, Peak Survey, LPI
Rango, Twining, AGE
Project Management – LPI, YNL, Vanir

Replacement Health/PE/Fitness/Dance Building (Measure S #4, Measure AA #104):

Architect – Gensler Architects
Contractor – Bernards Brothers
Engineering – IVA, Glumac
Inspection & Testing – Geolabs, Ellis Environmental, Twining, Rango
Inspection, AGE
Project Management – LPI

Early Childhood Development (Measure S #5, Measure V #104):

Architect – Carde Ten Architects, SVA Architects
Consultant – Child Educational Center
Contractor – The Nazerian Group, USA Shade
Engineering – Jacobs
Inspection & Testing – Geolabs, Rango Inspection, Twining
Project Management – LPI, Vanir, YNL

Malibu Site (Measure S #6, Measure AA #110, Measure V #103):

Architect – Quatro Design Group (QDG)
Contractor – Master Contracting, Icon West
Consultant – m2 Strategic, Parker Environmental, M6 Consultants
Engineering – Ensitu Services, Jacobs, CNA
Inspection & Testing – Peak Surveys, Ellis Environmental, JL Inspection, Ninyo
& Moore, Geolabs, Twining, B2E
Project Management – LPI, M6 Strategic, Vanir, YNL

Energy Efficiency Projects (Measure S #7, Measure AA #113):

Architect – N/A
Contractor – Compass Energy Solutions, Johnson Controls
Engineering – Compass Energy Solutions, Johnson Controls
Inspection & Testing – Ellis Environmental

Environmental Performance (Measure AA #101):

Architect – Kishimoto Architects
Contractor – SJ Amoroso Construction
Engineering – P2S Engineering
Inspection & Testing – Cannon, Peak Surveys
Project Management – LPI

Information Technology Relocation (Measure AA #102):

Architect – Morris Architects
Contractor – Minco, Bernards Brothers, Eidim AV Technology
Engineering – IVA, P2S Engineering
Inspection & Testing – Cannon, Peak Surveys, Geolabs, Ellis Environmental,
Twining, JL Inspection, Rango
Project Management – LPI, CCS Presentation

Media and Technology Complex (Measure AA #103):

Architect – Clive Wilkinson Architects, Morris Architects
Contractor – H.B. Parkco Construction, Fast Track Construction, CW
Driver, Dimension Data, Key Code Media, Omega
Construction
Consultant – EEG Services
Engineering – IVA, P2S Engineering
Inspection & Testing – Twining, Geolabs, BTC Labs – Vertical V,
JL Inspection, EEG Services, Ellis Environmental, Rango,
Cannon
Project Management – LPI

Madison East Wing Seismic Upgrade (Measure AA #107):

Architect – DLR Group – WWCOT, LPI
Contractor – Trimax, Bernards Brothers, Dimension Data
Engineering – IVA, Glumac
Inspection & Testing – Twining, Peak Surveys, LPI, All Group Engineering, EEG
Services, Ellis Environmental
Project Management – LPI

Business & Facilities Infrastructure (Measure AA #111):

Architect – LPI, Gwynne Pugh Urban Studio
Contractor – REC+S, Inc., Omega Construction,
Concept Consultant, Inc.
Engineering – N/A
Inspection & Testing – Ellis Environmental, JL Inspection
Project Management – LPI

Community Classroom & Facility Project (Measure AA #114)

Architect – Morris Architects
Contractor – Waisman Construction, Spinitar, Trimax
Engineering – IVA
Inspection & Testing – LPI, Twining
Project Management – LPI

Roadways, walkways, Grounds, Parking Lots, and Garages (Measure AA #116)

Architect – LPI, DLR Group - WWCOT
Contractor – Trimax, Pub Construction
Consultant – Walker Parking
Engineering – MK Engineering
Inspection & Testing – Ellis Environmental, Peak Surveys, LPI
Project Management – LPI

Emergency Lighting, Fire Alarm, and Security System (Measure AA #119)

Contractor – Red Hawk Fire and Security, Nexus
Engineering – MDC Engineers
Inspection & Testing – Rango
Project Management – LPI

Math and Science Addition (Measure AA #106/Measure V #101)

Architect – Cannon Design
Contractor – Icon West, The Nazerian Group
Consultant – N/A
Engineering – Arup
Inspection & Testing – AGE, Geolabs, Twining, B2E, JL Inspection
Project Management – Vanir, YNL

Classrooms Relocation (Measure V #114)

Architect – Gwynne Pugh
Contractor – The Nazerian Group
Inspection & Testing – AGE
Project Management – Vanir, YNL

Art Building Replacement (Measure V #105)

Architect – Little Architects
Consultant – Fehr and Peers
Contractor – PCN3, Inc.
Engineering – tk1sc, CNA
Inspection & Testing – B2 Environmental, Geolabs, CNA, Rango, Twining
Project Management – Vanir, YNL

Air Conditioning (Measure V #107)

Architect – P2S
Contractor – A&B Construction, Inc
Engineering – tk1sc, P2S
Inspection & Testing – Rango, Koury, B2 Environmental
Project Management – Vanir, YNL

Parking Structure 3 Improvement Project (Measure V #124)

Architect – SVA Architects

Gender Neutral Bathrooms (Measure V #125)

Contractor – Reyes Electrical Contractor
Architect – TSK Architects
Inspection & Testing – CNA, Geolabs, Spectrum Fire, JL Inspection

Renovation to Corsair Stadium Project (Measure AA #108)

Architect – SVA Architects, dsk Architects, Lewis-Schoenplein
Contractors - Golden Sun Firm Co
Inspection & Testing – Ellis Environmental

Athletic Facilities (Measure V #126)

Architect – dsk Architects
Consultants – Parker Environmental
Inspection & Testing – B2E, JL Inspection, CNA, Geolabs

Drescher Hall Renovation (Measure V #110)

Architect – NAC, Inc



Paid Vendors List

(Vendors that Received Payments from Bond Funds)

For the 12-month period July 1, 2024 to June 30, 2025 (FY 2024-25)

1 World Maps (Lab Equip)	Harding Larmore Kutcher
Accugov, Inc (Lab Equip)	Hardy Diagnostics (Lab Equip)
Across Intl. (Lab Equip)	Harris Fence Co.
Airgas Inc (Lab Equip)	Icon West Construction Co.
All Group Engineering	Idemia Inc (Lab Equip)
American Time Co.	Lewis Schoenplein Architects
Arup Engineering	Paradise Cay (Lab Equip)
B&H Photo (Labs Equip)	PCN3
B2 Environmental	Penn Relocation Services
Beckman Coulter (Lab Equip)	Rango Inspection
Best Buy	Refrigeration Ice Machines
Better Bones, LLC (Lab Equip)	Sigma Aldrich (Lab Equip)
CA State DSA	So Cal Edison
California Geological Survey, State	Suttles Plumbing
Cannon Design	SVA Architects
Carolina Bio Supply (Lab Equip)	Test Equity Labs (Lab Equip)
CDW- Gov Supplies	Thomas Scientific (Lab Equip)
Chris Nelson and Associates	Triarch Inc (Lab Equip)
Cole-Parmer (Lab Equip)	TSK Architects
Dell Computer	Twining
DSK Architects	Uline
Dunwell Technology	Unisource Solutions (Furniture)
EverFence Co.	Universal Shade Co
Fagen Friedman and Fulfroost	US3 Consulting
Fisher Scientific (Lab Equip)	Vanir Construction Management
Flinn Scientific (Lab Equip)	Vernier (Lab Equip)
Geolabs	VWR Instruments (Lab Equip)
Grainger Inc	
Graybar	
