

Citizens' Bond Oversight Committee (CBOC)

Meeting on July 19th, 2023

June 30th, 2023 Report

12 Months - FY 2022-23 (Preliminary)

BOND CAPITAL CONSTRUCTION REPORTS

District Management is responsible for the preparation and fair presentation of the statement of expenditures and bond proceeds in accordance with U.S. generally accepted accounting principles; this includes the design, implementation, and maintenance of internal control relevant to the preparation and fair presentation of the statement of expenditures of bond proceeds that is free from material misstatement, whether due to fraud or error.

This report is prepared in accordance with these requirements and all bond expenditures were made in compliance with all applicable laws.


Project Number	Project Name	Measure U Budget	Measure S Budget	Measure AA Budget	Measure V Budget	Interest	Other Funding Received *	Other Funding Pending **	Total Budget	Estimate at	Status	Bond Fu
U-A	Purchase of BAE Airport Site	\$30,280,878	Budget	Budget	Buaget		Received "	Penaing **	\$30,280,878	\$30,280,878	Completed	Kemain
U-B	Emeritus College Facility	\$8,909,940					\$693,842		\$9,603,782	\$9,603,782	Completed	
U-C	Purchase of 1738 Pearl Street	\$749,208					, ,		\$749,208	\$749,208	Completed	
U-D	PE Temp. Bldg. Replacement	\$2,797,033							\$2,797,033	\$2,797,033	Completed	
U-E	Remodel Library Village for Math	\$1,458,690							\$1,458,690	\$1,458,690	Completed	
U-F	SM Airport Campus Site Improvements	\$4,170,264							\$4,170,264	\$4,170,264	Completed	
U-G	SM Airport Campus West Building	\$19,709,741							\$19,709,741	\$19,709,741	Completed	
U-H	Theater Arts Renovation	\$19,544,314							\$19,544,314	\$19,544,314	Completed	
U-I	Earthquake Rpl. Liberal Arts North	\$6,011,584					\$6,496,141		\$12,507,725	\$12,507,725	Completed	
U-K	Earthquake Rpl. Liberal Arts South	\$6,108,150					\$10,625,070		\$16,733,220	\$16,733,220	Completed	
U-L	Shuttle Replacement Parking	\$18,969,509							\$18,969,509	\$18,969,509	Completed	
U-M	North Quad Plaza	\$11,388,463							\$11,388,463	\$11,388,463	Completed	ļ
U-Q	Infrastructure & Safety	\$4,003,084							\$4,003,084	\$4,003,084	Completed	ļ
U-R	Restroom Improvements	\$17,501							\$17,501	\$17,501	Completed	ļ
S-1	Athletic Fields Phase I, Corsair Field		\$4,372,535				\$67,530		\$4,440,065	\$4,440,065	Completed	ļ
S-1A	Athletic Fields Phase I, John Adams		\$2,969,807						\$2,969,807	\$2,969,807	Completed	<u> </u>
S-10	Pico Promenade Improvements, Phase I		\$1,018,009	 					\$1,018,009	\$1,018,009	Completed	
S-13	Adv. Architecture Related Exp for AA		\$0						\$0	\$0	Completed	₩
AA-114	Community Classroom & Facility Projects	6240.212	-	\$3,162,183					\$3,162,183	\$3,162,183	Completed	
U-T	14th and Pico Project	\$319,242		 					\$319,242	\$319,242	Completed	
U-N	Letters & Sci Demo/Restore	\$0	-	¢1.025.200					\$0	\$0	Completed	-
AA-108 S-2	Renovation of Corsair Stadium	-	627.627.62	\$1,035,299			£2.002.5=c		\$1,035,299	\$1,035,299	In Design	\$9
	Performing Arts Complex	40.011.001	\$37,697,625				\$2,992,576		\$40,690,201	\$40,690,201	Completed	
U-J S-3, AA-109	Music Complex Career Opportunity Center	\$2,011,371		\$0			\$2,618,113		\$4,629,484 \$0	\$4,629,484	Completed Completed	
AA-118	,			\$27,753					7.7	\$0		-
AA-118 AA-111	Infrastructure & Technology - Utility Business & Facilities Infrastructure			\$1,968,124					\$27,753 \$1,968,124	\$27,753 \$1,968,124	Completed Completed	-
AA-111 AA-117	Infrastructure & Technology - Technology			\$2,434,417					\$1,968,124	\$1,968,124	Completed	
S-7, AA-113	Energy Efficiency Projects		\$293,361	\$3,016,773			\$708,637		\$4.018.771	\$2,434,417	Completed	
S-15	Signage Safety/Information		\$706,713	\$3,010,773			\$700,037		\$706,713	\$706,713	Completed	
AA-102	Infrastructure & Technology - Information Technology Relocation		\$700,713	\$23,140,771			\$19,798		\$23,160,569	\$23,160,569	Completed	
S-8, AA-116	Satellite Campus Parking Facilities and Roadway		\$3,891,747	\$2,130,670			\$19,796		\$6,022,417	\$6,022,417	Completed	
AA-107	Madison East Wing Seismic Upgrade		\$5,091,747	\$30,161,852					\$30,161,852	\$30,161,852	Completed	
S-4, AA-104	Replacement Health/PE/Fitness Central Plant Building		\$11,603,383	\$44,428,222			\$208,847		\$56,240,452	\$56,240,452	Completed	
AA-101	Environmental Performance - Central Plant Connections		\$11,000,000	\$10,767,251			ψ200,01 <i>7</i>		\$10,767,251	\$10,767,251	Completed	
S-14, AA-115	Real Property Acquisition		\$45,597	\$24,638,386					\$24,683,983	\$24,683,983	Completed	
AA-103	Media and Technology Complex - Academy Site		Ų 13,337	\$124,669,502			\$6,835,391		\$131,504,893	\$131,504,893	Completed	\$1,1
AA-119	Emergency Lighting, Fire Alarm, and Security System			\$11,515,614			70,000,000		\$11,515,614	\$11,515,614	Completed	
15004829	Student Services Building	\$21,131,135	\$45,595,322	\$6,870,490	\$33,624,909	\$21,681,308	\$1,321,000		\$130,224,164	\$130,224,164	Completed	\$8,9
S-5, V-104	Early Childhood Development/Childcare		\$8,858,656	, . , ,	\$15,405,517	, , , , , , , , , , , , , , , , , , , ,	\$6,661,598		\$30,925,771	\$30,925,771	Completed	\$2,3
-6, AA-110, V-103	Malibu Center and Site Acquisition		\$25,132,568		\$34,558,420	\$2,294,791	, . , ,		\$61,985,779	\$61,985,779	Completed	\$8,1
S-11, AA-112, V-109	Master Planning	\$2,110,430	\$716,428	\$834,697	\$1,000,000				\$4,661,555	\$4,661,555	In Design	\$2
-P, AA-106, V-101	Replacement Math and Science Extension Building	\$308,336		\$2,244,008	\$82,317,992		\$15,159,528	\$24,928,472	\$124,958,336	\$124,958,336	In Construction	\$34,8
AA-105, V-110	Drescher - Academic Modernization, Bookstore, Pico Promenade II		1	\$5,082	\$13,000,000				\$13,005,082	\$13,005,082	In Planning	\$13,0
V-105	Art Building Replacement				\$24,000,000		\$286,093	\$10,614,907	\$34,901,000	\$34,901,000	In Design	\$22,0
V-106	Business Building Renovation				\$12,547,000			\$12,470,000	\$25,017,000	\$25,017,000	In Planning	\$12,5
V-107	Air Conditioning				\$10,777,654				\$10,777,654	\$10,777,654	In Construction	\$6
V-108	ADA				\$4,000,000				\$4,000,000	\$4,000,000	In Planning	\$4,0
V-111	Outdoor Classroom				\$321,723				\$321,723	\$321,723	Completed	
V-112	John Adams MS Auditorium (SMMUSD)				\$20,000,000				\$20,000,000	\$20,000,000	Completed	
V-113	City of Santa Monica				\$20,000,000				\$20,000,000	\$20,000,000	In Planning	\$20,0
V-114	Classrooms Relocation				\$7,400,000				\$7,400,000	\$7,400,000	Completed	\$1
V-124	Parking Structure 3 Improvement Project				\$1,500,000				\$1,500,000	\$1,500,000	In Design	\$1,4
V-125	Gender Neutral Bathrooms				\$3,500,000				\$3,500,000	\$3,500,000	In Design	\$3,4
V-126	Athletic Facilities				\$5,000,000				\$5,000,000	\$5,000,000	In Planning	\$4,9
S-12, V-120	Other Bond Related Expenses		\$476,636		\$300,000				\$776,636	\$776,636	In Planning	9
V-115	TBD				\$39,446,785				\$39,446,785	\$39,446,785	In Planning	\$39,
16, AA-121, V-121	Cost of Issuance		\$119,470		\$800,000				\$1,417,496	\$1,417,496	In Planning	Ş
AA-122, V-122	Management Reserve			\$1,446,709	\$15,500,000	\$6,152,892			\$23,099,601	\$23,099,601	In Planning	\$16,9
S-17, AA-123, V-123	Unissuable	\$1,127	\$2,143	\$4,171					\$7,441	\$7,441	On-Going	
	Project Totals	\$160,000,000	\$142 E00 000	\$205,000,000	\$345,000,000	\$20 129 001	\$54 604 164	\$49 012 270	\$1,076,336,534	\$1,076,326,534		\$195,4

SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of June 30, 2023

Total Bond Program (AA and V)	\$640,000,000
Total Bonds Issued	\$639,995,829
Total Expenses as of 6-30-23	\$444,574,060
Total Available Remaining	\$195,421,769
Total Unsold Bond	\$4,171

Measure AA Bond \$295,000,000	
Bond Issue Date	Amount
2010	\$100,000,000
2014	\$144,995,829
2017	\$50,000,000
Total Available	\$294,995,829
Expenses as of 6-30-23	\$291,167,660
Total Available Remaining	\$3,828,169
Unsold Bond Amount	\$4,171
Total Available as of 7-1-2023	\$3,832,340

Measure V Bond \$345,000,000	
Bond Issue Date	Amount
2018	\$180,000,000
2022	\$165,000,000
Total Available	\$345,000,000
Expenses as of 6-30-23	\$153,406,400
Total Available Remaining	\$191,593,600
Unsold Bond Amount	\$0
Total Available as of 7-1-2023	\$191,593,600

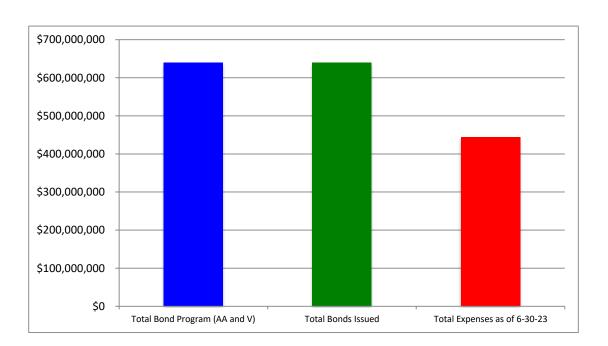


Interest	Measure AA	Measure V
As of 6-30-22	\$6,978,496	\$8,737,900
Expenditure / Arbitrage as of 6-30-22	\$5,192,948	\$0
Available Interest as of 7-1-22	\$1,785,548	\$8,737,900

(1) Original Bond \$135,000,000, refunding on 2-15-07 received additional \$8,500,000

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget As of June 30, 2023

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 6/30/23	Measure AA Expenditures as of 3/31/23	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant Connections	Completed	\$10,767,251	\$10,767,251	\$0	\$10,767,251	\$10,767,251	\$0	\$0
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$23,160,569	\$23,140,771	\$19,798	\$23,140,771	\$23,140,771	\$0	\$0
103	Media and Technology Complex - Academy Site	Completed	\$131,504,893	\$124,669,502	\$6,835,391	\$123,504,867	\$123,504,117	\$750	\$1,164,635
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$56,240,452	\$44,428,222	\$11,812,230	\$44,428,222	\$44,428,222	\$0	\$0
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	Completed	\$13,005,082	\$5,082	\$13,000,000	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	July 2024	\$124,958,336	\$2,244,008	\$122,714,328	\$2,004,184	\$2,004,184	\$0	\$239,824
107	Madison East Wing Seismic Upgrade	Completed	\$30,161,852	\$30,161,852	\$0	\$30,161,852	\$30,161,852	\$0	\$0
108	Renovation of Corsair Stadium	June 2024	\$1,035,299	\$1,035,299	\$0	\$58,299	\$39,899	\$18,400	\$977,000
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
110	Malibu Center	Completed	\$61,582,273	\$0	\$61,582,273	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$1,968,124	\$1,968,124	\$0	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	Completed	\$834,697	\$834,697	\$0	\$834,697	\$834,697	\$0	\$0
113	Energy Efficiency Projects	Completed	\$3,508,088	\$3,016,773	\$491,315	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$3,162,183	\$3,162,183	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$24,638,386	\$24,638,386	\$0	\$24,638,386	\$24,638,386	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$7,022,417	\$2,130,670	\$4,891,747	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$2,434,417	\$2,434,417	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$27,753	\$27,753	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	Completed	\$11,515,614	\$11,515,614	\$0	\$11,515,614	\$11,515,614	\$0	\$0
120	Student Services	Completed	\$130,224,164	\$6,870,490	\$123,353,674	\$6,870,490	\$6,870,490	\$0	\$0
121	Cost of Issuance	Completed	\$498,026	\$498,026	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$1,446,709	\$1,446,709	\$0	\$0	\$0	\$0	\$1,446,709
123	Unissuable Bond	Completed	\$4,171	\$4,171	\$0	\$0	\$0	\$0	\$4,171
	Project Totals		\$638,249,876	\$295,000,000	\$344,700,756	\$291,167,661	\$291,148,511	\$19,150	\$3,832,339



SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget History as of June 30, 2023


		Constitution	Preliminary	Measure AA	Measure AA		Measure AA
	Project Name	Completion	Measure AA Budget	Budget as of 3/31/23	Budget as of 6/30/23	Variance	Remaining as of 6/30/23
101	Environmental Performance - Central Plant Connections	Completed	\$12,034,042	\$10,767,251	\$10,767,251	\$0	\$0
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$13,287,218		\$23,140,771	\$0 \$0	\$0
103	Media and Technology Complex - Academy Site	Completed	\$57,480,824	\$124,669,502	\$124,669,502	\$0 \$0	\$1,164,635
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$29,232,317	\$44,428,222	\$44,428,222	\$0 \$0	\$1,104,033 \$n
105	Drescher - Academic Modernization, Bookstore, Pico Promenade II	Completed	\$34,026,480		\$5,082	\$0 \$0	\$0
106	Replacement Math and Science Extension Building	July 2024	\$68,259,000		\$2,244,008	\$0 \$0	\$239,824
107	Madison East Wing Seismic Upgrade	Completed	\$6,146,000		\$30,161,852	\$0 \$0	\$235,824
108	Renovation of Corsair Stadium	June 2024	\$11,203,000	\$1,035,299	\$1,035,299	\$0 \$0	\$977,000
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$32,384,000		\$1,033,233	\$0 \$0	\$977,000
110	Malibu Center	Completed	\$6,069,031	\$0	\$0	\$0 \$0	\$0 \$0
111	Business & Facilities Infrastructure	Completed	\$17,506,952	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	Completed	\$2,000,000		\$834,697	\$0 \$0	\$0 \$0
113	Energy Efficiency Projects	Completed	\$5,371,136		\$3,016,773	\$0 \$0	\$0 \$0
114	Community Classroom & Facility Projects	Completed	\$5,571,130	\$3,162,183	\$3,162,183	\$0 \$0	\$0
115	Real Property Acquisition	Completed	\$0	\$24,638,386	\$24,638,386	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$0	\$2,130,670	\$2,130,670	\$0 \$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$0	\$2,434,417	\$2,434,417	\$0 \$0	
118	Infrastructure & Technology - Utility	Completed	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	Completed	\$0	. ,	\$11,515,614	\$0	\$0
120	Student Services	Completed	\$0	\$6,870,490	\$6,870,490	\$0	\$0
121	Cost of Issuance	Completed	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$0	\$1,446,709	\$1,446,709	\$0	\$1,446,709
123	Unissuable Bond	Completed	\$0		\$4,171	\$0 \$0	
123	Project Totals	Sompleted	·	\$295,000,000	\$295,000,000	\$0 \$0	

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Project Schedule


As of June 30, 2023

101 Environmental Performance - Central Plant Connections		Project Name	Completion	20	20	2	021		20	22	20:	23	202	24
103 Media and Technology Complex - Academy Site	101	Environmental Performance - Central Plant Connections	Completed											
104 Replacement Health/PE/Fitness/Dance Building with Central Ple Completed 105 Drescher - Academic Modernization, Bookstore, Pico Promenad Completed 106 Replacement Math and Science Extension Building 107 Madison East Wing Seismic Upgrade 108 Renovation of Corsair Stadium 109 Career Opportunity and Advancement Center (Bundy) 109 Career Opportunity and Advancement Center (Bundy) 110 Malibu Center 111 Business & Facilities Infrastructure 112 Master Planning, Program Management, Overhead 113 Energy Efficiency Projects 114 Community Classroom & Facility Projects 115 Real Property Acquisition 116 Roadways, Walkways, Grounds, Parking Lots, and Garages 117 Infrastructure & Technology - Technology 118 Infrastructure & Technology - Technology 119 Emergency Lighting, Fire Alarm, and Security System 120 Student Services 121 Cost of Issuance 122 Management Reserve 123 Unissuable Bond 124 Completed 125 Unissuable Bond 126 Completed 127 Unissuable Bond 128 Completed 129 Unissuable Bond 120 Completed 130 Unissuable Bond 140 Completed 151 Unissuable Bond 152 Unissuable Bond 153 Unissuable Bond 154 Completed 155 Unissuable Bond 165 Completed 176 Unissuable Bond 177 Unissuable Bond 178 Unissuable Bond 178 Completed 179 Unissuable Bond 179 Unissuable Bond	102	Infrastructure & Technology - Information Technology Relocation	Completed											
105 Drescher - Academic Modernization, Bookstore, Pico Promenad 106 Replacement Math and Science Extension Building 107 Madison East Wing Seismic Upgrade 108 Renovation of Corsair Stadium 109 Career Opportunity and Advancement Center (Bundy) 100 Malibu Center 101 Malibu Center 102 Career Opportunity and Advancement Center (Bundy) 103 Master Planning, Program Management, Overhead 104 Completed 105 Completed 106 Repart Planning, Program Management, Overhead 107 Master Planning, Program Management, Overhead 108 Completed 109 Completed 110 Community Classroom & Facility Projects 111 Community Classroom & Facility Projects 112 Completed 113 Real Property Acquisition 114 Completed 115 Real Property Acquisition 116 Roadways, Walkways, Grounds, Parking Lots, and Garages 117 Infrastructure & Technology - Technology 118 Infrastructure & Technology - Technology 119 Emergency Lighting, Fire Alarm, and Security System 120 Student Services 121 Cost of Issuance 122 Management Reserve 123 Unissuable Bond 124 Completed 125 Unissuable Bond 126 Completed 127 Unissuable Bond 128 Unissuable Bond 129 Unissuable Bond	103	Media and Technology Complex - Academy Site	Completed											
106 Replacement Math and Science Extension Building 107 Madison East Wing Seismic Upgrade 108 Renovation of Corsair Stadium 109 Career Opportunity and Advancement Center (Bundy) 110 Malibu Center 111 Business & Facilities Infrastructure 112 Master Planning, Program Management, Overhead 113 Energy Efficiency Projects 114 Community Classroom & Facility Projects 115 Real Property Acquisition 116 Roadways, Walkways, Grounds, Parking Lots, and Garages 117 Infrastructure & Technology - Technology 118 Infrastructure & Technology - Utility 119 Emergency Lighting, Fire Alarm, and Security System 120 Student Services 121 Cost of Issuance 122 Management Reserve 123 Unissuable Bond 126 Completed 127 Infrastructure & Technology 128 Unissuable Bond 129 Completed 130 Completed 140 Completed 151 Completed 152 Unissuable Bond 153 Completed 154 Completed 155 Completed 166 Completed 177 Infrastructure & Technology - Utility 178 Completed 189 Completed 190 Student Services 191 Completed 192 Management Reserve 193 Unissuable Bond 193 Unissuable Bond	104	Replacement Health/PE/Fitness/Dance Building with Central Pla	Completed											
107 Madison East Wing Seismic Upgrade 108 Renovation of Corsair Stadium 109 Career Opportunity and Advancement Center (Bundy) 110 Malibu Center 111 Business & Facilities Infrastructure 112 Master Planning, Program Management, Overhead 113 Energy Efficiency Projects 114 Community Classroom & Facility Projects 115 Real Property Acquisition 116 Roadways, Walkways, Grounds, Parking Lots, and Garages 117 Infrastructure & Technology - Technology 118 Infrastructure & Technology - Utility 119 Emergency Lighting, Fire Alarm, and Security System 120 Student Services 121 Cost of Issuance 122 Management Reserve 123 Unissuable Bond 126 Completed 127 Unissuable Bond 128 Completed 129 Completed 120 Completed 120 Completed 121 Cost of Issuance 122 Management Reserve 123 Unissuable Bond 126 Completed 127 Unissuable Bond 128 Unissuable Bond 129 Completed 120 Completed 120 Completed 121 Unissuable Bond 122 Unissuable Bond	105	Drescher - Academic Modernization, Bookstore, Pico Promenad	Completed											
108 Renovation of Corsair Stadium 109 Career Opportunity and Advancement Center (Bundy) 110 Malibu Center 111 Business & Facilities Infrastructure 112 Master Planning, Program Management, Overhead 113 Energy Efficiency Projects 114 Community Classroom & Facility Projects 115 Real Property Acquisition 116 Roadways, Walkways, Grounds, Parking Lots, and Garages 117 Infrastructure & Technology - Technology 118 Infrastructure & Technology - Utility 119 Emergency Lighting, Fire Alarm, and Security System 120 Student Services 121 Cost of Issuance 122 Management Reserve 123 Unissuable Bond 130 Completed 140 Completed 151 Completed 163 Completed 174 Completed 175 Completed 176 Completed 177 Completed 178 Completed 179 Emergency Lighting, Fire Alarm, and Security System 180 Completed 191 Cost of Issuance 192 Management Reserve 193 Unissuable Bond 194 Completed 195 Completed 196 Completed 197 Completed 198 Completed 199 Completed 190 Completed 190 Completed 190 Completed 191 Cost of Issuance 191 Completed 192 Management Reserve 190 Completed	106	Replacement Math and Science Extension Building	July 2024											
109 Career Opportunity and Advancement Center (Bundy) 110 Malibu Center Completed 111 Business & Facilities Infrastructure Completed 112 Master Planning, Program Management, Overhead Completed 113 Energy Efficiency Projects Completed 114 Community Classroom & Facility Projects Completed 115 Real Property Acquisition Completed 116 Roadways, Walkways, Grounds, Parking Lots, and Garages Completed 117 Infrastructure & Technology - Technology Completed 118 Infrastructure & Technology - Utility Completed 119 Emergency Lighting, Fire Alarm, and Security System Completed 120 Student Services Completed 121 Cost of Issuance Completed Completed 122 Management Reserve On-Going 123 Unissuable Bond Completed	107	Madison East Wing Seismic Upgrade	Completed											
110 Malibu Center 111 Business & Facilities Infrastructure 112 Master Planning, Program Management, Overhead 113 Energy Efficiency Projects 114 Community Classroom & Facility Projects 115 Real Property Acquisition 116 Roadways, Walkways, Grounds, Parking Lots, and Garages 117 Infrastructure & Technology - Technology 118 Infrastructure & Technology - Utility 119 Emergency Lighting, Fire Alarm, and Security System 120 Student Services 121 Cost of Issuance 122 Management Reserve 123 Unissuable Bond 134 Completed 135 Completed 146 Completed 157 Completed 168 Completed 179 Infrastructure & Technology - Utility 170 Completed 170 Completed 171 Completed 171 Cost of Issuance 172 Completed 173 Unissuable Bond 174 Completed 175 Completed 176 Completed 177 Completed 178 Completed 179 Completed 170 Completed	108	Renovation of Corsair Stadium	June 2024											
111 Business & Facilities Infrastructure 112 Master Planning, Program Management, Overhead 113 Energy Efficiency Projects 114 Community Classroom & Facility Projects 115 Real Property Acquisition 116 Roadways, Walkways, Grounds, Parking Lots, and Garages 117 Infrastructure & Technology - Technology 118 Infrastructure & Technology - Utility 119 Emergency Lighting, Fire Alarm, and Security System 120 Student Services 121 Cost of Issuance 122 Management Reserve 123 Unissuable Bond 134 Completed 135 Completed 146 Completed 157 Completed 168 Completed 179 Infrastructure & Technology - Utility 170 Completed 170 Completed 171 Cost of Issuance 172 Cost of Issuance 173 Unissuable Bond 174 Completed 175 Completed 176 Completed 177 Completed 178 Completed 179 Completed 170 Completed	109	Career Opportunity and Advancement Center (Bundy)	Completed											
Master Planning, Program Management, Overhead Completed Senergy Efficiency Projects Completed Completed Completed Completed Real Property Acquisition Completed Infrastructure & Technology - Technology Infrastructure & Technology - Utility Emergency Lighting, Fire Alarm, and Security System Completed	110	Malibu Center	Completed											
113 Energy Efficiency Projects Completed 114 Community Classroom & Facility Projects Completed 115 Real Property Acquisition Completed 116 Roadways, Walkways, Grounds, Parking Lots, and Garages Completed 117 Infrastructure & Technology - Technology Completed 118 Infrastructure & Technology - Utility Completed 119 Emergency Lighting, Fire Alarm, and Security System Completed 120 Student Services Completed 121 Cost of Issuance Completed 122 Management Reserve On-Going 123 Unissuable Bond Completed	111	Business & Facilities Infrastructure	Completed											
114 Community Classroom & Facility Projects Completed Completed Completed Roadways, Walkways, Grounds, Parking Lots, and Garages Completed Infrastructure & Technology - Technology Completed Infrastructure & Technology - Utility Completed Student Services Completed Completed Completed Completed Unissuable Bond Completed	112	Master Planning, Program Management, Overhead	Completed											
115 Real Property Acquisition Completed 116 Roadways, Walkways, Grounds, Parking Lots, and Garages Completed 117 Infrastructure & Technology - Technology Completed 118 Infrastructure & Technology - Utility Completed 119 Emergency Lighting, Fire Alarm, and Security System Completed 120 Student Services Completed 121 Cost of Issuance Completed 122 Management Reserve On-Going 123 Unissuable Bond Completed	113	Energy Efficiency Projects	Completed											
116 Roadways, Walkways, Grounds, Parking Lots, and Garages Completed 117 Infrastructure & Technology - Technology Completed 118 Infrastructure & Technology - Utility Completed 119 Emergency Lighting, Fire Alarm, and Security System Completed 120 Student Services Completed 121 Cost of Issuance Completed On-Going 123 Unissuable Bond Completed	114	Community Classroom & Facility Projects	Completed											
117 Infrastructure & Technology - Technology Completed 118 Infrastructure & Technology - Utility Completed 119 Emergency Lighting, Fire Alarm, and Security System Completed 120 Student Services Completed 121 Cost of Issuance Completed On-Going 123 Unissuable Bond Completed	115	Real Property Acquisition	Completed											
118 Infrastructure & Technology - Utility Completed 119 Emergency Lighting, Fire Alarm, and Security System Completed Completed 120 Student Services Completed 121 Cost of Issuance Completed On-Going 123 Unissuable Bond Completed	116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed											
119 Emergency Lighting, Fire Alarm, and Security System Completed Completed Cost of Issuance Completed On-Going Unissuable Bond Completed Completed	117	Infrastructure & Technology - Technology	Completed											
120 Student Services Completed 121 Cost of Issuance Completed 122 Management Reserve On-Going 123 Unissuable Bond Completed	118	Infrastructure & Technology - Utility	Completed											
121 Cost of Issuance	119	Emergency Lighting, Fire Alarm, and Security System	Completed											
122 Management Reserve On-Going On-Goin	120	Student Services	Completed											
123 Unissuable Bond Completed	121	Cost of Issuance	Completed											
	122	Management Reserve	On-Going											
	123	Unissuable Bond	Completed											
In Planning In Construction														\Box


Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Prelim	Combined Totals
AA 7100062			1	1	Т			Т		1		ı	ı			
Environmental Performance - Central	I Plant Connoc	tions (101)														
Legal	Flant Connec	\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$125
Other Contract Services		\$0		\$49.837	\$16,239	\$0	\$0	\$0	\$0	\$9.920	\$0	\$0	\$0		\$0	\$75.996
Consultants		\$0	\$0	\$0	\$10,239	\$28		\$0	\$0	\$9,920	\$0	\$0	\$0		\$0	\$28
Building & Additions		\$0	\$0	\$0	\$361	\$729	\$640		\$6,934,044	\$446.861	\$0	\$0	\$0		\$0	\$8,711,229
Architect		\$0	\$385	\$148.311	\$176.897	\$36.256	\$040	\$1,326,392	\$0,934,044	\$0,001	\$15.699	\$0	\$0		\$0	\$377.547
Engineering		\$48.500	\$0	\$4,000	\$0	\$152,010	\$39,638	\$66,918	\$138,887	\$62,883	\$10,033	\$0	\$0		\$0	\$512.836
Inspection & Testing		\$0,500	\$0	\$7,688	\$0 \$0	\$132,010	\$0	\$7,310	\$137,150	\$4,382	\$0	\$0	\$0		\$0	\$156.529
Project Management		\$0	\$17.263	\$55,116	\$48.685	\$61.908	\$19.313	\$104.575	\$526.072	\$99.840	\$190	\$0	\$0		\$0	\$932.961
Cap Equipment		\$0	\$17,203	\$33,110	\$40,083	\$01,908	\$19,313	\$104,373	\$320,072	\$99,040	\$190	\$0	\$0		\$0	\$932,961
Non-Cap Equipment		\$0	\$0	\$0	\$0 \$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0			<u>\$0</u>
Total		\$48.500			\$242,307	\$250,931				\$623.886	\$15.889	\$0	\$0			\$10.767.251
Project Budget	\$10.767.251	Ψ40,300	Ψ17,040	Ψ£04,331	Ψ ∠+ 2,307	Ψ230,331	ψJ9,J91	ψ1,507,550	φι,ι30,132	ψ023,000	φ13,003	φ0	φυ	, 4 0	\$ 0	\$10,707,231
Less Other Funding	\$10,767,231															
Net																
Actual Measure AA Expenditures																
	80															
Running Balance	\$0															
Running Balance	\$0							1								
Running Balance AA 7100063	·															
Running Balance AA 7100063 Infrastructure & Technology - IT Relo	·	\$0	\$0	\$965	\$8.442	\$3.137	\$2,600	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$15 144
Running Balance AA 7100063	·	\$0 \$0	\$0 \$0	\$965 \$0	\$8,442 \$0	\$3,137 \$408	\$2,600 \$0	\$0 \$7.800	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$0 \$0	\$15,144 \$8,208
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies	·													\$0		\$15,144 \$8,208 \$184,543
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract	·	\$0	\$0	\$0	\$0	\$408	\$0	\$7,800	\$0	\$0 \$0	\$0	\$0	\$0	\$0 \$0	\$0	\$8,208
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants	·	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$408 \$107,390	\$0 \$0	\$7,800 \$77,074	\$0 \$79	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0 \$0	\$0 \$0	\$8,208 \$184,543
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal	·	\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$1,363	\$408 \$107,390 \$50	\$0 \$0 \$0	\$7,800 \$77,074 \$0	\$0 \$79 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0	\$8,208 \$184,543 \$1,413
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing	·	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$1,363 \$0	\$408 \$107,390 \$50 \$1,624	\$0 \$0 \$0 \$0	\$7,800 \$77,074 \$0 \$0	\$0 \$79 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage	·	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$1,363 \$0 \$0	\$408 \$107,390 \$50 \$1,624 \$1,567	\$0 \$0 \$0 \$0 \$0	\$7,800 \$77,074 \$0 \$0 \$0	\$0 \$79 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567 \$64,328
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage Other Contract Services	·	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$2,163	\$0 \$0 \$1,363 \$0 \$0 \$15,259	\$408 \$107,390 \$50 \$1,624 \$1,567 \$23,356	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$7,800 \$77,074 \$0 \$0 \$0 \$19,050	\$0 \$79 \$0 \$0 \$0 \$4,500	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567 \$64,328 \$51,116
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage Other Contract Services Moving	·	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$2,163	\$0 \$0 \$1,363 \$0 \$0 \$0 \$15,259 \$577	\$408 \$107,390 \$50 \$1,624 \$1,567 \$23,356 \$266	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$27,655	\$7,800 \$77,074 \$0 \$0 \$0 \$0 \$19,050 \$22,618	\$0 \$79 \$0 \$0 \$0 \$4,500 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage Other Contract Services Moving Site Improvement	·	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$2,163 \$0 \$0 \$0 \$505,580	\$0 \$0 \$1,363 \$0 \$0 \$0 \$15,259 \$577 \$24	\$408 \$107,390 \$50 \$1,624 \$1,567 \$23,356 \$266 \$0 \$9,667,362 \$287,201	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$27,655	\$7,800 \$77,074 \$0 \$0 \$19,050 \$22,618 \$0 \$1,203,916 \$120,091	\$0 \$79 \$0 \$0 \$0 \$4,500 \$0 \$165,229	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567 \$64,328 \$51,116 \$24
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage Other Contract Services Moving Site Improvement Building & Additions	·	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$2,163 \$0 \$0 \$0	\$0 \$0 \$1,363 \$0 \$0 \$15,259 \$577 \$24 \$1,767,083	\$408 \$107,390 \$50 \$1,624 \$1,567 \$23,356 \$266 \$0 \$9,667,362	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$27,655 \$0 \$4,288,987	\$7,800 \$77,074 \$0 \$0 \$19,050 \$22,618 \$0 \$1,203,916	\$0 \$79 \$0 \$0 \$4,500 \$0 \$165,229	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567 \$64,328 \$51,116 \$22 \$17,072,780
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage Other Contract Services Moving Site Improvement Building & Additions Architect	·	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$2,163 \$0 \$0 \$10,037 \$21,449	\$0 \$1,363 \$0 \$15,259 \$577 \$24 \$1,767,083 \$183,181 \$11,065 \$137,523	\$408 \$107,390 \$50 \$1,624 \$1,567 \$23,356 \$266 \$0 \$9,667,362 \$287,201 \$17,147 \$499,982	\$0 \$0 \$0 \$0 \$0 \$27,655 \$236,860 \$19,512 \$200,262	\$7,800 \$77,074 \$0 \$0 \$19,050 \$22,618 \$0 \$1,203,916 \$120,091 \$25,994	\$0 \$79 \$0 \$0 \$4,500 \$0 \$165,229 \$0 \$1,956	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567 \$64,328 \$51,116 \$24 \$17,072,780 \$1,920,223
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage Other Contract Services Moving Site Improvement Building & Additions Architect Engineering	·	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$2,163 \$0 \$0 \$0 \$10,037	\$0 \$1,363 \$0 \$15,259 \$577 \$24 \$1,767,083 \$183,181 \$11,065	\$408 \$107,390 \$50 \$1,624 \$1,567 \$23,356 \$266 \$0 \$9,667,362 \$287,201 \$17,147	\$0 \$0 \$0 \$0 \$0 \$27,655 \$0 \$4,288,987 \$236,860 \$19,512	\$7,800 \$77,074 \$0 \$0 \$19,050 \$22,618 \$0 \$1,203,916 \$120,091 \$25,994	\$0 \$79 \$0 \$0 \$4,500 \$0 \$165,229 \$0 \$1,956	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567 \$64,328 \$51,116 \$24 \$17,072,780 \$1,920,223 \$85,712
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage Other Contract Services Moving Site Improvement Building & Additions Architect Engineering Inspection & Testing	·	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$2,163 \$0 \$0 \$10,037 \$21,449	\$0 \$1,363 \$0 \$1,363 \$0 \$5,259 \$5,77 \$24 \$1,767,083 \$183,181 \$11,065 \$137,523 \$331,754 \$29,422	\$408 \$107,390 \$50 \$1,624 \$1,567 \$23,356 \$266 \$267,362 \$287,201 \$17,147 \$499,982 \$431,730 \$645,830	\$0 \$0 \$0 \$0 \$0 \$0 \$27,655 \$0 \$4,288,987 \$236,860 \$19,512 \$200,262 \$297,951 \$29,090	\$7,800 \$77,074 \$0 \$0 \$19,050 \$22,618 \$0 \$1,203,916 \$120,091 \$25,994	\$0 \$79 \$0 \$0 \$0 \$4,500 \$165,229 \$1,956 \$0 \$1,500 \$9,811	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567 \$64,328 \$51,116 \$24 \$17,072,780 \$1,920,223 \$85,712 \$878,868 \$1,280,653 \$1,245,576
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage Other Contract Services Moving Site Improvement Building & Additions Architect Engineering Inspection & Testing Project Management	·	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$105,049 \$102,91 \$33,460 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$2,163 \$0 \$0 \$0 \$10,037 \$21,449 \$84,991 \$0 \$0	\$0 \$1,363 \$0 \$1,363 \$0 \$15,259 \$577 \$24 \$1,767,083 \$183,181 \$11,065 \$137,523 \$331,754 \$29,422 \$18,344	\$408 \$107,390 \$1,624 \$1,567 \$23,356 \$266 \$9,667,362 \$287,201 \$17,147 \$499,982 \$431,730 \$645,830 \$10,852	\$0 \$0 \$0 \$0 \$0 \$27,655 \$236,860 \$19,512 \$200,262 \$297,951 \$29,090 \$277,219	\$7,800 \$77,074 \$0 \$0 \$19,050 \$22,618 \$0 \$1,203,916 \$120,091 \$25,994 \$568 \$22,978 \$568 \$22,978	\$0 \$79 \$0 \$0 \$0, \$4,500 \$165,229 \$0 \$1,956 \$1,500 \$1,500 \$9,811	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567 \$64,328 \$51,116 \$24 \$17,072,780 \$1,920,223 \$85,712 \$878,868 \$1,280,653 \$1,245,576
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage Other Contract Services Moving Site Improvement Building & Additions Architect Engineering Inspection & Testing Project Management Cap Equipment	ocation (102)	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$105,049 \$10,291 \$33,460	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$2,163 \$0 \$0 \$0 \$10,037 \$21,449 \$84,991	\$0 \$1,363 \$0 \$1,363 \$0 \$15,259 \$577 \$24 \$1,767,083 \$183,181 \$11,065 \$137,523 \$331,754 \$29,422 \$18,344	\$408 \$107,390 \$50 \$1,624 \$1,567 \$23,356 \$266 \$267,362 \$287,201 \$17,147 \$499,982 \$431,730 \$645,830	\$0 \$0 \$0 \$0 \$0 \$27,655 \$236,860 \$19,512 \$200,262 \$297,951 \$29,090 \$277,219	\$7,800 \$77,074 \$0 \$0 \$19,050 \$22,618 \$0 \$1,203,916 \$120,091 \$25,994 \$568 \$22,978 \$39,604	\$0 \$79 \$0 \$0 \$0 \$4,500 \$165,229 \$1,956 \$0 \$1,500 \$9,811	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567 \$64,328 \$51,116 \$17,072,780 \$1,920,223 \$85,712 \$878,868
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage Other Contract Services Moving Site Improvement Building & Additions Architect Engineering Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget	scation (102)	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$105,049 \$10,291 \$33,460 \$0 \$148,800 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$1 \$1 \$1 \$1 \$1 \$1 \$1 \$1 \$1 \$1 \$1 \$1	\$0 \$0 \$0 \$0 \$2,163 \$0 \$0 \$0 \$505,580 \$10,037 \$21,449 \$84,991 \$0 \$0 \$0 \$0	\$0 \$1,363 \$0 \$1,363 \$0 \$15,259 \$577 \$24 \$1,767,083 \$183,181 \$11,065 \$137,523 \$331,754 \$29,422 \$18,344	\$408 \$107,390 \$1,624 \$1,567 \$23,356 \$266 \$9,667,362 \$287,201 \$17,147 \$499,982 \$431,730 \$645,830 \$10,852	\$0 \$0 \$0 \$0 \$0 \$27,655 \$236,860 \$19,512 \$200,262 \$297,951 \$29,090 \$277,219	\$7,800 \$77,074 \$0 \$0 \$19,050 \$22,618 \$0 \$1,203,916 \$120,091 \$25,994 \$568 \$22,978 \$568 \$22,978	\$0 \$79 \$0 \$0 \$0, \$4,500 \$165,229 \$0 \$1,956 \$1,500 \$1,500 \$9,811	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567 \$64,328 \$51,116 \$17,072,780 \$1,920,223 \$85,78,868 \$1,280,653 \$1,245,576 \$328,994
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage Other Contract Services Moving Site Improvement Building & Additions Architect Engineering Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total	ocation (102)	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$10,049 \$0 \$10,291 \$33,460 \$0 \$0 \$144,800	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$2,163 \$0 \$0 \$0 \$505,580 \$10,037 \$21,449 \$84,991 \$0 \$0 \$0 \$0	\$0 \$1,363 \$0 \$1,363 \$0 \$15,259 \$577 \$24 \$1,767,083 \$183,181 \$11,065 \$137,523 \$331,754 \$29,422 \$18,344	\$408 \$107,390 \$1,624 \$1,567 \$23,356 \$266 \$9,667,362 \$287,201 \$17,147 \$499,982 \$431,730 \$645,830 \$10,852	\$0 \$0 \$0 \$0 \$0 \$27,655 \$236,860 \$19,512 \$200,262 \$297,951 \$29,090 \$277,219	\$7,800 \$77,074 \$0 \$0 \$19,050 \$22,618 \$0 \$1,203,916 \$120,091 \$25,994 \$568 \$22,978 \$568 \$22,978	\$0 \$79 \$0 \$0 \$0, \$4,500 \$165,229 \$0 \$1,956 \$1,500 \$1,500 \$9,811	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567 \$64,328 \$51,116 \$17,072,780 \$1,920,223 \$85,78,868 \$1,280,653 \$1,245,576 \$328,994
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage Other Contract Services Moving Site Improvement Building & Additions Architect Engineering Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net	\$23,160,569 \$19,798 \$23,140,771	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$10,049 \$10,291 \$33,460 \$0 \$0 \$148,800 <i>Received</i>	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$2 \$1 \$1 \$1 \$1 \$1 \$1 \$1 \$1 \$1 \$1 \$1 \$1 \$1	\$0 \$0 \$0 \$0 \$2,163 \$0 \$0 \$505,580 \$10,037 \$21,449 \$84,991 \$0 \$625,185	\$0 \$1,363 \$0 \$1,5259 \$577 \$1,767,083 \$183,181 \$11,065 \$137,523 \$331,754 \$29,422 \$18344 \$2,504,035	\$408 \$107,390 \$1,624 \$1,567 \$23,356 \$266 \$9,667,362 \$287,201 \$17,147 \$499,982 \$431,730 \$645,830 \$10,852	\$0 \$0 \$0 \$0 \$0 \$27,655 \$236,860 \$19,512 \$200,262 \$297,951 \$29,090 \$277,219	\$7,800 \$77,074 \$0 \$0 \$19,050 \$22,618 \$0 \$1,203,916 \$120,091 \$25,994 \$568 \$22,978 \$568 \$22,978	\$0 \$79 \$0 \$0 \$0, \$4,500 \$165,229 \$0 \$1,956 \$1,500 \$1,500 \$9,811	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567 \$64,328 \$51,116 \$17,072,780 \$1,920,223 \$85,78,868 \$1,280,653 \$1,245,576 \$328,994
Running Balance AA 7100063 Infrastructure & Technology - IT Relo Supplies Consultants Maintenance Contract Legal Printing Postage Other Contract Services Moving Site Improvement Building & Additions Architect Engineering Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding	\$23,160,569 \$19,798 \$23,140,771	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$10,049 \$10,291 \$33,460 \$0 \$0 \$148,800 <i>Received</i>	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$482,261 \$0 \$76,290 \$0 \$567,344	\$0 \$0 \$0 \$0 \$2,163 \$0 \$0 \$505,580 \$10,037 \$21,449 \$84,991 \$0 \$625,185	\$0 \$1,363 \$0 \$1,5259 \$577 \$1,767,083 \$183,181 \$11,065 \$137,523 \$331,754 \$29,422 \$18344 \$2,504,035	\$408 \$107,390 \$1,624 \$1,567 \$23,356 \$266 \$9,667,362 \$287,201 \$17,147 \$499,982 \$431,730 \$645,830 \$10,852	\$0 \$0 \$0 \$0 \$0 \$27,655 \$236,860 \$19,512 \$200,262 \$297,951 \$29,090 \$277,219	\$7,800 \$77,074 \$0 \$0 \$19,050 \$22,618 \$0 \$1,203,916 \$120,091 \$25,994 \$568 \$22,978 \$568 \$22,978	\$0 \$79 \$0 \$0 \$0, \$4,500 \$165,229 \$0 \$1,956 \$1,500 \$1,500 \$9,811	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$8,208 \$184,543 \$1,413 \$1,624 \$1,567 \$64,328 \$51,116 \$17,072,780 \$1,920,223 \$85,78,868 \$1,280,653 \$1,245,576 \$328,994



Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Prelim	Combined Totals
	g-:				,.,.,.,.,					,						
AA 7100061																
Media and Technology Complex - Ac	ademy Site (10	3)														
Consultants		\$0	\$0	\$20,675	\$12,576	\$9,488	\$7,789	\$2,102	\$0	\$12,922	\$0	\$0	\$0	\$0		\$65,551
Supplies		\$0	\$0	\$0	\$19,481	\$1,048	\$289	\$0	\$9,251	\$40,519	\$937	\$0	\$0	\$0	\$0	\$71,525
Maintenance Contract		\$0	\$0	\$0		\$0	\$0	\$0		\$23,561	\$0	\$0		\$0		\$39,483
Legal		\$16,903	\$0	\$7,958	\$43,363	\$5,066	\$26,186	\$49,155		\$36,221	\$26,991	\$121,256	\$100,053	\$200,783	\$166,941	\$816,309
Software Support		\$0	\$0	\$0	\$1,982	\$0	\$0	\$0	\$6,548	\$6,975	\$0	\$0	\$0	\$0		\$15,505
Service Fee		\$0	\$0	\$0		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0		\$17,000
Other Contract Services		\$3,993	\$5,763	\$13,456	\$39,188	\$0	\$0	\$5,853	\$22,622	\$18,628	\$7,690	\$7,550	\$0	\$0	\$0	\$124,743
Moving Expenses		\$0	\$0	\$0	\$38,756	\$0	\$0	\$0	\$0	\$97,543	\$17,556	\$0	\$0	\$0		\$153,855
Site Improvement		\$0	\$0	\$0	\$100,505	\$664	\$606	\$476	\$622	\$526	\$0	\$526	\$0	\$0		\$103,925
Building & Additions		\$0	\$538	\$1,498,660	\$3,543,657		\$17,734,534	\$23,465,347	\$16,267,550		\$219,234	\$626,512	-\$67,164	\$0		\$100,657,570
Architect		\$2,097,553	\$2,508,588	\$295,753	\$265,481	\$778,015	\$517,794		\$991,386	\$869,801	\$151,886	\$43,416	\$90,690	\$240,094	-\$1,327,000	\$8,572,392
Engineering		\$16,459	\$29,293	\$9,102	\$29,223	\$8,203	\$72,993			\$51,971	\$37,259	\$0	\$0	\$0		\$445,657
Inspection & Testing		\$64,905	\$27,527	\$123,842	\$235,287	\$563,746	\$1,381,801	\$641,972	\$525,264	\$207,240	\$27,210	\$1,212		\$0		\$3,800,005
Project Management		\$121,786	\$233,826	\$269,249		\$800,315	\$930,115	\$1,207,850	\$1,121,670	\$859,779	\$50,681	\$27,825	\$2,450	\$0		\$6,134,649
Cap Equipment		\$0	\$0	\$0	\$186,301	\$0	\$0	\$0	\$0	\$1,458,273	\$6,604	\$0	\$0	\$0		\$1,651,178
Non-Cap Equipment		\$0	\$0	\$0		\$0	\$0	\$0	\$326,845	\$490,727	\$7,167	\$0	\$0			\$835,520
Total		\$2,321,599	\$2,805,534	\$2,238,694	\$5,033,499	\$13,987,159	\$20,672,105	\$26,540,059	\$19,392,902	\$29,722,772	\$553,215	\$828,296	\$126,029	\$440,877	-\$1,157,872	\$123,504,867
Project Budget		Received														
Less Other Funding*		\$6,835,391	* Other Fund													
	\$124,669,502	·			03,412 receive	ed										
Actual Measure AA Expenditures			 Edison \$3 	1,979.48 rece	ived											
Running Balance	\$1,164,635															




Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Prelim	Combined Totals
· · · · · · · · · · · · · · · · · · ·			-	-		•							•	•	•	
AA 7100060																
Repl. Health/PE/Fitness/Dance Buildi	ng with Central	l Plant (104)														
Consultants		\$0	\$0	\$0		\$62	\$2,304	\$184	\$0	\$0	\$0	\$0	\$0	\$0		\$2,564
Supplies		\$0	\$0	\$0		\$7,089	\$195	\$484	\$20,947	\$0	\$0	\$0		\$0		\$28,715
Legal		\$0	\$0	\$0			\$0	\$663	\$80	\$0	\$0	\$0				\$742
Software Support		\$0	\$0	\$0		\$0	\$0	\$0	\$1,209	\$0	\$0	\$0	\$0	\$0	\$0	\$1,209
Site Improvement		\$0	\$0	\$0		\$0	\$559	\$440	\$575	\$0		\$0	\$0	\$0		\$1,574
Off Campus Printing		\$0	\$0	\$0		\$0	\$2,165	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$2,165
Postage		\$0	\$0	\$0	\$0	\$0	\$1,505	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,505
Other Contract Services		\$120	\$38	\$112	\$32,634	\$0	\$1,019	\$581	\$0	\$2,644	\$0	\$0	\$0	\$0		\$37,147
Building & Additions		\$0	\$0	\$0	\$817	\$4,188	\$1,623	\$13,783,023	\$14,880,829	\$5,315,393	-\$148,184	\$0	\$0	\$0	\$0	\$33,837,688
Architect		\$256,076	\$1,568,564	\$1,790,207	\$518,973	\$177,583	\$364,853	\$585,900	\$373,345	\$210,312	\$108,264	\$0	\$0	\$0	\$0	\$5,954,078
Engineering		\$0	\$8,507	\$31,650	\$7,871	\$6,529	\$9,276	\$76,712	\$51,025	\$11,318	\$2,900	\$0	\$0			\$205,788
Inspection & Testing		\$36,892	\$490	\$21,150	\$1,285	\$360	\$133,756	\$846,765	\$358,724	\$60,826	\$1,330	\$0	\$0	\$0	\$0	\$1,461,579
Project Management		\$34,968	\$113,379	\$118,783	\$94,768	\$108,528	\$463,418	\$564,240	\$487,065	\$312,539	\$20,242	\$0	\$0			\$2,317,928
Cap Equipment		\$0	\$0	\$0		\$0	\$0	\$0	\$164,793	\$68,425	\$0	\$0	\$0	\$0	\$0	\$233,218
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$9,015	\$0	\$206,229	\$127,078	\$0	\$0	\$0	\$0		\$342,322
Total		\$328,056	\$1,690,978	\$1,961,901	\$656,362	\$304,338	\$989,689	\$15,858,991	\$16,544,820	\$6,108,535	-\$15,448	\$0	\$0	\$0	\$0	\$44,428,222
Project Budget																
Less Other Funding*			* Other Fund													
	\$44,428,222		1) Measure S													
Actual Measure AA Expenditures	\$44,428,222		SCE \$190	,847.28, Gas	Co. \$18,000 re	eceived										
Running Balance	\$0															



Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23	Combined Totals
AA 7100065																
Drescher - Academic Modernization,	Bookstore, Pic	o Promenade (105)													
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Site Acquisition		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,082
Total		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,082
Project Budget																
Less Other Funding	\$13,000,000		* Other Fund	ing Source:												
Net	\$5,082		1) Measure \	/ 13,000,000 a	allocated											
Actual Measure AA Expenditures																
Running Balance	\$0															

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Prelim	Combined Totals
AA 7100090																
Replacement Math and Science Exte	nsion Building	(106)														
Legal		\$0	\$0	\$0			\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0			\$0	\$0	\$0	\$1,525	\$0	\$0	\$0	\$0	\$0	\$1,525
Site Acquisition		\$0	\$0				\$0	\$0	\$0		\$0	\$0	\$0	\$0		\$0
Building & Additions		\$0	\$0	\$0			\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$4,796
Architect		\$0	\$0	\$0			\$0	\$0	\$0	\$1,787,824	-\$94,695	\$0	\$0	\$0	\$0	\$1,693,130
Engineering		\$0	\$0	\$0			\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0			\$0	\$0	\$0		\$0	\$0	\$0	\$0		\$70,223
Project Management		\$0	\$0	\$0			\$0	\$0				\$0	\$0	\$0		\$234,510
Total		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$800	\$2,093,128	-\$94,695	\$0	\$0	\$0	\$0	\$2,004,184
Project Budget																
Less Other Funding		\$17,743,528														
	\$2,244,008		 Measure l 	J \$308,336 2) Measure V \$	82,317,992 all	ocated									
Actual Measure AA Expenditures			State of C	alifornia \$40,0	088,000 alloca	ted										
Running Balance	\$239,824															

AA 7100047																
Madison East Wing Seismic Upgrade	(107)															
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,197	\$0	\$0	\$0	\$0	\$0	\$0	\$6,197
Consultants		\$0	\$0	\$0	\$0	\$135	\$28	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$163
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$285	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$285
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$357
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$11,822	\$8,263	\$950	\$0	\$0	\$0	\$28,613
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$806	\$0	\$0	\$0	\$0	\$0	\$0	\$806
Other Contract Services		\$0	\$364	\$997	\$0	\$0	\$1,328	\$711	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,400
Building & Additions		\$0	\$656	\$312,643	\$0	\$4,248	\$6,030,371	\$8,829,626	\$4,949,223	\$3,967,591	\$0	\$0	\$0	\$0	\$0	\$24,094,358
Architect		\$76,073	\$398,050		\$65,444	\$57,480	\$199,100	\$404,764	\$122,764	\$103,824	\$0	\$0	\$0	\$0	\$0	\$1,978,088
Engineering		\$0	\$0	\$10,707	\$778	\$0	\$13,792	\$33,184	\$37,491	\$90	\$0	\$0	\$0	\$0	\$0	\$96,042
Inspection & Testing		\$0	\$19,848	\$16,752	\$3,036	\$5,851	\$676,323	\$405,443		\$4,703	\$0	\$0	\$0	\$0	\$0	\$1,244,832
Project Management		\$5,557	\$128,878	\$112,573	\$67,447	\$118,242	\$494,874	\$481,165	\$322,379	\$31,230	\$11,286	\$0	\$0	\$0	\$0	\$1,773,629
Cap Equipment		\$0	\$0	\$30,603	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$568,230
Non-Cap Equipment		\$0	\$0		\$9,788	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$366,851
Total		\$81,630	\$547,796	\$1,106,691	\$146,492	\$185,956	\$7,416,101	\$10,154,894	\$6,382,534	\$4,119,259	\$19,549	\$950	\$0	\$0	\$0	\$30,161,852
Project Budget	\$30,161,852															
Less Other Funding	\$0															
	\$30,161,852															
	\$30,161,852															
Running Balance	\$0															



Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Prelim	Combined Totals
AA 7100068																
Renovation to Corsair Stadium (108)																
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$30,759	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$23,000	\$53,759
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$4,540	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,540
Total		\$0	\$35,299	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$23,000	\$58,299
Project Budget																
Less Other Funding	\$0															
Net	\$1,035,299															
Actual Measure AA Expenditures	\$58,299															
Running Balance	\$977,000															

AA 7100067, 7100152, 7100155, 71001	157															
Business & Facilities Infrastructure (1	11)															
Supplies		\$0	\$0	\$0	\$1,493	\$4,840	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,333
Service Fee		\$0	\$0	\$0	\$12,885	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,885
Consultants		\$0	\$0	\$0	\$0	\$14	\$8	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$22
Maintenance Contract		\$0	\$0	\$0	\$0	\$1,366	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$1,366
Legal		\$0	\$0	\$75	\$0	\$0	\$0	\$1,105	\$0	\$0	\$0	\$0	\$0		\$0	\$1,180
Software License		\$0	\$0	\$0	\$0	\$375	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$375
Other Contract Services		\$0	\$6,289	\$6,988	\$750	\$0	\$2,209	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$16,236
Moving Services		\$0	\$0	\$0	\$395	\$0	\$0		\$0	\$0	\$0	\$0	\$0		\$0	\$395
Building & Additions		\$0	\$34,672	\$198,667	\$200,585	\$284,668	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$718,592
Architect		\$0	\$0	\$80,626	\$170,132	\$37,906	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$288,664
Engineering		\$0	\$0	\$0	\$3,705	\$9,735	\$6,840	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$20,280
Inspection & Testing		\$0	\$0	\$8,142	\$10,938	\$10,500	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$29,580
Project Management		\$0	\$3,073	\$154,904	\$87,291	\$139,821	\$3,571	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$388,659
Cap Equipment		\$0	\$0	\$0	\$35,892	\$80,090	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$115,982
Non-Cap Equipment		\$0	\$89,204	\$0	\$84,590	\$193,782	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$367,576
Total		\$0	\$133,238	\$449,401	\$608,656	\$763,095	\$12,628	\$1,105	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,968,124
Project Budget	\$1,968,124															
Less Other Funding	\$0															
Net	\$1,968,124															
Actual Measure AA Expenditures	\$1,968,124															
Running Balance	\$0															

AA 7100004																
Master Planning, Program Manageme	ent, Overhead	(112)														
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$139,302	\$187,927	\$245,329	\$1,270	\$0	\$0	\$0	\$0	\$573,828
Project Management		\$0	\$0	\$0	\$0	\$76,015	\$150	\$0	\$49,170	\$135,533	\$0	\$0	\$0	\$0	\$0	\$260,868
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$76,015	\$150	\$139,302	\$237,097	\$380,863	\$1,270	\$0	\$0	\$0	\$0	\$834,697
Project Budget																
Less Other Funding	\$0															
Net																
Actual Measure AA Expenditures																
Running Balance	\$0															

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Prelim	Combined Totals
AA 7100154																
Energy Efficiency Projects (113)																
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$189	\$2,108,853	\$990,389	-\$97,621	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,001,810
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$4,020	\$0	\$10,118	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14,138
Project Management		\$0	\$0	\$0	\$0	\$0	\$825	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$825
Non-Cap Equipment		\$0	\$0	\$0			\$0	\$0	\$0		\$0	\$0	\$0	\$0		\$0
Total		\$0	\$0	\$189	\$2,112,873	\$990,389	-\$86,678	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,016,773
Project Budget																
Less Other Funding	\$491,315		* Other Fund	ing Source:												
Net	\$3,016,773			715.00 receiv												
Actual Measure AA Expenditures	\$3,016,773		2) SCE \$446													
Running Balance	\$0		3) Gas Co. \$	26,080 receive	ed											

AA 7100064																
Community Classroom & Facility Proje	ects (114)															
Supplies		\$0	\$0	\$0	\$124	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$124
Legal		\$0	\$0	\$1,867	\$1,418			\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,285
Other Contract Services		\$0	\$3,720	\$1,869			\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,588
Building & Additions		\$0		\$1,369,441	\$408,696		\$0	\$0			\$0	\$0	\$0	\$0		\$2,211,712
Architect		\$0	\$263,833	\$48,120				\$0	\$0			\$0	\$0	\$0	\$0	\$313,272
Engineering		\$0	\$3,220	\$3,143	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,363
Inspection & Testing		\$0	\$41,002	\$80,885	\$1,495	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$123,382
Project Management		\$135	\$117,247	\$143,780	\$27,570	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$288,732
Non-Cap Equipment		\$0	\$0	\$209,726	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$209,726
Total		\$135	\$863,599	\$1,858,831	\$440,621	-\$1,003	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,162,183
Project Budget																
Less Other Funding	\$0															
Net	\$3,162,183															
Actual Measure AA Expenditures	\$3,162,183															
Running Balance	\$0															

-																
AA 7100057																
Real Property Acquisition (115)																
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$659	\$0	\$0	\$0	\$0	\$0	\$659
Other Contract Services		\$0	\$39	\$7,000	\$0	\$15,800	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$22,839
Site Acquisition		\$1,739,979	\$4,001,204	\$9,022,207	\$0	\$0	\$0	\$0	\$5,013,226	\$4,821,600	\$0	\$0	\$0	\$0	\$0	\$24,598,214
Inspection & Testing		\$8,689	\$7,986	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,674
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total			\$4,009,228	\$9,029,207	\$0	\$15,800	\$0	\$0	\$5,013,226	\$4,822,259	\$0	\$0	\$0	\$0	\$0	\$24,638,386
Project Budget	\$24,638,386															
Less Other Funding	\$0															
	\$24,638,386															
Actual Measure AA Expenditures																
Running Balance	\$0															

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Prelim	Combined Totals
-				•									•	•	•	
AA 7100058, 7100151, 7100156, 71000	059															
Roadways, Walkways, Grounds, Park	ing Lots, and (Garages (116)														
Supplies		\$0		\$0			\$0	\$0	\$0			\$0		\$0		\$4,616
Legal		\$0		\$0			\$0	\$0	\$0			\$0	Ψ	\$0		\$125
Consultants		\$0	\$0	\$0			\$0	\$0	\$0			\$0	Ψ			\$53,108
Other Contract Services		\$218		\$122	\$25,249		\$0	\$0	\$0		\$0	\$0	\$0			\$26,358
Building & Additions		\$185,345		\$113,784			\$0	\$0	\$0		\$0			\$0		\$1,602,864
Architect		\$0	\$0	\$0		\$19,225	\$1,240	\$0	\$0		\$0	\$0	Ψ	\$0		\$124,035
Engineering		\$0	\$0	\$0		\$1,445	\$0	\$0	\$0			\$0	\$0			\$2,540
Inspection & Testing		\$13,380		\$13,553			\$0	\$0	\$0							\$97,787
Project Management		\$24,404	\$12,439	\$21,945	\$54,095		\$1,411	\$0	\$0			\$0	\$0			\$219,237
Total		\$223,347	\$27,804	\$149,403	\$573,951	\$1,153,512	\$2,652	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,130,670
Project Budget																
Less Other Funding			* Other Fund													
Net	\$2,130,670		1) Measure S													
Actual Measure AA Expenditures			2) Measure \	': \$1,000,000	allocated											
Running Balance	\$0															

AA 7100069																
Infrastructure & Technology - Technology	ology (117)															
Software		\$0	\$0	\$0	\$0	\$0	\$218	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$218
Supplies		\$0	\$0	\$13,646	\$7,587	\$0	\$16,966	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$38,200
Maintenance Contract		\$0	\$9,472	\$46,300	\$210,581	\$18,944	\$42,415	\$9,472	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$337,186
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$49,589	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$49,589
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$207,423	\$33,063	\$576,294	\$0	\$1,145,668	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,962,449
Non-Cap Equipment		\$0	\$0	\$42,827	\$500	\$0	\$3,447	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$46,775
Total		\$0	\$216,896	\$135,838	\$794,963	\$18,944	\$1,258,304	\$9,472	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,434,417
Project Budget																
Less Other Funding	\$0															
Net	\$2,434,417															
Actual Measure AA Expenditures	\$2,434,417															
Running Balance	\$0															

AA 7100150																
Infrastructure & Technology - Utility	(118)															
Software License		\$0	\$12,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,000
Legal		\$0	\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$4,979	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,979
Project Management		\$0	\$3,240	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,240
Cap Equipment		\$0	\$0	\$7,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,534
Non-Cap Equipment		\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$20,219	\$7,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,753
Project Budget																
Less Other Funding	\$0															
Net																
Actual Measure AA Expenditures																
Running Balance	\$0															

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Prelim	Combined Totals
-																
AA 7100153																
Emergency Lighting, Fire Alarm, and	Security Syste	m (119)														
Supplies		\$0	\$0	\$0			\$0	\$0	\$2,671	\$0	\$0	\$0	\$0	\$0	\$0	\$5,020
Consultants/Legal		\$0	\$0	\$0			\$16	\$0	\$0		\$442	\$0		\$0		\$458
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$800	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$800
Maintenance Contract		\$0		\$648	\$0	\$39,700	\$0	\$2,700	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$43,048
Software Support		\$0	\$0	\$24,765	\$0	\$106,367	\$0	\$2,232	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$133,365
Other Contract Services		\$0	\$0	\$0	\$0	\$47,695	\$0	\$4,643	\$1,560	\$0	\$0	\$0	\$0	\$0	\$0	\$53,897
Building & Additions		\$0		\$0	\$0	\$110	\$2,648,866	\$4,129,145	\$1,308,230	\$763,170	\$26,375	\$79,172	\$0	\$0		\$8,955,068
Architect		\$0	\$0	\$0			\$18,925	\$0	\$0	\$5,047	\$0	\$0		\$0		\$23,972
Engineering		\$0	\$0	\$0			\$389,013	\$156,247	\$255,798	\$358,560	\$114,585	\$0		\$0		\$1,485,233
Inspection & Testing		\$0	\$0	\$0			\$0	\$58,831	\$4,800	\$0	\$0	\$0		\$0		\$63,631
Project Management		\$0	\$0	\$0		\$51,008	\$52,044	\$79,285	\$16,500	\$49,738	\$240	\$0		\$0		\$248,814
Cap Equipment		\$0	\$0	\$0		\$89,415	\$0	\$5,871	\$0	\$0	\$0	\$0		\$0		\$95,286
Non-Cap Equipment		\$0	\$0	\$6,087	\$0		\$8,348	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$407,022
Total		\$0	\$0	\$31,500	\$0	\$940,259	\$3,118,012	\$4,438,953	\$1,589,560	\$1,176,515	\$141,642	\$79,172	\$0	\$0	\$0	\$11,515,614
Project Budget																
Less Other Funding																
	\$11,515,614															
Actual Measure AA Expenditures																
Running Balance	\$0															

AA 7100142																
Student Services (120)																
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,165,626	\$3,704,864	\$0	\$0	\$0	\$0	\$6,870,490
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0		\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0		\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,165,626	\$3,704,864	\$0	\$0	\$0	\$0	\$6,870,490
Project Budget	\$6,870,490															
Less Other Funding	\$0		* Other Funding													
Net	\$6,870,490		 State of Califo 													
Actual Measure AA Expenditures	\$6,870,490		Measure U \$2				asure V \$33,62	4,909 allocated	l							
Running Balance	\$0		Measure U, S	& AA inter	ests \$21,681,308	allocated										

Cost of Issuance (121)																
Cost of Issuance		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$0	\$0	\$0	\$0	\$0	\$0	\$498,026
Total		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$0	\$0	\$0	\$0	\$0	\$0	\$498,026
Project Budget	\$498,026															
Less Other Funding	\$0															
Net																
Actual Measure AA Expenditures	\$498,026															
Running Balance	\$0	1														

Grand Total \$4,900,734 \$10,935,584 \$17,864,407 \$13,113,759 \$30,388,248 \$39,049,510 \$60,741,756 \$57,313,878 \$52,193,046 \$4	4,326,286 \$908,418 \$126,029 \$440,877 -\$1,134,872 \$291,167,660
---	--


Measure AA Interest		18/19 Final
Parking Garage and Grounds - Stude	ent Services (9)	
Site Improvement		\$0
Building & Additions		\$5,192,948
Architect		\$0
Engineering		\$0
Inspection & Testing		\$0
Project Management		\$0
Total		\$5,192,948
Project Budget	\$5,192,948	
tual Measure AA Interest Expenditures	\$5,192,948	
Running Balance	\$0	

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure V Bond Budget

As of June 30, 2023

	Project Name	Completion	Project Budget	Measure V Allocation	Other Funding	Measure V Expenditures as of 6/30/23	Measure V Expenditures as of 3/31/23	Measure V Expenditures Last Period	Total Measure V Remaining
101	Replacement Math and Science Extension Building	July 2024	\$124,958,336	\$82,317,992	\$42,640,344	\$47,677,035	\$52,666,542	-\$4,989,507	\$34,640,957
102	Student Services	Completed	\$130,224,164	\$33,624,909	\$96,599,255	\$24,674,746	\$24,607,893		\$8,950,163
103	Malibu Center	Completed	\$61,985,779	\$34,558,420	\$27,427,359	\$26,427,241	\$25,228,900	\$1,198,341	\$8,131,179
104	Early Childhood Development/Childcare	Completed	\$30,925,771	\$15,405,517	\$15,520,254	\$13,101,045	\$13,080,495	\$20,550	\$2,304,472
105	Art Building Replacement	August 2025	\$34,901,000	\$24,000,000	\$10,901,000	\$1,981,157	\$1,801,665	\$179,492	\$22,018,843
106	Business Building Renovation	December 2026	\$25,017,000	\$12,547,000	\$12,470,000	\$3,400	\$3,400	\$0	\$12,543,600
107	Air Conditioning	Completed	\$10,777,654	\$10,777,654	\$0	\$10,130,737	\$10,130,737	\$0	\$646,917
108	ADA	On-Going	\$4,000,000	\$4,000,000			\$0	\$0	\$4,000,000
109	Master Planning	December 2023	\$1,000,000	\$1,000,000	\$0	\$746,558	\$746,558	\$0	\$253,442
110	Drescher Hall Modernization	On-Going	\$13,005,082	\$13,000,000	\$5,082	\$0	\$0	\$0	\$13,000,000
111	Outdoor Classroom	On-Going	\$321,723	\$321,723	\$0	\$321,723	\$321,723	\$0	\$0
112	John Adams MS Auditorium (SMMUSD)	Completed	\$20,000,000	\$20,000,000	\$0	\$20,000,000	\$20,000,000	\$0	\$0
113	City of Santa Monica	On-Going	\$20,000,000	\$20,000,000	\$0	\$0	\$0	\$0	\$20,000,000
114	Classrooms Relocation	Completed	\$7,400,000	\$7,400,000	\$0	\$7,286,719	\$7,286,719	\$0	\$113,281
124	Parking Structure 3 Improvement Project	June 2024	\$1,500,000	\$1,500,000	\$0	\$26,280	\$6,866	\$19,414	\$1,473,720
125	Gender Neutral Bathrooms	June 2025	\$3,500,000	\$3,500,000	\$0	\$34,299	\$0	\$34,299	\$3,465,701
126	Athletic Facilities	June 2026	\$5,000,000	\$5,000,000	\$0	\$6,755	\$1,735	\$5,020	\$4,993,245
115	TBD	On-Going	\$39,446,785	\$39,446,785	\$0	\$0	\$0	\$0	\$39,446,785
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$0	\$244,553	\$244,554	-\$1	\$55,447
	Cost of Issuance	On-Going	\$800,000	\$800,000	\$0		\$744,152	\$0	\$55,848
122	Management Reserve	On-Going	\$15,500,000	\$15,500,000		\$0	\$0	\$0	\$15,500,000
	Unissuable Bond	On-Going	\$0	\$0		·	\$0		
	Project Totals		\$550,563,294	\$345,000,000	\$205,563,294	\$153,406,400	\$156,871,939	-\$3,465,539	\$191,593,600

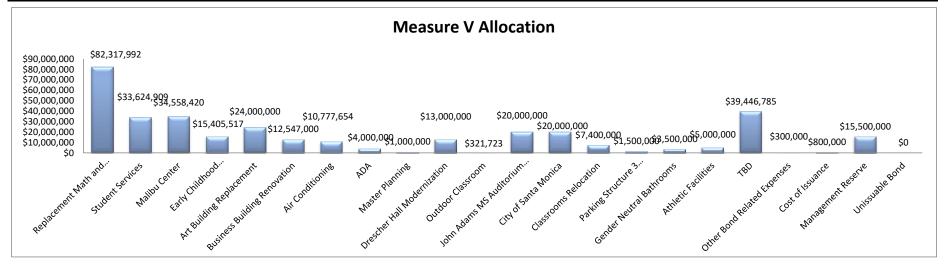

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure V Bond Budget History as of June 30, 2023

			Preliminary	Measure V	Measure V		Measure V
	Project Name	Completion	Measure V	Budget as of	Budget as of	Variance	Remaining as
			Budget	3/31/23	6/30/23		of 6/30/23
101	Replacement Math and Science Extension Building	July 2024	\$82,317,992	\$82,317,992	\$82,317,992	\$0	\$34,640,957
102	Student Services	Completed	\$21,130,252	\$33,624,909	\$33,624,909	\$0	\$8,950,163
103	Malibu Center	Completed	\$25,000,000	\$34,558,420	\$34,558,420	\$0	\$8,131,179
104	Early Childhood Development/Childcare	Completed	\$15,405,517	\$15,405,517	\$15,405,517	\$0	\$2,304,472
105	Art Building Replacement	August 2025	\$24,000,000	\$24,000,000	\$24,000,000	\$0	\$22,018,843
106	Business Building Renovation	December 2026	\$12,547,000	\$12,547,000	\$12,547,000	\$0	\$12,543,600
107	Air Conditioning	Completed	\$10,777,654	\$10,777,654	\$10,777,654	\$0	\$646,917
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$4,000,000	\$0	\$4,000,000
109	Master Planning	December 2023	\$450,000	\$1,000,000	\$1,000,000	\$0	\$253,442
110	Drescher Hall Modernization	On-Going	\$13,000,000	\$13,000,000	\$13,000,000	\$0	\$13,000,000
111	Outdoor Classroom	On-Going	\$10,000,000	\$321,723	\$321,723	\$0	\$0
112	John Adams MS Auditorium (SMMUSD)	Completed	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$0
113	City of Santa Monica	On-Going	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$20,000,000
114	Classrooms Relocation	Completed	\$0	\$7,400,000	\$7,400,000	\$0	\$113,281
124	Parking Structure 3 Improvement Project	June 2024	\$0	\$1,500,000	\$1,500,000	\$0	\$1,473,720
125	Gender Neutral Bathrooms	June 2025	\$0	\$3,500,000	\$3,500,000	\$0	\$3,465,701
126	Athletic Facilities	June 2026	\$0	\$5,000,000	\$5,000,000	\$0	\$4,993,245
115	TBD	On-Going	\$57,271,585	\$39,446,785	\$39,446,785	\$0	\$39,446,785
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$300,000	\$0	\$55,447
121	Cost of Issuance	On-Going	\$800,000	\$800,000	\$800,000	\$0	\$55,848
122	Management Reserve	On-Going	\$28,000,000	\$15,500,000	\$15,500,000	\$0	\$15,500,000
123	Unissuable Bond	On-Going	\$0	\$0	\$0	\$0	\$0
	Project Totals		\$345,000,000	\$345,000,000	\$345,000,000	\$0	\$191,593,600

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure V Project Schedule

As of June 30, 2023

	Project Name	Completion	202	20		202	21		2	022			202	3	202	24	20	25	20	026	
101	Replacement Math and Science Extension Building	July 2024																			
102	Student Services	Completed																			
103	Malibu Center	Completed																			
104	Early Childhood Development/Childcare	Completed																			
105	Art Building Replacement	August 2025																			٦
106	Business Building Renovation	December 2026																			
107	Air Conditioning	Completed																			
108	ADA	On-Going																			٦
109	Master Planning	December 2023																			1
110	Drescher Hall Modernization	On-Going																			
111	Outdoor Classroom	On-Going																			
112	John Adams SMMUSD	Completed																			
113	City of Santa Monica	On-Going																			
114	Classrooms Relocation	Completed																			
124	Parking Structure 3 Improvement Project	June 2024																			
125	Gender Neutral Bathrooms	June 2025																			
126	Athletic Facilities	June 2026																			
115	TBD	On-Going																			
120	Other Bond Related Expenses	On-Going																			
121	Cost of Issuance	On-Going																		П	7
122	Management Reserve	On-Going																			٦
123	Unissuable Bond	On-Going																			7
																					7
			In F	Planr	ing		I	n C	Cons	struc	ctio	n									╛

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Prelim	Combined Totals
V 7100090	i							
Replacement Math and Science Exten	sion Building (101)							
Legal		\$0	\$0	\$0	\$0	\$0	\$0	
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	
Moving Services		\$0	\$0	\$67,242	\$0	\$0	\$0	1 - /
Building & Additions		\$675	\$12,987	\$2,633	\$3,697,529	\$13,243,628	\$21,627,247	\$38,584,700
Architect		\$2,047,911	\$14,446	\$229,267	\$653,770	\$552,565	\$647,294	\$4,145,254
Engineering		\$0	\$0	\$19,622	\$6,966	\$10,940	\$0	\$37,529
Inspection & Testing		\$30,804	\$44,077	\$60,666	\$225,542	\$919,688	\$586,000	\$1,866,776
Project Management		\$130,874	\$617,805	\$347,350	\$474,483	\$866,097	\$448,495	\$2,885,104
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$90,431	\$90,431
Total		\$2,210,264	\$689,315	\$726,781	\$5,058,290	\$15,592,919	\$23,399,468	\$47,677,035
Project Budget	\$124,958,336	Received						
Less Other Funding	\$42,640,344	\$17,711,872	* Other Funding Sou	irce:				
Net	\$82,317,992		1) Measure U \$308,336	2) Measure AA \$2,244,0	08 allocated			
Actual Measure V Expenditures	\$47,677,035		3) State of California \$4	0,088,000 allocated				
Running Balance	\$34,640,957			•				
	1 2 / 2 2 / 2							
V 7100142								
Student Services Building (102)								
Supplies		\$0	\$71,445	\$38,162	\$0	\$0	\$0	\$109,607
Other Contract Services		\$0	\$0	\$59,784	\$6,935	\$0	\$0	\$66,719
Consultants		\$0	\$0	\$687	\$0	\$0	\$0	\$687
Software Support		\$0	\$189,120	\$0	\$0	\$0	\$0	\$189,120
Moving Services		\$0	\$55,062	\$9,056	\$0	\$0	\$0	\$64,118
Building & Additions		\$0	\$12,355,060	\$4,201,966	\$355,441	\$0	\$46,749	\$16,959,216
Architect		\$0	\$419,829	\$530,797	\$186,296	\$27,836	\$12,649	\$1,177,407
Engineering		\$0	\$140,458	\$67,481	\$0	\$0	\$0	\$207,939
Inspection & Testing		\$55,202	\$296,732	\$131,128	\$21,146	\$0	\$7,150	\$511,358
Project Management		\$0	\$900,333	\$219,425	\$85,310	\$13,020	\$0	\$1,218,088
Cap Equipment		\$0	\$1,565,928	\$90,915	\$0	\$0	\$0	\$1,656,844
Non-Cap Equipment		\$0	\$2,279,541	\$196,313	\$37,790	\$0	\$0	\$2,513,644
Total		\$55,202	\$18,273,508	\$5,545,714	\$692,918	\$40,856	\$66,548	\$24,674,746
Project Budget	\$130,224,164	·	* Other Funding Sou	irce:			·	
Less Other Funding	\$96,599,255		1) State of California \$1	,321,000 received				
Net	\$33,624,909			.35 3) Measure S 45,59	5,322,			
Actual Measure V Expenditures	\$24,674,746		4) Measure AA \$6,870,4	, , , , , , , , , , , , , , , , , , ,				
Running Balance	\$8,950,163		5) Measure U, S & AA in	terests \$21,681,308 allo	cated			

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Prelim	Combined Totals
V 7100015								
Malibu Site Acquisition and Center (10	03)							
Supplies		\$0	\$0	\$0	\$0	\$0	\$11,134	\$11,134
Software Support		\$0	\$0	\$0	\$0	\$0	\$8,281	\$8,281
Legal		\$0	\$0	\$0	\$0	\$0	\$131,244	\$131,244
Other Contract Services		\$0	\$0	\$2,713	\$38,163	\$0	\$136,245	\$177,121
Consultants		\$0	\$0	\$0	\$0	\$0	\$38,267	\$38,267
Moving Services		\$0	\$0	\$0	\$0	\$0	\$23,871	\$23,871
Building & Additions		\$0	\$0	\$2,642,861	\$3,388,666	\$8,734,478	\$6,768,448	\$21,534,453
Architect		\$0	\$0	\$0	\$155,448	\$493,355	\$224,867	\$873,670
Engineering		\$0	\$0	\$8,482	\$0	\$15,268	\$8,641	\$32,392
Inspection & Testing		\$0	\$0	\$51,754	\$633,723	\$511,002	\$156,883	\$1,353,361
Project Management		\$0	\$0	\$49,588	\$581,175	\$626,405	\$378,160	\$1,635,328
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$60,513	\$60,513
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$12,015	\$535,594	\$547,608
Total		\$0	\$0	\$2,755,398	\$4,797,174	\$10,392,522	\$8,482,146	\$26,427,241
Project Budget	\$61,985,779							
Less Other Funding	\$27,427,359		* Other Funding Sou	rce:				
Net	\$34,558,420		1) Measure S \$25,132,5	568				
Actual Measure V Expenditures	\$26,427,241		2) Interest Allocated \$2	,294,791				
Running Balance	\$8,131,179		,					
5 11 11	, , , , ,							
V 7100104								
Early Childhood Development/Childca	are (104)							
Supplies		\$0	\$0	\$35,150	\$5,332	-\$500	-\$96	\$39,886
Other Contract Services		\$0	\$0	\$35,344	\$15,128	\$0	\$0	\$50,472
Consultants		\$0	\$0	\$16	\$0	\$0	\$0	
Software Support		\$0	\$0	\$6,158	\$0	\$5,677	\$5,677	\$17,513
Legal		\$0	\$0	\$96	\$0	\$0	\$0	\$96
Building & Additions		\$0	\$0	\$8,879,770	\$1,603,432	\$0	\$73,242	\$10,556,444
v					\$275,924	\$105,158	\$27,612	
Architect		\$0	\$0	\$262,660	\$275,924	\$105,156	\$27,012	\$671,354

\$0

\$0

\$0

\$0

\$0

\$0

\$0

\$0

\$0

\$0

\$6,661,598

Received

Inspection & Testing

Project Management

Total

Project Budget

Less Other Funding

Running Balance

Actual Measure V Expenditures

\$30,925,771

\$15,520,254

\$15,405,517

\$13,101,045

\$2,304,472

Cap Equipment
Non-Cap Equipment

* Other Funding Source:

1) City of Santa Monica \$6,661,598 committed

\$135,767

\$384,714

\$92,913

\$2,513,210

\$0

\$3,700

\$2,144

\$131,730

\$0

\$0

\$13,249

\$122,833

\$0

\$0

\$0

\$502,377

\$771,137

\$32,448

\$421,155

\$13,101,045

2) Measure S \$8,858,656 allocated

\$349,661

\$384,279

\$32,448

\$328,242

\$10,333,272

Other Contract Services \$0 \$0 \$0 \$0 Consultants \$0 \$0 \$20,991 \$40,710 \$1,344 Moving Services \$0 \$0 \$0 \$0 \$0 Building & Additions \$184 \$407,369 \$3,040 \$0 \$1,791 \$108 Architect \$0 \$0 \$39,542 \$569,178 \$28,572 \$65 Engineering \$0 \$0 \$0 \$0 \$40,750	,190 \$706,48 \$0 \$40,75 ,352 \$155,77 ,775 \$470,76
Art Complex (105) Legal	\$0 \$\$ \$0 \$\$ \$0 \$63,04 \$0 \$\$,812 \$521,01 ,190 \$706,48 \$0 \$40,75 ,352 \$155,77 ,775 \$470,76
Legal	\$0 \$\$ \$0 \$\$ \$0 \$63,04 \$0 \$\$,812 \$521,01 ,190 \$706,48 \$0 \$40,75 ,352 \$155,77 ,775 \$470,76
Other Contract Services	\$0 \$\$ \$0 \$\$ \$0 \$63,04 \$0 \$\$,812 \$521,01 ,190 \$706,48 \$0 \$40,75 ,352 \$155,77 ,775 \$470,76
Consultants	\$0 \$63,04 \$0 \$,812 \$521,01 ,190 \$706,48 \$0 \$40,75 ,352 \$155,77 ,775 \$470,76
Moving Services	\$0 \$ \$,812 \$521,01 ,190 \$706,48 \$0 \$40,75 ,352 \$155,77 ,775 \$470,76
Building & Additions	,812 \$521,01 ,190 \$706,48 \$0 \$40,75 ,352 \$155,77 ,775 \$470,76
Architect \$0 \$0 \$0 \$39,542 \$569,178 \$228,572 \$655	,190 \$706,48 \$0 \$40,75 ,352 \$155,77 ,775 \$470,76
Engineering	\$0 \$40,75 ,352 \$155,77 ,775 \$470,76
Inspection & Testing	,352 \$155,77 ,775 \$470,76
Project Management \$0	,775 \$470,76
Cap Equipment \$0	
Non-Cap Equipment	
Total	\$0 \$
Project Budget \$34,901,000 Received Less Other Funding \$10,901,000 \$506,957 * Other Funding Source: Net \$24,000,000 1) State of California \$10,901,000 pending Actual Measure V Expenditures \$1,981,157 Running Balance \$22,018,843 V 7100243	\$0 \$
Less Other Funding \$10,901,000 \$506,957 *Other Funding Source: Net \$24,000,000 1) State of California \$10,901,000 pending Actual Measure V Expenditures \$1,981,157 Running Balance \$22,018,843 V 7100243 1	457 \$1,981,15
Net \$24,000,000 1) State of California \$10,901,000 pending	
Net \$24,000,000 1) State of California \$10,901,000 pending	
Actual Measure V Expenditures \$1,981,157 Running Balance \$22,018,843 V 7100243	
V 7100243	
V 7100243	
Business Building Replacement (106)	
Legal \$0 \$0 \$0 \$0 \$0	\$0 \$
Other Contract Services \$0 \$0 \$0 \$0 \$0	\$0 \$
Consultants \$0 \$0 \$0 \$0 \$0	\$0 \$
Moving Services \$0 \$0 \$0 \$0 \$0	\$0 \$
Building & Additions \$0 \$0 \$0 \$0 \$0	\$0 \$
Architect \$0 \$0 \$0 \$0 \$0	\$0 \$
Engineering \$0 \$0 \$0 \$0 \$0	\$0 \$
Inspection & Testing \$0 \$0 \$0 \$0 \$0	\$0 \$
Project Management \$0 \$0 \$3,400 \$0 \$0	\$0 \$3,40
Cap Equipment \$0 \$0 \$0 \$0 \$0	\$0 \$
Non-Cap Equipment \$0 \$0 \$0 \$0 \$0	\$0 \$
Total \$0 \$0 \$3,400 \$0 \$0	\$0 \$3,40
Project Budget \$25,017,000	
Less Other Funding \$12,470,000 * Other Funding Source:	
Net \$12,547,000 1) State Funding \$12,470,000	
Actual Measure V Expenditures \$3,400	
Running Balance \$12,543,600	

Dusingto	Durdmet	47/40 Final	40/40 Final	40/00 Final	00/04 Final	04/00 Final	00/02 Prolim	Combined Totale
Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Prelim	Combined Totals
V 7100188			1	I	1	I	1	
Air Conditioning (107)								
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$(
Consultants		\$0	\$0	\$0	\$0	\$0 \$0	\$0	\$(
Building & Additions		\$0 \$0	\$0	\$2,451	\$7,537,201	\$733,457	\$0	\$8,273,110
Architect		\$0 \$0	\$79,000	\$2,431	\$7,537,201	\$39,872	\$3,280	\$122,152
Engineering		\$417,960	\$217,966	\$26,992	\$81,868	\$109,823	\$3,375	\$857,984
Inspection & Testing		\$0	\$54,810	\$776	\$253,936	\$125,639	\$0	\$435,160
Project Management		\$4,370	\$4,570	\$35,700	\$365,350	\$32,340	\$0	\$442,330
Total		\$422,330	\$356,346	\$65,919	\$8,238,355	\$1,041,132	\$6,655	\$10,130,737
Project Budget	\$10,777,654	V.22,000	4000,0 10	400,010	+0,200,000	4.,6,.62	40,000	V.0,.00,.0
Less Other Funding	\$0							
Net	\$10,777,654							
Actual Measure V Expenditures	\$10,130,737							
Running Balance	\$646,917							
	ψο (σ)327							
V 7100004								
Master Plan (109)								
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$(
Consultants		\$0	\$0	\$0	\$0	\$48,000	\$0	\$48,000
Advertising		\$0	\$641	\$0	\$0	\$0	\$0	\$64:
Architect		\$0	\$112,073	\$528,182	\$37,861	\$0	\$14,900	\$693,016
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$(
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$(
Project Management		\$0	\$3,800	\$1,100	\$0	\$0	\$0	\$4,900
Total		\$0	\$116,515	\$529,282	\$37,861	\$48,000	\$14,900	\$746,558
Project Budget	\$1,000,000							
Less Other Funding	\$0							
Net	\$1,000,000							
Actual Measure V Expenditures	\$746,558							
Running Balance	\$253,442							
V 7100237								
Outdoor Classroom (111)								
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$100,000	\$102,023	\$102,495	\$0	\$0	\$0	\$304,518
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$(
Project Management		\$0	\$17,205	\$0	\$0	\$0	\$0	\$17,205
Total		\$100,000	\$119,228	\$102,495	\$0	\$0	\$0	\$321,723
Project Budget	\$321,723							
Less Other Funding	\$0							
Net	\$321,723							
Actual Measure V Expenditures	\$321,723							
Running Balance	\$0							

		.=		10.00, 2020				
Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Prelim	Combined Totals
	ı	T	T					
V 7100268								
Parking Structure 3 Imp Project (124)								
Other Contract Services		\$0	\$0	\$0	\$0	\$0		\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0		\$0
Architect		\$0	\$0	\$0	\$0	\$0		\$26,282
Engineering		\$0	\$0	\$0	\$0	\$0		\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0		\$0
Project Management		\$0	\$0	\$0	\$0	\$0		\$0
Total		\$0	\$0	\$0	\$0	\$0	\$26,282	\$26,282
Project Budget	\$1,500,000							
Less Other Funding	\$0							
Net	\$1,500,000							
Actual Measure V Expenditures	\$26,282							
Running Balance	\$1,473,718							
V 7100270								
Gender Neutral Bathroom Project (125	5)							
Other Contract Services	•	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0		\$20,809
Engineering		\$0	\$0	\$0	\$0	\$0		\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0		\$13,490
Project Management		\$0	\$0	\$0	\$0	\$0		\$0
Total		\$0	\$0	\$0		\$0		\$34,299
Project Budget	\$3,500,000	* - 1	* - 1	*-1	**	*-	, , , , , , , , , , , , , , , , , , , ,	, , , , , ,
Less Other Funding	\$0							
Net	\$3,500,000							
Actual Measure V Expenditures	\$34,299							
Running Balance	\$3,465,701							
Ruilling Balance	\$3,403,701							
V 7100271								
Athletic Facilities (126)								
Legal		\$0	\$0	\$0	\$0	\$0	\$6,755	\$6,755
Other Contract Services		\$0	\$0	\$0	\$0	\$0		\$0,733
		\$0	\$0	\$0	\$0	\$0 \$0		\$0
Building & Additions Architect		\$0	\$0	\$0 \$0	\$0 \$0	\$0		\$0
		\$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0		\$0
Engineering		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		
Inspection & Testing		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$C
Project Management Total		\$0 \$0	\$0 \$0	\$0	\$0	\$0		\$6,755
	¢E 000 000	φυ	φυ	φu	φu	\$ 0	φ0,/33	φ 0,7 55
Project Budget	\$5,000,000 \$0							
Less Other Funding								
Net	\$5,000,000							
Actual Measure V Expenditures	\$6,755							
Running Balance	\$4,993,245							

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	22/23 Prelim	Combined Totals
	ı		ı	ı				
V 7100243								
Classrooms Relocation (114)					1.	4	1.	4
Supplies		\$0	\$0	\$0	\$0	\$11,963	\$0	\$11,963
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$3,467	\$5,709,329	\$391,967	\$0	\$0	\$6,104,763
Supplies		\$0	\$0	\$4,982	\$0	\$0	\$0	
Architect		\$0	\$184,434	\$78,179	\$92,082	\$0	\$0	\$354,695
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	
Inspection & Testing		\$0	\$16,795	\$115,194	\$25,996	\$0	\$0	\$157,985
Project Management		\$0	\$61,520	\$476,831	\$55,650	\$0	\$0	\$594,001
Non-Cap Equipment		\$0	\$0	\$58,331	\$0	\$0	\$0	\$58,331
Total		\$0	\$266,216	\$6,442,846	\$565,695	\$11,963	\$0	\$7,286,719
Project Budget	\$7,400,000							
Less Other Funding	\$0							
Net	\$7,400,000							
Actual Measure V Expenditures	\$7,286,719							
Running Balance	\$113,281							
V 7100255								
John Adams MS Auditorium - SMMUS	D (112)							
Building and Additions		\$0	\$0	\$0	\$15,000,000	\$5,000,000	\$0	\$20,000,000
-								
Total		\$0	\$0	\$0	\$15,000,000	\$5,000,000	\$0	\$20,000,000
Project Budget	\$20,000,000	· .	·	·			•	
Less Other Funding	\$0							
Net	\$20,000,000							
Actual Measure V Expenditures	\$20,000,000							
Running Balance	\$0							

Combined Totals

22/23 Prelim

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE V EXPENDITURES FUND 42.5 As of June 30, 2023

19/20 Final

20/21 Final

21/22 Final

18/19 Final

Projects

Budget

17/18 Final

1 10,000	Daaget	17710111101	10/13 1 11141	13/20 1 11101	ZO/ZIIIIIIII	Z I/ZZ I IIIGI	ZZ/ZO I ICIIII	Outibilica rotais
S7100048								
Other Bond Related Expenses (116)								
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	
Lease/Rental		\$0	\$13,590	\$18,171	\$6,814	\$0	\$0	\$38,5
Supplies		\$0	\$0	\$0	\$0	\$0		
Legal		\$0	\$0	\$0	\$0			
Software License		\$0	\$0	\$0	\$0	\$0		
Advertising		\$0	\$0	\$0	\$770	\$900	\$0	
Other Contract Services		\$0	\$0	\$0	\$0			
Building & Additions		\$184	\$191,065	\$0	\$0	\$0		
Inspection & Testing		\$0	\$13,060	\$0	\$0			
Project Management		\$0	\$0	\$0	\$0	\$0		
Cap Equipment		\$0	\$0	\$0	\$0			
Non-Cap Equipment		\$0	\$0	\$0	\$0	· ·		
Total		\$184	\$217,715	\$18,171	\$7,584	\$900	\$0	\$244,5
Project Budget								
Less Other Funding	\$0							
Net	\$300,000							
	7300,000							
Actual Measure V Expenditures	\$244,554							
Actual Measure V Expenditures Running Balance	\$244,554							
'	\$244,554							
'	\$244,554		-					
Running Balance	\$244,554	\$291,277	\$0	\$0	\$0			\$744,18
Running Balance Cost of Issuance (117)	\$244,554	\$291,277 \$291,277	\$0 \$0	\$0 \$0	\$0 \$0			\$744,18 \$744,1 8
Running Balance Cost of Issuance (117) Cost of Issuance	\$244,554 \$55,446		\$0 \$0	\$0 \$0			\$0 \$0	\$744,1: \$744, 1:
Running Balance Cost of Issuance (117) Cost of Issuance Total	\$244,554 \$55,446 \$5800,000		\$0 \$0	\$0 \$0			\$0 \$0	\$744,1 \$744, 1
Running Balance Cost of Issuance (117) Cost of Issuance Total Project Budget	\$244,554 \$55,446 \$50,000 \$800,000		\$0 \$0	\$0 \$0			\$0 \$0	\$744,1: \$744, 1:
Running Balance Cost of Issuance (117) Cost of Issuance Total Project Budget Less Other Funding	\$244,554 \$55,446 \$55,446 \$800,000 \$0 \$800,000		\$0 \$0	\$0 \$0			\$0 \$0	\$744,1 \$744, 1

Grand Total	\$3,079,439	\$20,483,307	\$26,712,421	\$37,650,605	\$33,015,286	\$32,465,342	\$153,406,400

SMC Bond Program (Measure AA and V) Bond Contractor List as of 6-30-2023

Student Services (Measure U #0, Measure S #9, Measure AA #120, Measure V #102):

Architect – Steinberg Architects, Morris Architects, SVA Architects

Contractor – Minco, Bernards Brothers, Spinitar, Nazerian

Engineering – IVA, Cogent Energy Engineering, XL Fire

Inspection & Testing – Geo Labs, BTC Labs - Vertical V, Peak Survey, LPI Rango Inc., Twining, AGE

Project Management - LPI, YNL, Vanir

Replacement Health/PE/Fitness/Dance Building (Measure S #4, Measure AA #104):

Architect - Gensler Architects

Contractor - Bernards Brothers

Engineering – IVA, Glumac

Inspection & Testing – GeoLabs, Ellis Environmental, Twining, Rango

Inspection, AGE

Project Management - LPI

Early Childhood Development (Measure S #5, Measure V #104):

Architect - Carde Ten Architects, SVA Architects

Consultant - Child Educational Center

Contractor - The Nazerian Group

Engineering – Jacobs

Inspection & Testing - Geo Labs, Rango Inspection, Twining

Project Management - LPI, Vanir, YNL

Malibu Site (Measure S #6, Measure AA #110, Measure V #103):

Architect - Quatro Design Group

Contractor - Master Contracting, Icon West

Consultant – m2 Strategic, Parker Environmental, M6 Consultants

Engineering – Ensitu Services, Jacobs, CNA

Inspection & Testing – Peak Surveys, Ellis Environmental, JL Inspection, Ninyo

& Moore, GeoLabs, Twining

Project Management - LPI, m6 Strategic, Vanir, YNL

Energy Efficiency Projects (Measure S #7, Measure AA #113):

Architect - N/A

Contractor – Compass Energy Solutions, Johnson Controls

Engineering - Compass Energy Solutions, Johnson Controls

Inspection & Testing - Ellis Environmental

Environmental Performance (Measure AA #101):

Architect - Kishimoto Architects

Contractor – SJ Amoroso Construction

Engineering – P2S Engineering

Inspection & Testing – Cannon, Peak Surveys

Project Management - LPI

Information Technology Relocation (Measure AA #102):

Architect – Morris Architects

Contractor - Minco, Bernards Brothers, Eidim AV Technology

Engineering – IVA, P2S Engineering

Inspection & Testing - Cannon, Peak Surveys, Geo Labs, Ellis Environmental,

Twining, JL Inspection, Rango Inc.

Project Management - LPI, CCS Presentation

Media and Technology Complex (Measure AA #103):

Architect - Clive Wilkinson Architects, Morris Architects

Contractor – H.B. Parkco Construction, Fast Track Construction, CW

Driver, Dimension Data, Key Code Media, Omega Construction

Consultant - EEG Services

Engineering – IVA, P2S Engineering

Inspection & Testing – Twining, Geo Labs, BTC Labs – Vertical V,

JL Inspection, EEG Services, Ellis Environmental, Rango

Inc., Cannon

Project Management – LPI

Madison East Wing Seismic Upgrade (Measure AA #107):

Architect - DLR Group - WWCOT, LPI

Contractor - Trimax, Bernards Brothers, Dimension Data

Engineering – IVA, Glumac

Inspection & Testing - Twining, Peak Surveys, LPI, All Group Engineering, EEG

Services, Ellis Environmental

Project Management - LPI

Business & Facilities Infrastructure (Measure AA #111):

Architect - LPI, Gwynne Pugh Urban Studio

Contractor - REC+S, Inc., Omega Construction,

Concept Consultant, Inc.

Engineering – N/A

Inspection & Testing - Ellis Environmental, JL Inspection

Project Management - LPI

Community Classroom & Facility Project (Measure AA #114)

Architect - Morris Architects

Contractor – Waisman Construction, Spinitar, Trimax

Engineering – IVA

Inspection & Testing – LPI, Twining

Project Management - LPI

Roadways, walkways, Grounds, Parking Lots, and Garages (Measure AA #116)

Architect - LPI, DLR Group - WWCOT

Contractor – Trimax, Pub Construction

Consultant - Walker Parking

Engineering – MK Engineering

Inspection & Testing - Ellis Environmental, Peak Surveys, LPI

Project Management – LPI

Emergency Lighting, Fire Alarm, and Security System (Measure AA #119)

Contractor – Red Hawk Fire and Security, Nexus

Engineering - MDC Engineers

Inspection & Testing - Rango Inc.

Project Management - LPI

Math and Science Addition (Measure AA #106/Measure V #101)

Architect - Cannon Design

Contractor – Icon West, The Nazerian Group

Consultant – N/A

Engineering – Arup

Inspection & Testing – AGE

Project Management - Vanir, YNL

Classrooms Relocation (Measure V #114)

Architect – Gwynne Pugh

Contractor - The Nazerian Group

Inspection & Testing – AGE

Project Management - Vanir, YNL

Art Building Replacement (Measure V #105)

Architect – Little Architects

Contractor - N/A

Engineering – tk1sc

Inspection & Testing – B2 Environmental, Geolabs, CNA

Project Management - Vanir, YNL

Air Conditioning (Measure V #107)

Architect - P2S

Contractor – A&B Construction, Inc

Engineering – tk1sc, P2S

Inspection & Testing - Rango Inc., Koury, B2 Environmental

Project Management - Vanir, YNL

Parking Structure 3 Improvement Project (Measure V #124)

Architect – SVA Architects

Gender Neutral Bathrooms (Measure V #125)

Architect – TSK Architects

Athletic Facilities (Measure V #126)

Architect - TBD



Paid Vendors List

(Vendors that Received Payments from Bond Funds)

For the 12 month period July 1, 2022 to June 30, 2023 (FY 2022-23)

Adaptive Building Group

All Group Engineering (AGE)

ARC Printing
B2 Environmental
Cannon Design

Charter Communications
Chris Nelson and Associates

Commline

Dell Computer Dick Blick Art

Division of State Architect (DSA)

DLR Architects

Fagen Friedman and Fulfrost (FFF)

GeoLabs Grainger Inc

Harding Larmore Kuther

Icon West Construction Company

Identiv

ITSavvy

Jacobs Engineering
JH Technologies
JL Inspection

Little Architects

LPI

M6 Consulting McMurray Stern

Nth Generation

Montgomery Hardware Nazerian Construction

P2S

Pacific Office Design
QDG Architecture
Rango Inspection
School Health Corp
School Outfitters
Shade Structures Inc
Suttles Plumbing
SVA Architects

tk1sc

TSK Architects

Twining

Vanir Construction Management

Virco Manufacturing Williams Scotsman
