



CITIZENS' BOND OVERSIGHT COMMITTEE

ANNUAL REPORT, 2010-2011

Submitted to the Santa Monica Community College District

BOARD OF TRUSTEES

Dr. Andrew Walzer, Chair

Dr. Margaret Quiñones-Perez, Vice-Chair

Dr. Susan Aminoff

Judge David Finkel (Ret.)

Dr. Nancy Greenstein

Louise Jaffe

Rob Rader

Joshua Scuteri, 2011-2012 Student Trustee

CITIZENS' BOND OVERSIGHT COMMITTEE 2010-2011

Bruce Sultan, Chair Paul Leoni, Vice-Chair Deborah Arvesen Clarence Chapman Todd Flora Tiffany Inabu Corin Kahn Nimish Patel Christine Thornton

Staff Support
Greg Brown, Director of Facilities/Planning
Charlie Yen, Director of Contracts
Lisa Rose, Committee Coordinator



Santa Monica Community College District

CITIZENS' BOND OVERSIGHT COMMITTEE

TΔ	RI	F	OF	Co	NT	FN	ITS
	чов	-	\mathbf{v}	-			

	Page No
Statement of Compliance	
Measure U	3
Measure S	4
Measure AA	5
Citizens' Bond Oversight Committee Proceedings and Activities	6
Minutes of Meetings	
July 21, 2010	7
October 20, 2010	
January 19, 2011	
April 20, 2011	13
Capital Outlay Program – Bond Project Descriptions and Project Statu Measure U Reports	s16
Project Schedule	27
Bond Budget	
Expenditures	29
Measure S Reports	
Project Schedule	38
Bond Budget	
Expenditures	40
Measure AA Reports	
Project Schedule	49
Bond Budget	
Expenditures	51
Bond Sales/Expenses Report	59



ANNUAL REPORT, 2010-2011

STATEMENT OF COMPLIANCE MEASURE U FUNDS

This Annual Report is submitted to the Board of Trustees by the Santa Monica Community College District Citizens' Bond Oversight Committee.

The Committee advises that, to the best of its knowledge, the Santa Monica Community College District is in compliance with the requirements in Article XIIIA, Section I(b)(3) of the California Constitution. In particular, bond revenue has been expended only for the purposes so described in Measure U and no funds were used for any teacher or administrative salaries or other operating expenses as prohibited by Article XIIIA, Section I(b)(3)(a) of the California Constitution.

Respectfully Submitted:	
,	Bruce Sultan, Chair
	Citizens' Bond Oversight Committee
Date:	



ANNUAL REPORT, 2010-2011

STATEMENT OF COMPLIANCE MEASURE S FUNDS

This Annual Report is submitted to the Board of Trustees by the Santa Monica Community College District Citizens' Bond Oversight Committee.

The Committee advises that, to the best of its knowledge, the Santa Monica Community College District is in compliance with the requirements in Article XIIIA, Section I(b)(3) of the California Constitution. In particular, bond revenue has been expended only for the purposes so described in Measure S and no funds were used for any teacher or administrative salaries or other operating expenses as prohibited by Article XIIIA, Section I(b)(3)(a) of the California Constitution.

Respectfully Submitted:	
,	Bruce Sultan, Chair Citizens' Bond Oversight Committee
Date:	



ANNUAL REPORT, 2010-2011

STATEMENT OF COMPLIANCE MEASURE AA FUNDS

This Annual Report is submitted to the Board of Trustees by the Santa Monica Community College District Citizens' Bond Oversight Committee.

The Committee advises that, to the best of its knowledge, the Santa Monica Community College District is in compliance with the requirements in Article XIIIA, Section I(b)(3) of the California Constitution. In particular, bond revenue has been expended only for the purposes so described in Measure AA and no funds were used for any teacher or administrative salaries or other operating expenses as prohibited by Article XIIIA, Section I(b)(3)(a) of the California Constitution.

Respectfully Submitted:	
,	Bruce Sultan, Chair Citizens' Bond Oversight Committee
Date:	



ANNUAL REPORT, 2010-2011

CITIZENS' BOND OVERSIGHT COMMITTEE PROCEEDINGS AND ACTIVITIES

Meetings of the Citizens' Bond Oversight Committee

The Committee conducts its meetings in accordance with provisions of the Ralph M. Brown Public Meetings Act, Government Code Sections 54950 et seq. Meeting notices and agendas are sent to members of the Committee within the required period of time and are also posted at eight Santa Monica College campus locations and satellite sites.

Meeting notices, agendas, minutes and all documents and reports received by the Committee members are a matter of public record and made available on the SMC website:

(www.smc.edu/admin/trustees/CitizensBondOversightCommittee/default.htm)

The SMC Bond Program website is located at: www.smcbondprogram.com

Minutes of the quarterly meetings are included on the following pages.

Santa Monica Community College District



Citizens' Bond Oversight Committee MEETING – July 21, 2010 MINUTES

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, July 21, 2010 in Drescher Hall Room 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

I. **CALL TO ORDER** - 8:05 a.m.

2. ROLL CALL

Bruce Sultan, Chair - Present
Paul Leoni, Vice-Chair - Not Present
Deborah Arvesen - Present
Clarence Chapman - Present
Todd Flora - Present
Cameron Henton - Not Present
Corin Kahn - Present
Nimish Patel - Present
Christine Thornton - Present

Others Present:

Greg Brown, Director of Facilities and Planning
Don Girard, Senior Director, Government Relations/Institutional Communications
Bob Isomoto, Vice-President, Business/Administration
Lee Paul, LPI Inc.
Lisa Rose, Committee Coordinator
Charlie Yen, Director, Events and Contracts

3. APPROVAL OF MINUTES - April 21, 2010

Motion was made by Deborah Arvesen and seconded by Clarence Chapman to approve the minutes of April 21, 2010.

Motion made by: Deborah Arvesen
Seconded by: Clarence Chapman
Unanimously approved

4. INTRODUCTION OF REAPPOINTED AND NEW MEMBERS

At its meeting on July 6, 2010, the SMCCD Board of Trustees appointed the following members to the Citizens' Bond Oversight Committee, for a two-year term, 2010-2012:

Todd Flora, Local business/taxpayers' organization Corin Kahn, Local community (Sunset Park) Nimish Patel, Local community Christine Thornton (incumbent) – Local community (Sunset Park)*

Note: A representative of a senior citizens' organization and a student representative will be appointed in the fall.

^{*}Reappointed for a second two-year term, 2010-2012

5. **PUBLIC COMMENTS** - None

6. REPORTS and DISCUSSION

Measures U and S (reports included with agenda)

- Project Schedule: The first phase (demolition, excavation and shoring) of the Student Services Building project has been completed. Plans for Phase 2 are in DSA for review, but the approval process is very slow. It is expected that this three-year construction project will begin the first part of 2011. State funding for this project is committed.
- Budget: Once final FEMA funds are received, \$2.1 million will be applied to Measure U projects and the numbers will be adjusted.

Measure AA (reports included with agenda)

- Project Schedule: Upcoming projects include the Media and Technology Complex (Academy of Entertainment and Technology), the Replacement Health/PE/Fitness/ Dance Building which includes a central plant, information technology relocation, and build-out of the rest of the Bundy campus.
- The Board of Trustees will be approving a new Facilities Master Plan and the EIR at its meeting on August 3, 2010. Copies of the final Facilities Master Plan will be sent to members of the Citizens' Bond Oversight Committee following Board approval.
- State funding for future projects is dependent on the sale of bonds not yet approved by the voters.
- Escrow has closed on the purchase of the building next to Foster's Freeze on Pico Boulevard. The property at Pico and 14th is currently being used for parking, and there are no plans for the site.

Update on Malibu Site

An agreement has been negotiated with the County of Los Angeles to build a satellite campus on the county-owned land in the Malibu Civic Center. The District is waiting for the lease agreement to be finalized by the County.

Bond Sales/Expenses Report

 The final report for 2009-2010 Bond Sales/Expenses will be presented at the next meeting.

7. SCHEDULE OF MEETINGS, 2010-2011

Wednesdays at 8 a.m.
October 20, 2010
January 19, 2011
April 20, 2011

8. ADJOURNMENT - 9:05 p.m.

The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, October 20, 2010 at 8 a.m. at a Santa Monica College location. There will be a Powerpoint presentation detailing all construction projects.

The SMC Bond Program website can be accessed at: www.smcbondprogram.com



A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, October 20, 2010 in Drescher Hall Room 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

I. **CALL TO ORDER** - 8:09 a.m.

2. ROLL CALL

Bruce Sultan, Chair - Present
Paul Leoni, Vice-Chair - Present
Deborah Arvesen - Not Present
Clarence Chapman - Present
Todd Flora - Present
Cameron Henton - Present
Corin Kahn - Present
Nimish Patel - Present
Christine Thornton - Present

Others Present:

Greg Brown, Director of Facilities and Planning
Don Girard, Senior Director, Government Relations/Institutional Communications
Bob Isomoto, Vice-President, Business/Administration
Lee Paul, LPI Inc.
Lisa Rose, Committee Coordinator
Charlie Yen, Director, Contracts

3. APPROVAL OF MINUTES – July 21, 2010

Motion was made by Deborah Arvesen and seconded by Clarence Chapman to approve the minutes of July 21, 2010. *Unanimously approved*

3. <u>CITIZENS' BOND OVERSIGHT COMMITTEE ANNUAL REPORT, 2009-2010</u>

Motion was made by Paul Leoni and seconded by Christine Thornton to approve the Annual Report 2009-2010 as presented. It was noted that the financial statements included in the Annual Report have not yet been audited; the official audit report for 2009-2010 will be presented to the Committee in January, 2011. *Unanimously approved*

Operation and Maintenance Budgets for Bond Projects/Facilities

In response to a question about financial support for sustaining facilities after they are built, it was reported that the Board evaluates the operational costs of a new project prior to the award of contract for the project. The policy was established in 2004 with the approval of the Measure S bond program. The AET/KCRW project was cited as an example of SMC's evaluation process.

OVERVIEW OF FACILITIES MASTER PLAN

The SMCCD Board of Trustees approved the Facilities Master Plan in August, 2010. The following projects are in progress and/or design.

Main campus

- Information Technology Relocation
- Health/Physical Education/Fitness/Central Plant
- Math/Science Extension/Replacement
- Corsair Stadium
- Drescher Hall Renovation

Academy of Entertainment and Technology

- New Parking Structure
- Addition to existing AET Building
- KCRW

Performing Arts Campus

East Wing Replacement Building

Other Projects

- Child Development Center
- Malibu Campus
- Bundy Campus West Building Classrooms
- Bundy Career Opportunity Center

6. REPORTS and DISCUSSION

Bond Construction Program Reports, October 2010 (quarterly reports will be sent to the Committee)

Measures U, S and AA (reports included with agenda)

Measure U - expenditures last quarter were \$11,612 (architecture fees for Student Services Project)

Measure S - expenditures last quarter were \$236,231

Measure AA - expenditures last quarter were \$1,071.0002 (mostly architecture fees)

Update on Malibu Site

The District is still in negotiations on the lease agreement with the County of Los Angeles to build a satellite campus on the county-owned land in the Malibu Civic Center.

Bond Sales/Expenses Report

Total available bond funds remaining = \$162,713,711

7. SCHEDULE OF MEETINGS, 2010-2011

Wednesdays at 8 a.m. January 19, 2011 April 20, 2011

8. ADJOURNMENT - 9:26 p.m.

The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, January 19, 2011 at 8 a.m. at a Santa Monica College location

The SMC Bond Program website can be accessed at: www.smcbondprogram.com



Santa Monica Community College District

Citizens' Bond Oversight Committee MEETING – January 19, 2011 MINUTES

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, January 19, 2011 in Drescher Hall Room 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

I. CALL TO ORDER - 8:05 a.m.

2. ROLL CALL

Bruce Sultan, Chair - Present
Paul Leoni, Vice-Chair - Present
Deborah Arvesen - Present
Clarence Chapman - Present
Todd Flora - Present
Tiffancy Inabu - Present
Corin Kahn - Not Present
Nimish Patel - Present
Christine Thornton - Not Present

Others Present:

Sara Banda, representing Vicenti Lloyd & Stutzman, LLP
Chris Bonvenuto, Director of Fiscal Services
Greg Brown, Director of Facilities and Planning
Don Girard, Senior Director, Government Relations/Institutional Communications
Bob Isomoto, Vice-President, Business/Administration
Lee Paul, LPI Inc.
Lisa Rose, Committee Coordinator
Charlie Yen, Director, Contracts

3. APPROVAL OF MINUTES - October 20, 2010

Motion was made by Paul Leoni and seconded by Clarence Chapman to approve the minutes of October 20, 2010, as corrected.

Motion made by: Paul Leoni Seconded by: Todd Flora

Unanimously approved

4. INTRODUCTION OF NEW MEMBER

Tiffany Inabu was appointed by the Board of Trustees to serve as the student representative on the Citizens' Bond Oversight Committee.

5. **CONFLICT OF INTEREST FORMS**

Members were reminded to sign and submit their Conflict of Interest forms for 2011.

6. REPORTS and DISCUSSION

2009-2010 Financial Audit and Performance Audit Reports

Chris Bonvenuto, Director of Fiscal Services, provided an overview of the 2009-2010 Financial Audit and Performance Audit Reports. The Auditor indicated that there were no instances of noncompliance in both audits and did not identify any exceptions or deficiencies. *Highlights are attached.*

Motion was made by Paul Leoni and seconded by Deborah Arvesen to accept without exception the 2009-2010 Audit Reports: *Unanimously approved*.

Measure U, S and AA and Bond Sales Expenses Reports (reports included with agenda)

- Charlie Yen reported that the following clarifications suggested at the last meeting have been incorporated into the detailed oversight reports: All Reports include other funding amounts and sources; Measure S Reports shows Malibu - other expenses (Storm/Waste Water Treatment Center)
- The pie charts included on the individual project pages shows expenses to date. Most
 projects are in the planning stage, so the expenses for architects are the majority of
 expenses to date.
- The length of time for the Department of State Architect (DSA) to approve construction projects is unbelievably long at this time, about double what it should be. It is planned to start the construction phase on the Student Services project and the parking structure at the Academy of Entertainment and Technology this summer. The delay in DSA affects the sale of bonds, employment for construction projects and sequencing of projects.
- It was suggested that future expenditure/oversight reports indicate funds allocated versus funds appropriated.

Bond Sales/Expenses Report

The Bond Sales/Expenses Report indicates total bond amounts, bond issue dates/amounts, unsold bond amount and total available as of January 1, 2011.

7. **PUBLIC COMMENTS** - None

8. SCHEDULE OF MEETINGS, 2010-2011

Wednesdays at 8 a.m. April 20, 2011

9. ADJOURNMENT – 9:13 a.m.

The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, April 20, 2011 at 8 a.m. (location to be determined).

Santa Monica Community College District



Citizens' Bond Oversight Committee MEETING – April 20 2011 MINUTES

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, April 20, 2011 in Drescher Hall Room 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

I. CALL TO ORDER - 8:05 a.m.

2. ROLL CALL

Bruce Sultan, Chair – Present
Paul Leoni, Vice-Chair – Present
Deborah Arvesen – Not Present
Clarence Chapman – Present
Todd Flora – Present
Tiffancy Inabu – Present
Corin Kahn – Present
Nimish Patel – Present
Christine Thornton – Present

Others Present:

Greg Brown, Director of Facilities and Planning
Don Girard, Senior Director, Government Relations/Institutional Communications
Bob Isomoto, Vice-President, Business/Administration
Lee Paul, LPI Inc.
Lisa Rose, Committee Coordinator
Chui L. Tsang, Superintendent/President
Lisalee Anne Wells, Bond Counsel, Fulbright and Jaworski, LLP
Charlie Yen, Director, Contracts

3. APPROVAL OF MINUTES - January 19, 2011

Motion was made by Todd Flora and seconded by Clarence Chapman to approve the minutes of January 19, 2011.

Unanimously approved

4 PUBLIC COMMENTS - None

5. REPORTS and DISCUSSION

Articles on Los Angeles Community College District Bond Construction Program

In response to recent press on the Los Angeles Community College District Bond Construction Program, a comparison of the bond programs managed by the LACCD and SMCCD was presented (see attached document). In response to a question about liability, it was clarified that the Citizens' Bond Oversight Committee has no liability because it does not make decisions, it is an advisory body. In addition, members are covered under the District's Errors and Omissions policy.

The Role of Citizens' Bond Oversight Committee

Lisalee Anne Wells, Bond Counsel with Fulbright and Jaworski, LLP, presented an overview of the bond program and the Citizens' Bond Oversight Committee that included how bonds are paid by taxpayers, the historical framework, campaign promises, and how the bonds are segregated and spent. The presentation also included the requirements for the Citizens' Bond Oversight Committee, such as compliance with the Brown Act, annual reporting, responsibilities, purpose and support provided by the District.

Reports Submitted

Measure U

- Project Schedule
- Budget
- Expenditures

Measure S

- Project Schedule
- Budget
- Expenditures

Measure AA

- Project Schedule
- Budget
- Expenditures

Bond Sales/Expenses Report

Highlights of the Reports:

- The District received a payment from FEMA in the amount of \$834,763 for the Earthquake Replacement Liberal Arts North (Measure U Project I)
- The District received a rebate in the amount of \$217,323 for Energy Efficiency Projects (Measure S Project 7)
- The major expenses in Measure AA are for architects and property acquisition. The District is purchasing property on Pico Blvd. and 16th (next to the WISE building). The property will be used as swing space during construction. The long-term use of the property has not been determined.
- Malibu Property: The lease agreement for the property at the Malibu Civic Center will
 be submitted to the Los Angeles County Board of Supervisors within two months.
 Once the lease is approved, improvements to the Malibu Center will move along more
 quickly and the expenditures will be included on the Measure AA report.

Budget Update - Chui L. Tsang, Superintendent/President

The District is dealing with the budget situation on a daily basis and is facing a \$10 million reduction for the coming year. Even though state funding is not clear at this time, planning the schedules for 2011-2012 is underway. Summer 2011 will be about one-third smaller than 2010; Fall 2011 will be slightly reduced; Winter 2012 will be eliminated; Spring 2012 will be slightly reduced. These schedules will not meet the student demand, however, the District is working on a number of possibilities to come up with self-funded program so that students can meet their educational demands, although there are many restrictions to this type of program. The District is also looking at priority enrollment issues and has created a task force to address the changes as the state level.

6. ELECTION VICE-CHAIR FOR 2011-2012

Todd Flora was unanimously elected Vice-Chair, 2011-2012

7. <u>INFORMATION - Expiring terms of members of the Citizens' Bond Oversight</u> Committee

The terms of the following members of the Citizens' Bond Oversight Committee are expiring effective July 1, 2011 and are eligible for reappointment for a second two-year term:

Clarence Chapman Bruce Sultan

The terms of the following members of the Citizens' Bond Oversight Committee are expiring effective July 1, 2011 and are not eligible for reappointment for a second two-year term:

Deborah Arvesen Paul Leoni

The Board of Trustees will follow a recruitment and application process to appoint/reappoint members to fill the vacancies.

8. SCHEDULE OF MEETINGS, 2011-2012

Wednesdays at 8 a.m. July 20, 2011 October 19, 2011 January 18, 2012 April 18, 2012

9. ADJOURNMENT - 9:27 a.m.



SANTA MONICA COMMUNITY COLLEGE DISTRICT

Capital Outlay Program Bond Project Descriptions And Project Status

July 2011

Prepared by Greg Brown, Facilities Planning

Introduction

The college's capital outlay program consists of the following projects funded primary from our local bond programs, Measure U, Measure S, and Measure AA. Additional funding sources are noted for each project. Projects are listed by the approximate dates of completion, although the schedule is pending on several projects. Project descriptions for projects in planning are subject to change. Project descriptions for completed projects are the original descriptions although current programs may have changed.

Section I - Completed Projects:

Emeritus College

Project Description: Emeritus College, a program designed for lifelong learning, was located in a rented storefront on the first level of a parking garage on 2nd Street. The program long ago outgrew its- former home. The first use of Measure U bond funds was the purchase of a newly constructed four story building further north on 2nd Street. This building gives Emeritus a permanent home with room to accommodate all their programs including a computer room, exercise studios and art classroom. There is also a large multipurpose room on the first floor for lectures, films and productions. The building shell was completed when the college purchased the building and the interior improvements were completed by the college.

Project Schedule: Completed 2003
Project Bond Allocation: \$8,909,940

Funding Sources: Measure U, SMC Foundation

Library Renovation and Expansion

Project Description: The college's main library which was damaged in the 1994 Northridge Earthquake was seismically upgraded, modernized and expanded. The project added more book area, more study space and a large computer lab. Seating for students was more than doubled.

Project Schedule: Completed 2003
Project Bond Allocation: \$23,600,000
Funding Sources: Measure T, State, FEMA

Relocate Kinesiology, Dance, Recreation and Athletics

Project Description: The former offices of the Kinesiology, Dance, Recreation and Athletics departments were in a temporary building installed in 1976. The temporary buildings had numerous maintenance problems and code deficiencies. The college has removed these buildings to create open space on the campus. The project has resulted in a similar amount of offices and has added a conference room and workroom to make a more useable office facility. The offices are on the second floor of the gymnasium complex, where the east bleachers of the stadium used to be located, making better use of the limited ground space on the campus.

Project Schedule: Completed 2004 **Project Bond Allocation:** \$2,797,033

Funding Sources: Measure U

Library Village Renovation - Math

Project Description: With the completion of the new Library, the "Temporary Library" was made available for renovation. The Math department was working out of temporary buildings that were set up after the 1994 earthquake. Those buildings will need to be removed to make way for the Liberal Arts – South Building. With this renovated facility all of the Math department is located in one building with additional classroom and lab facilities.

Project Schedule: Completed 2004
Project Bond Allocation: \$1,458,690

Funding Sources: Measure U

Bundy Campus (Former BAE Systems Site next to Santa Monica Airport)

Project Description: The 1998 Santa Monica College Facilities Master Plan proposed that additional property be purchased for instructional facilities and parking. In December 2001, the SMC Board of Trustees approved the purchase of the 10.4 acre parcel of land south of the Santa Monica Airport, owned and occupied by BAE Systems, with about 1,200 employees. BAE accessed the property through two vehicular entrances through the Santa Monica Airport and one on Stewart Avenue. In May 2003, BAE Systems ceased occupancy. In July 2003, the SMC Board of Trustees approved certain property improvements, including roadway access to the lower portion of the property from Bundy, safety modifications, and utility relocations.

In September 2003, SMC began an ongoing series of neighborhood meetings with nearby residents. These meetings resulted in consensus for a 10-foot sound wall on the perimeter of the property along both the Stanwood Place and Stewart Avenue sides of the campus, along with hundreds of new trees and new landscaping. These improvements addressed quality of life issues by creating a buffer between the college and the residential neighborhood. The College intends to prohibit both vehicular and pedestrian access to the campus from Stewart Avenue (excepting emergency vehicles) and require all access from either Bundy or Airport Avenue.

In March 2004, the SMC Board of Trustees approved the demolition and removal of Building #1, a very large one-story manufacturing and warehouse building; the demolition and removal of Building #3, a smaller one-story manufacturing building; the renovation of Building #4 (West Building), the four-story office building; and additional landscaping improvements. The removal of the manufacturing and warehouse facilities resulted in a reduction of 100,000 square feet of building space on the property. In accordance with CEQA, the Board of Trustees adopted a Mitigated Negative Declaration in connection with its approval of the adaptive reuse of Building #4. The four-story building is used for the College's Nursing program, Early Childhood Education program, Continuing Education program, and one floor for general education classes.

In July of 2004 construction commenced on a complete renovation of the West Building. The building was finished and opened for classes in summer of 2005. In January of 2005, the Board of Trustees approved a group of architects and consultants to plan the long term future of the site. A number of meetings were held with faculty, staff, students and community members to review possible future uses for the site. A master plan, environmental impact report and traffic study were approved by the Board in February of 2007.

Part of the master plan included a new traffic signal to enhance the safety of those entering the campus. The City of Los Angeles has approved a new traffic signal and driveway for the campus.

Project Schedule: West Building Completed 2005

Master Plan and EIR Completed

Traffic signal and driveway, Completed 2009

Project Bond Allocation: West Building: \$29,291,387 (Includes related site work)

Driveway and traffic signal \$5,411,382

Funding Sources: Measure U and S (Driveway and Signal)

Renovation, Theater Arts

Project Description: Originally designed as a small children's theater and a radio theater, the Little Theater (later called the Main Stage) at Santa Monica College was first occupied in 1952.

It received some minor remodeling and renovation over the years, but was never been modified to accommodate its current use as a facility for the production of drama and musical theater. Its physical limitations severely restricted the type of productions which were be presented, therefore limiting the experience of our acting, directing, and technical theater students and restricting the creativity of students, faculty and staff. Along with numerous functional improvements, significant ADA and Fire Code upgrade and compliance measures were part of this project.

The new project has full theatrical lighting and sound facilities, a larger stage with space above to fly scenery out of audience view, larger dressing rooms with showers and full costume shop. Scenery can now be built in the scene shop and moved to the stage, before all large scenery pieces were built on stage, limiting stage use for classes and rehearsals.

Project Schedule: Completed 2006
Project Bond Allocation: \$19,569,266

Funding Sources: Measure U

Music Complex

Project Description: The former Music Building was completed as part of the original campus in 1952. Since 1985, the SMC Music Department has added a symphony orchestra, concert band, and an opera workshop to its performance group offerings as well as increasing the number of applied music classes to include string, woodwind, brass and percussion classes as well as the piano, voice, recorder and guitar classes it has traditionally offered. The new facility has 27 practice rooms instead of 14 in the former building. The additional practice rooms and support areas have significantly improved the quality of the educational experience for music students.

The Music department move is needed to make room for the planned Student Services complex which will take the ground space currently occupied by Music and the Amphitheater.

Project Schedule: Completed 2007 **Project Bond Allocation:** \$1,967,421

Funding Sources: Measure U

Performing Arts Complex

Project Description: The Music and Performing Arts Complex, Madison Campus project is SMC's new comprehensive teaching, exhibit and performance facility for the arts. Within the framework of SMC's overall mission, the new facility will strive to promote artistic excellence, creativity, collaboration, and the free exchange of ideas in an open, caring, challenging yet supportive community of learners, thereby building new and future generations of artists and audiences.

The Music and Performing Arts Complex will serve as an academic institution, accommodating the arts education programs and departments of SMC and serving the College community through exceptional training in the performing arts. Throughout the academic year, the theater will serve as a large classroom or lecture hall suitable for screenings, performance workshops, guest speakers, and other classroom activities and College-related uses.

The facility's intent is to present programs and performances that reflect the cultural diversity, the multiplicity of interests, and the full range of ages that characterize the students of SMC and the residents of the region. The theater hopes to set a new standard for artistic excellence for SMC students and to attract the highest caliber of visiting artists to the venue.

The theater will be located on the 4.4-acre former Madison Elementary School leased from the Santa Monica-Malibu Unified School District for 66 years, at 1310 11th Street. The theater addition is about 34,000 square feet and the existing building is about 40,000 square feet. The facility will have 541 seat and state of the art sound, lighting and production facilities. The project includes parking for 301 cars as well as improvements to the existing rehearsal hall.

Project Schedule: Completed 2008

Project Bond Allocation: \$36,486,648, Total Project Cost \$39,479,224

Funding Sources: Measure S and SMC Foundation

Earthquake Replacement Liberal Arts North Earthquake Replacement Liberal Arts South

Project Description: The Liberal Arts Bldg, originally constructed in 1952, was extensively damaged during the 1994 Northridge Earthquake. The college has determined that the replacement of the Liberal Arts Building is a more sensible, safe, and prudent course of action to take, rather than restoring the building back to it's original 1952 configuration with respect to poor functionality, low technology and low efficiency.

The new building has two wings, one that is being planned for the history department and another for the social sciences. The first phase has nine new classrooms and faculty offices, the second phase has 15 new classrooms and faculty offices including lab and tutoring space. Each classroom will be a "smart" classroom wired for computer and instructional technology.

The district has obtained funding from a variety of sources including federal, state and local (City of Santa Monica). Due to the funding timelines of the granting agencies the construction on one wing was started before funds were released for the second wing.

Project Schedule North: Completed 2006 **Project Schedule South:** Completed 2007

Project Bond Allocation: \$12,619,066, Total Project Cost \$30,365,036

Funding Sources: City of Santa Monica Earthquake Redevelopment, State, FEMA, Measure U

Shuttle Replacement Parking

Project Description: The College has operated a shuttle parking lot at the Santa Monica Airport since 1988. This remote shuttle lot has played a major part in the college's transportation management program. In November of 2005 the City of Santa Monica commenced construction of a public park at the Airport and has temporarily moved the shuttle lot to a beach parking lot. The beach lot is not suitable for long term use by the college and the City has asked to college to leave the location after the spring semester. In January of 2007 the college completed a purchase of 2.35 acres from Verizon at the corner of Stewart and Exposition in Santa Monica. Soon thereafter construction commenced on a 220 space parking lot which opened for fall 2007.

Project Schedule: Completed 2007
Project Bond Allocation: \$18,967,156

Funding Sources: Measure U

Northwest Quad Development

Project Description: Santa Monica College has very limited land space. Over the years both the number of students and the number of buildings have grown on campus. In addition to this, after the 1994 Northridge earthquake a large number of temporary structures were placed on the campus to hold programs that were dislodged from their original buildings for repairs and renovations.

With the planned removal of many of the temporary structures the college will have the opportunity to create some much need open space on the campus. In addition, the 1998 Master Plan calls for the removal of the Amphitheater to make way for the planned Student Services complex. An area needs to be provided for student events that were formally held in the amphitheater. The new Library, Campus Theater, and Liberal Arts will face the new "quad" area creating a central focal point for this portion of the campus.

Project Schedule: Completed 2008
Project Bond Allocation: \$11,493,568

Funding Sources: Measure U

Campus Infrastructure/Safety

Project Description: The major portion of the Santa Monica College campus was opened in 1952. Much of the original infrastructure still remains. Some of the infrastructure was damaged in the 1994 Northridge Earthquake. Pieces of the original infrastructure have been repaired and replaced over the years on a piecemeal basis. Changes in technology have rendered much of the original infrastructure obsolete. In addition changes in our society require that additional efforts are needed to provide a safe and secure environment for the campus community. Other safety upgrades include earthquake retrofits.

This project proposes to update the infrastructure for traffic, water, gas, sewer, electrical, fire and security based upon recent master planning efforts. It also includes a suitable facility for the colleges Information Technology area. The changes will be coordinated with building construction activity in the area. As part of the infrastructure project, the college will address circulation including improvement of the Pico Blvd. presentation, signage and way finding.

Project Schedule: Substantially Complete **Project Bond Allocation:** \$7,649,901

Funding Sources: Measure U

Physical Education and Athletic Fields

Project Description: SMC currently offers credit classes in physical education, athletics, and kinesiology; non-credit courses in health and conditioning (through Emeritus College); and not-for credit courses in recreation and fitness (through Continuing and Community Education). Compared to most other campuses, SMC is deficient in field space. The Physical Education program lacks outdoor facilities available at other campuses, including a baseball field, a softball field, and a practice field for football, a soccer field, outdoor volleyball courts, and outdoor basketball courts. The District rents field space in order to offer some of these programs; however, there is insufficient field space in Santa Monica.

This project provides for field improvements and for the retrofit of existing District fields and athletic facilities or other fields available to the District for year-round usage. The first renovation will be the John Adams Middle School Field. This field is shared by the College, School District, City and community groups. The second field project will be the colleges Corsair Field. All fields will be made available for community use when not in instructional use.

Project Schedule: John Adams Middle School Field, Completed 2008

SMC Corsair Field, Completed 2009

Project Bond Allocation: \$8,439,445

Funding Sources: Measure S

Section II - Projects in Construction Phase

Student Services Building

Project Description: In conformance with the 1998 SMC Adopted Master Plan this project will combine and provide improved user access to various student services and some administrative functions.

The new Student Services portion of this proposed building will facilitate the centralization of all Student Services operations that are also presently dispersed throughout the campus, and housed in temporary buildings. This project provides office and service space for approximately 25 Student Services functions.

The Administration portion of this proposed project will house Academic and Student Services administrators, and to be integrated along with the Student Services functions to provide a one-stop service delivery location. The new building will be sited near the Pico Boulevard main entrance to the SMC campus and thereby provide immediate access for students and members of the college community.

This proposed project also includes accommodation for vehicular access/egress, and underground parking, all in compliance with the Master Plan goal to provide more below grade vehicle parking at the main campus.

Project Schedule: Phase I completed; Phase II in DSA; Fall 2014 completion

Estimated Project Cost: \$94,027,100

Funding Sources: Measure S, U and State of California

Bundy West Building Classroom Completion

Project Description: Approximately 6,500 of unplanned space was left available when the West Building was completed at the Bundy Campus in 2005. With the expansion of the Workforce Development program along with the need for classroom swing space during construction at other sites, the vacant space will be converted to academic use.

Project Schedule: In design-development phase of planning

Estimated Project Cost: \$3,221,000 Funding Sources: Measure AA

Future Projects

Section III - Projects in Active Planning Phases

Media and Technology-Driven Programs Complex (Academy Campus)

Project Description: The college operates a variety of programs in the digital arts, media, communication, and broadcasting fields. These programs currently reside in 1950s era buildings that cannot support the modern infrastructure necessary for digital and online programs. A new Media and Technology complex is proposed to house these digital technology-intensive programs. The facilities will have the data, communications, electrical, and ventilation systems necessary to support these programs in the future. The proposed location is a campus site in the heart of Santa Monica's media and entertainment district where some of SMC's existing digital arts programs are housed. One phase of the project would renovate and add additional space to the existing building to house and expand SMC's Communication programs. An additional phase would relocate the College's radio station, which has outgrown its space, into a new building on the site. Moving KCRW, a nationally-recognized leader in new media and online delivery, to this site would provide a dynamic asset to SMC's current and future media and technology-driven instructional programs.

Project Schedule: Parking Structure, In DSA; Buildings: Completing Construction Drawings

Estimated Project Cost: \$61,480,824

Funding Sources: Measure AA, KCRW Foundation

Replacement Health, Fitness, Dance, and PE Building plus Central Plant (Main Campus)

Project Description: The systems of the existing building are in poor condition and the fire safety system needs upgrading. A new replacement building would also provide today's more specialized fitness and individual sports labs, as well as remedy an existing deficiency in support facilities for women and an existing deficiency in practice and demonstration rooms for dance.

Since this building is located in the center of campus it is an ideal location for the central cooling plant which is an energy efficiency project designed to generate chilled water for efficiently for air cooling in buildings throughout the main campus.

Project Schedule: In design-development phase of planning

Estimated Project Cost: \$40,200,333

Funding Sources: Measure AA, State Energy Incentives, Energy Cost Savings

Information Technology Relocation (Main Campus)

Project Description: The Information Technology department, located in Drescher Hall, supports the use of information systems on campus. The current server room can no longer support the power and air conditioning needs of the increasingly more powerful servers that are in use today. The plan is to move the department to a new building adjacent to the college's Media Center, which is located on the south end of the Library. Much of the campus technology infrastructure is already located in the Media Center and the department's work cooperatively on many projects.

The project will consist of a new 14,000 SF building and 11,000 SF remodeling of the existing Media Center. The space vacated in Drescher Hall will be converted to academic use as part of a future project.

Project Schedule: In design-development phase of planning

Estimated Project Cost: \$13,287,218

Funding Sources: Measure AA

East Wing Earthquake Renovation - Performing Arts Campus

Project Description: During the construction of other improvements recently at the Performing Arts Campus (formerly the Madison site) it was discovered by our engineers that earthquake renovations required after the 1933 Long Beach Earthquake were never performed. The cost of bring the building up to current codes was near the cost of a replacement building so the district planners have recommended a new more functional building that would replace the current multipurpose room and add a music classroom and offices for the Broad Stage.

Project Schedule: In construction drawings phase of design

Estimated Project Cost: \$12,292,000

Funding Sources: Measure AA

Energy Efficiency Projects

Project Description: This project provides for upgrades to existing and future District facilities, for energy efficiency, including the use of certain energy generation and cogeneration technologies, and to meet modern sustainability practice.

Project Schedule: Solar and Energy Efficiency Projects – In Planning

Estimated Project Cost: \$4,650,136

Funding Sources: Measure S, District Capital Funds, State Energy Incentives, Energy Cost Savings

Section IV - Future Projects

Projects with funding sources identified but not yet in active planning:

Malibu Site Acquisition and Facility

Project Description: In the 1970s and early 1980s, Santa Monica College offered about 70 general education classes and several non-credit classes in Malibu throughout a semester. Today, the program is limited to a few classes offered as part of the Emeritus College program for older adults. The program reduction was due to a loss of State funds following the passage of Proposition 13 and the inability to find sites to offer classes. There is currently the possibility of a State action that will provide annual operational funding up to \$1 million additional for educational centers such as the proposed Malibu facility, over and above the operational funding available from State apportionment available from FTE earned at the site.

The recommended site acquisition and facility will be a classroom facility to provide general education classes, Emeritus College classes, and special interest classes, along with a physical education component with field space that will be shared with the community. There are also site opportunities to promote interpretative programs in Natural History. The District will take an active role in being environmentally beneficial to the Malibu area.

Project Schedule: Property acquisition phase

Estimated Project Cost: \$31,069,031 Funding Sources: Measure S, AA

Early Childhood Development Lab & Replacement Childcare Center

Project Description: SMC currently offers childcare through a cooperative agreement arrangement with the Santa Monica-Malibu Unified School District and Easter Seals. Childcare has been offered at three sites: at the John Adams Middle School site, at the Olympic High School site, and at a leased facility from the Assistance League.

The approximately 3,000 square-foot Assistance League building was originally constructed in 1963, lacks fire sprinklers, and requires facility improvements. Additionally, the lease rental has been significantly increased. As a consequence, the District has vacated this site.

The District lacks a teaching laboratory facility in Early Childhood Education available at many other community colleges. This project provides for a replacement childcare center for College students and a new Early Childhood Development Lab to be operated in conjunction with the childcare facility. The District will seek public agency, institutional, and non-profit partnerships in order to reduce capital costs and to operate the facility in a cost-effective manner. The City of Santa Monica has indicated its willingness to be a partner in this project.

Project Schedule: Completing final arrangements for site and financing with City of SM

Estimated Project Cost: \$11,000,000+

Funding Sources: Measure S with City of Santa Monica

Replacement Math and Science Extension Building (Main Campus)

Project Description: The math department is currently operating in a temporary facility that is nearing the end of its life cycle. Additionally, new California regulations require an increase in minimum math competencies beginning in Fall 2009. The current facility lacks the infrastructure to support modern classroom technology. The Earth, Life, and Physical Sciences programs are operating in spaces that are too small and scattered around the campus. This inhibits the sharing of resources and incurs expensive replacement costs for laboratory teaching materials. There are insufficient science lab classrooms to offer needed course sections for the Allied Health and Nursing program.

New Career Opportunity and Career Advancement Instructional and Job-Training Building (Bundy Campus)

Project Description: SMC's workforce development program is now regarded as one of the most successful in California. A new facility would provide the program with modern classrooms that can be adapted to ongoing need, including the one-stop services often required in training and working with employers to hire employees new to the workforce. The facility would house training programs provided by college, city, county, and other agency providers. The new facility would also allow SMC to provide advanced instruction tailored to the needs of the Westside workforce, in partnership with other agencies. The facility is included in the Bundy Campus Master Plan.

Drescher Hall: Academic Facilities Modernization, Bookstore, Pico Promenade

Project Description: A current project includes the transformation of the Pico Boulevard side of the campus. One component of this project is a remodel of Drescher Hall, built in the 1960s for the teaching of vocational trades. The building lacks modern infrastructure and is not easily accessible on the first floor. The Photography Department is currently split between this building and the Business Building. This modernization project consolidates the photo program in one location in Drescher Hall and accommodates an expanded use of digital photo technologies. Also, ESL (English as a Second Language) is currently in temporary facilities located at the far edge of campus. This project will consolidate ESL in Drescher Hall and provide an opportunity for program modernizations and improvements. The modernization will also provide a fire system upgrade.

The college bookstore is currently operating in a building designed for the number of students attending the college in 1950. There have been only minor upgrades to the current facility. There is not enough room to accommodate the required number of textbooks and there is no room for general merchandise that is needed by students and specialty items such as computers and electronics.

This project would also make improvements to the college frontage on Pico including a transit plaza to serve the increasing number of students that take advantage of public transportation.


SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure U Project Schedule As of June 30, 2011

	Project Name	Completion	2010	2011	2012	2013	2014
٧	Purchase of BAE Airport Site	Completed					
В	Emeritus College Facility	Completed					
၁	Purchase of 1738 Pearl Street	Completed					
O	PE Temp. Bldg. Replacement	Completed					
Ш	Remodel Library Village for Math	Completed					
ш	SM Airport Campus Site Improvements	Completed					
Э	SM Airport Campus West Building	Completed					
I	Theater Arts Renovation	Completed					
-	Earthquake Rpl. Liberal Arts North	Completed					
ſ	Music Complex	Completed					
X	Earthquake Rpl. Liberal Arts South	Completed					
Γ	Shuttle Replacement Parking	Completed					
Σ	North Quad Plaza	Completed					
z	Letters & Sci Demo/Restore	Move to AA					
0	Student Services Building	October 2014					
Ь	Science Complex Addition	Move to AA					
Ø	Infrastructure & Safety	Completed					
Я	Restroom Improvements	Completed					
S	Master Planning	Completed					
Т	14th and Pico Project	On Hold					
	* SM Airport Campus also known as Bundy Site	Site	In Coi	In Construction			

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure U Bond Budget As of June 30, 2011

Budget Measure U Allocation Other Funding Of 6/30/11 Expenditures as of 6/30/11 Expenditures as consistent Expenditures as of 6/30/11 Measure U of 3/31/11 Measure U of 3/31/11 Measure U of 3/31/11 Measure U of 6/30/11 Measure U of 6/30/11 Measure U of 3/31/11 Measure Expenditures as Sub/31/11 Expenditures as Sub/31/11 Expenditures as Sub/31/11 Expenditures as Sub/31/11 Expenditures as Sub/31/11 Measure U of 3/31/11 Measure U of 3/31/11 Measure U of 3/31/11 Measure U of 3/31/11 Measur										
Purchase of BAE Airport Site Completed \$30,280,878 \$30,879 \$30,280,878		Project Name	Completion		Measure U Allocation			Measure U Expenditures of 3/31/11	Measure U Expenditures Last Period	Total Measure U Remaining
Emeritus College Facility Completed \$9,603,782 \$8,909,940 \$699,842 \$8,909,940 \$8,909,940 Purchase of 1738 Pearl Street Completed \$749,208 \$749,208 \$749,208 \$749,208 \$749,208 Purchase of 1738 Pearl Street Completed \$749,208 \$749,203 \$5,797,033 \$2,797,034 \$2,797,034 \$2,1470,264	⋖		Completed	\$30,280,878	\$30,280,878	0\$	\$30,280,878	\$30,280,878	0\$	0\$
Purchase of 1738 Pearl Street Completed \$749,208 \$749,203 \$749,208 \$749,208 \$749,208 \$749,203 \$749,033 \$749,034 \$749,034 \$749,034 \$749,034 \$740,034 <th< th=""><th>В</th><th></th><th>Completed</th><th>\$9,603,782</th><th>\$8,909,940</th><th>\$693,842</th><th>\$8,909,940</th><th></th><th>\$0</th><th>\$0</th></th<>	В		Completed	\$9,603,782	\$8,909,940	\$693,842	\$8,909,940		\$0	\$0
PE Temp. Bidg. Replacement Completed \$2,797,033 \$2,797,033 \$2,797,033 \$2,797,033 Remodel Library Village for Math Completed \$1,458,690 \$1,458,690 \$0 \$1,456,690 \$1,456,690 SM Airport Campus Site Improvements Completed \$1,470,264 \$4,170,264 \$6,170,264 \$4,170,264 \$1,456,690 SM Airport Campus West Building Completed \$19,709,741 \$19,709,741 \$10,0974 \$10,0974 \$10,009,741 \$10,009,	ပ		Completed	\$749,208	\$749,208	\$0	\$749,208	\$749,208	0\$	\$0
Remodel Library Village for Math Completed \$1,458,690 \$1,458,690 \$1,458,690 \$1,458,690 \$1,458,690 \$1,458,690 \$1,458,690 \$1,458,690 \$1,458,690 \$1,458,690 \$1,458,690 \$1,458,690 \$1,458,690 \$1,470,264 \$2,170,264 \$2,170,264 \$2,170,264 \$2,170,264 \$2,170,264 \$2,170,264 \$2,170,264 \$2,170,264 \$2,170,274 <th>Ω</th> <th></th> <th>Completed</th> <th>\$2,797,033</th> <th>\$2,797,033</th> <th>\$0</th> <th>\$2,797,033</th> <th>\$2,797,033</th> <th>\$0</th> <th>\$0</th>	Ω		Completed	\$2,797,033	\$2,797,033	\$0	\$2,797,033	\$2,797,033	\$0	\$0
SM Airport Campus Site Improvements Completed \$4,170,264 \$6,170,274 \$4,170,264<	Ш		Completed	\$1,458,690	\$1,458,690	0\$	\$1,458,690	\$1,458,690	0\$	0\$
SM Airport Campus West Building Completed \$19,709,741 \$19,709,741 \$19,709,741 \$19,709,741 \$19,709,741 \$19,709,741 \$19,709,741 \$19,709,741 \$19,709,741 \$19,709,741 \$19,709,741 \$19,709,741 \$19,709,741 \$19,709,741 \$19,709,741 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$19,490,949 \$10,	ш		Completed	\$4,170,264	\$4,170,264	0\$	\$4,170,264	\$4,170,264	\$0	0\$
Theater Arts Renovation Completed \$19,497,949 \$19,497,949 \$19,497,949 \$19,496,949 \$19,496,949 \$19,496,949 Earthquake Rpl. Liberal Arts North Completed \$12,507,725 \$6,154,973 \$7,633,209 \$7,633,209 \$7,633,209 Music Complex Completed \$4,623,547 \$2,005,434 \$2,005,116 \$2,004,434 Earthquake Rpl. Liberal Arts South Completed \$16,733,220 \$6,108,150 \$108,150 \$108,150 Shuttle Replacement Parking Completed \$11,388,463			Completed	\$19,709,741	\$19,709,741	0\$	\$19,709,741	\$19,709,741	0\$	0\$
Earthquake Rpl. Liberal Arts North Completed \$12,507,725 \$6,352,752 \$6,164,973 \$7,633,209 \$7,633,209 Music Complex Completed \$4,623,547 \$2,005,434 \$2,618,113 \$2,006,434 \$2,004,434 Earthquake Rpl. Liberal Arts South Completed \$16,733,220 \$6,108,150 \$6,108,150 \$6,108,150 Shuttle Replacement Parking Completed \$18,969,509 \$18,969,509 \$18,969,509 \$18,969,509 \$18,969,509 \$18,969,509 North Quad Plaza Completed \$11,388,463 <th>ェ</th> <td></td> <th>Completed</th> <td>\$19,497,949</td> <td>\$19,497,949</td> <td>0\$</td> <td>\$19,496,949</td> <td>\$19,496,949</td> <td>0\$</td> <td>\$1,000</td>	ェ		Completed	\$19,497,949	\$19,497,949	0\$	\$19,496,949	\$19,496,949	0\$	\$1,000
Music Complex Completed \$4,623,547 \$2,005,434 \$2,005,116 \$2,004,434 Earthquake Rpi. Liberal Arts South Completed \$16,733,220 \$6,108,150 \$6,108,150 \$6,108,150 \$6,108,150 Shuttle Replacement Parking Completed \$18,969,509 <th>_</th> <td>Earthquake Rpl. Liberal Arts North</td> <th>Completed</th> <td>\$12,507,725</td> <td>\$6,352,752</td> <td>\$6,154,973</td> <td>\$7,633,209</td> <td>\$7,633,209</td> <td>0\$</td> <td>-\$1,280,457</td>	_	Earthquake Rpl. Liberal Arts North	Completed	\$12,507,725	\$6,352,752	\$6,154,973	\$7,633,209	\$7,633,209	0\$	-\$1,280,457
Earthquake Rpl. Liberal Arts South Completed \$16,733,220 \$6,108,150<	7	Music Complex	Completed	\$4,623,547	\$2,005,434	\$2,618,113	\$2,005,116	\$2,004,434	\$682	\$318
Shuttle Replacement Parking Completed \$18,969,509 \$18,969,509 \$0 \$18,969,509 \$18,969,509 North Quad Plaza Completed \$11,388,463 \$1,388,463 \$1,388,463 \$11,388,463 <	ㅗ		Completed	\$16,733,220	\$6,108,150	\$10,625,070	\$6,108,150	\$6,108,150	0\$	0\$
North Quad Plaza Completed \$11,388,463 \$10,388,463 \$11,483 \$11,483 \$11,483 \$11,483 \$11,483,878 \$11,483,878 \$11,483,878 \$11,483,878 \$11,483,878 \$11,483,878 \$11,483,878 \$11,483,878 \$11,483,878 \$11,483,878 \$11,483,878 \$11,483,878 \$11,48	_	Shuttle Replacement Parking	Completed	\$18,969,509	\$18,969,509	\$0	\$18,969,509	\$18,969,509	\$0	\$0
Letters & Sci Demo/Restore Move to AA \$0 \$0 \$0 \$0 Student Services Building October 2014 \$53,521,913 \$20,816,196 \$32,708,239 \$2,082,330 \$2,081,098 Science Complex Addition Move to AA \$308,336 \$4,030,284 \$4,030,284 \$6 \$3,948,796 \$3,930,803 Infrastructure & Safety Completed \$417,501 \$17,501 \$17,501 \$17,501 \$17,501 Restroom Improvements Completed \$2,110,430 \$2,110,430 \$2,110,430 \$2,110,430 \$2,110,430 \$319,242 H4th and Pico Project On Hold \$319,242 \$142,443,878 \$142,443,878 \$142,443,878 \$142,443,878	Σ		Completed	\$11,388,463	\$11,388,463	0\$	\$11,388,463	\$11,388,463	0\$	0\$
Student Services Building October 2014 \$53,521,913 \$20,816,196 \$32,708,239 \$2,082,330 \$2,081,098 Science Complex Addition Move to AA \$308,336 \$308,342 \$308,342 \$308,342 \$308,342 \$308,342 \$3	z		Move to AA	\$0	\$0	\$0	\$0		0\$	\$0
Science Complex Addition Move to AA \$308,336 \$308,336 \$0 \$308,336 \$308,342 \$308,342 \$308,346 \$308,342<	0		October 2014	\$53,521,913	\$20,816,196	\$32,708,239	\$2,082,330		\$1,232	\$18,733,866
Infrastructure & Safety Completed \$4,030,284 \$4,030,284 \$4,030,284 \$5,948,796 \$3,948,796 \$3,930,803 Restroom Improvements Completed \$17,501 \$1	Д		Move to AA	\$308,336	\$308,336	\$0	\$308,336		\$0	\$0
Restroom Improvements Completed \$17,501 \$17,501 \$0 \$17,501 \$17,501 \$17,501 \$17,501 \$17,501 \$17,501 \$17,501 \$17,501 \$10,430 \$10,430 \$10,430 \$10,430 \$10,430 \$10,430 \$10,430 \$10,430 \$10,430 \$10,430 \$10,430 \$10,430 \$10,430 \$10,430 \$10,430 \$10,430 \$10,430 \$10,443 \$10,443,878	Ø		Completed	\$4,030,284	\$4,030,284	\$0	\$3,948,796	\$3,930,803	\$17,993	\$81,488
Master Planning Completed \$2,110,430 \$2,110,430 \$0 \$2,110,430<	~		Completed	\$17,501	\$17,501	\$0	\$17,501	\$17,501	\$0	\$0
14th and Pico Project On Hold \$319,242 \$319,242 \$0 \$142,463.785 \$142,463.785 \$142,463.785 \$142,443.878	S		Completed	\$2,110,430	\$2,110,430	\$0	\$2,110,430	\$2,110,430	\$0	\$0
\$212.800.237 \$160.000.000 \$52.800.237 \$142.463.785 \$142.443.878	—	14th and Pico Project	On Hold	\$319,242	\$319,242	\$0	\$319,242	\$319,242	\$0	\$0
		Project Totals		\$212,800,237	\$160,000,000	\$52,800,237	\$142,463,785	\$142,443,878	\$19,907	\$17,536,215

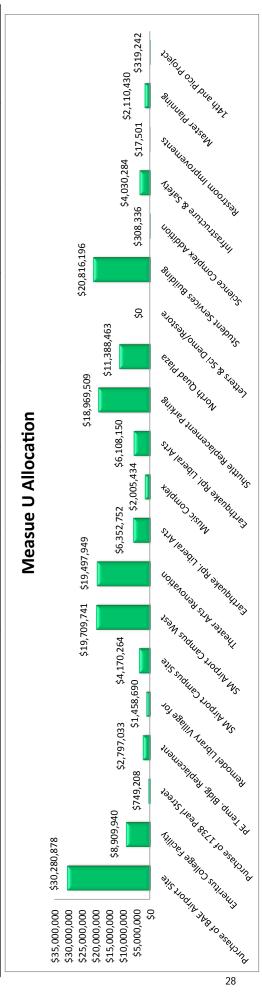

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals	otals
U7100010												
Purchase of BAE Airport Site (A)												
Site Acquisition		80	\$0	\$0	\$30,280,878	\$0	0 \$0		\$0 80		\$30,28	280,878
Total		80	\$0	\$0	\$30,280,878							\$30,280,878
Project Budget	\$30,280,878											
Less Other Funding	\$0											
Net	\$30,280,878											
Actual Measure U Expenditures	\$30,280,878											
Running Balance	\$0											
U7100028												
Emeritus College Facility (B)												
Site Acquisition		\$8,658,675	\$0	\$0	0\$	0\$	0\$				\$0 \$8,6	\$8,658,675
Legal		\$14,649	\$3,009	\$20,421	0\$							\$38,078
Architect		\$93,735	\$27,831		\$0	0\$	0\$		\$0		\$1	\$121,727
Engineering		\$18,400	\$0									18,400
Supply		\$	\$4,461	\$0			0\$ 0					\$4,461
Building & Additions		\$	\$17,496									21,496
Cap Equipment		0\$	\$49,406									49,406
Non-Cap Equipment		0\$	-\$2,197		-\$108							\$2,305
Total		\$8,785,459	\$100,007									09,940
Project Budget	\$9,603,782	Received										
Less Other Funding*	\$693,842	\$693,842		* Other Funding Source:	3 Source:							
Net	\$8,909,940			Emeritus College Foundation \$693,842 received	ge Foundation	\$693,842 rece	sived					
Actual Measure U Expenditures	\$8,909,940											
Running Balance	\$0											
U7100006												
1738 Pearl Street (C)												
Site Acquisition		0\$	\$704,534		0\$							\$704,534
Site Improvement		0\$	\$3,250	\$0	\$0	\$0	0\$		0\$		0\$	\$3,250
Building & Additions		0\$	\$41,424		0\$							41,424
Total		0\$	\$749,208		\$0							\$749,208
Project Budget	\$749,208											
Less Other Funding	\$0											
Net	\$749,208											
Actual Measure U Expenditures	\$749,208											
Running Balance	\$0											

1 of 9

7/7/11

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final 08/09 Final 09/10 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100026											
PE Temporary Building Replacement (D)											
Architect		\$148,055	\$42,372	\$6,220	\$485	0\$				0\$	\$1,761\$
Building & Additions		\$43,866	\$1,922,493	\$		\$0	0\$			\$0	\$
Inspection & Testing		\$6,455			0\$	0\$		0\$	0\$ (0	0\$	\$143,681
Project Management		\$4,800		\$5,225		\$0			0\$	\$0	,
Advertising and Moving Expenses		\$263	\$0		0\$	\$0			0\$	\$0	
Total		\$203,939	\$2,157,622	\$434,987	\$485	\$0		\$0	0\$ 0	\$0	\$2,797,033
Project Budget	\$2,797,033										
Less Other Funding	\$0										
Net	\$2,797,033										
Actual Measure U Expenditures	\$2,797,033										
Running Balance	\$0										
U7100310											
Remodel Library Village for Math (E)											
Moving Exp.		0\$	\$38,625	0\$	0\$	0\$		0\$	0\$ (0	0\$	\$38,625
Building & Additions		\$0	\$1,036,490	\$115,6	0\$	\$0		0\$	0\$	\$0	\$1,152,14;
Architect		\$104,992	\$27,141	\$1,3					0\$	\$0	
Engineering		0\$	\$2,658	0\$			\$0			0\$	
Inspection & Testing		0\$	\$27,083	\$25,175		0\$		0\$	0\$ (0	0\$	
Project Management		0\$		\$4,400	0\$	0\$		0\$	0\$ (0	0\$	820,93\$
Advertising and Moving Expenses		\$207	\$10,137	\$12,623		0\$				0\$.96'ZZ\$
Total		\$105,199	\$1,193,813	\$159,191	\$486	0\$		0\$	0\$ (0\$	\$1,458,690
Project Budget	\$1,458,690										
Less Other Funding	\$0										
Net	\$1,458,690										
Actual Measure U Expenditures	\$1,458,690										
Running Balance	\$0										

2 of 9

7/7/11

30

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final 0	08/09 Final 09/10 Final	09/10 Final	10/11	Comb	Combined Totals
700007												
0.7100027												
SM Airport Campus Site Improvements (F)		Ę	#06 004	#O4	95 070	6	Ç	É	É	•	Ç	000
Salphiles		000	\$20,234 \$25		0,000	\$54.074	000	00	000	9 6	000	\$33,00Z
MISC FEES		000	000		90	404,274	000	9	Q	9	2 5	904,739
Other Contract Services		\$3,860	\$11,508		\$1,501		0\$	<u>Q</u>	0,5	**	09	\$25,302
Site Improvement		\$0	\$0	\$15,182		\$7,237		80	80	9)	\$0	\$28,209
Building & Additions		0\$	\$1,495,697	\$		0\$		0\$	0\$	5)	0\$	\$3,171,309
Architect		\$104,934	\$200		0,	\$0		\$0	\$0	6)	00	\$149,004
Engineering		\$35,000	\$148,304	\$950		\$0		\$0	\$	67	\$0	\$194,294
Inspection & Testing		\$5,032	\$118,662			\$0		\$0	\$0	67	0,0	\$314,965
Project Management		\$750	\$155,798	\$38,425	\$1,365	\$220		\$0	\$	67	0\$	\$196,558
City Fees, Advertising and Security System		\$16,587	\$1,802		\$150	\$4,375	0\$	\$0	\$	67	0\$	\$23,241
Total		\$166,163	\$1,958,530	\$1,926,352	\$73,113	\$46,106		\$	\$	5	0,0	\$4,170,264
Project Budget	\$4,170,264											
Less Other Funding	\$0											
Net	\$4,170,264											
Actual Measure U Expenditures	\$4,170,264											
Running Balance	\$0											
U7110027												
SM Airport Campus West Building (G)												
Supply		\$0	\$0	\$17,650	\$28,017	\$0	\$0	\$0	\$0	6)	\$0	\$45,667
Other Contract Services		\$0	\$0	80	\$3,576	\$0	\$0	\$0	\$0	\$	\$0	\$3,576
Moving Expenses		80	\$0	\$180	\$15,824	\$0	0\$	\$0	\$0	\$	\$0	\$16,004
Building & Additions		80		\$15,037,532	\$1	\$46,946		80	\$0	\$	\$0	\$16,340,543
Architect		80	\$971,954	\$1,043,950		\$1,147		80	\$0	\$	30	\$2,066,830
Engineering		80	\$2,920	\$9,800	\$5,010	\$963		80	\$0	\$	\$0	\$18,693
Inspection & Testing		80	\$21,173			\$0	80	80	\$0	\$	30	\$157,539
Project Management		\$0	\$14,450			0\$	0\$	80	\$0	6)	09	\$342,121
Cap Equipment		\$0	\$49,795		\$4,792	\$0	0\$	80	\$0	6)	00	\$380,969
Non-Cap Equipment		\$0	\$0	\$280,558	0,	\$0	0\$	80	\$0	6)	\$0	\$337,798
Total		0\$	\$1,060,292	\$17,156,277	\$1,444,115	\$49,056	0\$	0\$	0\$	57	90	\$19,709,741
Project Budget	\$19,709,741											
Less Other Funding	\$0											
Net	\$19,709,741											
Actual Measure U Expenditures	\$19,709,741											
Running Balance	\$0											

3 of 9

7/7/11

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
112400035											
Theatre Arts Renovation (H)											
Supplies		\$0	\$8.904	-\$14	\$12.858	\$16,619	\$0	\$0	\$0	\$0	\$38,367
Legal		\$0		\$0	0\$	80	\$0	0\$	\$0	80	0\$
Moving Services		0\$	\$0	0\$	\$0	\$14,061	0\$	0\$	0\$	0\$	\$14,061
Other Contract Services		\$0		0\$	\$0	\$0	0\$	\$5,245	0\$	0\$	\$5,245
Rental / Lease		\$0	\$1,4	\$2,200	0\$	\$0	0\$	0\$	\$0	\$0	\$3,646
Building & Additions		\$528	8	\$4,540,487	\$10,897,603	\$56,122	\$25,220	0\$	0\$	\$0	\$16,846,590
Architect		\$289,913	100	\$423,416	\$82,639	\$0	0\$	0\$	0\$	0\$	\$1,165,181
Engineering		\$6,174	\$2,981		\$2,375		0\$	0\$	0\$	0\$	\$29,386
Inspection & Testing		\$150		\$353,890	\$297,675		0\$	0\$	0\$	0\$	\$667,616
Project Management		\$150			\$193,898	97	\$230	0\$	0\$	0\$	\$439,013
Cleaning, Storage and Installation		\$			\$2,548		0\$	0\$	0\$	0\$	\$5,627
Cap Equipment		\$0	\$3	0\$	\$6,458	\$59,689	0\$	0\$	0\$	0\$	\$97,785
Non-Cap Equipment		\$		0\$	\$36,749	\$145,294	0\$	0\$	0\$	0\$	\$184,432
Total		\$296,915	\$1.8	\$5,520,804	\$11,532,803	\$311,236	\$25,450	\$5,245	\$0	0\$	\$19,496,949
Project Budget	\$19,497,949										
Less Other Funding	\$0										
Net	\$19,497,949										
Actual Measure U Expenditures	\$19,496,949										
Running Balance	\$1,000										
U7100110											
Earthquake Rpl. Liberal Arts North (I)											
Supplies		\$0			\$0	\$1,408	0\$	\$75	0\$	0\$	\$1,483
Legal		\$0		0\$	\$0	\$887	0\$	0\$	0\$	0\$	\$887
Other Contract Services		\$0			\$0	\$75	0\$	0\$	0\$	0\$	\$75
Building & Additions		\$265		\$1,043,660	\$5,916,281	-\$973,001	\$321,345	\$14,898	0\$	-\$834,764	\$5,488,685
Architect		0\$		\$102,8	\$209,490	\$216,563	\$21,215	\$3,465	0\$	0\$	\$1,165,289
Engineering		\$3,248	\$4,295		\$250		\$250	0\$	0\$	0\$	\$8,043
Inspection & Testing		\$0	\$0	\$28,3	\$326,203		0\$	0\$	0\$	0\$	\$432,458
Project Management		\$0			\$128,937	\$124,222	\$255	\$1,155	\$286	0\$	\$314,475
Advertising and Fees		\$0			\$0		\$0	0\$	\$0	\$0	\$7,330
Cap-Equipment		\$0	\$0	0\$	\$0	\$25,356		0\$		0\$	\$37,935
Non-Cap Equipment		\$0		0\$	\$2,033	\$	\$4,093	0\$	0\$	0\$	\$176,550
Total		\$3,513	\$642,095	\$1,215,679	\$6,583,194	-\$356,123		\$19,592	\$286	-\$834,764	\$7,633,209
Project Budget	\$12,507,725	Received									
Less Other Funding*	\$6,154,973			* Other Funding Source:	Source:						
Net	\$6,352,752			City of Santa Monica \$4,039,753 received	onica \$4,039,7	53 received					
Actual Measure U Expenditures	\$7,633,209			FEMA \$2,115,2	20 commited, 3	FEMA \$2,115,220 commited, \$834,764 received	þ				
Running Balance	-\$1,280,457										

4 of 9

7/7/11

Authorition Continued Services State S	U7100013, U7100047 Music Complex (J)											
## State of California 94.458 (19.00) **State of California 94.458 (1	Music Complex (J)											
Second Heat												
Section Sect	Advertising		0\$	0\$	\$436	\$0	0\$				0\$	
Second Color Seco	Supplies		0\$	\$0	0\$	\$0	\$194				\$0	
Section Sect	Consultants		\$	\$0	0\$	\$0	\$0				\$0	
Secretary Secr	Other Contract Services		\$0	\$0	0\$	\$0	\$0				\$0	
Secretary Secr	Moving Services		\$0	\$0	0\$	\$0	\$0				\$0	
Second Heat	Building & Additions		\$0	\$0	\$356,464	,293,	-\$737,213				\$0	
Secretary Secr	Architect		0\$	\$187,922	\$22,500		\$38,448		\$14,		\$681	
Second Head	Engineering		0\$	0\$	0\$				\$21		0\$	
Substitution Subs	Inspection & Testing		0\$	0\$							0\$	
Second Holland Received Second Holland Holland Received Second Holland Hol	Project Management		0\$	\$170					\$1		0\$	
Section of the control of the cont	Cap Equipment		0\$	0\$		\$0	0\$				0\$	
St. Cont. St.	Non-Cap Equipment		0\$	0\$		\$0	\$29,852				0\$	
\$4,023,247 Received \$2,018,113 Received	Total		\$0	\$188,092		\$1,386,568	-\$585,566				\$681	
\$2.618.113 \$2.618.113	Project Budget	\$4,623,547										
\$\frac{\cau{1}{\cut{1}{	Less Other Funding*	\$2,618,113			* Other Funding	3 Source:						
\$2,005,116	Net	\$2,005,434			Prop T Refinan	ce \$2,618,113	received					
\$318 Sandari (K) Sandari	Actual Measure U Expenditures	\$2,005,116										
touth (K) 50 \$865 \$2,497 \$379 \$22,3811 \$75 \$0 50 50 50 50 50 50 50 50 50 50 50 50 50 50 \$0<	Running Balance	\$318										
Secondary Seco			•									
count (K) \$60 \$86.5 \$2.497 \$379 \$27.811 \$75 \$80 \$80 \$60	0/100111											
\$60 \$0 \$25,2497 \$379 \$22,811 \$75 \$80 \$80 \$60	Earthquake Kpl. Liberal Arts South (K)								ļ			
\$0 \$0 \$0 \$2,203 \$50 \$0 <t< td=""><td>Supply</td><td></td><td>\$0</td><td>80</td><td>\$855</td><td>\$2,497</td><td>\$379</td><td></td><td></td><td></td><td>0\$</td><td></td></t<>	Supply		\$0	80	\$855	\$2,497	\$379				0\$	
\$0 \$0 \$0 \$4,053 \$0 <th< td=""><td>Legal</td><td></td><td>\$0</td><td>\$0</td><td>\$0</td><td>\$0</td><td>\$0</td><td></td><td></td><td></td><td>\$0</td><td></td></th<>	Legal		\$0	\$0	\$0	\$0	\$0				\$0	
\$0 \$0 \$17,265 \$41,435 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$17,265 \$41,435 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0.154 \$202 \$202 \$0 <	Moving Services		\$0	\$0	\$0	\$0	\$0				\$0	
\$6.154 \$202 \$0 \$0 \$0.50 \$202 \$0	Consultants		\$0	\$0	\$0	\$17,265	\$41,435				\$0	97
\$0 \$0 \$26,302 \$3,091,306 \$5,706,802 \$4,642,459 \$50 \$51,516 \$50 \$56,324 \$50,984 \$5,549 \$50 \$5 \$0 \$0 \$31,25 \$156 \$163,506 \$183,877 \$39,984 \$2,549 \$50 \$50 \$0 \$0 \$0 \$126 \$156 \$50 <t< td=""><td>Other Contract Services</td><td></td><td>0\$</td><td>0\$</td><td>\$6,154</td><td>\$202</td><td>0\$</td><td></td><td></td><td></td><td>0\$</td><td></td></t<>	Other Contract Services		0\$	0\$	\$6,154	\$202	0\$				0\$	
\$6 \$10 \$886,555 \$503,297 \$163,506 \$183,877 \$39,984 \$2,549 \$0 \$6 \$10 \$6 \$10 <td>Building & Additions</td> <td></td> <td>0\$</td> <td>0\$</td> <td>\$26,302</td> <td></td> <td>\$5,706,802</td> <td></td> <td></td> <td>\$91</td> <td>0\$</td> <td></td>	Building & Additions		0\$	0\$	\$26,302		\$5,706,802			\$91	0\$	
\$6 \$0 \$3,125 \$150 \$53,344 \$500 \$0	Architect		0\$	\$0	\$836,555	-\$50	\$163,506	\$18	\$39,	\$2,	\$0	
\$6 \$0 \$0 \$179,798 \$296,015 \$68,273 \$0 \$0 \$0 \$17,22 \$1,278 \$0 \$0 \$0 \$0 \$1,278 \$0	Engineering		0\$	\$0	\$3,125		\$5,344				\$0	
\$6 \$0 \$0 \$43,989 \$262,598 \$52,690 \$1,772 \$1,278 \$0 \$1 \$0 \$0 \$0 \$0 \$1,772 \$1,278 \$0 \$0 \$1 \$1 \$1 \$1 \$2	Inspection & Testing		80	\$0	0\$	٥,					\$0	
\$6 \$0<	Project Management		0\$	\$0	0\$	\$43,989			\$1	\$1,	\$0	
\$16,733,220 \$0 \$0 \$0 \$6,534,806 \$4,261,656 \$34,757 \$95,342 \$0 \$6 \$16,733,220 Received * Other Funding Source: * Other Funding Source: * Other Funding Source: S6,108,150 City of Santa Monica \$6,167,070 received \$6,108,150 \$0 State of California \$4,458,000 received State of California \$4,458,000 received State of California \$4,458,000 received	Cap-Equipment		80	\$0	0\$	\$0					\$0	
\$16,733,220 Received * Other Funding Source: * Other Funding \$6,100 received * Other Funding \$6,100 received * Other Funding \$6,100 received \$6,108,150 \$ State of California \$4,458,000 received \$ Source: * Other Funding \$10,000 received * Other Funding \$2,100 received <th< td=""><td>Non-Cap Equipment</td><td></td><td>0\$</td><td>\$0</td><td>0\$</td><td>0\$</td><td></td><td></td><td></td><td></td><td>\$0</td><td></td></th<>	Non-Cap Equipment		0\$	\$0	0\$	0\$					\$0	
\$16,733,220 Received * Other Funding Source: \$10,625,070 \$10,625,070 \$10,625,070 \$6,108,150 City of Santa Monica \$6,167,070 received \$6,108,150 State of California \$4,458,000 received	Total		0\$	0\$	\$872,991	\$2,831,909	\$6,534,806			\$6\$	0\$	
\$10,625,070 \$6,108,150 \$6,108,150 \$6,108,150 \$0	Project Budget	\$16,733,220	Received									
\$6,108,150 \$6,108,150 \$0	Less Other Funding*	\$10,625,070	\$10,625,070		* Other Funding	g Source:						
\$6,108,150 \$0	Net	\$6,108,150			City of Santa N	lonica \$6,167,0	70 received					
	Actual Measure U Expenditures	\$6,108,150			State of Califor	nia \$4,458,000	received					
	Running Balance	\$0										

5 of 9

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final 08/09 Final 09/10 Final	08/09 Final	09/10 Final	10/11	Combined Totals
•											
U7100221											
Shuttle Replacement Parking (L)											
Supplies		\$0	\$0	\$0	0\$	0\$	\$1,347	\$0	\$0	\$0	\$1,347
Legal		\$0	\$0	\$0	\$8,462	\$35,103	\$0	\$0	\$0	\$0	\$43,565
Site Acquisition		\$0	\$0	\$0	0\$	\$16,903,087	\$0	\$0	\$0	\$0	\$16,903,087
Site Improvement		\$0	\$0	\$0	0\$	\$3,027	\$0	\$0	\$0	\$0	\$3,027
Building & Additions		\$0	\$0	\$0	0\$	\$484,000	\$1,252,224	\$2,353	\$0	\$0	\$1,738,577
Architect		\$0	\$0	\$0	0\$	\$51,569	\$7,208	\$0	\$0	\$0	\$58,777
Inspection & Testing		\$0	\$0	\$0	0\$	\$139,822	\$41,250	\$0	\$0	\$0	\$181,072
Project Management		\$0	\$0	\$0	0\$	\$7,631	\$32,425	\$0	\$0	\$0	\$40,056
Total		0\$	0\$	0\$	\$8,462	\$17,624,240	\$1,334,455	\$2,353	0\$	0\$	\$18,969,509
Project Budget	\$18,969,509										
Less Other Funding	\$0										
Net	\$18,969,509										
Actual Measure U Expenditures	\$18,969,509										
Running Balance	\$0										

U7100321											
North Quad Plaza (M)											
Legal		\$0	0\$	0\$	\$0	\$0	\$3,825	\$5,604	\$0	0\$	\$9,429
Building & Additions		\$0	0\$	0\$	\$0	-\$443	\$6,130,081	\$3,634,487	\$0	0\$	\$9,764,125
Architect		\$0	\$231,055	\$8,444	\$140,048	\$435,618	\$171,225	\$68,633	\$2,901	\$10,483	\$1,068,407
Engineering		\$0	0\$	0\$	\$0	\$0	\$0	\$0	\$0	0\$	\$0
Inspection & Testing		0\$	0\$	0\$	\$0	\$0	\$186,220	\$107,477	\$328	0\$	\$294,025
Project Management		\$0	0\$	\$760	\$210	\$2,200	\$135,601	\$55,782	\$606	0\$	\$195,158
Printing		0\$	\$1,900	0\$	\$0	\$0	\$0	80	0\$	0\$	\$1,900
Cap Equipment		0\$	0\$	0\$	\$0	\$0	\$0	\$55,420	0\$	0\$	\$55,420
Total		0\$	\$232,955	\$9,204	\$140,258	\$437,375	\$6,626,952	\$6,626,952 \$3,927,402	\$3,834	\$10,483	\$11,388,463
Project Budget	\$11,388,463										
Less Other Funding	\$0										
Net	\$11,388,463										
Actual Measure U Expenditures	\$11,388,463										
Running Balance	\$0										

6 of 9

7/7/11

Projects	Budget	02/03 Final 03/04	03/04 Final	04/05 Final	05/06 Final	Final 04/05 Final 05/06 Final 06/07 Final	07/08 Final 08/09 Final 09/10 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100500, U7126450, U7100334, U7100142											
Student Services Building (O)											
Supplies		\$2,014	\$0	0\$	\$0	\$0	\$0	\$718	\$0	\$0	\$2,732
PC Upgrades		0\$	\$765	0\$	\$0	\$0	\$0	0\$	\$0	\$0	\$765
Consultants		0\$	\$0	0\$	\$0	\$9,334	\$55,693	0\$	\$0	\$0	\$65,027
Legal		0\$	\$0	0\$	\$0	\$38	\$2,775	\$31,776	\$0	\$0	\$34,588
Other Contract Services		\$210	\$0	0\$	\$0	\$0	\$17,561	\$17,495	\$18,817	-\$70	\$54,014
Moving		\$7,571	\$0	0\$	\$0	\$0	\$0	\$616	\$0	\$0	\$8,187
Building & Additions		\$359,141	\$2,441	0\$	\$0	\$0	\$0	0\$	\$0	\$0	\$361,582
Architect		\$31,782	\$0	\$235,230	\$0	\$43,992	0\$	\$690,099	\$208,521	\$38,643	\$1,248,268
Engineering		\$1,838	\$0	0\$	\$0	\$0	\$0	\$6,205	\$27,363	\$3,171	\$38,576
Inspection & Testing		0\$	\$0	0\$	\$0	0\$	\$25,670	\$34,687	0\$	\$0	\$60,358
Project Management		\$4,650	\$0	\$2,470	\$0	\$1,100	0\$	\$124,148	0\$	\$0	\$132,368
Cap Equipment		\$29,063	\$0	0\$	\$0	0\$	\$8,745	950'8\$	0\$	\$0	\$75,864
Total		\$466,268	\$3,207	\$237,700	0\$	\$54,464	\$110,445	\$913,802	\$254,701	\$41,744	\$2,082,330
Project Budget	\$53,521,913	Received		* Other Funding Source:	g Source:						
Less Other Funding*	\$32,705,717	\$1,321,000		State of Califor	nia \$16,803,00	State of California \$16,803,000 allocated, \$1,321,000 received	321,000 receive	Ø			
Net	\$20,816,196			District Capital	District Capital Funds \$10,208,069 commited	,069 commited					
Actual Measure U Expenditures	\$2,082,330			Measure U Inte	Measure U Interest \$5,694,648 allocated	3 allocated					
Running Balance	\$18,733,866										



Project Discription:


departments and college administration in a single complex at the front of the campus Consolidates various student services

Facility Size: 83,634 sq/ft & 500 cars underground parking structure

Status: In plan check with DSA

Architect: Steinberg Architects

Contractor:

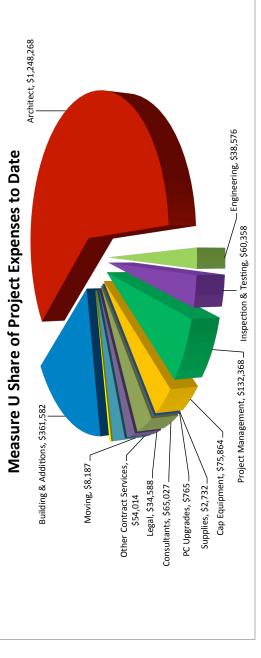

7 of 9

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100090											
Science Complex Additional (P)											
Architect		0\$	0\$	0\$	0\$	\$246,425	\$61,911	0\$	0\$	0\$	\$308,336
Total		0\$	0\$	0\$	0\$	\$246,425	\$61,911	0\$		0\$	\$308,336
Project Budget	\$308,336										
Less Other Funding	\$0										
Net	\$308,336										
Actual Measure U Expenditures	\$308,336										
Running Balance	\$0										
U6780000, U7100022, U7100331, U7100550,											
U7100005, U7100030, U7100031, U7100029,											
U7100003, U7100008, U7100332, U7100072,											
U/100042, U/100056, U/100039											
Infrastructure & Safety (Q)											
Supplies		0\$	0\$	\$254	0\$	0\$	\$0	\$1,700	\$1,393	0\$	\$3,347
Consultants		\$0	0\$	\$0	\$0	\$0	\$0	\$16,734	0\$	\$0	\$16,734
Maintenance Agreement		\$0	0\$	\$0	\$0	\$0	\$0			\$14,673	\$14,673
Legal		\$0	0\$	\$0	\$0	\$0	\$3,527	\$3,294		\$0	\$6,821
Other Contract Services		\$0	0\$	\$0	\$0	\$0	\$7,825		\$203,3	\$3,320	\$295,973
Building & Additions		\$681,900	\$195,175	\$20,600	\$0	\$200,620	\$733			\$0	\$1,099,028
Architect		\$69,081	\$42,108	\$0	\$155,321	\$448,507	\$91,127	\$4,227	0\$	\$0	\$810,370
Engineering		\$8,050	0\$	\$0	\$6,750	\$12,0	\$18,429			\$0	\$47,589
Inspection & Testing		\$2,241		\$0	\$0		\$5,807			\$0	\$12,298
Project Management		\$0	\$2,805	\$0	0\$	\$3,520	\$1,840	82\$	\$196	\$0	\$8,399
Cap Equipment		\$0	0\$	\$343,861	0\$		\$0	\$895,171	\$349,531	\$40,002	\$1,628,565
Non-Cap Equipment		\$0	0\$	\$0	0\$	0\$	\$0	0\$	\$4,2	\$0	\$4,216
Advertising		80	\$785	80	\$0		\$0			\$0	\$785
Total		\$761,272	\$245,122	\$364,715	\$162,071	\$664,647	\$129,287	\$1,004,968	\$558,718	\$57,995	\$3,948,796
Project Budget	\$4,030,284										
Less Other Funding	\$0										
Net	\$4,030,284										
Actual Measure U Expenditures	\$3,948,796										
Running Balance	\$81,488										

8 of 9

7/7/11

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
117100007									-		
Restroom Improvement (R)											
Supplies		\$0	\$564		\$1,075			\$0	\$0	\$0	\$1,639
Other Contract Services		\$0	\$0	\$0	\$3,803	\$0	\$0	\$0	\$0	\$0	
Building & Additions		\$0	\$1,305		\$7,891			\$0	\$0	\$0	
Inspection & Testing		\$0	\$2,043		\$820			\$0	\$0	\$0	
Total		\$0	\$3,912		\$13,589			\$0	\$0	\$0	
Project Budget	\$17,501										
Less Other Funding	\$0										
Net	\$17,501										
Actual Measure U Expenditures	\$17,501										
Running Balance	\$0										
U7100004, U7110020											
Master Planning (S)											
Consultants		\$9,000	\$26,516	\$158,449			\$17,998	\$363,342	0\$	0\$	\$
Architect		0\$	\$17,617	\$126,433	\$10	\$126,7	\$346,827	\$276,985	0\$	0\$	\$998,647
Rental / Lease		\$0	\$0				\$0	\$0	\$0	\$	
Postage		\$0	\$0			\$0	\$0	0\$	\$0	\$	
Reimbursement to SMC		\$0	\$0				\$0	0\$	\$0	\$	
Project Management		\$0	\$0	0\$	\$0		\$0	\$113	\$0	\$0	
Total		\$9,000	\$44,133	\$321,335	\$478,593	\$252,105	\$364,825	\$640,439	\$0	\$	\$2,110,430
Project Budget	\$2,110,430										
Less Other Funding	0\$										
Net	\$2,110,430										
Actual Measure U Expenditures	\$2,110,430										
Running Balance	\$0										
U7100024											
14th and Pico Project (T)											
Consultants		\$0	\$888		\$0		\$0	\$0	\$0	\$0	
Architect		\$258,601	\$47,343	80	\$0	\$0		\$0	\$0	\$0	\$
Inspection & Testing		\$12,070	\$0		0\$			0\$	\$0	0\$	\$12,070
Project Management		0\$	\$340		0\$			0\$	\$0	0\$	
Total		\$270,671	\$48,571		0\$			0\$	0\$	0\$	\$319,242
Project Budget	\$319,242										
Less Other Funding	\$0										
Net	\$319,242										
Actual Measure U Expenditures	\$319,242										
Running Balance	\$0										
Grand Total		\$11,068,400	\$10,432,055	28,685,697	\$54,940,416	\$25,278,771	\$5,283,853	\$6,585,573	\$912,880	-\$723,860	\$142,463,786

Note: Project N had no expenses

9 of 9

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure S Project Schedule As of June 30, 2011

က


Project Name	Completion	2010	2011	2012	2013	2014
Athletic Fields Phase I, Corsair Field	Completed					
Athletic Fields Phase I, John Adams	Completed					
Performing Arts Center	Completed					
Career Opportunity Center	Move to AA					
Replacement Health/PE/Fitness Building	September 2014					
Early Childhood Development/Childcare	In Planning					
Malibu Site Acquisition and Facility	Not Scheduled					
Energy Efficiency Projects	On-Going					
Satellite Campus Parking Facilities and Roadway Improvements	Completed					
Parking Garage, Grounds and Equipment - Student Services	October 2014					
Pico Promenade Improvements	Completed					
Master Planning	On-Going					
Other Bond Related Expenses	On-Going					
Adv. Architecture Related Exp for AA	Completed					
Real Property Acquisition	On-Going					
Signage Safety/Information	On-Going					
		In Planning		In Construction	nction	

တ


∞

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure S Bond Budget As of June 30, 2011

	Project Name	Completion	Project Budget	Measure S Allocation	Other Funding	Measure S Expenditures as of 6/30/11	Measure S Expenditures as of 3/31/11	Measure S Expenditures Last Period	Total Measure S Remaining
1	1 Athletic Fields Phase I, Corsair Field	Completed	\$4,440,768	\$4,373,238	\$67,530	\$4,372,535	\$4,372,535	0\$	\$203
1A	1A Athletic Fields Phase I, John Adams	Completed	\$2,970,807	\$2,970,807	0\$	\$2,969,807	\$2,969,807	0\$	\$1,000
2	Performing Arts Complex	Completed	\$40,603,541	\$37,610,965	\$2,992,576	\$37,610,571	\$37,608,541	\$2,030	\$394
3	Career Opportunity Center	Move to AA	0\$	0\$	0\$	0\$	0\$	0\$	0\$
4	Replacement Health/PE/Fitness Building	September 2014	\$40,200,333	\$4,816,093	\$35,384,240	\$772,976	\$772,976	0\$	\$4,043,117
2	Early Childhood Development/Childcare	In Planning	\$11,318,000	\$7,000,000	\$4,318,000	\$10,446	\$10,446	\$0	\$6,989,554
9	Malibu Site Acquisition and Facility	Not Scheduled	\$31,069,031	\$25,000,000	\$6,069,031	\$5,233,682	\$5,230,992	\$2,690	\$19,766,318
7	7 Energy Efficiency Projects	On-Going	\$1,293,570	\$1,076,248	\$217,322	\$293,361	\$293,361	\$0	\$782,887
8	Satellite Campus Parking Facilities and Roadway Improvements	Completed	\$4,875,000	\$4,875,000	\$0	\$3,820,983	\$3,820,689	\$294	\$1,054,017
6	Parking Garage, Grounds and Equipment - Student Services	October 2014	\$53,143,653	\$52,690,653	\$453,000	\$14,668,516	\$14,598,721	\$69,795	\$38,022,137
10	10 Pico Promenade Improvements	Completed	\$1,018,009	\$1,018,009	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	11 Master Planning	On-Going	\$750,000	\$750,000	0\$	\$708,583	\$708,583	0\$	\$41,417
12	12 Other Bond Related Expenses	On-Going	\$662,764	\$662,764	\$0	\$114,917	\$97,403	\$17,514	\$547,847
13	13 Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	0\$	\$0	\$0	\$0
14	14 Real Property Acquisition	On-Going	\$50,000	\$50,000	\$0	\$45,597	\$45,597	\$0	\$4,403
15	15 Signage Safety/Information	On-Going	\$606,223	\$606,223	\$0	\$236,289	\$222,732	\$13,557	\$369,934
	Project Totals		\$193,001,699	\$143,500,000	\$49,501,699	\$71,876,272	\$71,770,392	\$105,880	\$71,623,728

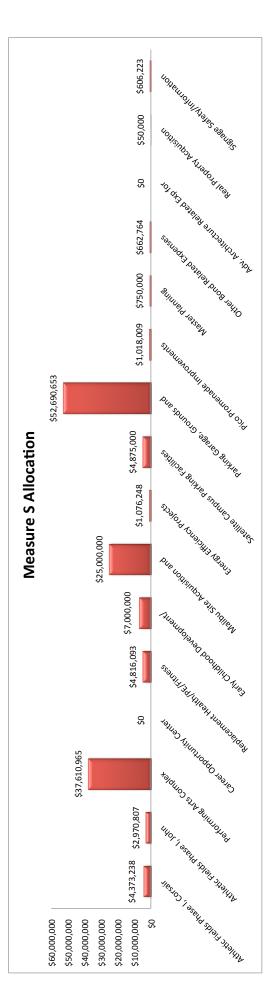

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100019									
Athletic Field Phase I, Corsair Field (1)									
Legal		\$0	0\$	0\$	\$301	\$175	0\$	0\$	\$476
Building & Additions		\$0	\$0	\$0	\$300,380	\$2,579,095	\$0	0\$	\$2,879,475
Architect		\$27,332	\$43,815	\$197,557	\$252,736	\$279,173	\$26,563	0\$	\$827,176
Inspection & Testing		\$0	\$0	0\$	\$23,411	\$57,585	\$640	\$296	\$81,932
Project Management		0\$	\$0	0\$	\$9,871	\$42,374	\$265	0\$	\$52,810
Cap Equipment		0\$	0\$	0\$	0\$	\$483,017	\$35,271	0\$	\$518,288
Non-Cap Equipment		0\$	0\$	0\$	0\$	\$2,066	\$10,312	0\$	\$12,378
Total		\$27,332	\$43,815	\$197,557	\$586,699	\$3,443,485	\$73,350	\$296	\$4,372,535
Project Budget	\$4,440,768	Received							
Less Other Funding*	\$67,530	\$67,530							
Net	\$4,373,238		* Other Funding Source:	g Source:					
Actual Measure S Expenditures	\$4,372,535		Metropolitan W	Metropolitan Water District \$67,530 received	7,530 received				
Running Balance	\$703								

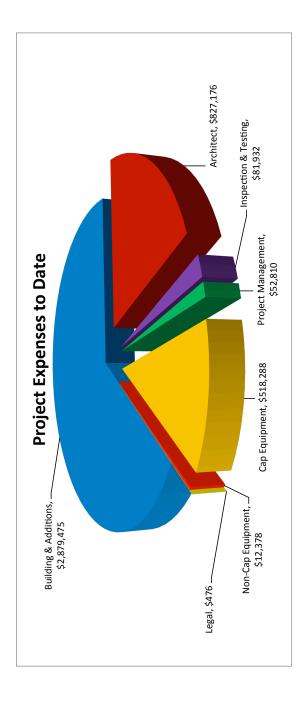


Athletic Field Phase I, Corsair Field Project Description: Renovation of the Corsair Field, stadium lighting and sound system

Status: Completed, 2009

Architect: CO Architects

Contractor: Byrom Davey, Inc.

Projects	Budget	04/05 Final	05/06 Final	04/05 Final 05/06 Final 06/07 Final 07/08 Final 08/09 Final 09/10 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100038									
Athletic Field Phase I, John Adams (1A)									
Legal		0\$	\$0	0\$	\$75	\$0	0\$	\$0	\$75
Building & Additions		0\$	0\$	\$0	\$16,556	\$1,395,261	0\$	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	0\$	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	0\$	\$49,984	0\$	\$0	\$56,066
Project Management		0\$	0\$	0\$	\$10,921	\$45,170	\$38	0\$	\$56,128
Cap Equipment		0\$	0\$	0\$	0\$	\$1,290,672	0\$	0\$	\$1,290,672
Non-Cap Equipment		\$0	\$0	0\$	0\$	\$11,334	0\$	\$0	\$11,334
Total		\$0	\$8,681	\$97,148	\$39,701	\$2,824,239	\$38	\$0	\$2,969,807
Project Budget	\$2,970,807								
Less Other Funding	\$0								
Net	\$2,970,807								
Actual Measure S Expenditures	\$2,969,807								
Running Balance	\$1,000								

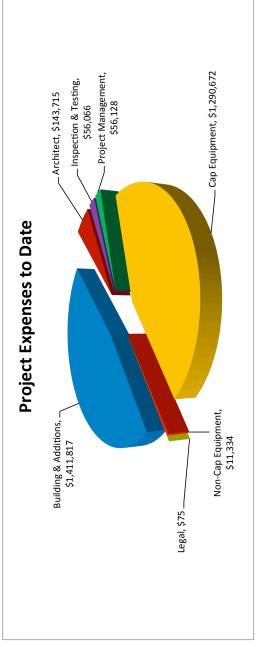

Architect: Caldwell Architects

Status: Completed, 2008

Contractor: Byrom Davey, Inc.


7/7/11

2 of 9

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE S EXPENDITURES

FUND 42.3 As of June 30, 2011

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100012									
Performing Arts Center (2)									
Consultants		0\$	\$0	0\$	\$121,790	\$76,639	\$0	0\$	\$198,429
Other Contract Services		0\$	\$0	\$4,269	\$0	\$22,729	\$22	\$68	\$27,088
Supplies		0\$	\$0	0\$	\$14,565	\$5,810	\$0	0\$	\$20,375
Legal		0\$	\$0	\$34,329	\$275,667	\$492,731	\$15,629	0\$	\$818,356
Advertising		0\$	0\$	0\$	\$320	\$0	\$0	0\$	\$320
Building & Additions		\$7,784,151	\$10,292,986	\$8,930,813	\$2,991,903	\$1,629,990	\$50,000	0\$	\$31,679,843
Architect		0\$	\$811,312	\$182,457	\$412,309	\$121,588	\$108	\$1,962	\$1,529,736
Engineering		0\$	\$3,600	\$5,250	\$1,500	\$9,650	\$0	0\$	\$20,000
Inspection & Testing		\$104,308	\$722,685	\$411,193	\$210,381	\$22,256	\$0	0\$	\$1,470,823
Project Management		\$31,984	\$155,732	\$248,876	\$263,690	\$47,915	\$3,244	0\$	\$751,441
Cap Equipment		0\$	\$0	\$130,218	\$292,262	\$342,693	\$0	\$0	\$765,476
Non-Cap Equipment		0\$	\$0	\$15,124	\$93,106	\$220,455	\$0	\$0	\$328,685
Total		\$7,920,443	\$11,986,315	\$9,962,528	\$4,677,797	\$2,992,455	\$69,003	\$2,030	\$37,610,571
Project Budget	\$40,603,541	Received							
Less Other Funding*	\$2,992,576	\$2,992,576	*	Other Funding Source:	g Source:				
Net	\$37,610,965		_	Madison Proje	Madison Project Foundation \$2,992,576 received	2,992,576 rece	ived		
Actual Measure S Expenditures	\$37,610,571								
Running Balance	\$394								

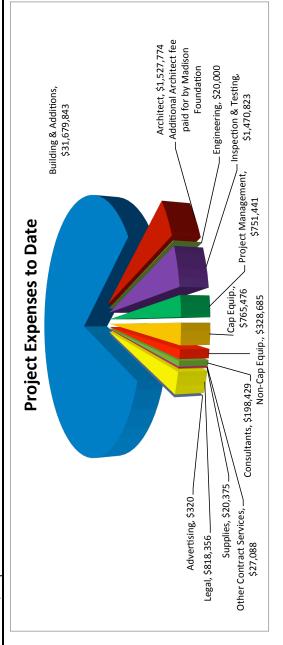

Performing Arts Center

Project Description: Construction of a state-of-the-art 499 seat performing arts theater

Status: Completed, 2008

Architect: Renzo Zecchetto

Contractor: FTR International

3 of 9

State Stat	Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
State Stat	S7100033, S7100144									
Second Color Seco	Replacement Health/PE/Fitness Building (4)									
Increese S. 16.34 S.25.94 S.0 S.0 S.14.31 S.75 S.0 Institutese S. 16.34 S.25.94 S.0 S.0 S.14.31 S.0 Institutese S. 16.34 S.25.94 S.0 S.0 S.0 S.0 S.0 Institutese S. 16.34 S.3.94 S.3.94 S.0 S.0 S.0 S.0 S.0 S.0 Institutese S. 16.34 S.3.94 S.3.94 S.0 S.0 S.0 S.0 S.0 S.0 Institutese S. 16.34 S.3.94 S.3.94 S.0 S.0 S.0 S.0 S.0 S.0 S.0 Institutese S. 16.34 S. 16.34 S. 16.34 S. 16.34 S. 16.34 S. 16.34 Institute and Facilities (6)	Supplies		\$0	\$0	\$0				\$0	\$163
State Stat	Legal		\$0		\$0				\$0	\$1,488
1972 1972	Other Contract Services		\$1,634		\$0		\$2		\$0	\$27,985
18 18 18 18 18 18 18 18	Repair Facility		\$0	\$4,861	\$0				\$0	\$4,86
1972 1972	Supplies		\$4,809		0\$				0\$	\$5,09
Page	Building & Additions		0\$		0\$			\$526,552	0\$	\$638,962
Page	Architect		\$0		0\$					\$41,04
Section Sect	Inspection & Testing		\$0		0\$					\$20,88
Section	Project Management		\$0		0\$					\$32,49
SAG 364 240 SAG 363 Set 240 Set 16 000	Total		\$6,443		0\$					\$772,97
Expenditures \$58,384,240 Paresure AA \$53,384,240 Paresure AB \$54,316,000 Paresure AB \$54,316,000 Paresure AB \$6,189 Paresure AB \$6,	Project Budget	\$40,200,333								
Expenditures \$4,310.093 Measure AA \$36,384,240 allocated \$4,043,117 \$4,043,117 \$1,029.009 \$1,000.000 \$1,00	Less Other Funding*	\$35,384,240			* Other Fundir	ng Source:				
Sacrotation	Net	\$4,816,093			Measure AA \$	35,384,240 allo	cated			
ST ST ST ST ST ST ST ST	Actual Measure 5 Expenditures	\$717,970								
Development/Childcare (5) SO	National Dataset	,OtO,t								
Percelopment/Childcare (5) \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	S7100045									
STATION STATIAN STATION STATIAN STATION STATIAN STATION STATION STATION STATION STATION STATIAN STATION STAT	Early Childhood Development/Childcare (5)									
ST1.318 000 Seceroted Secretored Sec	Consultants		\$0	\$0	\$				0\$	\$9,20
ng* \$0 \$0 \$9,200 \$0 \$1,246 <t< td=""><td>Project Management</td><td></td><td>\$0</td><td>0\$</td><td>0\$</td><td></td><td></td><td></td><td>\$1,246</td><td>\$1,24</td></t<>	Project Management		\$0	0\$	0\$				\$1,246	\$1,24
St. 1.318, 000 Scelived	Total		\$0	0\$	0\$				\$1,246	\$10,446
Sci 989,554 Septemble Se	Project Budget	\$11,318,000	Received							
ST,000,000 ST,000,000 ST,000,000 ST,000,000 ST,000,000 ST,000,000 ST,000,000 ST,0046 ST,0446 ST,	Less Other Funding*	\$4,318,000	\$0		* Other Fundir	ng Source:				
Expenditures \$6,989,564	Net	\$7,000,000			City of Santa I	Monica \$4,318	000 commited			
1015 \$6,989,554 \$6,989,554 \$6,989,554 \$6,989,554 \$6,989,564 \$6,989,564 \$6,989,564 \$6,889,569 \$6,889,569 <td>Actual Measure S Expenditures</td> <td>\$10,446</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>	Actual Measure S Expenditures	\$10,446								
nisition and Facilities (6) S0 \$0 <t< td=""><td>Running Balance</td><td>\$6,989,554</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></t<>	Running Balance	\$6,989,554								
no.15stition and Facilities (6) \$0 \$0 \$0 \$30,000 \$0	#70007#G ##0007#G									
Instituon and ractifies (b) \$0 <t< td=""><td>S/1000//, S/100015</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></t<>	S/1000//, S/100015									
ns	Mailibu Site Acquisition and Facilities (b)		\$0		8			U #	\$	00 08\$
ns \$0<	Legal		\$0	2227	11	86.1			0\$	\$51.17
ng \$0<	Building & Additions		80		٠١				80	9
ng \$4,388 \$3,750 \$141,462 \$0 \$0 \$0 \$0 \$1 \$0 \$220 \$0 \$0 \$2,690 \$0 \$2,690 \$0 \$2,690 \$0 \$2,690 \$0 \$2,690 \$0 \$2,690 \$0 \$2,690 \$0 \$2,690 \$0 \$2,690 \$0 \$2,690<	Architect		\$0		0\$				\$	0\$
ent \$0 \$0 \$220 \$0 \$0 \$2,690 er Treatment Center \$0	Inspection & Testing		က	\$3	\$141,462				0\$	\$149,600
er Treatment Center \$0 <td>Project Management</td> <td></td> <td>\$0</td> <td>0\$</td> <td>\$220</td> <td></td> <td></td> <td></td> <td>\$2,690</td> <td>\$2,910</td>	Project Management		\$0	0\$	\$220				\$2,690	\$2,910
er Treatment Center \$0 \$2,500,000 \$0 \$2,500,000 \$0 \$0 \$2,500,000 \$0	Other Contract Services		\$0	\$0					\$0	\$0
\$4,388 \$2,531,472 \$158,468 \$6,159 \$2,530,504 \$0 \$2,690 ng* \$6,069,031 * Other Funding Source: * Other Funding Source: * Other Funding Source: Expenditures \$5,233,682 * S5,233,682 \$19,766,318 \$19,766,318	Storm/Waste Water Treatment Center		\$0						0\$	\$5,000,000
\$31,069,031 \$6,069,031 \$25,000,000 \$5,233,682 \$19,766,318	Total		\$4,388					0\$	\$2,690	\$5,233,682
mg* \$6,069,031 \$25,000,000 Expenditures \$5,233,682 \$19,766,318	Project Budget	\$31,069,031								
\$25,000,000 S5,233,682 \$19,766,318	Less Other Funding*	\$6,069,031			* Other Fundir	ng Source:				
Expenditures	Net	\$25,000,000			Measure AA \$	6,069,031 alloo	ated			
	Actual Measure S Expenditures	\$5,233,682								
	Kunning Balance	\$19,766,318								

4 of 9

7/7/11

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
						1			
S7100043, S7100066									
Energy Efficiency Projects (7)									
Legal		\$0	\$0	0\$		\$988	\$0	\$0	\$988
Building & Additions		80	\$0	0\$	0\$	\$106,921	\$355,294	-\$180,342	\$281,873
Engineering		\$	\$0	\$0	\$10,500	\$0	\$0	\$0	\$10,500
Inspection & Testing		\$0	\$0	0\$		\$0	\$0	\$0	\$0
Project Management		\$0	\$0	0\$	0\$	\$0	\$0	\$0	\$0
Total		\$0	\$0	0\$	\$10,500	\$107,910	\$355,294	-\$180,342	\$293,361
Project Budget	\$1,293,570	Received							
Less Other Funding*	\$217,322	\$217,322		* Other Fundin	g Source:				
Net	\$1,076,248			SCE & The Ga	SCE & The Gas Co. \$217,322 received	2 received			
Actual Measure S Expenditures	\$293,361								
Running Balance	\$782,887								
S7100091, S7100092									
Satellite Campus Parking Facilities and Roadway Improvements (8)	Improvements ((8							
Legal		\$0	\$0	0\$		\$175	\$0	\$0	\$475
Other Contract Services		\$0	\$0	\$0	\$300	\$0	\$0	\$0	\$300
Advertising		0\$	\$0	0\$		0\$	\$0	\$0	\$0
Consultants		\$0	\$0	0\$	0\$	\$0	\$0	\$0	\$0
Supplies		\$0	\$0	0\$		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$278,178	\$1,860,152	\$449,543	\$37,777	\$2,625,651
Architect		\$0	\$0	\$324,919	\$324,864	\$136,911	\$34,490	\$1,397	\$822,582
Inspection & Testing		\$0	\$0	0\$	\$31,100	\$185,947	\$28,218	\$360	\$245,626
Project Management		\$0	\$0	\$0	\$18,288	\$64,880	\$31,137	\$8,659	\$122,964
Non-Cap Equipment		\$0	\$0	0\$		0\$	\$3,387	\$0	\$3,387
Total		0\$	0\$	\$324,919	\$653,031	\$2,248,065	\$546,775	\$48,194	\$3,820,983
Project Budget	\$4,875,000								
Less Other Funding	80								
Net	\$4,875,000								
Actual Measure S Expenditures	\$3,820,983								
Running Balance	\$1,054,017								


5 of 9

7/7/11

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE S EXPENDITURES

FUND 42.3 As of June 30, 2011

Projects	Budget	04/05 Final	4/05 Final 05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100142									
Parking Garage and Grounds - Student Services (9)									
Supplies		\$0	\$0	\$0	\$0	\$1,745	\$0	\$0	\$1,745
Consultants		\$0	\$0	0\$	\$0	\$20,700	\$0	\$0	\$20,700
Legal		\$0	\$0	\$0	\$0	\$2,154	\$17,486	\$4,337	\$23,977
Other Contract Services		\$0	\$0	\$0	\$0	\$1,508	\$10,952	\$1,863	\$14,323
Building & Additions		\$0	\$0	\$0	\$0	\$2,555,940	\$5,925,152	\$1,447	\$8,482,538
Architect		\$0	\$0	0\$	\$2,266,766	\$2,674,054	\$0	\$33,778	\$4,974,598
Engineering		\$0	\$0	0\$	\$0	\$4,813	\$38,330	\$42,968	\$86,110
Inspection & Testing		\$0	\$0	\$0	\$0	\$131,009	\$161,847	\$50,305	\$343,161
Project Management		\$0	\$0	0\$	\$0	\$158,766	\$373,559	\$174,645	\$706,970
Cap Equipment		\$0	\$0	0\$	\$	\$0	\$14,393	\$0	\$14,393
Total		\$0	\$	\$	\$2,266,766	\$5,550,689	\$6,541,719	\$309,342	\$14,668,516
Project Budget	\$53,143,653	Received							
Less Other Funding*	\$453,000	\$0		* Other Funding Source:	g Source:				
Net	\$52,690,653			State of California	State of California \$453,000 allocated	llocated			
Actual Measure S Expenditures	\$14,668,516								
Running Balance	\$38,022,137								

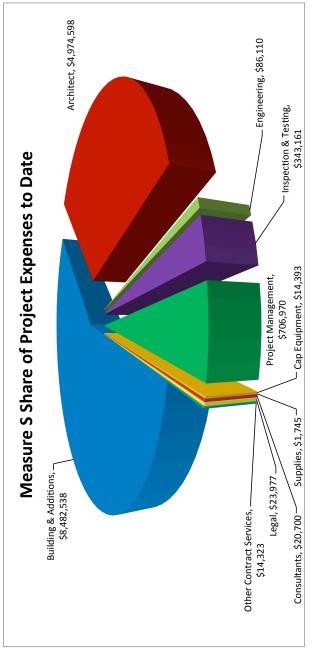

Parking Garage and Grounds - Student Services

Project Description:
Consolidates various student services
departments and college administration in a
single complex at the front of the campus

Facility Size: 83,634 sq/ft & 500 cars underground parking structure

Status: Phase 1 completed Phase 2 in plan check with DSA

Architect: Steinberg Architects

Contractor:

45

7/7/11

6 of 9

Insprovements (10)	Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
Tripprovements (10) Sept.	000000									
A Secretary State of Secretary S	Pico Promenade Improvements (10)									
Color Colo	Building & Additions		\$					\$0	\$0	\$884.09
Column C	Architect		0\$					\$864	80	\$98,59
Column C	Inspection & Testing		0\$					0\$	\$0	\$7,591
Colored St. Colored St	Project Management		\$0					\$0	\$0	\$27,73
1, 10, 10, 10, 10, 10, 10, 10, 10, 10,	Total							\$864	\$0	\$1,018,00
Expenditures	Project Budget	\$1,018,009								
Comparison Com	Less Other Funding	0\$								
(11) (12) (13) (14) (15) (15) (15) (15) (16) (17) (18) (19) (17) (19) (19) (19) (19) (19) (19) (19) (19	Net	\$1,018,009								
11 11 12 12 13 14 15 15 15 15 15 15 15	Actual Measure S Expenditures Running Balance	\$00,810,14								
Color Colo		-								
1,11, 1,11, 1,11, 1,11, 1,11, 1,11, 1,11, 1,11, 1,11, 1,11, 1,11, 1,11, 1,1,1, 1,1,1, 1,1,1, 1,1,1, 1,1,1,1,	S7100004									
SAPER SAPE	Master Planning (11)									
rivices 50 <t< td=""><td>Consultants</td><td></td><td>0\$</td><td></td><td></td><td></td><td></td><td>\$441,549</td><td>\$13,320</td><td>\$454,869</td></t<>	Consultants		0\$					\$441,549	\$13,320	\$454,869
rickes SO SO <th< td=""><td>Printing</td><td></td><td>0\$</td><td></td><td></td><td></td><td></td><td>\$4,157</td><td>0\$</td><td>\$4,157</td></th<>	Printing		0\$					\$4,157	0\$	\$4,157
rouces \$0 \$0 \$0 \$0 \$422 \$422 \$442<	Advertising		\$0					\$3,000	\$0	\$3,00
ent \$0 \$0 \$0 \$10,2368 ent \$0 \$0 \$0 \$10,2368 ng \$0 \$0 \$0 \$0 \$10,2368 ng \$750,000 \$0 \$0 \$0 \$0 \$10,538 ng \$750,000 \$0 \$0 \$0 \$0 \$0 \$10,638 ng \$750,000 \$750,000 \$2 \$0 \$0 \$0 \$10,738 respenditures \$7708,583 \$708,583 \$0 \$0 \$0 \$10,774 feed Expenses (12) \$0 \$0 \$0 \$0 \$0 \$0 \$17,747 red \$0 \$	Other Contract Services		\$0					\$442	\$200	\$642
rent \$0 \$	Architect		\$0					\$192,358	\$24,736	
STSOLOGO SSOLOGO SSOLOGO SSOLOGO SSOLOGO SSOLOGO STSOLOGO STS	Project Management		\$0					\$16,638	\$9,341	\$25,979
STS0,000	Filling Fees		\$0					\$0	\$2,842	
rexpenditures \$750,000 rexpenditures \$750,000 rexpenditures \$708,583 seq Expenses (12) \$60,000 respenditures \$708,583 respenditures \$708,583 respenditures \$708,583 \$708,583 respenditures \$708,583 \$708,583 \$708,583 respenditures \$708,583 \$708,583 \$708,583 \$708,583 respenditures \$708,583 \$708,583 \$708,583 \$708,583 \$708,583 respenditures \$708,583 \$708,58	Total							\$658,143	\$50,439	
ng \$0 Expenditures \$750,000 Expenditures \$41,417 red Expenses (12) \$61,817 red Expenses (12) \$0 \$	Project Budget	\$750,000								
ted Expenses (12)	Less Other Funding	\$0								
texpenditures \$708,583 sted Expenses (12) \$641,417 sted Expenses (12) \$60 \$6 \$60 \$60 \$63,638 sted Expenses (12) \$60	Net	\$750,000								
ted Expenses (12) \$41,417 red Expenses (12) \$0 \$0 \$0 \$3,638 expenses (12) \$0 \$0 \$0 \$3,638 expenses (12) \$0 \$0 \$0 \$3,638 expenditures \$0 \$0 \$0 \$0 \$0 solution \$0 \$0 \$0 \$0 \$0 \$0 ent \$0 \$0 \$0 \$0 \$0 \$0 \$0<	Actual Measure S Expenditures	\$708,583								
ted Expenses (12) 50 180 50 180 <td>Running Balance</td> <td>\$41,417</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>	Running Balance	\$41,417								
ted Expenses (12) \$0 \$0 \$0 \$0 \$0.3,638 red Expenses (12) \$0 \$0 \$0 \$0 \$0 \$0.3,638 stock \$0 \$0 \$0 \$0 \$0 \$0.3,638 stock \$0 \$0 \$0 \$0 \$0 \$0.3,17 stock \$0 \$0 \$0 \$0 \$0 \$0.3,17 stock \$0 \$0 \$0 \$0 \$0 \$0 \$0.0 stock \$0		-								
tred Expenses (12) \$0 \$0 \$0 \$0.53(6.38) stock (12) \$0 \$0 \$0 \$0 \$0.53(6.38) stock (12) \$0 \$0 \$0 \$0 \$0.53(6.38) stock (12) \$0 \$0 \$0 \$0 \$0 \$0 stock (12) \$0	\$7100048									
Second Fig. 19	Other Bond Related Expenses (12)		•					000	Ç	C C
services 50 <	salidac		9 6					40,000	977	00,00
ent \$60 \$50 \$60 \$50 \$50 \$50 \$50 \$50 \$50 \$50 \$50 \$50 \$5	Legal Software License		000					48,917	\$11,409 64,007	\$20,380
ent \$0 \$0 \$0 \$1,20 ent \$0 \$0 \$0 \$17,206 ent \$0 \$0 \$0 \$17,206 ent \$0 \$0 \$0 \$0 \$17,747 ent \$0 \$0 \$0 \$0 \$17,747 ent \$0 \$0 \$0 \$0 \$17,747 ent \$0 \$0 \$0 \$0 \$0 \$0 sed2,764 \$0 \$0 \$0 \$1,800 \$50,185 ng \$662,764 \$0 \$0 \$1,800 \$50,185 expenditures \$114,917 \$14,917 \$14,917 \$14,917	Advortising		9					00000	100,14	
ent \$50 \$50 \$50 \$50 \$77747 \$7777 \$77	Advertishing Other Contract Services		9					\$17.206	\$23 342	
ent \$50 \$50 \$50 \$50 \$17,747 \$50 \$50 \$50 \$50 \$50 \$50 \$50 \$50 \$50 \$50	Moving Services		0#					\$400	1 C (S)	
ent \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	Project Management		0\$					\$17 747	\$13 179	
ent \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	Cap Equipment		0\$					0\$	\$10,086	\$10,086
solution \$0 \$0 \$1,800 \$50,185 ng \$662,764 \$0 \$1,800 \$50,185 ng \$662,764 \$662,764 \$14,917 Expenditures \$14,917 \$547,847	Non-Cap Equipment		S					\$0	\$2,860	
ng \$662,764 Sec 764 \$662,764 Expenditures \$114,917 \$547,847	Total		0\$					\$50,185	\$62,932	
ng Expenditures	Project Budget	\$662,764								
Expenditures	Less Other Funding	0\$								
Expenditures	Net	\$662,764								
	Actual Measure S Expenditures	\$114,917								
	Running Balance	\$547,847								

7 of 9

7/7/11

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100049									
Adv Architecture Related Exp for AA (13)									
Legal		\$0	0\$			0\$		\$0	
Other Contract Services		\$	0\$	0\$	0\$	0\$	0\$	\$0	
Architect		\$0	\$0			0\$		\$0	\$0
Engineering		\$0	\$0		0\$	0\$	0\$	\$0	
Inspection & Testing		0\$	0\$		0\$	\$45,734	-\$45,734	0\$	\$0
Project Management		0\$	0\$	0\$	0\$	0\$	0\$	0\$	0\$
Total		\$	\$0		0\$	\$45,7	-\$45,734	\$0	\$0
Project Budget	\$0								
Less Other Funding	\$0								
Net	\$0								
Actual Measure S Expenditures	\$0								
Running Balance	0\$								
S7100057									
Real Property Acquisition (14)									
Other Contract Services		\$0	\$0	\$0		0\$	\$18,721	\$0	
Architect		\$0	\$0		0\$	0\$		\$0	
Engineering		0\$	\$0				0\$	\$0	
Inspection & Testing		0\$	0\$	0\$	0\$	0\$		0\$	
Project Management		0\$	\$0				,	\$0	
Total		0\$	\$0		0\$		\$45,597	\$0	\$45,597
Project Budget	\$50,000								
Less Other Funding	0\$								
Net	\$50,000								
Actual Measure S Expenditures	\$45,597								
Running Balance	\$4,403								

8 of 9

7/7/11

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final 09/10 Final	09/10 Final	10/11	Combined Totals
S7100072									
Campus Signage (15)									
Supplies		\$0	\$0	0\$	\$0	\$0	\$0	\$303	\$303
Consultants		\$0	\$0	0\$	\$0	\$0	\$32,225	\$23,725	\$55,950
Other Contract Services		\$0	\$0	0\$	\$0	\$0	\$0	\$187	\$187
Architect		\$0	\$0	0\$	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	0\$	\$0	\$0	\$0	\$638	\$638
Inspection & Testing		\$0	\$0	0\$	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	0\$	\$0	\$0	\$0	\$22,953	\$22,953
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$156,258	\$156,258
Total		0\$	0\$	0\$	0\$	0\$	\$32,225	\$204,064	\$236,289
Project Budget	\$606,223								
Less Other Funding	\$0								
Net	\$606,223								
Actual Measure S Expenditures	\$236,289								
Running Balance	\$369,934								

8,606 \$14,601,36	0,819,624 \$8,933,2	21 \$8,321,918 \$	8,606 \$14,601,30
--------------------	----------------------	-------------------	-------------------

Note: Project 3 had no expenses


SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure AA Project Schedule As of June 30, 2011

		;							
	Project Name	Completion	2010	2011	2012	2013	2014	2015	2016
101	Environmental Performance - Central Plant Connections	September 2014							
102	Infrastructure & Technology - Information Technology Relocation	February 2014							
103	Media and Technology Complex - Academy Site	September 2014							
104	Replacement Health/PE/Fitness/Dance Building with Central Plant	September 2014							
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	December 2016							
106	Replacement Math and Science Extension Building	December 2016							
107	Madison East Wing Seismic Upgrade	August 2013							
108	Renovation of Corsair Stadium	Not Scheduled							
109	Career Opportunity and Advancement Center (Bundy)	Not Scheduled							
110	Malibu Center	Not Scheduled							
111	Business & Facilities Infrastructure	On-Going							
112	Master Planning, Program Management, Overhead	On-Going							
113	Energy Efficiency Projects	On-Going							
114	Community Classroom & Facility Projects	December 2011							
115	Real Property Acquisition	On-Going							
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going							
			lu I	In Planning	In Construction	nction			


SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget As of June 30, 2011

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 6/30/11	Measure AA Expenditures as of 3/31/11	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	101 Environmental Performance - Central Plant Connections	September 2014	\$4,882,119	\$4,882,119	0\$	\$62,550	\$51,132	\$11,418	\$4,819,569
102	2 Infrastructure & Technology - Information Technology Relocation	February 2014	\$13,287,218	\$13,287,218	0\$	\$586,547	600′92ε\$	\$210,538	\$12,700,671
103	3 Media and Technology Complex - Academy Site	September 2014	\$61,480,824	\$57,700,824	000'082'£\$	\$5,015,125	\$4,881,617	\$133,508	\$52,685,699
104	4 Replacement Health/PE/Fitness/ Dance Building with Central Plant	September 2014	\$40,200,333	\$35,384,240	\$4,816,093	\$1,846,819	\$1,234,609	\$612,210	\$33,537,421
105	5 Drescher - Academic Modernization, Bookstore, Pico Promenade	December 2016	\$34,026,480	\$34,026,480	0\$	0\$	0\$	0\$	\$34,026,480
106	6 Replacement Math and Science Extension Building	December 2016	\$108,103,000	\$68,259,000	\$40,134,000	0\$	0\$	0\$	\$68,259,000
107	7 Madison East Wing Seismic Upgrade	August 2013	\$12,292,000	\$12,292,000	0\$	\$619,810	\$467,035	\$152,775	\$11,672,190
108	8 Renovation of Corsair Stadium	Not Scheduled	\$11,203,000	\$11,203,000	0\$	\$32,299	\$13,714	\$21,585	\$11,167,701
109	9 Career Opportunity and Advancement Center (Bundy)	Not Scheduled	\$41,391,000	\$29,384,000	\$12,007,000	0\$	0\$	0\$	\$29,384,000
110	0 Malibu Center	Not Scheduled	\$31,069,031	\$6,069,031	\$25,000,000	0\$	0\$	0\$	\$6,069,031
111	1 Business & Facilities Infrastructure	On-Going	\$6,140,952	\$6,140,952	0\$	\$133,238	\$130,172	\$3,066	\$6,007,714
112	2 Master Planning, Program Management, Overhead	On-Going	\$1,650,000	\$1,650,000	0\$	0\$	0\$	0\$	\$1,650,000
113	3 Energy Efficiency Projects	On-Going	\$4,650,136	\$4,150,136	0\$	0\$	0\$	0\$	\$4,150,136
114	4 Community Classroom & Facility Projects	December 2011	\$3,221,000	\$3,221,000	0\$	\$577,172	\$288,970	\$288,202	\$2,643,828
115	5 Real Property Acquisition	On-Going	\$6,000,000	\$6,000,000	0\$	\$5,757,895	\$5,781,653	-\$23,758	\$242,105
116	6 Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going	\$350,000	\$350,000	0\$	\$251,152	\$240,787	\$10,365	\$98,848
117	7 Infrastructure & Technology - Technology	On-Going	\$500,000	\$500,000	0\$	\$216,896	\$216,896	0\$	\$283,104
118	118 Infrastructure & Technology - Utility	On-Going	\$500,000	\$500,000	0\$	\$20,219	\$2,760	\$17,459	\$479,781
	Project Totals		\$380,947,093	\$295,000,000	\$85,737,093	\$15,122,722	\$13,685,354	\$1,437,368	\$279,877,278

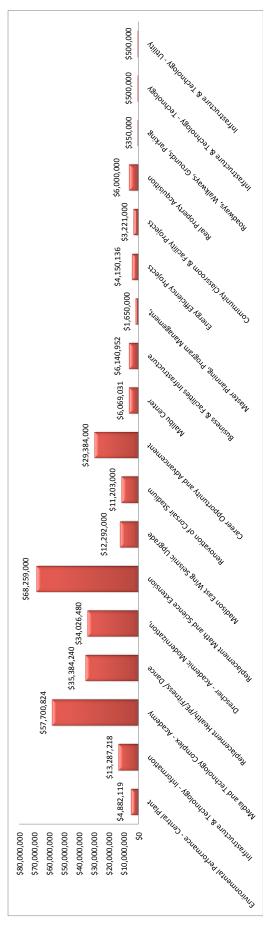

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100062				
Environmental Performance - Central Plant Connections (101)				
Legal		0\$	0\$	\$0
Other Contract Services		0\$	0\$	\$0
Consultants		0\$	0\$	\$0
Building & Additions		\$0	0\$	\$0
Architect		0\$	\$382	\$385
Engineering		\$48,500	0\$	\$48,500
Inspection & Testing		0\$	0\$	\$0
Project Management		0\$	\$13,665	\$13,665
Cap Equipment		\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0
Total		\$48,500	\$14,050	\$62,550
Project Budget	\$4,882,119			
Less Other Funding	\$0			
Net	\$4,882,119			
Actual Measure AA Expenditures	\$62,550			
Running Balance	\$4,819,569			

AA 7100063 AA 7100063 AA 7100063 AB A 7100063 AB A 7100063 AB A A 7100063 AB A A A A A A A A A A A A A A A A A A	Projects	Budget	09/10 Final	10/11	Combined Totals
63 cture & Technology - IT Relocation (102) tts tts tAdditions tAdditions					
trs trs trs trs trs trs trs trs	AA 7100063				
ts \$0 \$0 t, Additions \$10,291 \$8,460,7 anagement \$10,291 \$8,468,737,48 \$10,60,9 soment \$0 \$0 \$0 \$10,60,9 sequipment \$13,287,218 \$148,800 \$437,747 \$586,5 sasure AA Expenditures \$13,287,218	I—				
tist \$0 \$	Legal		\$0	\$0	0\$
Additions \$0 \$10,291	Consultants		\$0	\$0	0\$
\$0 \$0 \$0 \$105,049 \$355,748 \$460,7 \$10,291 \$8,468 \$106,9 \$10,291 \$8,468 \$106,9 \$10,291 \$8,468 \$106,9 \$10,291 \$10,291 \$106,9 \$0 \$0 \$0 \$0 \$13,287,218 \$148,800 \$437,747 \$586,5 \$286,547 \$18,800 \$18,800 \$18,800 \$20 \$12,700,671 \$18,800 \$18,200 \$18,800 \$20 \$20	Supplies		\$0	\$0	0\$
hitect \$105,049 \$355,748 \$460,7 bection & Testing \$10,291 \$8,468 \$18,7 bection & Testing \$10,291 \$18,7 \$18,7 bection & Testing \$18,7 \$18,7 \$18,7 bection & Testing \$10,291	Building & Additions		0\$	0\$	0\$
ection & Testing \$10,291 \$8,468 \$18,7 lect Management \$33,460 \$73,532 \$106,9 b Equipment \$0 \$0 \$0 Cap Equipment \$0 \$0 \$0 Cap Equipment \$0 \$0 \$0 ect Budget \$148,800 \$437,747 \$586,5 s Other Funding \$13,287,218 \$13,287,218 \$13,287,218 all Measure AA Expenditures \$13,287,218 \$13,287,218 \$13,287,218 all Measure AA Expenditures \$13,287,218 \$13,287,218 \$13,287,218 all Measure AA Expenditures \$13,287,218 \$13,287,218 \$13,287,218	Architect		\$105,049	\$355,748	\$460,797
lect Management \$33,460 \$73,532 \$106,9 Equipment \$0 \$0 \$0 Cap Equipment \$0 \$0 \$0 al \$148,800 \$437,747 \$586,5 lect Budget \$0 \$437,747 \$586,5 s Other Funding \$13,287,218 \$13,287,218 \$13,287,218 al Measure AA Expenditures \$13,287,218 \$13,287,218 \$13,287,218 al Measure AA Expenditures \$12,700,671 \$12,700,671 \$12,700,671	Inspection & Testing		\$10,291	\$8,468	\$18,759
Equipment \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$1 \$2 \$2 \$2 \$2 \$2 \$2 \$2 \$3 \$2 \$3	Project Management		\$33,460	\$73,532	\$106,992
Cap Equipment \$0 \$0 \$0 \$148,800 \$437,747 \$586,5 \$286,5 \$286,5 \$31,287,218 \$31,287,	Cap Equipment		\$0	0\$	0\$
sal \$148,800 \$437,747 lect Budget \$13,287,218 s Other Funding \$0 Lal Measure AA Expenditures \$13,287,218 Ining Balance \$12,700,671	Non-Cap Equipment		\$0	\$0	0\$
lect Budget \$13,287, s Other Funding \$13,287, Lal Measure AA Expenditures \$586, ning Balance \$12,700,	Total		\$148,800	\$437,747	\$586,547
s Other Funding \$13,287,, and Measure AA Expenditures \$586, ining Balance \$12,700,	Project Budget	\$13,287,218			
ual Measure AA Expenditures Ining Balance	Less Other Funding	0\$			
11.8	Net	\$13,287,218			
	Actual Measure AA Expenditures	\$586,547			
	Running Balance	\$12,700,671			

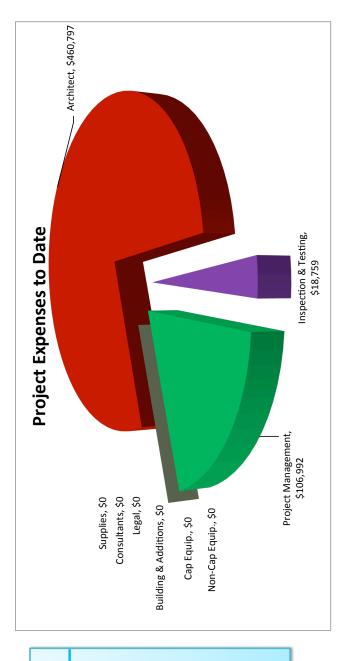

Infrastructure & Technology -IT Relocation


Project Description:
Relocation of IT/Telecom Departments, and renovation of Media Center

Facility Size: 9,230 sq/ft Status: In design development

Architect: Morris Architects

Contractor:

Projects	Budget	09/10 Final	10/11 (Combined Totals
AA 7100061				
Media and Technology Complex - Academy Site (103)				
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Legal		\$16,903	\$0	\$16,903
Other Contract Services		\$3,993	\$5,446	\$9,439
Advertising		0\$	\$0	0\$
Building & Additions		0\$	\$238	\$538
Architect		\$2,097,553	\$2,408,588	\$4,506,141
Engineering		\$16,459	\$26,553	\$43,012
Inspection & Testing		\$64,905	\$22,628	\$87,533
Project Management		\$121,786	\$229,773	\$351,558
Cap Equipment		\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	0\$
Total		\$2,321,599	\$2,693,526	\$5,015,125
Project Budget	\$61,480,824	Received		
Less Other Funding*	\$3,780,000	\$803,412		
Net	\$57,700,824	\$57,700,824 * Other Funding Source:	nrce:	
Actual Measure AA Expenditures	\$5,015,125	KCRW Foundation	\$5,015,125 KCRW Foundation \$3,780,000 commited,	d,
Running Balance	\$52,685,700	\$52,685,700 \$803,412 received		

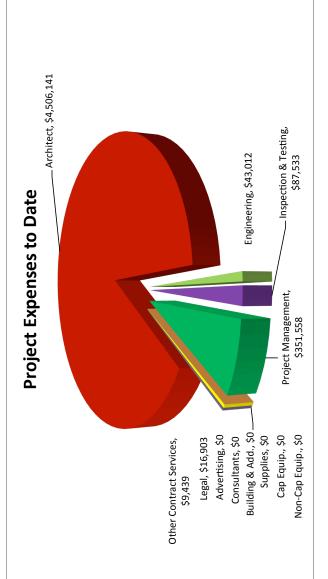

Media and Technology Complex -**Academy Site**

Project Description:

Renovation and new extension to the existing building, new building for KCRW, and a new parking structure


Facility Size: Building - 47,172 sq/ft Parking Structure - 450 spaces

Status: Building in construction drawings Parking structure in DSA

Architect: Clive Wilkinson Architects

Contractor:

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100060				
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)				
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Other Contract Services		\$120	\$38	\$158
Building & Additions		\$0	\$0	80
Architect		\$256,076	\$1,399,227	\$1,655,303
Engineering		0\$	\$8,507	\$8,507
Inspection & Testing		\$36,892	\$490	\$37,382
Project Management		\$34,968	\$110,502	\$145,470
Total		\$328,056	\$1,518,764	\$1,846,819
Project Budget	\$40,200,333			
Less Other Funding*	\$4,816,093	\$4,816,093 * Other Funding Source:	nrce:	
Net	\$35,384,240	\$35,384,240 Measure S \$4,816,093 allocated	393 allocated	
Actual Measure AA Expenditures	\$1,846,819			
Running Balance	\$33,537,421			

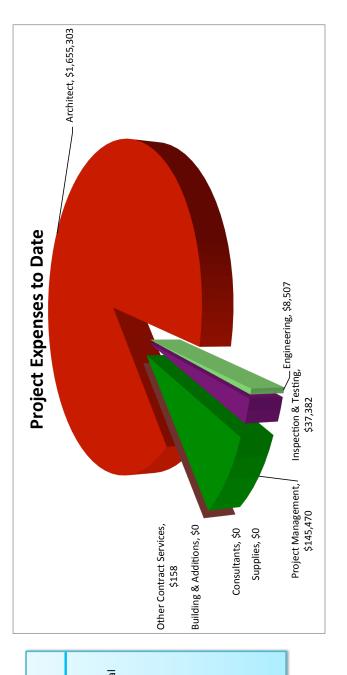

Repl. Health/PE/Fitness/Dance Building with Central Plant


center, dance studios, and new central Replacement of locker rooms, fitness Project Description:

plant

Status: In design development Facility Size: 62,000 sq/ft

Architect: Gensler Architects

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100047				
Madison East Wing Seismic Upgrade (107)				
Consultants		\$0	\$0	\$0
Supplies		\$0	0\$	\$0
Legal		0\$	0\$	\$0
Other Contract Services		\$0	\$320	\$350
Building & Additions		\$0	\$656	\$656
Architect		\$76,073	\$398,050	\$474,123
Inspection & Testing		0\$	\$18,408	\$18,408
Project Management		\$5,557	\$120,716	\$126,273
Total		\$81,630	\$538,180	\$619,810
Project Budget	\$12,292,000			
Less Other Funding	\$0			
Net	\$12,292,000			
Actual Measure AA Expenditures	\$619,810			
Running Balance	\$11,672,190			

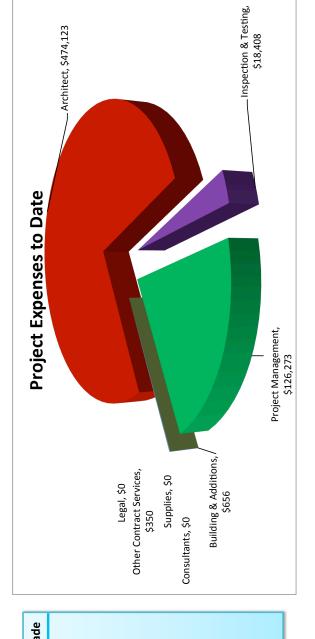

Madison East Wing Seismic Upgrade

Project Description:
Replacement of east wing with a new multipurpose room and additional classrooms

Facility Size: 15,461 sq/ft

15,461 sq/π

Status: In design development

Architect: DLR Group WWCOT

Contractor:

	-			
AA 7100068			_	
Renovation to Corsair Stadium (108)				
Other Contract Services		0\$	0\$	0\$
Building & Additions		0\$	\$0	\$0
Architect		0\$	\$30,759	\$30,759
Engineering		\$0	80	0\$
nspection & Testing		\$0	0\$	0\$
Project Management		\$0	\$4,540	\$4,540
Total		\$0	\$35,299	\$35,299
Project Budget	\$11,203,000			
Less Other Funding	80			
Net	\$11,203,000			
Actual Measure AA Expenditures	\$35,299			
Running Balance	\$11,167,701			
AA 7100067				
Business & Facilities Infrastructure (111)				
Other Contract Services		\$0	\$6,289	\$6,289
Building & Additions		\$0	\$34,672	\$34,672
Architect		\$0	\$0	\$0
Engineering		80	0\$	\$0
Inspection & Testing		\$0	0\$	\$0
Project Management		0\$	\$3,073	\$3,073
Non-Cap Equipment		80	\$89,204	\$89,204
Total		\$0	\$133,238	\$133,238
Project Budget	\$6,140,952			
Less Other Funding	\$0			
Net	\$6,140,952			
Actual Measure AA Expenditures	\$133,238			
Running Balance	\$6,007,714			
Community Classroom & Facility Projects (114)				
Other Contract Services		80	\$2,989	\$2,989
Building & Additions		0\$	\$191,851	\$191,851
Architect		0\$	\$247,460	\$247,460
Engineering		0\$	\$2,208	\$2,208
Inspection & Testing		0\$	\$27,883	\$27,883
Project Management		\$135	\$104,647	\$104,782
Total		\$135	\$577,037	\$577,172
Project Budget	\$3,221,000			
Less Other Funding	0\$			
Net	\$3,221,000			
Actual Measure AA Expenditures	\$577,172			
- (000 010 00			

Projects	Budget	09/10 Final	10/11	Compined lotals
AA 7100057				
Real Property Acquisition (115)				
Legal		\$0	\$0	\$0
Other Contract Services		\$0	\$39	\$39
Site Acquisition		\$1,739,979	\$4,001,204	\$5,741,182
Inspection & Testing		\$8,689	\$7,986	\$16,674
Project Management		0\$	\$0	\$0
Total		\$1,748,667	\$4,009,228	\$5,757,895
Project Budget	\$6,000,000			
Less Other Funding	\$0			
Net	\$6,000,000			
Actual Measure AA Expenditures	\$5,757,895			
Running Balance	\$242,105			
4.4.74000.50				
RAY 100030 Roadways Walkways Grounds Parking Lots and Garages (116)				
		O\$	\$0	0\$
Other Contract Services		\$218	\$770	\$988
Building & Additions		\$185,345	\$6,731	\$192.076
Inspection & Testing		\$13,380	\$7,865	\$21,245
Project Management		\$24,404	\$12,439	
Total		\$223.347	\$27.804	
Project Budget	\$350,000			
Less Other Funding	\$0			
Net	\$350,000			
Actual Measure AA Expenditures	\$251,152			
Running Balance	\$98,848			
AA 7100069				
Infrastructure & Technology - Technology (117)				
Maintenance Contract		\$0	\$9,472	\$9,472
Building & Additions		\$0	\$0	\$0
Architect		\$0	\$0	\$0
Inspection & Testing		80	\$0	\$0
Project Management		80	\$0	\$0
Cap Equipment		80	\$207,423	\$207,423
Non-Cap Equipment		0\$	0\$	0\$
Total		0\$	\$216,896	\$216,896
Project Budget	\$500,000			
Less Other Funding	\$0			
Net	\$500,000			
Actual Measure AA Expenditures	\$216,896			
	4083 107			

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100069				
Infrastructure & Technology - Utility (118)				
Sofeware License		\$0	\$12,000	\$12,000
Legal		80	0\$	0\$
Building & Additions		80	0\$	0\$
Architect		80	0\$	0\$
Inspection & Testing		0\$	\$4,979	\$4,979
Project Management		0\$	\$3,240	\$3,240
Cap Equipment		0\$	0\$	0\$
Non-Cap Equipment		0\$	\$0	0\$
Total		0\$	\$20,219	\$20,219
Project Budget	\$500,000			
Less Other Funding	\$0			
Net	\$500,000			
Actual Measure AA Expenditures	\$20,219			
Running Balance	\$479,781			

\$15,122,722	
\$10,221,988	
\$4,900,734	

Grand Total

SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of June 30, 2011

\$17,536,215	Total Available as of 7-1-11
\$1,127	Unsold Bond Amount
\$17,535,088	Total Available Remaining
\$142,463,785	Expenses as of 6-30-11
\$159,998,873	Total Available
\$10,998,992	2010
\$11,999,987	2007
\$89,999,923	2005
\$21,999,971	2004
\$25,000,000	2002
Amount	Bond Issue Date
	Measure U Bond \$160,000,000

\$598,500,000 \$383,496,730 \$229,462,779 \$154,033,951

\$215,003,270

Total Expenses as of 6-30-11 Total Available Remaining Total Unsold Bond

Total Bond Total Available

Measure S Bond \$143,500,000 (1)	
Bond Issue Date	Amount
2002	\$58,000,000
2007	\$8,500,000
5009	\$56,997,857
Total Available	\$123,497,857
Expenses as of 6-30-11	\$71,876,272
Total Available Remaining	\$51,621,585
Unsold Bond Amount	\$20,002,143
Total Available as of 7-1-11	\$71,623,728

11 sue Date 2010 9 11 11 13	Measure AA Bond \$295,000,000		
2010 8 fe-30-11 8 Remaining 8	Bond Issue Date		Amount
f6-30-11 Remaining		2010	\$100,000,000
	Total Available		\$100,000,000
6	Expenses as of 6-30-11		\$15,122,722
	Total Available Remaining		\$84,877,278
	Unsold Bond Amount		\$195,000,000
Total Available as of 7-1-11 \$279,	Total Available as of 7-1-11		\$279,877,278

000 000		
000,000,007\$		
\$600,000,000		
\$500,000,000		
\$400,000,000		
\$300,000,000		
\$200,000,000		
\$100,000,000		
Ç		
2	Total Bond Total Available	Total Expenses as of 6-30-11

Interest	Measure U	Measure S	Measure AA
As of 6-30-10	\$5,694,648	\$7,329,902	\$512,487
Arbitrage Payment as of 6-30-10	0\$	\$393,004	\$0
Available Interest as of 6-30-10	\$5,694,648	\$6,936,898	\$512,487

Cost of Issuance Refund	Measure U	Measure S
As of 6-30-10	\$20,688	\$32,575

(1) Original Bond \$135,000,000.00, refunding on 2-15-07 received additional \$8,500,000.00
