



Citizens' Bond Oversight Committee

December 31, 2020 Report (Q2 2020-21)

January 20th, 2021

BOND CAPITAL CONSTRUCTION REPORTS

District Management is responsible for the preparation and fair presentation of the statement of expenditures and bond proceeds in accordance with U.S. generally accepted accounting principles; this includes the design, implementation, and maintenance of internal control relevant to the preparation and fair presentation of the statement of expenditures of bond proceeds that is free from material misstatement, whether due to fraud or error.

This quarterly report is prepared in accordance with these requirements and all bond expenditures were made in compliance with all applicable laws.

Santa Monica College - Bond Capital Construction Budget Summary - 12-31-2020

Project Number	Project Name	Measure U Budget	Measure S Budget	Measure AA Budget	Measure V Budget	Interest	Other Funding Received *	Other Funding Pending **	Total Budget	Estimate at Completion	Status	Bond Funds Remaining
U-A	Purchase of BAE Airport Site	\$30,280,878							\$30,280,878	\$30,280,878	Completed	\$0
U-B	Emeritus College Facility	\$8,909,940					\$693,842		\$9,603,782	\$9,603,782	Completed	\$0
U-C	Purchase of 1738 Pearl Street	\$749,208							\$749,208	\$749,208	Completed	\$0
U-D	PE Temp. Bldg. Replacement	\$2,797,033							\$2,797,033	\$2,797,033	Completed	\$0
U-E	Remodel Library Village for Math	\$1,458,690							\$1,458,690	\$1,458,690	Completed	\$0
U-F	SM Airport Campus Site Improvements	\$4,170,264							\$4,170,264	\$4,170,264	Completed	\$0
U-G	SM Airport Campus West Building	\$19,709,741							\$19,709,741	\$19,709,741	Completed	\$0
U-H	Theater Arts Renovation	\$19,544,314							\$19,544,314	\$19,544,314	Completed	\$0
U-I	Earthquake Rpl. Liberal Arts North	\$6,011,584					\$6,496,141		\$12,507,725	\$12,507,725	Completed	\$0
U-K	Earthquake Rpl. Liberal Arts South	\$6,108,150					\$10,625,070		\$16,733,220	\$16,733,220	Completed	\$0
U-L	Shuttle Replacement Parking	\$18,969,509							\$18,969,509	\$18,969,509	Completed	\$0
U-M	North Quad Plaza	\$11,388,463							\$11,388,463	\$11,388,463	Completed	\$0
U-Q	Infrastructure & Safety	\$4,003,084							\$4,003,084	\$4,003,084	Completed	\$0
U-R	Restroom Improvements	\$17,501							\$17,501	\$17,501	Completed	\$0
S-1	Athletic Fields Phase I, Corsair Field		\$4,372,535				\$67,530		\$4,440,065	\$4,440,065	Completed	\$0
S-1A	Athletic Fields Phase I, John Adams		\$2,969,807						\$2,969,807	\$2,969,807	Completed	\$0
S-10	Pico Promenade Improvements, Phase I		\$1,018,009						\$1,018,009	\$1,018,009	Completed	\$0
S-13	Adv. Architecture Related Exp for AA		\$0						\$0	\$0	Completed	\$0
AA-114	Community Classroom & Facility Projects			\$3,162,183					\$3,162,183	\$3,162,183	Completed	\$0
U-T	14th and Pico Project	\$319,242							\$319,242	\$319,242	Completed	\$0
U-N	Letters & Sci Demo/Restore	\$0							\$0	\$0	Completed	\$0
AA-108	Renovation of Corsair Stadium			\$35,299					\$35,299	\$35,299	Completed	\$0
S-2	Performing Arts Complex		\$37,697,625				\$2,992,576		\$40,690,201	\$40,690,201	Completed	\$0
U-J	Music Complex	\$2,011,371					\$2,618,113		\$4,629,484	\$4,629,484	Completed	\$0
S-3, AA-109	Career Opportunity Center			\$0					\$0	\$0	Completed	\$0
AA-118	Infrastructure & Technology - Utility			\$27,753					\$27,753	\$27,753	Completed	\$0
AA-111	Business & Facilities Infrastructure			\$1,968,124					\$1,968,124	\$1,968,124	Completed	\$0
AA-117	Infrastructure & Technology - Technology			\$2,434,417					\$2,434,417	\$2,434,417	Completed	\$0
S-7, AA-113	Energy Efficiency Projects		\$293,361	\$3,016,773			\$708,637		\$4,018,771	\$4,018,771	Completed	\$0
S-15	Signage Safety/Information		\$706,713						\$706,713	\$706,713	Completed	\$0
AA-102	Infrastructure & Technology - Information Technology Relocation			\$23,140,771			\$19,798		\$23,160,569	\$23,160,569	Completed	\$0
S-8, AA-116	Satellite Campus Parking Facilities and Roadway		\$3,891,747	\$2,130,670					\$6,022,417	\$6,022,417	Completed	\$0
AA-107	Madison East Wing Seismic Upgrade			\$30,161,852					\$30,161,852	\$30,161,852	Completed	\$0
S-4, AA-104	Replacement Health/PE/Fitness Central Plant Building		\$11,603,383	\$44,428,222			\$208,847		\$56,240,452	\$56,240,452	Completed	\$0
AA-101	Environmental Performance - Central Plant Connections			\$10,767,251					\$10,767,251	\$10,767,251	Completed	\$0
S-14, AA-115	Real Property Acquisition		\$45,597	\$24,638,386					\$24,683,983	\$24,683,983	Completed	\$0
AA-103	Media and Technology Complex - Academy Site			\$124,314,322			\$6,835,391		\$131,149,713	\$131,149,713	Completed	\$218,315
AA-119	Emergency Lighting, Fire Alarm, and Security System			\$11,520,794					\$11,520,794	\$11,520,794	Completed	\$5,180
15004829	Student Services Building	\$21,131,135	\$45,595,322	\$6,870,490	\$33,624,909	\$21,681,308	\$1,321,000		\$130,224,164	\$130,224,164	Completed	\$9,449,292
S-5, V-104	Early Childhood Development/Childcare		\$8,858,656		\$15,405,517		\$4,441,065	\$2,220,533	\$30,925,771	\$30,925,771	Completed	\$4,011,230
S-6, AA-110, V-103	Malibu Site Acquisition and Facility		\$25,000,000		\$34,558,420	\$2,023,853			\$61,582,273	\$61,582,273	In Construction	\$38,893,214
U-S, S-11, AA-112, V-109	Master Planning	\$2,110,430	\$716,428	\$834,697	\$1,000,000				\$4,661,555	\$4,661,555	In Design	\$324,403
U-P, AA-106, V-101	Replacement Math and Science Extension Building	\$308,336		\$2,244,008	\$82,317,992		\$2,584,000	\$37,504,000	\$124,958,336	\$124,958,336	In Construction	\$78,817,470
AA-105, V-110	Drescher - Academic Modernization, Bookstore, Pico Promenade II			\$5,082	\$13,000,000				\$13,005,082	\$13,005,082	In Planning	\$13,000,000
V-105	Art Building Replacement		\$24,000,000		\$24,000,000		\$286,093	\$10,614,907	\$34,901,000	\$34,901,000	In Design	\$23,206,356
V-106	Business Building Renovation				\$12,547,000			\$12,470,000	\$25,017,000	\$25,017,000	In Planning	\$12,543,600
V-107	Air Conditioning				\$10,777,654				\$10,777,654	\$10,777,654	In Construction	\$8,935,805
V-108	ADA				\$4,000,000				\$4,000,000	\$4,000,000	In Planning	\$4,000,000
V-111	Outdoor Classroom				\$321,723				\$321,723	\$321,723	In Planning	\$0
V-112	SMMUSD				\$20,000,000				\$20,000,000	\$20,000,000	In Construction	\$20,000,000
V-113	City of Santa Monica				\$20,000,000				\$20,000,000	\$20,000,000	In Planning	\$20,000,000
V-114	Classrooms Relocation				\$6,900,000				\$6,900,000	\$6,900,000	In Construction	\$43,080
S-12, V-120	Other Bond Related Expenses		\$609,204		\$300,000				\$909,204	\$909,204	In Planning	\$191,955
V-115	TBD				\$39,446,785				\$39,446,785	\$39,446,785	In Planning	\$39,446,785
S-16, AA-121, V-121	Cost of Issuance		\$119,470	\$498,026	\$800,000				\$1,417,496	\$1,417,496	In Planning	\$508,723
AA-122, V-122	Management Reserve			\$2,796,709	\$26,000,000		\$6,152,892		\$34,949,601	\$34,949,601	In Planning	\$28,796,709
U-U, S-17, AA-123, V-123	Unissuable	\$1,127	\$2,143	\$4,171					\$7,441	\$7,441	On-Going	\$0
Project Totals		\$160,000,000	\$143,500,000	\$295,000,000	\$345,000,000	\$29,858,053	\$39,898,103	\$62,809,440	\$1,076,065,596	\$1,076,065,596		\$302,392,117

* City of SM: \$14,647,889; FEMA: \$2,456,388; State: \$8,363,000; Prop T: \$2,618,113; DWP: \$86,245; SCE: \$844,284; Gas Co.: \$106,262; Madison Foundation: \$2,992,576; KCRW: \$6,803,412; Emeritus College Foundation: \$693,842; Bond Interest and Cost of Issuance Refund: \$29,858,053
 ** City of SM: \$2,220,533; State: \$60,588,907

SANTA MONICA COMMUNITY COLLEGE DISTRICT


Bond Sales / Expenses Report

As of December 31, 2020

Measure S Bond \$143,500,000 (1)	
Bond Issue Date	Amount
2005	\$58,000,000
2007	\$8,500,000
2009	\$56,997,857
2017	\$20,000,000
Total Available	\$143,497,857
Expenses as of 12-31-20	\$136,090,433
Total Available Remaining	\$7,407,424
Unsold Bond Amount	\$2,143
Total Available as of 1-1-21	\$7,409,567

Total Bond Program (S,AA,V)	\$783,500,000
Total Bonds Issued	\$618,493,686
Total Expenses as of 12-31-20	\$486,790,929
Total Available Remaining	\$131,702,757
Total Unsold Bond	\$165,006,314

Measure AA Bond \$295,000,000	
Bond Issue Date	Amount
2010	\$100,000,000
2014	\$144,995,829
2017	\$50,000,000
Total Available	\$294,995,829
Expenses as of 12-31-20	\$291,748,512
Total Available Remaining	\$3,247,317
Unsold Bond Amount	\$4,171
Total Available as of 1-1-21	\$3,251,488

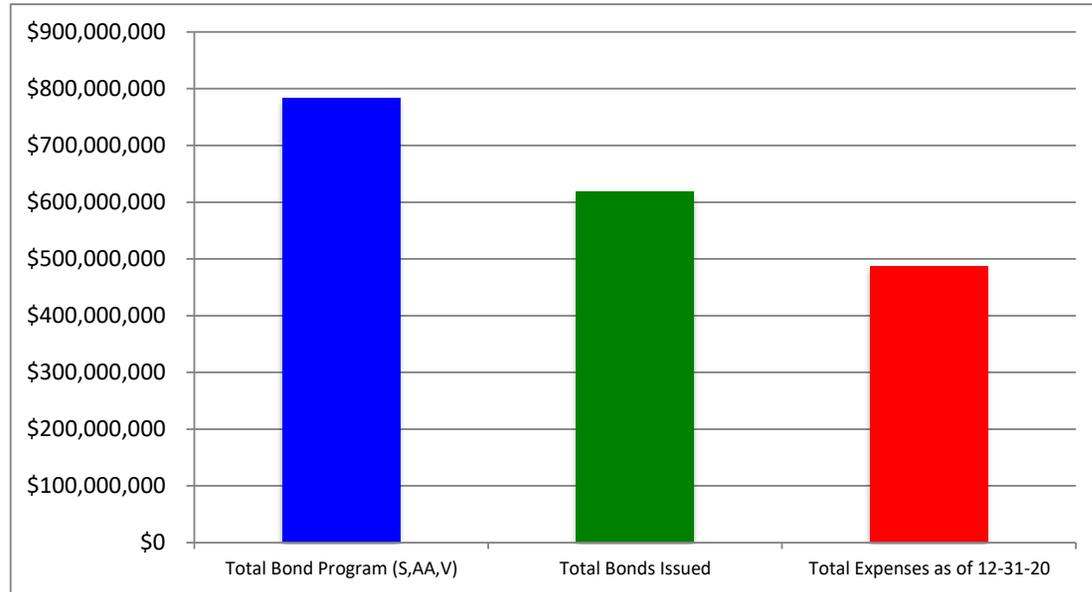

Measure V Bond \$345,000,000	
Bond Issue Date	Amount
2018	\$180,000,000
Total Available	\$180,000,000
Expenses as of 12-31-20	\$58,951,984
Total Available Remaining	\$121,048,016
Unsold Bond Amount	\$165,000,000
Total Available as of 1-1-21	\$286,048,016


Interest	Measure S	Measure AA	Measure V
As of 6-30-20	\$12,070,525	\$6,892,308	\$6,722,728
Expenditure / Arbitrage as of 6-30-20	\$9,853,563	\$5,192,948	\$0
Available Interest as of 7-1-20	\$2,216,962	\$1,699,360	\$6,722,728

Cost of Issuance Refund	Measure S
As of 6-30-20	\$35,575
Expenditure as of 6-30-20	\$0
Available as of 7-1-20	\$35,575

(1) Original Bond \$135,000,000, refunding on 2-15-07 received additional \$8,500,000

SANTA MONICA COMMUNITY COLLEGE DISTRICT
Measure S Bond Budget
As of December 31, 2020

	Project Name	Completion	Project Budget	Measure S Allocation	Other Funding	Measure S Expenditures as of 12/31/20	Measure S Expenditures as of 9/30/20	Measure S Expenditures Last Period	Total Measure S Remaining
1	Athletic Fields Phase I, Corsair Field	Completed	\$4,440,065	\$4,372,535	\$67,530	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	Completed	\$2,969,807	\$2,969,807	\$0	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	Completed	\$40,690,201	\$37,697,625	\$2,992,576	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	Completed	\$58,272,030	\$11,603,383	\$46,668,647	\$11,603,383	\$11,603,383	\$0	\$0
5	Early Childhood Development/Childcare	Completed	\$30,925,771	\$8,858,656	\$22,067,115	\$8,858,656	\$8,858,656	\$0	\$0
6	Malibu Site Acquisition and Facility	August 2022	\$61,582,273	\$25,000,000	\$36,582,273	\$17,725,144	\$17,725,144	\$0	\$7,274,856
7	Energy Efficiency Projects	Completed	\$510,683	\$293,361	\$217,322	\$293,361	\$293,361	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred	\$7,022,417	\$3,891,747	\$3,130,670	\$3,891,747	\$3,891,747	\$0	\$0
9	Parking Garage, Grounds and Equipment - Student Services	Completed	\$130,224,164	\$45,595,322	\$84,628,842	\$45,595,322	\$45,595,322	\$0	\$0
10	Pico Promenade Improvements	Completed	\$1,018,009	\$1,018,009	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	Completed	\$716,428	\$716,428	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	On-Going	\$609,204	\$609,204	\$0	\$476,636	\$476,636	\$0	\$132,568
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	Completed	\$45,597	\$45,597	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	Completed	\$706,713	\$706,713	\$0	\$706,713	\$706,713	\$0	\$0
16	Cost of Issuance	Completed	\$119,470	\$119,470	\$0	\$119,470	\$119,470	\$0	\$0
17	Unissuable Bond	Completed	\$2,143	\$2,143	\$0	\$0	\$0	\$0	\$2,143
	Project Totals		\$339,852,832	\$143,500,000	\$196,354,975	\$136,090,433	\$136,090,433	\$0	\$7,409,567

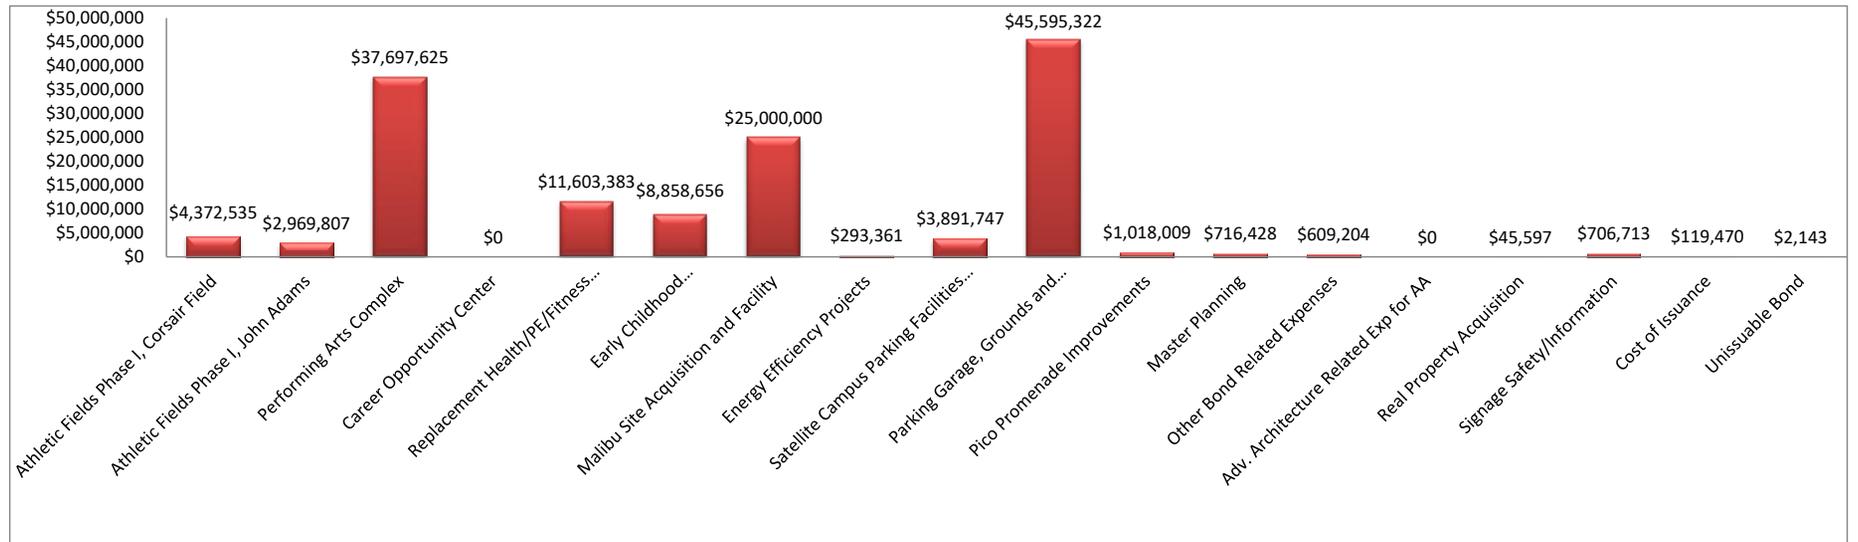

SANTA MONICA COMMUNITY COLLEGE DISTRICT
Measure S Bond Budget History
as of December 31, 2020

	Project Name	Completion	Preliminary Measure S Budget	Measure S Budget as of 9/30/20	Measure S Budget as of 12/31/20	Variance	Measure S Remaining as of 12/31/20
1	Athletic Fields Phase I, Corsair Field	Completed	\$1,800,000	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	Completed	\$35,200,000	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	Completed	\$24,000,000	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	Completed	\$20,000,000	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	Completed	\$20,000,000	\$11,603,383	\$11,603,383	\$0	\$0
5	Early Childhood Development/Childcare	Completed	\$7,000,000	\$8,858,656	\$8,858,656	\$0	\$0
6	Malibu Site Acquisition and Facility	August 2022	\$25,000,000	\$25,000,000	\$25,000,000	\$0	\$7,274,856
7	Energy Efficiency Projects	Completed	\$2,000,000	\$293,361	\$293,361	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred	\$0	\$3,891,747	\$3,891,747	\$0	\$0
9	Parking Garage, Grounds and Equipment - Student Services	Completed	\$0	\$45,595,322	\$45,595,322	\$0	\$0
10	Pico Promenade Improvements, Phase I	Completed	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	Completed	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	On-Going	\$0	\$609,204	\$609,204	\$0	\$132,568
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	Completed	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	Completed	\$0	\$706,713	\$706,713	\$0	\$0
16	Cost of Issuance	Completed	\$0	\$119,470	\$119,470	\$0	\$0
17	Unissuable Bond	Completed	\$0	\$2,143	\$2,143	\$0	\$2,143
	Project Totals		\$135,000,000	\$143,500,000	\$143,500,000	\$0	\$7,409,567

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure S Project Schedule

As of December 31, 2020

	Project Name	Completion	2018	2019	2020	2021	2022
1	Athletic Fields Phase I, Corsair Field	<i>Completed</i>					
1A	Athletic Fields Phase I, John Adams	<i>Completed</i>					
2	Performing Arts Center	<i>Completed</i>					
3	Career Opportunity Center	<i>Completed</i>					
4	Replacement Health/PE/Fitness Building	<i>Completed</i>					
5	Early Childhood Development/Childcare	<i>Completed</i>					
6	Malibu Site Acquisition and Facility	August 2022					
7	Energy Efficiency Projects	<i>Completed</i>					
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred					
9	Parking Garage, Grounds and Equipment - Student Services	<i>Completed</i>					
10	Pico Promenade Improvements	<i>Completed</i>					
11	Master Planning	<i>Completed</i>					
12	Other Bond Related Expenses	On-Going					
13	Adv. Architecture Related Exp for AA	<i>Completed</i>					
14	Real Property Acquisition	<i>Completed</i>					
15	Signage Safety/Information	<i>Completed</i>					
16	Cost of Issuance	<i>Completed</i>					
17	Unissuable Bond	<i>Completed</i>					
			In Planning	In Construction			

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE S EXPENDITURES
 FUND 42.3
 As of December 31, 2020

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals	
S7100019																				
Athletic Field Phase I, Corsair Field (1)																				
Legal		\$0	\$0	\$0	\$301	\$175	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$476
Building & Additions		\$0	\$0	\$0	\$300,380	\$2,579,095	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,879,475
Architect		\$27,332	\$43,815	\$197,557	\$252,736	\$279,173	\$26,563	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$827,176
Inspection & Testing		\$0	\$0	\$0	\$23,411	\$57,585	\$640	\$296	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$81,932
Project Management		\$0	\$0	\$0	\$9,871	\$42,374	\$565	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$52,810
Cap Equipment		\$0	\$0	\$0	\$0	\$483,017	\$35,271	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$518,288
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$2,066	\$10,312	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,378
Total		\$27,332	\$43,815	\$197,557	\$586,699	\$3,443,485	\$73,350	\$296	\$0	\$0	\$0	\$4,372,535								
Project Budget	\$4,440,065	Received																		
Less Other Funding*	\$67,530	\$67,530																		
Net	\$4,372,535																			
Actual Measure S Expenditures	\$4,372,535																			
Running Balance	\$0																			

* Other Funding Source:
 Metropolitan Water District \$67,530 received


Athletic Field Phase I, Corsair Field

Project Description:
 Renovation of the Corsair Field, stadium lighting and sound system

Status:
 Completed, 2009

Architect:
 CO Architects

Contractor:
 Byrom Davey, Inc.

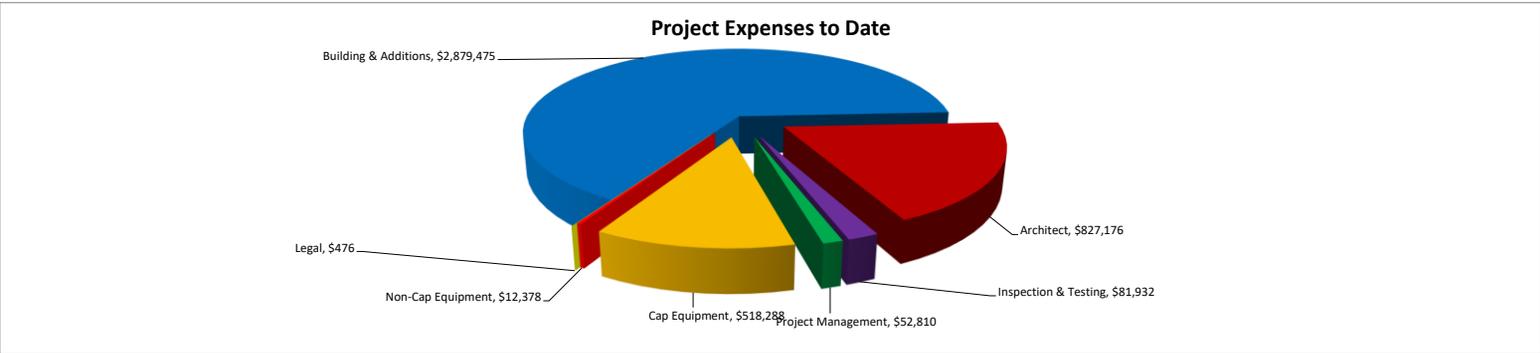

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE S EXPENDITURES
 FUND 42.3
 As of December 31, 2020

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals	
S7100038																				
Athletic Field Phase I, John Adams (1A)																				
Legal		\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$75
Building & Additions		\$0	\$0	\$0	\$16,556	\$1,395,261	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	\$0	\$49,984	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$56,066
Project Management		\$0	\$0	\$0	\$10,921	\$45,170	\$38	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$56,128
Cap Equipment		\$0	\$0	\$0	\$0	\$1,290,672	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,290,672
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$11,334	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,334
Total		\$0	\$8,681	\$97,148	\$39,701	\$2,824,239	\$38	\$0	\$0	\$0	\$2,969,807									
Project Budget	\$2,969,807																			
Less Other Funding	\$0																			
Net	\$2,969,807																			
Actual Measure S Expenditures	\$2,969,807																			
Running Balance	\$0																			


Athletic Field Phase I, John Adams

Project Description:
Renovation of John Adams Field and lighting

Status:
Completed, 2008

Architect:
Caldwell Architects

Contractor:
Byrom Davey, Inc.

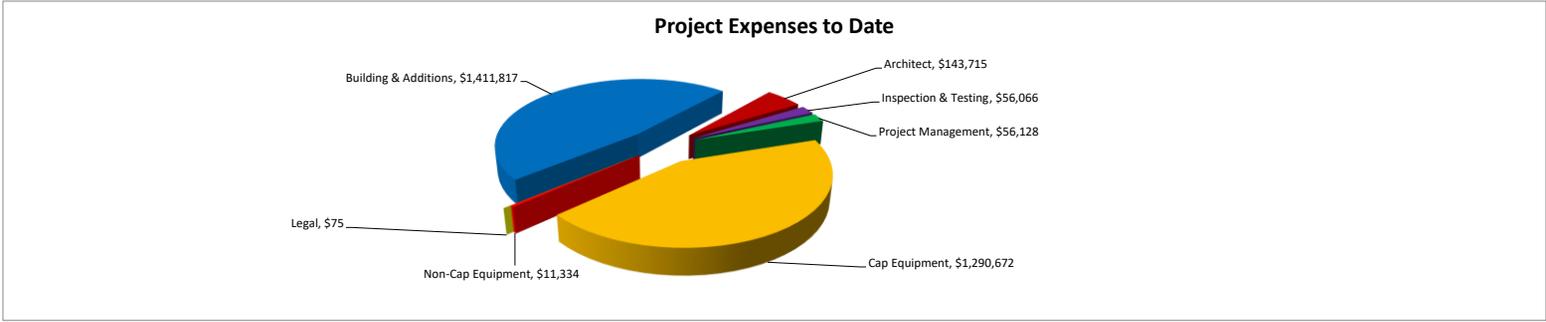

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE S EXPENDITURES
 FUND 42.3
 As of December 31, 2020

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals
S7100012																			
Performing Arts Center (2)																			
Consultants		\$0	\$0	\$0	\$121,790	\$76,639	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$198,429
Other Contract Services		\$0	\$0	\$4,269	\$0	\$22,729	\$22	\$68	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,088
Supplies		\$0	\$0	\$0	\$14,565	\$5,810	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,375
Legal		\$0	\$0	\$34,329	\$275,667	\$492,731	\$15,629	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$818,356
Advertising		\$0	\$0	\$0	\$320	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$320
Building & Additions		\$7,784,151	\$10,292,986	\$8,930,813	\$2,991,903	\$1,629,990	\$50,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$31,679,843
Architect		\$0	\$811,312	\$182,457	\$412,309	\$121,588	\$108	\$1,962	\$0	\$0	\$87,054	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,616,790
Engineering		\$0	\$3,600	\$5,250	\$1,500	\$9,650	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,000
Inspection & Testing		\$104,308	\$722,685	\$411,193	\$210,381	\$22,256	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,470,823
Project Management		\$31,984	\$155,732	\$248,876	\$263,690	\$47,915	\$3,244	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$751,441
Cap Equipment		\$0	\$0	\$130,218	\$292,565	\$342,693	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$765,476
Non-Cap Equipment		\$0	\$0	\$15,124	\$93,106	\$220,455	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$328,685
Total		\$7,920,443	\$11,986,315	\$9,962,528	\$4,677,797	\$2,992,455	\$69,003	\$2,030	\$0	\$0	\$87,054	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$37,697,625
Project Budget	\$40,690,201	Received																	
Less Other Funding*	\$2,992,576	\$2,992,576																	
Net	\$37,697,625																		
Actual Measure S Expenditures	\$37,697,625																		
Running Balance	\$0																		

* Other Funding Source:
 Madison Project Foundation \$2,992,576 received


Performing Arts Center

Project Description:
 Construction of a state-of-the-art 499 seat performing arts theater

Status:
 Completed, 2008

Architect:
 Renzo Zecchetto

Contractor:
 FTR International

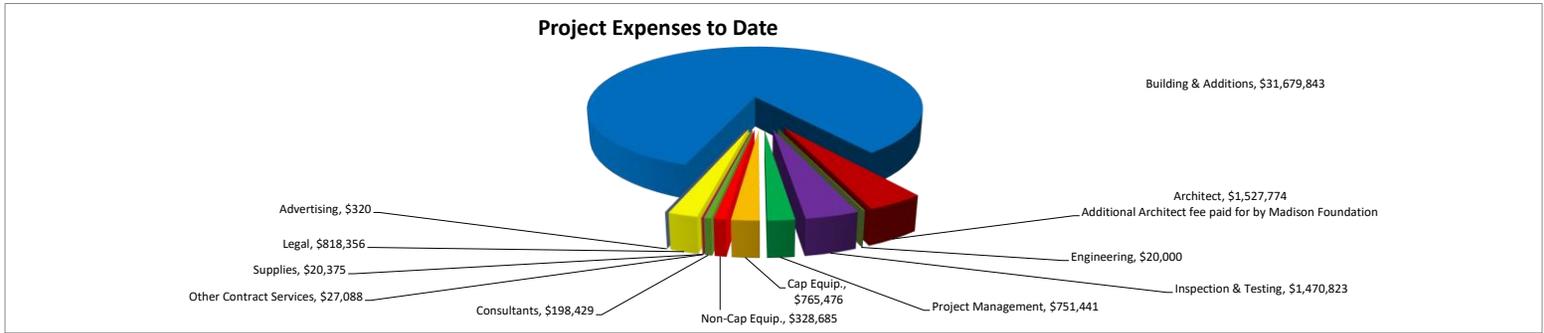

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE S EXPENDITURES
 FUND 42.3
 As of December 31, 2020

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals
S7100033, S7100144, S7100060																			
Replacement Health/PE/Fitness Building (4)																			
Supplies	\$4,809	\$288	\$0	\$0	\$0	\$163	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,260
Legal	\$0	\$0	\$0	\$0	\$1,413	\$75	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,488
Other Contract Services	\$1,634	\$25,934	\$0	\$0	\$253	\$165	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,985
Repair Facility	\$0	\$4,861	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,861
Building & Additions	\$0	\$0	\$0	\$0	\$112,410	\$526,552	\$0	\$0	\$0	\$0	\$6,037,080	\$4,775,714	\$0	\$0	\$0	\$0	\$0	\$0	\$11,451,757
Architect	\$0	\$0	\$0	\$0	\$0	\$41,044	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$41,044
Inspection & Testing	\$0	\$0	\$0	\$0	\$6,518	\$14,363	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,881
Project Management	\$0	\$0	\$0	\$0	\$9,070	\$23,425	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$32,495
Cap Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$17,613	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$17,613
Total	\$6,443	\$31,083	\$0	\$0	\$129,663	\$605,787	\$17,613	\$0	\$0	\$0	\$6,037,080	\$4,775,714	\$0	\$0	\$0	\$0	\$0	\$0	\$11,603,383
Project Budget	\$58,272,030																		
Less Other Funding*	\$46,668,647																		
Net	\$11,603,383																		
Actual Measure S Expenditures	\$11,603,383																		
Running Balance	\$0																		
* Other Funding Source: Measure AA \$46,459,800 allocated SCE \$190,847.28, Gas Co. \$18,000 received																			
S7100045																			
Early Childhood Development/Childcare (5)																			
Supplies	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$294	\$0	\$0	\$0	\$294
Consultants	\$0	\$0	\$0	\$9,200	\$0	\$0	\$0	\$0	\$0	\$4,800	\$12,930	\$14,078	\$1,388	\$0	\$0	\$0	\$0	\$0	\$42,395
Legal	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,690	\$6,905	\$0	\$0	\$0	\$0	\$0	\$8,595
Building & Additions	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$242	\$747,457	\$5,197,194	\$182,301	\$0	\$0	\$6,127,193
Architect	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$966	\$51,792	\$142,428	\$142,968	\$476,827	\$78,408	\$67,918	\$329,152	\$0	\$0	\$0	\$1,290,458
Engineering	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,888	\$0	\$0	\$0	\$3,888
Inspection & Testing	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$37,796	\$7,475	\$823	\$2,323	\$0	\$4,085	\$296,806	\$2,256	\$0	\$0	\$351,564
Project Management	\$0	\$0	\$0	\$0	\$0	\$0	\$1,246	\$21,980	\$58,247	\$33,435	\$8,803	\$3,118	\$0	\$307,493	\$599,950	\$0	\$0	\$0	\$1,034,270
Total	\$0	\$0	\$0	\$9,200	\$0	\$0	\$1,246	\$22,946	\$152,635	\$196,268	\$166,670	\$485,344	\$85,555	\$1,127,247	\$6,426,989	\$184,557	\$0	\$0	\$8,858,656
Project Budget	\$30,925,771	Received																	
Less Other Funding*	\$22,067,115	\$4,441,066																	
Net	\$8,858,656																		
Actual Measure S Expenditures	\$8,858,656																		
Running Balance	\$0																		
* Other Funding Source: City of Santa Monica \$6,661,598 committed Measure V \$15,405,517 allocated																			
S7100077, S7100015																			
Malibu Site Acquisition and Facilities (6)																			
Consultants	\$0	\$0	\$0	\$0	\$30,000	\$0	\$0	\$72,157	\$68,109	\$30,342	\$66,277	\$60,262	\$3,406	\$17	\$0	\$0	\$0	\$0	\$330,570
Legal	\$0	\$27,722	\$16,787	\$6,159	\$504	\$0	\$0	\$0	\$0	\$1,360	\$78,851	\$40,114	\$7,353	\$6,324	\$0	\$0	\$0	\$0	\$185,174
Other Contract Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,092	\$0	\$0	\$1,820	\$0	\$0	\$0	\$115,267	\$0	\$0	\$0	\$119,178
Building & Additions	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$536	\$0	\$0	\$0	\$2,019,660	\$3,136,052	\$2,002,677	\$0	\$0	\$7,158,925
Architect	\$0	\$0	\$0	\$0	\$0	\$0	\$966	\$257,584	\$732,891	\$173,610	\$34,753	\$151,772	\$341,307	\$331,426	\$101,080	\$0	\$0	\$0	\$2,125,390
Engineering	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$785	\$562	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,346
Inspection & Testing	\$4,388	\$3,750	\$141,462	\$0	\$0	\$0	\$0	\$98,022	\$15,575	\$22,939	\$10,960	\$0	\$0	\$39,460	\$322,234	\$60,231	\$0	\$0	\$719,020
Project Management	\$0	\$0	\$220	\$0	\$0	\$0	\$2,886	\$55,064	\$53,185	\$47,778	\$118,144	\$97,856	\$46,400	\$431,268	\$747,160	\$485,580	\$0	\$0	\$2,085,539
Storm/Waste Water Treatment Center	\$0	\$2,500,000	\$0	\$0	\$2,500,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,000,000
Total	\$4,388	\$2,531,472	\$158,468	\$6,159	\$2,530,504	\$0	\$2,886	\$228,301	\$395,237	\$836,407	\$449,662	\$232,985	\$208,931	\$2,838,036	\$4,652,138	\$2,649,568	\$0	\$0	\$17,725,144
Project Budget	\$25,000,000																		
Less Other Funding*	\$0																		
Net	\$25,000,000																		
Actual Measure S Expenditures	\$17,725,144																		
Running Balance	\$7,274,856																		

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE S EXPENDITURES
 FUND 42.3
 As of December 31, 2020

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals	
S7100043, S7100066																				
Energy Efficiency Projects (7)																				
Legal		\$0	\$0	\$0	\$0	\$988	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$988
Building & Additions		\$0	\$0	\$0	\$0	\$106,921	\$355,294	-\$180,342	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$281,873
Engineering		\$0	\$0	\$0	\$10,500	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$10,500
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$10,500	\$107,910	\$355,294	-\$180,342	\$0	\$0	\$0	\$293,361								
Project Budget	\$510,683	Received																		
Less Other Funding*	\$217,322	\$217,322																		
Net	\$293,361	* Other Funding Source: SCE & The Gas Co. \$217,322 received																		
Actual Measure S Expenditures	\$293,361																			
Running Balance	\$0																			

S7100091, S7100092, S7100147																					
Satellite Campus Parking Facilities and Roadway Improvements (8)																					
Legal		\$0	\$0	\$0	\$300	\$175	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$475
Other Contract Services		\$0	\$0	\$0	\$300	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$300
Advertising		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$278,178	\$1,860,152	\$449,543	\$37,777	\$0	\$0	\$0	\$64	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,625,714
Architect		\$0	\$0	\$324,919	\$324,864	\$136,911	\$34,490	\$1,397	\$2,289	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$824,871
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$30,896	\$5,470	\$12,165	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$48,531
Inspection & Testing		\$0	\$0	\$0	\$31,100	\$185,947	\$28,218	\$360	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$245,626
Project Management		\$0	\$0	\$0	\$18,288	\$64,880	\$31,137	\$8,659	\$0	\$2,569	\$10,730	\$6,046	\$535	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$142,844
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$3,387	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,387
Total		\$0	\$0	\$324,919	\$653,031	\$2,248,065	\$546,775	\$48,194	\$2,289	\$2,569	\$41,626	\$11,580	\$12,700	\$0	\$3,891,747						
Project Budget	\$7,022,417																				
Less Other Funding	\$3,130,670																				
Net	\$3,891,747	* Other Funding Source: Measure AA \$2,130,670, Measure V \$1,000,000 allocated																			
Actual Measure S Expenditures	\$3,891,747																				
Running Balance	\$0																				

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE S EXPENDITURES
 FUND 42.3
 As of December 31, 2020

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals
S7100142																			
Parking Garage and Grounds - Student Services (9)																			
Supplies	\$0	\$0	\$0	\$0	\$0	\$1,745	\$0	\$0	\$648	\$0	\$0	\$813	\$0	\$0	\$0	\$0	\$0	\$0	\$3,206
Consultants	\$0	\$0	\$0	\$0	\$0	\$20,700	\$0	\$0	\$0	\$0	\$0	\$0	\$1,740	\$0	\$0	\$0	\$0	\$0	\$22,440
Legal	\$0	\$0	\$0	\$0	\$0	\$2,154	\$17,486	\$4,800	\$2,257	\$17,221	\$0	\$3,570	\$0	\$0	\$0	\$0	\$0	\$0	\$47,488
Other Contract Services	\$0	\$0	\$0	\$0	\$0	\$1,508	\$10,952	\$1,986	\$46	\$0	\$12,083	\$5,034	\$0	\$0	\$0	\$0	\$0	\$0	\$31,608
Site Improvement	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,086	\$0	\$1,308	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,394
Building & Additions	\$0	\$0	\$0	\$0	\$0	\$2,555,940	\$5,925,152	\$78,717	\$77,320	\$5,509	\$715	\$0	\$3,721	\$11,308,792	\$16,249,515	\$0	\$0	\$0	\$36,205,381
Architect	\$0	\$0	\$0	\$2,266,766	\$2,674,054	\$0	\$37,111	\$75,163	\$0	\$0	\$0	\$0	\$0	\$0	\$287,176	\$0	\$0	\$0	\$5,340,270
Engineering	\$0	\$0	\$0	\$0	\$4,813	\$38,330	\$42,968	\$50,952	\$9,735	\$0	\$0	\$0	\$0	\$0	\$49,171	\$0	\$0	\$0	\$195,968
Inspection & Testing	\$0	\$0	\$0	\$0	\$0	\$131,009	\$161,847	\$54,069	\$32,306	\$30,909	\$4,123	\$22,296	\$38,186	\$516,217	\$851,397	\$0	\$0	\$0	\$1,842,359
Project Management	\$0	\$0	\$0	\$0	\$0	\$158,766	\$373,559	\$184,088	\$92,118	\$224,994	\$59,525	\$29,714	\$50,380	\$285,057	\$420,233	\$0	\$0	\$0	\$1,878,433
Cap Equipment	\$0	\$0	\$0	\$0	\$0	\$14,393	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14,393
Non-Cap Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,381	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,381
Total	\$0	\$0	\$0	\$0	\$2,266,766	\$5,550,689	\$6,541,719	\$403,737	\$342,192	\$289,454	\$76,445	\$62,735	\$94,027	\$12,110,066	\$17,857,492	\$0	\$0	\$0	\$45,595,322
Project Budget	\$130,224,164																		
Less Other Funding*	\$84,628,842																		
Net	\$45,595,322																		
Actual Measure S Expenditures	\$45,595,322																		
Running Balance	\$0																		

* Other Funding Source:
 State of California \$1,321,000 received
 Measure U \$21,131,135, Measure AA \$6,870,490, Measure V \$33,624,909 allocated
 Measure U, S & AA interests \$21,681,308 allocated

Parking Garage and Grounds - Student Services


Project Description:
 Consolidates various student services departments and college administration in a single complex at the front of the campus

Facility Size:
 110,000 sq/ft & 500 cars underground parking structure

Status:
 Phase 1 completed
 Phase 2 In construction

Architect:
 Steinberg Architects, Morris Architects

Contractor:
 Minaco, Bernards

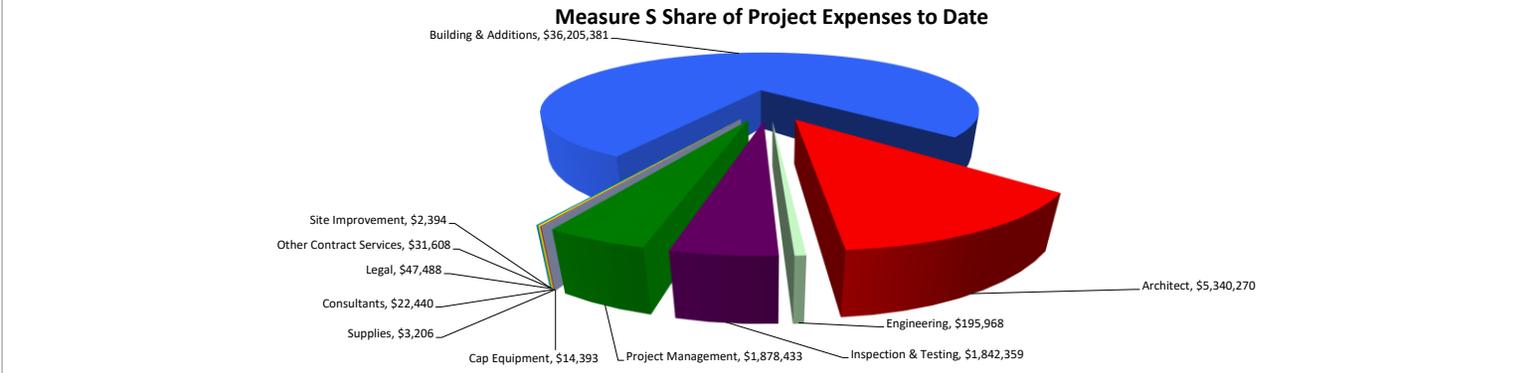


SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE S EXPENDITURES
 FUND 42.3
 As of December 31, 2020

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals	
S7100044																				
Pico Promenade Improvements (10)																				
Building & Additions		\$0	\$0	\$0	\$690	\$883,401	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$884,091
Architect		\$0	\$0	\$0	\$69,190	\$28,540	\$864	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$98,595
Inspection & Testing		\$0	\$0	\$0	\$0	\$7,591	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,591
Project Management		\$0	\$0	\$0	\$2,185	\$25,548	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,733
Total		\$0	\$0	\$0	\$72,066	\$945,080	\$864	\$0	\$0	\$0	\$1,018,009									
Project Budget	\$1,018,009																			
Less Other Funding	\$0																			
Net	\$1,018,009																			
Actual Measure S Expenditures	\$1,018,009																			
Running Balance	\$0																			
S7100044																				
Master Planning (11)																				
Consultants		\$0	\$0	\$0	\$0	\$0	\$441,549	\$13,320	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$454,869
Printing		\$0	\$0	\$0	\$0	\$0	\$4,157	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,157
Advertising		\$0	\$0	\$0	\$0	\$0	\$3,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,000
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$442	\$200	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$642
Architect		\$0	\$0	\$0	\$0	\$0	\$192,358	\$24,736	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$217,094
Project Management		\$0	\$0	\$0	\$0	\$0	\$16,638	\$9,341	\$0	\$0	\$7,845	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$33,824
Filing Fees		\$0	\$0	\$0	\$0	\$0	\$0	\$2,842	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,842
Total		\$0	\$0	\$0	\$0	\$0	\$658,143	\$50,439	\$0	\$0	\$7,845	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$716,428
Project Budget	\$716,428																			
Less Other Funding	\$0																			
Net	\$716,428																			
Actual Measure S Expenditures	\$716,428																			
Running Balance	\$0																			
S7100048																				
Other Bond Related Expenses (12)																				
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,971	\$2,524	\$6,239	\$1,354	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$13,089
Lease/Rental		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,142	\$15,099	\$15,285	\$14,809	\$13,418	\$13,120	\$16,611	\$17,281	\$23,757	\$0	\$0	\$140,522
Supplies		\$0	\$0	\$0	\$0	\$0	\$3,638	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,638
Legal		\$0	\$0	\$0	\$0	\$0	\$8,917	\$15,649	\$13,401	\$450	\$503	\$38,130	\$9,186	\$0	\$0	\$0	\$0	\$0	\$0	\$86,236
Software License		\$0	\$0	\$0	\$0	\$0	\$0	\$1,997	\$0	\$3,565	\$0	\$4,200	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$9,762
Advertising		\$0	\$0	\$0	\$0	\$0	\$2,278	\$0	\$0	\$0	\$0	\$0	\$0	\$864	\$0	\$0	\$0	\$0	\$0	\$3,142
Other Contract Services		\$0	\$0	\$0	\$0	\$1,800	\$17,206	\$23,558	\$19,208	\$15,816	\$13,627	\$13,952	\$12,963	\$11,760	\$18,900	\$15,225	\$0	\$0	\$0	\$164,014
Moving Services		\$0	\$0	\$0	\$0	\$0	\$400	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$400
Project Management		\$0	\$0	\$0	\$0	\$0	\$17,747	\$13,179	\$11,963	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$42,888
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$10,086	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$10,086
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$2,860	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,860
Total		\$0	\$0	\$0	\$0	\$1,800	\$50,185	\$67,328	\$55,713	\$37,901	\$31,939	\$77,330	\$36,921	\$25,744	\$35,511	\$32,506	\$23,757	\$0	\$0	\$476,636
Project Budget	\$609,204																			
Less Other Funding	\$0																			
Net	\$609,204																			
Actual Measure S Expenditures	\$476,636																			
Running Balance	\$132,568																			

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE S EXPENDITURES
 FUND 42.3
 As of December 31, 2020

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals
S7100049																			
Adv Architecture Related Exp for AA (13)																			
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Budget	\$0																		
Less Other Funding	\$0																		
Net	\$0																		
Actual Measure S Expenditures	\$0																		
Running Balance	\$0																		
S7100057																			
Real Property Acquisition (14)																			
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$18,721	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$6,336	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$20,540	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$45,597	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Budget	\$45,597																		
Less Other Funding	\$0																		
Net	\$45,597																		
Actual Measure S Expenditures	\$45,597																		
Running Balance	\$0																		
S7100072																			
Campus Signage (15)																			
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$303	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$32,225	\$23,725	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$187	\$0	\$836	\$0	\$0	\$0	\$1,051	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$638	\$0	\$0	\$1,440	\$1,325	\$416,937	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$22,953	\$0	\$0	\$8,260	\$8,388	\$28,622	\$165	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$156,258	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,402	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$32,225	\$204,064	\$0	\$836	\$9,700	\$9,712	\$445,559	\$4,618	\$0	\$0	\$0	\$0	\$0
Project Budget	\$706,713																		
Less Other Funding	\$0																		
Net	\$706,713																		
Actual Measure S Expenditures	\$706,713																		
Running Balance	\$0																		
S																			
Cost of Issuance (16)																			
Cost of Issuance		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$119,470	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$119,470	\$0	\$0	\$0	\$0	\$0
Project Budget	\$119,470																		
Less Other Funding	\$0																		
Net	\$119,470																		
Actual Measure AA Expenditures	\$119,470																		
Running Balance	\$0																		
Grand Total		\$7,958,606	\$14,601,366	\$10,740,621	\$8,321,918	\$20,819,624	\$8,933,245	\$617,492	\$651,441	\$878,632	\$1,287,285	\$6,814,769	\$6,083,251	\$12,554,384	\$21,858,285	\$11,111,633	\$2,857,882	\$0	\$136,090,434

SANTA MONICA COMMUNITY COLLEGE DISTRICT
 Measure AA Bond Budget
 As of October 1, 2010

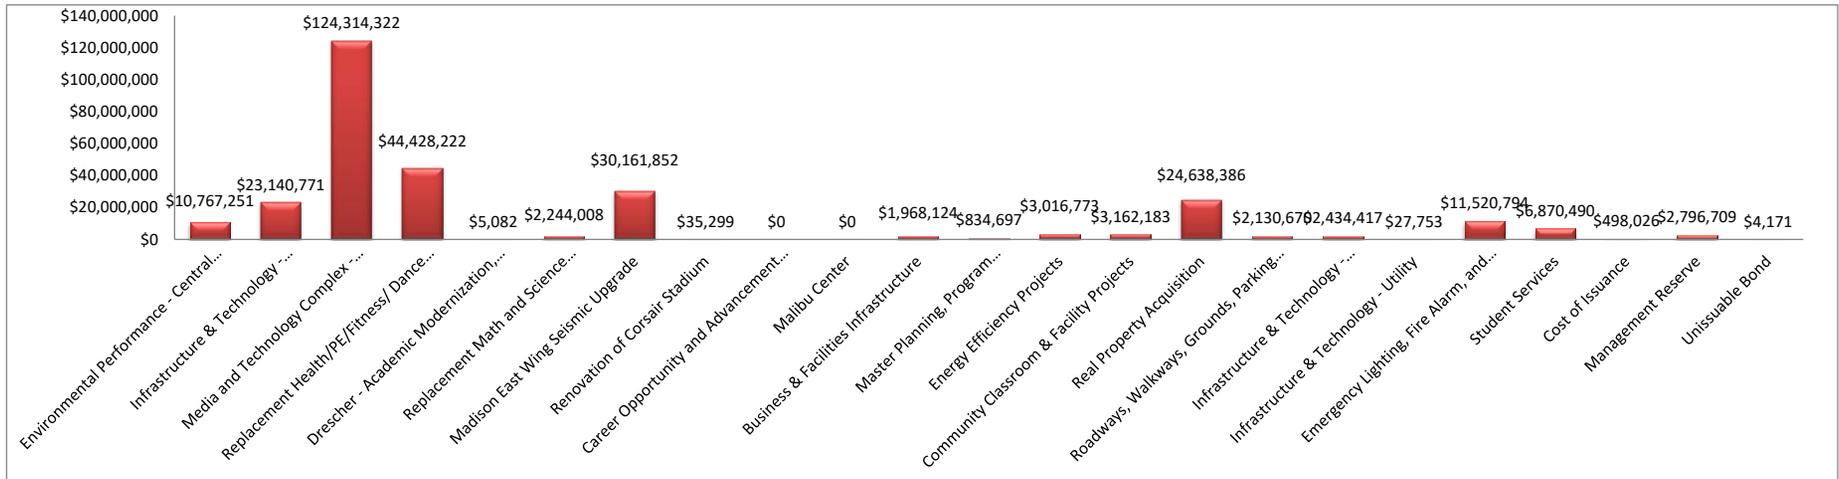

SANTA MONICA COMMUNITY COLLEGE DISTRICT
Measure AA Bond Budget History
as of December 31, 2020

	Project Name	Completion	Preliminary Measure AA Budget	Measure AA Budget as of 9/30/20	Measure AA Budget as of 12/31/20	Variance	Measure AA Remaining as of 12/31/20
101	Environmental Performance - Central Plant Connections	Completed	\$12,034,042	\$10,767,251	\$10,767,251	\$0	\$0
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$13,287,218	\$23,140,771	\$23,140,771	\$0	\$0
103	Media and Technology Complex - Academy Site	Completed	\$57,480,824	\$124,314,322	\$124,314,322	\$0	\$218,315
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$29,232,317	\$44,428,222	\$44,428,222	\$0	\$0
105	Drescher - Academic Modernization, Bookstore, Pico Promenade II	Deferred	\$34,026,480	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	January 2024	\$68,259,000	\$2,244,008	\$2,244,008	\$0	\$239,824
107	Madison East Wing Seismic Upgrade	Completed	\$6,146,000	\$30,161,852	\$30,161,852	\$0	\$0
108	Renovation of Corsair Stadium	Completed	\$11,203,000	\$35,299	\$35,299	\$0	\$0
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$32,384,000	\$0	\$0	\$0	\$0
110	Malibu Center	August 2022	\$6,069,031	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$17,506,952	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	On-Going	\$2,000,000	\$834,697	\$834,697	\$0	\$0
113	Energy Efficiency Projects	Completed	\$5,371,136	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$0	\$24,638,386	\$24,638,386	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$0	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	On-Going	\$0	\$11,520,794	\$11,520,794	\$0	\$5,180
120	Student Services	Completed	\$0	\$6,870,490	\$6,870,490	\$0	\$0
121	Cost of Issuance	Completed	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$0	\$2,796,709	\$2,796,709	\$0	\$2,796,709
123	Unissuable Bond	Completed	\$0	\$4,171	\$4,171	\$0	\$4,171
	Project Totals		\$295,000,000	\$295,000,000	\$295,000,000	\$0	\$3,264,199

SANTA MONICA COMMUNITY COLLEGE DISTRICT
 MEASURE AA EXPENDITURES
 FUND 42.4
 As of December 31, 2020

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals
AA 7100062														
Environmental Performance - Central Plant Connections (101)														
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$125
Other Contract Services		\$0	\$0	\$49,837	\$16,239	\$0	\$0	\$0	\$0	\$9,920	\$0	\$0	\$0	\$75,996
Consultants		\$0	\$0	\$0	\$0	\$28	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$28
Building & Additions		\$0	\$0	\$0	\$361	\$729	\$640	\$1,328,592	\$6,934,044	\$446,861	\$0	\$0	\$0	\$8,711,229
Architect		\$0	\$385	\$148,311	\$176,897	\$36,256	\$0	\$0	\$0	\$0	\$15,699	\$0	\$0	\$377,547
Engineering		\$48,500	\$0	\$4,000	\$0	\$152,010	\$39,638	\$66,918	\$138,887	\$62,883	\$0	\$0	\$0	\$512,836
Inspection & Testing		\$0	\$0	\$7,688	\$0	\$0	\$0	\$7,310	\$137,150	\$4,382	\$0	\$0	\$0	\$156,529
Project Management		\$0	\$17,263	\$55,116	\$48,685	\$61,908	\$19,313	\$104,575	\$526,072	\$99,840	\$190	\$0	\$0	\$932,961
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$48,500	\$17,648	\$264,951	\$242,307	\$250,931	\$59,591	\$1,507,396	\$7,736,152	\$623,886	\$15,889	\$0	\$0	\$10,767,251
Project Budget	\$10,767,251													
Less Other Funding	\$0													
Net	\$10,767,251													
Actual Measure AA Expenditures	\$10,767,251													
Running Balance	\$0													

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE AA EXPENDITURES
FUND 42.4
As of December 31, 2020

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals
AA 7100063														
Infrastructure & Technology - IT Relocation (102)														
Supplies		\$0	\$0	\$965	\$8,442	\$3,137	\$2,600	\$0	\$0	\$0	\$0	\$0	\$0	\$15,144
Consultants		\$0	\$0	\$0	\$0	\$408	\$0	\$7,800	\$0	\$0	\$0	\$0	\$0	\$8,208
Maintenance Contract		\$0	\$0	\$0	\$0	\$107,390	\$0	\$77,074	\$79	\$0	\$0	\$0	\$0	\$184,543
Legal		\$0	\$0	\$0	\$1,363	\$50	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,413
Printing		\$0	\$0	\$0	\$0	\$1,624	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,624
Postage		\$0	\$0	\$0	\$0	\$1,567	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,567
Other Contract Services		\$0	\$0	\$2,163	\$15,259	\$23,356	\$0	\$19,050	\$4,500	\$0	\$0	\$0	\$0	\$64,328
Moving		\$0	\$0	\$0	\$577	\$266	\$27,655	\$22,618	\$0	\$0	\$0	\$0	\$0	\$51,116
Site Improvement		\$0	\$0	\$0	\$24	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$24
Building & Additions		\$0	\$0	\$0	\$1,767,083	\$9,667,362	\$4,288,987	\$1,203,916	\$165,229	-\$19,798	\$0	\$0	\$0	\$17,072,780
Architect		\$105,049	\$482,261	\$505,580	\$183,181	\$287,201	\$236,860	\$120,091	\$0	\$0	\$0	\$0	\$0	\$1,920,223
Engineering		\$0	\$0	\$10,037	\$11,065	\$17,147	\$19,512	\$25,994	\$1,956	\$0	\$0	\$0	\$0	\$85,712
Inspection & Testing		\$10,291	\$8,793	\$21,449	\$137,523	\$499,982	\$200,262	\$568	\$0	\$0	\$0	\$0	\$0	\$878,868
Project Management		\$33,460	\$76,290	\$84,991	\$331,754	\$431,730	\$297,951	\$22,978	\$1,500	\$0	\$0	\$0	\$0	\$1,280,653
Cap Equipment		\$0	\$0	\$0	\$29,422	\$645,830	-\$29,090	\$589,604	\$9,811	\$0	\$0	\$0	\$0	\$1,245,576
Non-Cap Equipment		\$0	\$0	\$0	\$18,344	\$10,852	\$277,219	\$1,891	\$20,689	\$0	\$0	\$0	\$0	\$328,994
Total			\$148,800	\$567,344	\$625,185	\$2,504,035	\$11,697,901	\$5,321,956	\$2,091,584	\$203,764	-\$19,798	\$0	\$0	\$23,140,771
Project Budget	\$23,160,569	Received												
Less Other Funding	\$19,798	\$19,798												
Net	\$23,140,771													
Actual Measure AA Expenditures	\$23,140,771													
Running Balance	\$0													

*** Other Funding Source:**
1) Edison \$19,798 received

Infrastructure & Technology - IT Relocation


Project Description:
Relocation of IT/Telecom Departments, and renovation of Media Center

Facility Size:
9,230 sq/ft

Status:
Completed

Architect:
Morris Architects

Contractor:
Minco, Bernards Brothers

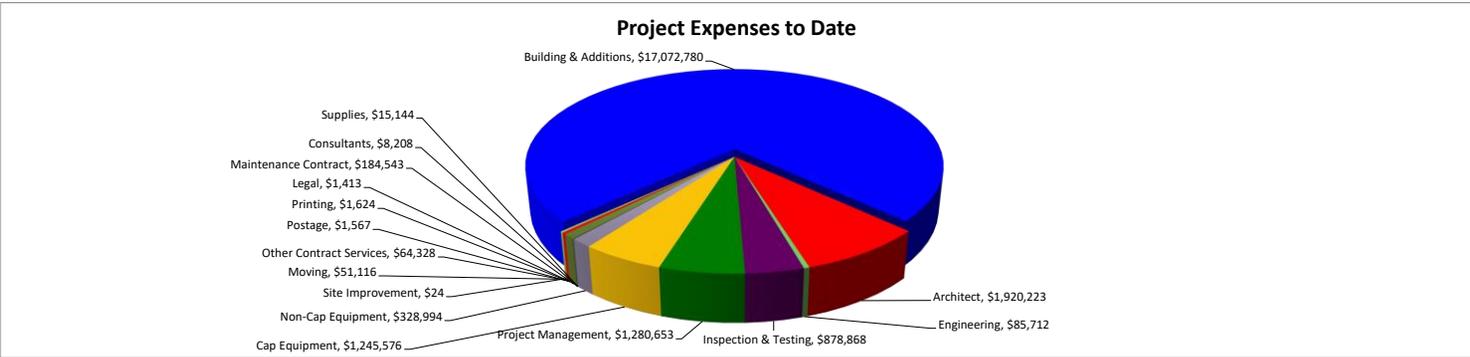

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE AA EXPENDITURES
FUND 42.4
As of December 31, 2020

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals
AA 7100060														
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)														
Consultants		\$0	\$0	\$0	\$14	\$62	\$2,304	\$184	\$0	\$0	\$0	\$0	\$0	\$2,564
Supplies		\$0	\$0	\$0	\$0	\$7,089	\$195	\$484	\$20,947	\$0	\$0	\$0	\$0	\$28,715
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$663	\$80	\$0	\$0	\$0	\$0	\$742
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,209	\$0	\$0	\$0	\$0	\$1,209
Site Improvement		\$0	\$0	\$0	\$0	\$0	\$559	\$440	\$575	\$0	\$0	\$0	\$0	\$1,574
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$0	\$2,165	\$0	\$0	\$0	\$0	\$0	\$2,165
Postage		\$0	\$0	\$0	\$0	\$0	\$1,505	\$0	\$0	\$0	\$0	\$0	\$0	\$1,505
Other Contract Services		\$120	\$38	\$112	\$32,634	\$0	\$1,019	\$581	\$0	\$2,644	\$0	\$0	\$0	\$37,147
Building & Additions		\$0	\$0	\$0	\$817	\$4,188	\$1,623	\$13,783,023	\$14,880,829	\$5,315,393	-\$148,184	\$0	\$0	\$33,837,688
Architect		\$256,076	\$1,568,564	\$1,790,207	\$518,973	\$177,583	\$364,853	\$585,900	\$373,345	\$210,312	\$108,264	\$0	\$0	\$5,954,078
Engineering		\$0	\$8,507	\$31,650	\$7,871	\$6,529	\$9,276	\$76,712	\$51,025	\$11,318	\$2,900	\$0	\$0	\$205,788
Inspection & Testing		\$36,892	\$490	\$21,150	\$1,285	\$360	\$133,756	\$846,765	\$358,724	\$60,826	\$1,330	\$0	\$0	\$1,461,579
Project Management		\$34,968	\$113,379	\$118,783	\$94,768	\$108,528	\$463,418	\$564,240	\$487,065	\$312,539	\$20,242	\$0	\$0	\$2,317,928
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$164,793	\$68,425	\$0	\$0	\$0	\$233,218
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$9,015	\$206,229	\$127,078	\$0	\$0	\$0	\$342,322
Total		\$328,056	\$1,690,978	\$1,961,901	\$656,362	\$304,338	\$989,689	\$15,858,991	\$16,544,820	\$6,108,535	-\$15,448	\$0	\$0	\$44,428,222
Project Budget	\$56,240,452													
Less Other Funding*	\$11,812,230													
Net	\$44,428,222													
Actual Measure AA Expenditures	\$44,428,222													
Running Balance	\$0													

* Other Funding Source:
1) Measure S - \$11,603,383 allocated
2) SCE \$190,847.28, Gas Co. \$18,000 received

Repl. Health/PE/Fitness/Dance Building with Central Plant


Project Description:
Replacement of locker rooms, fitness center, dance studios, and new central plant

Facility Size:
62,000 sq/ft

Status:
In construction

Architect:
Gensler Architects

Contractor:
Bernards Brothers

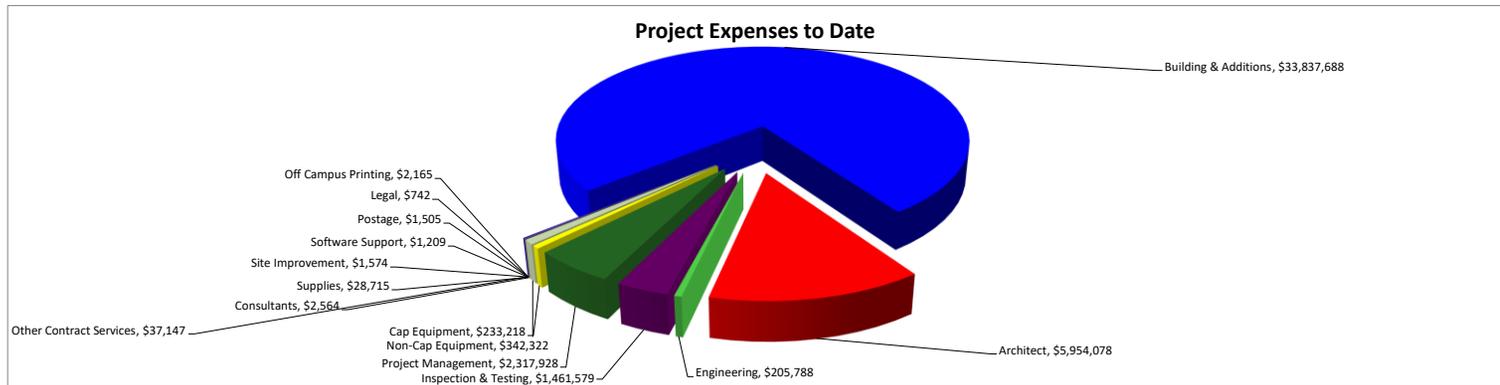

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE AA EXPENDITURES
FUND 42.4
As of December 31, 2020

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals
AA 7100065														
Drescher - Academic Modernization, Bookstore, Pico Promenade (105)														
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Site Acquisition		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,082
Total		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,082
Project Budget	\$13,005,082													
Less Other Funding	\$13,000,000													
Net	\$5,082													
Actual Measure AA Expenditures	\$5,082													
Running Balance	\$0													
* Other Funding Source: 1) Measure V 13,000,000 allocated														
AA 7100090														
Replacement Math and Science Extension Building (106)														
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,525	\$0	\$0	\$0	\$1,525
Site Acquisition		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,796	\$0	\$0	\$0	\$4,796
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,787,824	-\$94,695	\$0	\$0	\$1,693,130
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$70,223	\$0	\$0	\$0	\$70,223
Project Management		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$800	\$228,760	\$0	\$0	\$0	\$234,510
Total		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$800	\$2,093,128	-\$94,695	\$0	\$0	\$2,004,184
Project Budget	\$124,958,336	Received												
Less Other Funding	\$122,714,328	\$2,584,000												
Net	\$2,244,008													
Actual Measure AA Expenditures	\$2,004,184													
Running Balance	\$239,824													
* Other Funding Source: 1) Measure U \$308,336 2) Measure V \$82,317,992 allocated 3) State of California \$40,088,000 allocated														

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE AA EXPENDITURES
FUND 42.4
As of December 31, 2020

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals
AA 7100047														
Madison East Wing Seismic Upgrade (107)														
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,197	\$0	\$0	\$0	\$0	\$6,197
Consultants		\$0	\$0	\$0	\$0	\$135	\$28	\$0	\$0	\$0	\$0	\$0	\$0	\$163
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$285	\$0	\$0	\$0	\$0	\$0	\$0	\$285
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$357	\$0	\$0	\$0	\$0	\$357
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,579	\$11,822	\$8,263	\$950	\$0	\$28,613
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$806	\$0	\$0	\$0	\$0	\$806
Other Contract Services		\$0	\$364	\$997	\$0	\$0	\$1,328	\$711	\$0	\$0	\$0	\$0	\$0	\$3,400
Building & Additions		\$0	\$656	\$312,643	\$0	\$4,248	\$6,030,371	\$8,829,626	\$4,949,223	\$3,967,591	\$0	\$0	\$0	\$24,094,358
Architect		\$76,073	\$398,050	\$550,589	\$65,444	\$57,480	\$199,100	\$404,764	\$122,764	\$103,824	\$0	\$0	\$0	\$1,978,088
Engineering		\$0	\$0	\$10,707	\$778	\$0	\$13,792	\$33,184	\$37,491	\$90	\$0	\$0	\$0	\$96,042
Inspection & Testing		\$0	\$19,848	\$16,752	\$3,036	\$5,851	\$676,323	\$405,443	\$112,876	\$4,703	\$0	\$0	\$0	\$1,244,832
Project Management		\$5,557	\$128,878	\$112,573	\$67,447	\$118,242	\$494,874	\$481,165	\$322,379	\$31,230	\$11,286	\$0	\$0	\$1,773,629
Cap Equipment		\$0	\$0	\$30,603	\$0	\$0	\$0	\$0	\$537,627	\$0	\$0	\$0	\$0	\$568,230
Non-Cap Equipment		\$0	\$0	\$71,827	\$9,788	\$0	\$0	\$0	\$285,236	\$0	\$0	\$0	\$0	\$366,851
Total		\$81,630	\$547,796	\$1,106,691	\$146,492	\$185,956	\$7,416,101	\$10,154,894	\$6,382,534	\$4,119,259	\$19,549	\$950	\$0	\$30,161,852
Project Budget	\$30,161,852													
Less Other Funding	\$0													
Net	\$30,161,852													
Actual Measure AA Expenditures	\$30,161,852													
Running Balance	\$0													

Madison East Wing Seismic Upgrade

Project Description:
Replacement of east wing with a new multipurpose room and additional classrooms


Facility Size:
20,838 sq/ft

Status:
In construction

Architect:
DLR Group WWCOT

Contractor:
Bernards Brothers

Project Expenses to Date

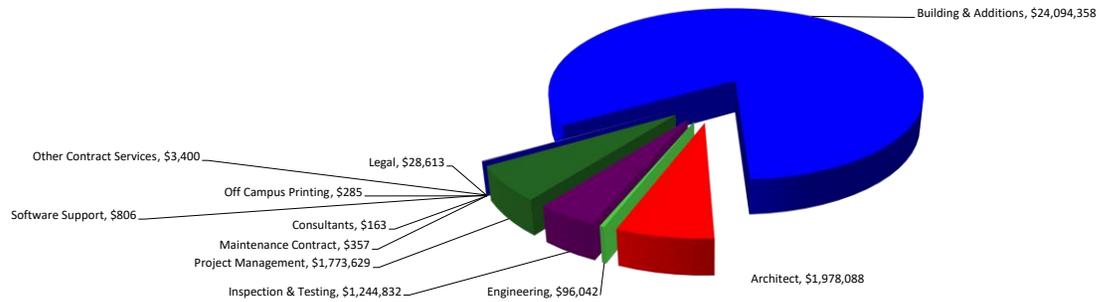

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE AA EXPENDITURES
FUND 42.4
As of December 31, 2020

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals
AA 7100068														
Renovation to Corsair Stadium (108)														
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$30,759	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$30,759
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$4,540	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,540
Total		\$0	\$35,299	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$35,299
Project Budget	\$35,299													
Less Other Funding	\$0													
Net	\$35,299													
Actual Measure AA Expenditures	\$35,299													
Running Balance	\$0													
AA 7100067, 7100152, 7100155, 7100157														
Business & Facilities Infrastructure (111)														
Supplies		\$0	\$0	\$0	\$1,493	\$4,840	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,333
Service Fee		\$0	\$0	\$0	\$12,885	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,885
Consultants		\$0	\$0	\$0	\$0	\$14	\$8	\$0	\$0	\$0	\$0	\$0	\$0	\$22
Maintenance Contract		\$0	\$0	\$0	\$0	\$1,366	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,366
Legal		\$0	\$0	\$75	\$0	\$0	\$0	\$1,105	\$0	\$0	\$0	\$0	\$0	\$1,180
Software License		\$0	\$0	\$0	\$0	\$375	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$375
Other Contract Services		\$0	\$6,289	\$6,988	\$750	\$0	\$2,209	\$0	\$0	\$0	\$0	\$0	\$0	\$16,236
Moving Services		\$0	\$0	\$0	\$395	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$395
Building & Additions		\$0	\$34,672	\$198,667	\$200,585	\$284,668	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$718,592
Architect		\$0	\$0	\$80,626	\$170,132	\$37,906	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$288,664
Engineering		\$0	\$0	\$0	\$3,705	\$9,735	\$6,840	\$0	\$0	\$0	\$0	\$0	\$0	\$20,280
Inspection & Testing		\$0	\$0	\$8,142	\$10,938	\$10,500	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$29,580
Project Management		\$0	\$3,073	\$154,904	\$87,291	\$139,821	\$3,571	\$0	\$0	\$0	\$0	\$0	\$0	\$388,659
Cap Equipment		\$0	\$0	\$0	\$35,892	\$80,090	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$115,982
Non-Cap Equipment		\$0	\$89,204	\$0	\$84,590	\$193,782	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$367,576
Total		\$0	\$133,238	\$449,401	\$608,656	\$763,095	\$12,628	\$1,105	\$0	\$0	\$0	\$0	\$0	\$1,968,124
Project Budget	\$1,968,124													
Less Other Funding	\$0													
Net	\$1,968,124													
Actual Measure AA Expenditures	\$1,968,124													
Running Balance	\$0													
AA 7100004														
Master Planning, Program Management, Overhead (112)														
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$139,302	\$187,927	\$245,329	\$1,270	\$0	\$0	\$573,828
Project Management		\$0	\$0	\$0	\$0	\$76,015	\$150	\$0	\$49,170	\$135,533	\$0	\$0	\$0	\$260,868
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$76,015	\$150	\$139,302	\$237,097	\$380,863	\$1,270	\$0	\$0	\$834,697
Project Budget	\$834,697													
Less Other Funding	\$0													
Net	\$834,697													
Actual Measure AA Expenditures	\$834,697													
Running Balance	\$0													

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE AA EXPENDITURES
FUND 42.4
As of December 31, 2020

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals
AA 7100058, 7100151, 7100156, 7100059														
Roadways, Walkways, Grounds, Parking Lots, and Garages (116)														
Supplies	\$0	\$0	\$0	\$0	\$0	\$4,616	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,616
Legal	\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$125
Consultants	\$0	\$0	\$0	\$48,090	\$5,018	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$53,108
Other Contract Services	\$218	\$770	\$122	\$25,249	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$26,358
Building & Additions	\$185,345	\$6,731	\$113,784	\$321,603	\$975,401	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,602,864
Architect	\$0	\$0	\$0	\$103,569	\$19,225	\$1,240	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$124,035
Engineering	\$0	\$0	\$0	\$1,095	\$1,445	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,540
Inspection & Testing	\$13,380	\$7,865	\$13,553	\$20,126	\$42,865	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$97,787
Project Management	\$24,404	\$12,439	\$21,945	\$54,095	\$104,943	\$1,411	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$219,237
Total		\$223,347	\$27,804	\$149,403	\$573,951	\$1,153,512	\$2,652	\$0	\$0	\$0	\$0	\$0	\$0	\$2,130,670
Project Budget	\$7,022,417													
Less Other Funding	\$4,891,747													
Net	\$2,130,670													
Actual Measure AA Expenditures	\$2,130,670													
Running Balance	\$0													
* Other Funding Source: 1) Measure S \$3,891,747 2) Measure V \$1,000,000 allocated														
AA 7100069														
Infrastructure & Technology - Technology (117)														
Software	\$0	\$0	\$0	\$0	\$0	\$218	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$218
Supplies	\$0	\$0	\$13,646	\$7,587	\$0	\$16,966	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$38,200
Maintenance Contract	\$0	\$9,472	\$46,300	\$210,581	\$18,944	\$42,415	\$9,472	\$0	\$0	\$0	\$0	\$0	\$0	\$337,186
Other Contract Services	\$0	\$0	\$0	\$0	\$0	\$49,589	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$49,589
Building & Additions	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment	\$0	\$207,423	\$33,063	\$576,294	\$0	\$1,145,668	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,962,449
Non-Cap Equipment	\$0	\$0	\$42,827	\$500	\$0	\$3,447	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$46,775
Total		\$0	\$216,896	\$135,838	\$794,963	\$18,944	\$1,258,304	\$9,472	\$0	\$0	\$0	\$0	\$0	\$2,434,417
Project Budget	\$2,434,417													
Less Other Funding	\$0													
Net	\$2,434,417													
Actual Measure AA Expenditures	\$2,434,417													
Running Balance	\$0													
AA 7100150														
Infrastructure & Technology - Utility (118)														
Software License	\$0	\$12,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,000
Legal	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing	\$0	\$4,979	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,979
Project Management	\$0	\$3,240	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,240
Cap Equipment	\$0	\$0	\$7,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,534
Non-Cap Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$20,219	\$7,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,753
Project Budget	\$27,753													
Less Other Funding	\$0													
Net	\$27,753													
Actual Measure AA Expenditures	\$27,753													
Running Balance	\$0													

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE AA EXPENDITURES
FUND 42.4
As of December 31, 2020

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20-21	Combined Totals
AA 7100153														
Emergency Lighting, Fire Alarm, and Security System (119)														
Supplies		\$0	\$0	\$0	\$0	\$2,348	\$0	\$0	\$2,671	\$0	\$0	\$0	\$0	\$5,020
Consultants/Legal		\$0	\$0	\$0	\$0	\$0	\$16	\$0	\$0	\$0	\$442	\$0	\$0	\$458
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$800	\$0	\$0	\$0	\$0	\$0	\$0	\$800
Maintenance Contract		\$0	\$0	\$648	\$0	\$39,700	\$0	\$2,700	\$0	\$0	\$0	\$0	\$0	\$43,048
Software Support		\$0	\$0	\$24,765	\$0	\$106,367	\$0	\$2,232	\$0	\$0	\$0	\$0	\$0	\$133,365
Other Contract Services		\$0	\$0	\$0	\$0	\$47,695	\$0	\$4,643	\$1,560	\$0	\$0	\$0	\$0	\$53,897
Building & Additions		\$0	\$0	\$0	\$0	\$110	\$2,648,866	\$4,129,145	\$1,308,230	\$763,170	\$26,375	\$79,172	\$0	\$8,955,068
Architect		\$0	\$0	\$0	\$0	\$0	\$18,925	\$0	\$0	\$5,047	\$0	\$0	\$0	\$23,972
Engineering		\$0	\$0	\$0	\$0	\$211,030	\$389,013	\$156,247	\$255,798	\$358,560	\$114,585	\$0	\$0	\$1,485,233
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$58,831	\$4,800	\$0	\$0	\$0	\$0	\$63,631
Project Management		\$0	\$0	\$0	\$0	\$51,008	\$52,044	\$79,285	\$16,500	\$49,738	\$240	\$0	\$0	\$248,814
Cap Equipment		\$0	\$0	\$0	\$0	\$89,415	\$0	\$5,871	\$0	\$0	\$0	\$0	\$0	\$95,286
Non-Cap Equipment		\$0	\$0	\$6,087	\$0	\$392,586	\$8,348	\$0	\$0	\$0	\$0	\$0	\$0	\$407,022
Total		\$0	\$0	\$31,500	\$0	\$940,259	\$3,118,012	\$4,438,953	\$1,589,560	\$1,176,515	\$141,642	\$79,172	\$0	\$11,515,614
Project Budget	\$11,520,794													
Less Other Funding	\$0													
Net	\$11,520,794													
Actual Measure AA Expenditures	\$11,515,614													
Running Balance	\$5,180													
AA 7100142														
Student Services (120)														
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,165,626	\$3,704,864	\$0	\$0	\$6,870,490
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,165,626	\$3,704,864	\$0	\$0	\$6,870,490
Project Budget	\$6,870,490													
Less Other Funding	\$0													
Net	\$6,870,490													
Actual Measure AA Expenditures	\$6,870,490													
Running Balance	\$0													
* Other Funding Source:														
1) State of California \$1,321,000 received														
2) Measure U \$21,131,135, Measure S \$45,595,322, Measure V \$33,624,909 allocated														
3) Measure U, S & AA interests \$21,681,308 allocated														
Cost of Issuance (121)														
Cost of Issuance		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$0	\$0	\$0	\$0	\$498,026
Total		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$0	\$0	\$0	\$0	\$498,026
Project Budget	\$498,026													
Less Other Funding	\$0													
Net	\$498,026													
Actual Measure AA Expenditures	\$498,026													
Running Balance	\$0													
Grand Total		\$4,900,734	\$10,935,584	\$17,864,407	\$13,113,759	\$30,388,248	\$39,049,510	\$60,741,756	\$57,313,878	\$52,193,046	\$4,326,286	\$908,418	\$12,887	\$291,748,512


Measure AA Interest	18/19 Final
Parking Garage and Grounds - Student Services (9)	
Site Improvement	\$0
Building & Additions	\$5,192,948
Architect	\$0
Engineering	\$0
Inspection & Testing	\$0
Project Management	\$0
Total	\$5,192,948
Project Budget	\$5,192,948
Actual Measure S Interest Expenditures	\$5,192,948
Running Balance	\$0

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure V Bond Budget

As of December 31, 2020

	Project Name	Completion	Project Budget	Measure V Allocation	Other Funding	Measure V Expenditures as of 12/31/20	Measure V Expenditures as of 9/30/20	Measure V Expenditures Last Period	Total Measure V Remaining
101	Replacement Math and Science Extension Build	January 2024	\$124,958,336	\$82,317,992	\$42,640,344	\$4,269,588	\$3,740,346	\$529,242	\$78,048,404
102	Student Services	Completed	\$130,224,164	\$33,624,909	\$96,599,255	\$24,267,524	\$24,175,617	\$91,907	\$9,357,385
103	Malibu Center	August 2022	\$61,582,273	\$34,558,420	\$27,023,853	\$5,494,056	\$2,940,062	\$2,553,994	\$29,064,364
104	Early Childhood Development/Childcare	October 2020	\$30,925,771	\$15,405,517	\$15,520,254	\$12,409,212	\$11,394,287	\$1,014,925	\$2,996,305
105	Art Building Replacement	June 2023	\$34,901,000	\$24,000,000	\$10,901,000	\$1,003,031	\$793,644	\$209,387	\$22,996,969
106	Business Building Renovation	December 2026	\$25,017,000	\$12,547,000	\$12,470,000	\$3,400	\$3,400	\$0	\$12,543,600
107	Air Conditioning	February 2021	\$10,777,654	\$10,777,654	\$0	\$3,077,137	\$1,841,849	\$1,235,288	\$7,700,517
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$0	\$0	\$0	\$0	\$4,000,000
109	Master Planning	December 2021	\$1,000,000	\$1,000,000	\$0	\$683,658	\$675,597	\$8,061	\$316,342
110	Drescher Hall Modernization	On-Going	\$13,005,082	\$13,000,000	\$5,082	\$0	\$0	\$0	\$13,000,000
111	Outdoor Classroom	On-Going	\$321,723	\$321,723	\$0	\$321,723	\$321,723	\$0	\$0
112	SMMUSD	August 2021	\$20,000,000	\$20,000,000	\$0	\$0	\$0	\$0	\$20,000,000
113	City of Santa Monica	On-Going	\$20,000,000	\$20,000,000	\$0	\$0	\$0	\$0	\$20,000,000
114	Classrooms Relocation	October 2020	\$6,900,000	\$6,900,000	\$0	\$6,888,495	\$6,856,920	\$31,575	\$11,505
115	TBD	On-Going	\$39,446,785	\$39,446,785	\$0	\$0	\$0	\$0	\$39,446,785
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$0	\$242,884	\$240,613	\$2,271	\$57,116
121	Cost of Issuance	On-Going	\$800,000	\$800,000	\$0	\$291,277	\$291,277	\$0	\$508,723
122	Management Reserve	On-Going	\$26,000,000	\$26,000,000	\$0	\$0	\$0	\$0	\$26,000,000
123	Unissuable Bond	On-Going	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Totals			\$550,159,788	\$345,000,000	\$205,159,788	\$58,951,985	\$53,275,335	\$5,676,650	\$286,048,015

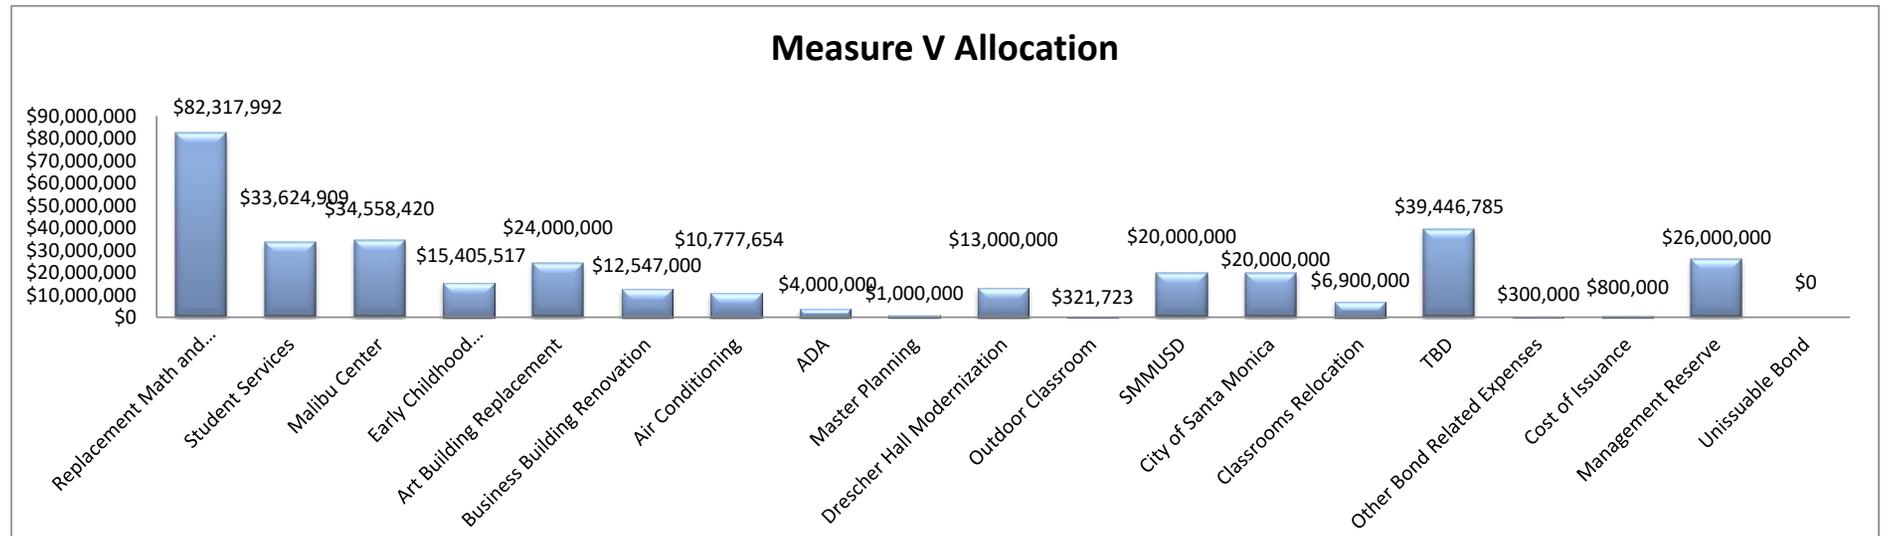

SANTA MONICA COMMUNITY COLLEGE DISTRICT
Measure V Bond Budget History
as of December 31, 2020

	Project Name	Completion	Preliminary Measure V Budget	Measure V Budget as of 9/30/20	Measure V Budget as of 12/31/20	Variance	Measure V Remaining as of 12/31/20
101	Replacement Math and Science Extension Building	January 2024	\$82,317,992	\$82,317,992	\$82,317,992	\$0	\$78,577,646
102	Student Services	Completed	\$21,130,252	\$33,624,909	\$33,624,909	\$0	\$9,449,292
103	Malibu Center	August 2022	\$25,000,000	\$34,558,420	\$34,558,420	\$0	\$31,618,358
104	Early Childhood Development/Childcare	Completed	\$15,405,517	\$15,405,517	\$15,405,517	\$0	\$4,011,230
105	Art Building Replacement	June 2023	\$24,000,000	\$24,000,000	\$24,000,000	\$0	\$23,206,356
106	Business Building Renovation	December 2026	\$12,547,000	\$12,547,000	\$12,547,000	\$0	\$12,543,600
107	Air Conditioning	February 2021	\$10,777,654	\$10,777,654	\$10,777,654	\$0	\$8,935,805
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$4,000,000	\$0	\$4,000,000
109	Master Planning	December 2021	\$450,000	\$1,000,000	\$1,000,000	\$0	\$324,403
110	Drescher Hall Modernization	On-Going	\$13,000,000	\$13,000,000	\$13,000,000	\$0	\$13,000,000
111	Outdoor Classroom	On-Going	\$10,000,000	\$321,723	\$321,723	\$0	\$0
112	SMMUSD	August 2021	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$20,000,000
113	City of Santa Monica	On-Going	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$20,000,000
114	Classrooms Relocation	October 2020	\$0	\$6,900,000	\$6,900,000	\$0	\$43,080
115	TBD	On-Going	\$57,271,585	\$39,446,785	\$39,446,785	\$0	\$39,446,785
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$300,000	\$0	\$59,387
121	Cost of Issuance	On-Going	\$800,000	\$800,000	\$800,000	\$0	\$508,723
122	Management Reserve	On-Going	\$28,000,000	\$26,000,000	\$26,000,000	\$0	\$26,000,000
123	Unissuable Bond	On-Going	\$0	\$0	\$0	\$0	\$0
	Project Totals		\$345,000,000	\$345,000,000	\$345,000,000	\$0	\$291,724,665

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure V Project Schedule

As of December 31, 2020

	Project Name	Completion	2019	2020	2021	2022	2023	2024
101	Replacement Math and Science Extension Building	January 2024						
102	Student Services	Completed						
103	Malibu Center	August 2022						
104	Early Childhood Development/Childcare	Completed						
105	Art Building Replacement	June 2023						
106	Business Building Renovation	December 2026						
107	Air Conditioning	February 2021						
108	ADA	On-Going						
109	Master Planning	December 2021						
110	Drescher Hall Modernization	On-Going						
111	Outdoor Classroom	On-Going						
112	SMMUSD	August 2021						
113	City of Santa Monica	On-Going						
114	Classrooms Relocation	October 2020						
115	TBD	On-Going						
120	Other Bond Related Expenses	On-Going						
121	Cost of Issuance	On-Going						
122	Management Reserve	On-Going						
123	Unissuable Bond	On-Going						

In Planning In Construction

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE V EXPENDITURES
FUND 42.5
As of December 31, 2020

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21	Combined Totals
V 7100090						
Replacement Math and Science Extension Building (101)						
Legal		\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$67,242	\$0	\$67,242
Building & Additions		\$675	\$12,987	\$2,633	\$414,266	\$430,561
Architect		\$2,047,911	\$14,446	\$229,267	\$101,303	\$2,392,927
Engineering		\$0	\$0	\$19,622	\$2,995	\$22,618
Inspection & Testing		\$30,804	\$44,077	\$60,666	\$23,086	\$158,632
Project Management		\$130,874	\$617,805	\$347,350	\$101,579	\$1,197,608
Cap Equipment		\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0
Total		\$2,210,264	\$689,315	\$726,781	\$643,229	\$4,269,588
Project Budget	\$124,958,336	Received				
Less Other Funding	\$42,640,344	\$2,584,000	* Other Funding Source:			
Net	\$82,317,992		1) Measure U \$308,336 2) Measure AA \$2,244,008 allocated			
Actual Measure V Expenditures	\$4,269,588		3) State of California \$40,088,000 allocated			
Running Balance	\$78,048,404					

V 7100142						
Student Services Building (102)						
Supplies		\$0	\$71,445	\$38,162	\$0	\$109,607
Other Contract Services		\$0	\$0	\$59,784	\$6,935	\$66,719
Consultants		\$0	\$0	\$687	\$0	\$687
Software Support		\$0	\$189,120	\$0	\$0	\$189,120
Moving Services		\$0	\$55,062	\$9,056	\$0	\$64,118
Building & Additions		\$0	\$12,355,060	\$4,201,966	\$245,709	\$16,802,734
Architect		\$0	\$419,829	\$530,797	\$54,555	\$1,005,181
Engineering		\$0	\$140,458	\$67,481	\$0	\$207,939
Inspection & Testing		\$55,202	\$296,732	\$131,128	\$21,146	\$504,208
Project Management		\$0	\$900,333	\$219,425	\$64,755	\$1,184,513
Cap Equipment		\$0	\$1,565,928	\$90,915	\$0	\$1,656,844
Non-Cap Equipment		\$0	\$2,279,541	\$196,313	\$0	\$2,475,854
Total		\$55,202	\$18,273,508	\$5,545,714	\$393,100	\$24,267,524
Project Budget	\$130,224,164		* Other Funding Source:			
Less Other Funding	\$96,599,255		1) State of California \$1,321,000 received			
Net	\$33,624,909		2) Measure U \$21,131,135 3) Measure S 45,595,322,			
Actual Measure V Expenditures	\$24,267,524		4) Measure AA \$6,870,490 allocated			
Running Balance	\$9,357,385		5) Measure U, S & AA interests \$21,681,308 allocated			

V 7100015						
Malibu Site Acquisition (103)						
Legal		\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$2,713	\$38,163	\$40,876
Consultants		\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$2,642,861	\$2,295,030	\$4,937,891
Architect		\$0	\$0	\$0	\$43,233	\$43,233
Engineering		\$0	\$0	\$8,482	\$0	\$8,482
Inspection & Testing		\$0	\$0	\$51,754	\$111,576	\$163,330
Project Management		\$0	\$0	\$49,588	\$250,656	\$300,244
Cap Equipment		\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$2,755,398	\$2,738,658	\$5,494,056
Project Budget	\$61,582,273		* Other Funding Source:			
Less Other Funding	\$27,023,853		1) Measure S \$25,000,000			
Net	\$34,558,420		2) Interest Allocated \$2,023,853			
Actual Measure V Expenditures	\$5,494,056					
Running Balance	\$29,064,364					

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE V EXPENDITURES
FUND 42.5
As of December 31, 2020

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21	Combined Totals
V 7100104						
Early Childhood Development/Childcare (104)						
Supplies		\$0	\$0	\$35,150	\$5,332	\$40,482
Other Contract Services		\$0	\$0	\$35,344	\$3,217	\$38,561
Consultants		\$0	\$0	\$16	\$0	\$16
Software Support		\$0	\$0	\$6,158	\$0	\$6,158
Legal		\$0	\$0	\$96	\$0	\$96
Building & Additions		\$0	\$0	\$8,879,770	\$1,829,161	\$10,708,932
Architect		\$0	\$0	\$262,660	\$0	\$262,660
Engineering		\$0	\$0	\$19,448	\$0	\$19,448
Inspection & Testing		\$0	\$0	\$349,661	\$89,020	\$438,681
Project Management		\$0	\$0	\$384,279	\$130,848	\$515,127
Cap Equipment		\$0	\$0	\$32,448	\$0	\$32,448
Non-Cap Equipment		\$0	\$0	\$328,242	\$18,362	\$346,604
Total		\$0	\$0	\$10,333,272	\$2,075,939	\$12,409,212
Project Budget	\$30,925,771	Received				
Less Other Funding	\$15,520,254	\$4,441,066				
Net	\$15,405,517					
Actual Measure V Expenditures	\$12,409,212					
Running Balance	\$2,996,305					
				* Other Funding Source: 1) City of Santa Monica \$6,661,598 committed 2) Measure S \$8,858,656 allocated		

V 7100240						
Art Complex (105)						
Legal		\$0	\$0	\$14,811	\$0	\$14,811
Other Contract Services		\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$20,991	\$35,460	\$56,450
Moving Services		\$0	\$0	\$0	\$0	\$0
Building & Additions		\$184	\$407,369	\$3,040	\$0	\$410,592
Architect		\$0	\$0	\$39,542	\$240,920	\$280,462
Engineering		\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$35,495	\$25,052	\$42,228	\$102,775
Project Management		\$0	\$1,600	\$85,708	\$50,632	\$137,940
Cap Equipment		\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0
Total		\$184	\$444,464	\$189,143	\$369,240	\$1,003,031
Project Budget	\$34,901,000					
Less Other Funding	\$10,901,000					
Net	\$24,000,000					
Actual Measure V Expenditures	\$1,003,031					
Running Balance	\$22,996,969					
				* Other Funding Source: 1) State of California \$10,901,000 pending		

SANTA MONICA COMMUNITY COLLEGE DISTRICT
 MEASURE V EXPENDITURES
 FUND 42.5
 As of December 31, 2020

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21	Combined Totals
V 7100243						
Business Building Replacement (106)						
Legal		\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$3,400	\$0	\$3,400
Cap Equipment		\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$3,400	\$0	\$3,400
Project Budget	\$25,017,000					
Less Other Funding	\$12,470,000					
Net	\$12,547,000					
Actual Measure V Expenditures	\$3,400					
Running Balance	\$12,543,600					
Air Conditioning (107)						
Other Contract Services		\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$2,451	\$2,082,817	\$2,085,268
Architect		\$0	\$79,000	\$0	\$0	\$79,000
Engineering		\$417,960	\$217,966	\$26,992	\$21,863	\$684,781
Inspection & Testing		\$0	\$54,810	\$776	\$46,117	\$101,703
Project Management		\$4,370	\$4,570	\$35,700	\$81,745	\$126,385
Total		\$422,330	\$356,346	\$65,919	\$2,232,542	\$3,077,137
Project Budget	\$10,777,654					
Less Other Funding	\$0					
Net	\$10,777,654					
Actual Measure V Expenditures	\$3,077,137					
Running Balance	\$7,700,517					

* Other Funding Source:
 1) State Funding \$12,470,000

SANTA MONICA COMMUNITY COLLEGE DISTRICT
 MEASURE V EXPENDITURES
 FUND 42.5
 As of December 31, 2020

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21	Combined Totals
V 7100004						
Master Plan (109)						
Other Contract Services		\$0	\$0	\$0	\$0	\$0
Advertising		\$0	\$641	\$0	\$0	\$641
Architect		\$0	\$112,073	\$528,182	\$37,861	\$678,116
Engineering		\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$3,800	\$1,100	\$0	\$4,900
Total		\$0	\$116,515	\$529,282	\$37,861	\$683,658
Project Budget	\$1,000,000					
Less Other Funding	\$0					
Net	\$1,000,000					
Actual Measure V Expenditures	\$683,658					
Running Balance	\$316,342					

V 7100237						
Outdoor Classroom (111)						
Other Contract Services		\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0
Architect		\$100,000	\$102,023	\$102,495	\$0	\$304,518
Engineering		\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$17,205	\$0	\$0	\$17,205
Total		\$100,000	\$119,228	\$102,495	\$0	\$321,723
Project Budget	\$321,723					
Less Other Funding	\$0					
Net	\$321,723					
Actual Measure V Expenditures	\$321,723					
Running Balance	\$0					

SANTA MONICA COMMUNITY COLLEGE DISTRICT
MEASURE V EXPENDITURES
FUND 42.5
As of December 31, 2020

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21	Combined Totals
V 7100243						
Classrooms Relocation (114)						
Other Contract Services		\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$3,467	\$5,709,329	\$90,871	\$5,803,666
Supplies		\$0	\$0	\$4,982	\$0	\$4,982
Architect		\$0	\$184,434	\$78,179	\$13,112	\$275,725
Engineering		\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$16,795	\$115,194	\$25,996	\$157,985
Project Management		\$0	\$61,520	\$476,831	\$49,455	\$587,806
Non-Cap Equipment		\$0	\$0	\$58,331	\$0	\$58,331
Total		\$0	\$266,216	\$6,442,846	\$179,434	\$6,888,495
Project Budget	\$6,900,000					
Less Other Funding	\$0					
Net	\$6,900,000					
Actual Measure V Expenditures	\$6,888,495					
Running Balance	\$11,505					
S7100048						
Other Bond Related Expenses (116)						
Consultants		\$0	\$0	\$0	\$0	\$0
Lease/Rental		\$0	\$13,590	\$18,171	\$6,814	\$38,576
Supplies		\$0	\$0	\$0	\$0	\$0
Legal		\$0	\$0	\$0	\$0	\$0
Software License		\$0	\$0	\$0	\$0	\$0
Advertising		\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0
Building & Additions		\$184	\$191,065	\$0	\$0	\$191,249
Inspection & Testing		\$0	\$13,060	\$0	\$0	\$13,060
Project Management		\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0
Total		\$184	\$217,715	\$18,171	\$6,814	\$242,884
Project Budget	\$300,000					
Less Other Funding	\$0					
Net	\$300,000					
Actual Measure V Expenditures	\$242,884					
Running Balance	\$57,116					
Cost of Issuance (117)						
Cost of Issuance		\$291,277	\$0	\$0	\$0	\$291,277
Total		\$291,277	\$0	\$0	\$0	\$291,277
Project Budget	\$800,000					
Less Other Funding	\$0					
Net	\$800,000					
Actual Measure V Expenditures	\$291,277					
Running Balance	\$508,723					
Grand Total		\$3,079,439	\$20,483,307	\$26,712,421	\$8,676,816	\$58,951,984

**SMC Bond Program
Contractor List as of 12-31-2020**

Student Services (Measure U #0, Measure S #9, Measure AA #120, Measure V #102):

Architect – Steinberg Architects, Morris Architects
Contractor – Minco, Bernards Brothers, Spinitar
Engineering – IVA, Cogent Energy Engineering, XL Fire
Inspection & Testing – Geo Labs, BTC Labs - Vertical V, Peak Survey, LPI
Rango Inc., Twining, AGE
Project Management – LPI, YNL, Vanir

Replacement Health/PE/Fitness/Dance Building (Measure S #4, Measure AA #104):

Architect – Gensler Architects
Contractor – Bernards Brothers
Engineering – IVA, Glumac
Inspection & Testing – Geo Labs, Ellis Environmental, Twining, Rango Inc.
Project Management – LPI

Early Childhood Development (Measure S #5, Measure V #104):

Architect – Carde Ten Architects
Consultant – Child Educational Center
Contractor – The Nazerian Group
Engineering – Jacobs
Inspection & Testing – Geo Labs, Rango Inc., Twining
Project Management – LPI, Vanir, YNL

Malibu Site (Measure S #6, Measure AA #110, Measure V #103):

Architect – Quatro Design Group
Contractor – Master Contracting, Icon West
Consultant – m2 Strategic, Parker Environmental
Engineering – Ensitu Services, Jacobs
Inspection & Testing – Peak Surveys, Ellis Environmental, JL Inspection, Ninyo
& Moore, JL Inspection
Project Management – LPI, m6 Strategic, Vanir, YNL

Energy Efficiency Projects (Measure S #7, Measure AA #113):

Architect – N/A
Contractor – Compass Energy Solutions, Johnson Controls
Engineering – Compass Energy Solutions, Johnson Controls
Inspection & Testing – Ellis Environmental

Environmental Performance (Measure AA #101):

Architect – Kishimoto Architects
Contractor – SJ Amoroso Construction
Engineering – P2S Engineering
Inspection & Testing – Cannon, Peak Surveys
Project Management – LPI

Information Technology Relocation (Measure AA #102):

Architect – Morris Architects
Contractor – Minco, Bernards Brothers, Eidim AV Technology
Engineering – IVA, P2S Engineering
Inspection & Testing – Cannon, Peak Surveys, Geo Labs, Ellis Environmental,
Twining, JL Inspection, Rango Inc.
Project Management – LPI, CCS Presentation

Media and Technology Complex (Measure AA #103):

Architect – Clive Wilkinson Architects, Morris Architects
Contractor – H.B. Parkco Construction, Fast Track Construction, CW
Driver, Dimension Data, Key Code Media, Omega
Construction
Consultant – EEG Services
Engineering – IVA, P2S Engineering
Inspection & Testing – Twining, Geo Labs, BTC Labs – Vertical V,
JL Inspection, EEG Services, Ellis Environmental, Rango
Inc., Cannon
Project Management – LPI

Madison East Wing Seismic Upgrade (Measure AA #107):

Architect – DLR Group – WWCOT, LPI
Contractor – Trimax, Bernards Brothers, Dimension Data
Engineering – IVA, Glumac
Inspection & Testing – Twining, Peak Surveys, LPI, All Group Engineering, EEG
Services, Ellis Environmental
Project Management – LPI

Business & Facilities Infrastructure (Measure AA #111):

Architect – LPI, Gwynne Pugh Urban Studio
Contractor – REC+S, Inc., Omega Construction,
Concept Consultant, Inc.
Engineering – N/A
Inspection & Testing – Ellis Environmental, JL Inspection
Project Management – LPI

Community Classroom & Facility Project (Measure AA #114)

Architect – Morris Architects
Contractor – Waisman Construction, Spinitar, Trimax
Engineering – IVA
Inspection & Testing – LPI, Twining
Project Management – LPI

Satellite Campus Parking Facilities and Roadway Improvements (Measure S #8)

Architect - N/A
Contractor - N/A
Engineering - MK Engineering Group
Inspection & Testing - N/A
Project Management - LPI

Roadways, walkways, Grounds, Parking Lots, and Garages (Measure AA #116)

Architect - LPI, DLR Group - WWCOT
Contractor - Trimax, Pub Construction
Consultant - Walker Parking
Engineering - MK Engineering
Inspection & Testing - Ellis Environmental, Peak Surveys, LPI
Project Management - LPI

Emergency Lighting, Fire Alarm, and Security System (Measure AA #119)

Contractor - Red Hawk Fire and Security, Nexus
Engineering - MDC Engineers
Inspection & Testing - Rango Inc.
Project Management - LPI

Signage Safety/Information (Measure S #15)

Contractor - Sign Excellence
Consultant - APCO
Project Management - LPI

Math and Science Addition (Measure AA #106)

Architect - Cannon Design
Contractor - Icon West, The Nazerian Group
Consultant - N/A
Engineering - Arup
Inspection & Testing - AGE
Project Management - Vanir, YNL

Classrooms Relocation (Measure V #114)

Architect - Gwynne Pugh
Contractor - The Nazerian Group
Inspection & Testing - AGE
Project Management - Vanir, YNL

Art Building Replacement (Measure V #105)

Architect - Little Architects
Contractor - N/A
Inspection & Testing - N/A
Project Management - Vanir

Air Conditioning (Measure V #107)
Architect - P2S
Contractor - A&B Construction
Inspection & Testing - Rango Inc.
Project Management - Vanir



Vendors and Contractors List

(Received Payments from Bond Funds)

For the Period June 30, 2020 to December 31, 2020

Arup Engineering	Mobile Modular
A&B Construction, Inc.	Montgomery Hardware
All Group Engineering (AGE)	Morris Architects, Inc.
ARC Document Solutions	Nazerian Group, The
Apple Computer	P2S
Carde Ten Architects	Parker Environmental
Cannon Parkin Architects	QDG Architecture
Dell Computer	Rango Inspection
DLR Group	SHI Intl
Endeavor Advanced Solutions	Southern California Edison
GeoLabs	School Specialties
Gwynne Pugh Architects	Twining
Icon West	TK1SC
Koury Engineering	Vanir Construction Management
Little Architects	YNL Architects
LPI, Inc.	
Los Angeles, County of	
