An aerial photograph of the Santa Monica Community College District campus. The image shows a modern building with a large glass facade and a prominent red overhang. In the foreground, there is a paved plaza with several palm trees and a small fountain. People are seen walking and sitting on the plaza. The sky is clear and blue.

SANTA MONICA  
COMMUNITY COLLEGE  
DISTRICT

CITIZENS' BOND  
OVERSIGHT  
COMMITTEE

2021-2022 Annual Report



Santa Monica Community College District  
**Citizens' Bond Oversight Committee**

**ANNUAL REPORT, 2021-2022**

## ANNUAL REPORT, 2021-2022

Submitted to the  
Santa Monica Community College District  
BOARD OF TRUSTEES  
FALL 2022

Dr. Louise Jaffe, Chair  
Barry Snell, Vice-Chair  
Dr. Susan Aminoff  
Dr. Nancy Greenstein  
Dr. Margaret Quiñones-Perez  
Rob Rader  
Dr. Sion Roy  
Catalina Fuentes Aguirre, Student Trustee

### CITIZENS' BOND OVERSIGHT COMMITTEE 2021-2022

Elizabeth Greenwood, Chair  
Bruce Sultan, Vice-Chair  
Patrick Acosta  
Heather Anderson  
Alfred Barrett  
Anne Plechner  
Elaine Polachek  
Katherine Reuter  
Donald Schort  
Joshua Elizondo

#### Staff Support

Christopher Bonvenuto, VP, Business and Administration  
Don Girard, Senior Director, Government Relations/  
Institutional Communications  
Charlie Yen, Director, Facilities Planning  
John Greenlee, Director, Facilities Finance  
Yu-Ngok Lo, Assistant Director, Facilities Planning  
Olinka Rodriguez, Committee Coordinator



## TABLE OF CONTENTS

	<u>Page No.</u>
<b>Statement of Compliance</b>	
Measure V .....	3
Measure S.....	4
Measure AA.....	5
<b>Citizens' Bond Oversight Committee Proceedings and Activities.....</b>	<b>6</b>
<b>Minutes of Meetings</b>	
July 21, 2021 (cancelled) .....	n/a
October 20, 2021 .....	7
January 26, 2022 .....	10
April 20, 2022 .....	13
<b>SMC Capital Outlay Program – Bond Project Descriptions and Project Status.....</b>	<b>15</b>
<b>SMC Capital Construction Budget Summary as of June 30, 2022 .....</b>	<b>22</b>
<b>Bond Sales/Expenses Report .....</b>	<b>23</b>
<b>Budget/History</b>	
• Measure S .....	24
• Measure AA .....	35
• Measure V.....	48
<b>Project Schedule/Expenditures</b>	
• Measure S .....	26
• Measure AA .....	37
• Measure V.....	50
<b>SMC Bond Program – Contractor List as of June 30, 2022 .....</b>	<b>56</b>



STATEMENT OF COMPLIANCE  
MEASURE V FUNDS

This Annual Report is submitted to the Board of Trustees by the Santa Monica Community College District Citizens' Bond Oversight Committee.

The Committee advises that, to the best of its knowledge, the Santa Monica Community College District is in compliance with the requirements in Article XIII A, Section 1(b)(3) of the California Constitution. In particular, bond revenue has been expended only for the purposes so described in Measure V and no funds were used for any teacher or administrative salaries or other operating expenses as prohibited by Article XIII A, Section 1(b)(3)(a) of the California Constitution.

Respectfully Submitted:

**Elizabeth Greenwood, Chair**  
Citizens' Bond Oversight Committee

Date: October 19, 2022



**STATEMENT OF COMPLIANCE**  
**MEASURE S FUNDS**

This Annual Report is submitted to the Board of Trustees by the Santa Monica Community College District Citizens' Bond Oversight Committee.

The Committee advises that, to the best of its knowledge, the Santa Monica Community College District is in compliance with the requirements in Article XIII A, Section 1(b)(3) of the California Constitution. In particular, bond revenue has been expended only for the purposes so described in Measure S and no funds were used for any teacher or administrative salaries or other operating expenses as prohibited by Article XIII A, Section 1(b)(3)(a) of the California Constitution.

Respectfully Submitted:

**Elizabeth Greenwood, Chair**  
Citizens' Bond Oversight Committee

Date: October 19, 2022



**STATEMENT OF COMPLIANCE**  
**MEASURE AA FUNDS**

This Annual Report is submitted to the Board of Trustees by the Santa Monica Community College District Citizens' Bond Oversight Committee.

The Committee advises that, to the best of its knowledge, the Santa Monica Community College District is in compliance with the requirements in Article XIII A, Section 1(b)(3) of the California Constitution. In particular, bond revenue has been expended only for the purposes so described in Measure AA and no funds were used for any teacher or administrative salaries or other operating expenses as prohibited by Article XIII A, Section 1(b)(3)(a) of the California Constitution.

Respectfully Submitted:

**Elizabeth Greenwood, Chair**  
Citizens' Bond Oversight Committee

Date: October 19, 2022



**CITIZENS' BOND OVERSIGHT COMMITTEE**  
**PROCEEDINGS AND ACTIVITIES**

**Meetings of the Citizens' Bond Oversight Committee**

The Committee conducted its meetings in accordance with provisions of the Ralph M. Brown Public Meetings Act, Government Code Sections 54950 et seq.

During the COVID-19 (Coronavirus) Global Pandemic, members of the Citizens' Bond Oversight Committee participated in the meetings telephonically or by Zoom Conference, in accordance with Executive Order N-29-20 issued by Governor Gavin Newsom and dated March 17, 2020.

Meeting notices, agendas, minutes and all documents and reports received by the Committee members are a matter of public record and made available on the SMC website:

<https://www.smc.edu/administration/governance/citizens-bond-oversight-committee/>

The SMC Bond Program website is located at: [www.smcbondprojects.com](http://www.smcbondprojects.com)

Minutes of the quarterly meetings are included on the following pages.



A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee (CBOC) was held on Wednesday, October 20, 2021. The meeting was conducted via Zoom Conference.

1. **CALL TO ORDER** – 12:01 p.m.

2. **ROLL CALL – Members of the Citizens' Bond Oversight Committee**

Heather Anderson, Chair – Present  
Elizabeth Greenwood, Vice-Chair – Present  
Patrick Acosta – Absent  
Alfred Barrett – Present  
Anne Plechner – Present  
Elaine Polachek – Present  
Katherine Reuter – Absent  
Donald Schort – Present  
Bruce Sultan – Present  
Emily Lu – Present

CBOC Support Staff Present

Chris Bonvenuto, Vice President, Business and Administration  
Don Girard, Senior Director, Government Relations/Institutional Communications  
John Greenlee, Director of Facilities Finance  
Olinka Rodriguez, Citizens' Bond Oversight Committee Coordinator  
Charlie Yen, Director of Facilities Planning

3. **APPROVAL OF MINUTES OF CBOC MEETING, April 21, 2021**

Motion was made by Alfred Barrett and seconded by Donald Schort to approve the minutes of the Citizens' Bond Oversight Committee meeting held on April 21, 2021. *Minutes were approved.*  
New members abstained from voting on the minutes.

4. **INTRODUCTION OF REAPPOINTED MEMBERS AND NEW MEMBERS TO THE CBOC**

At its meeting on July 6, 2021, the SMCCD Board of Trustees approved reappointments to the Citizens' Bond Oversight Committee for a two-year term, 2021-2023 as follows:

- Reappointment of Current Members, 2021-2023:
  - Patrick Acosta
  - Heather Anderson
  - Elizabeth Greenwood
  - Don Schort

At its meeting on July 6, 2021 and September 14, 2021, the SMCCD Board of Trustees approved the appointment to the Citizens' Bond Oversight Committee for a two-year term, 2021-2023 as follows:

- Appointment of New Members, 2021-2023:
  - Anne Plechner
  - Elaine Polachek
  - Katherine Reuter
  - Bruce Sultan

At its meeting on October 5, 2021, the SMCCD Board of Trustees approved appointments to the Citizens' Bond Oversight Committee for a one-year term, 2021-2022 as follows:

- Appointment of New Member, 2021-2022:
  - Emily Lu

5. **ELECTION OF CHAIR AND VICE CHAIR, 2022-2023**

Elizabeth Greenwood and Bruce Sultan were unanimously elected Chair and Vice Chair, respectively for 2022-2023.

6. **CITIZENS' BOND OVERSIGHT COMMITTEE ANNUAL REPORT, 2020-2021**

The members approved the CBOC annual report, 2020-2021.

New members abstained from voting on the CBOC annual report 2020-2021.

7. **REPORTS and DISCUSSION**

Bond Projects Website

<https://www.smc.edu/administration/governance/citizens-bond-oversight-committee/index.php>

A. **Bond Construction Projects**

- Malibu Campus: Installation of the walls, the roof, and glass windows continues. New landscaping on the tiered grass area for students to gather outdoors. The walls of the holding cells in the Sheriff's Substation jail have been built. The communication tower's footing was begun. The project is continuing as planned with estimated completion date of October 2022.
- The Math/Science Project: Renderings were shared of what completed project would resemble. The footing of the project is currently being installed. The project will include classrooms, labs and the observatory/planetarium and will be the largest building on campus once completed. The estimated completion date for this project is July 2024.
- HVAC Project: HVAC lines on the roof and side of the Science Building to chill the water system were installed. Also, a duct in the gym, new units were put in near Sky Box and a new HVAC system were installed on the Madison Campus. The project was completed on July 2021. Phase 3 was approved to begin connecting Drescher Hall to the Central Plant.
- John Adams Auditorium Project: Planning is underway for the grand opening of the 750-seat auditorium with state-of-the-art sound system. The estimated completion date for this project is November 2021.
- Art Complex Project: Location of the project is on Pico Boulevard, 14<sup>th</sup> Street and Bay Street, the renderings showed views of the interior classrooms, courtyard, lobby and exterior views. One of the design elements will be an exterior revolving art piece on the corner of the building to share art with the community. The estimated completion date for this project is August 2024.
- Early Childhood Lab School Project: Photographs of the furnished interior and exterior of the completed project were shared. The project was completed March 2021.

B. Measure S, AA and V Budget Summaries and Bond Sales Expense Reports

The SMC Bond Capital Construction Budget Summary as of September 30, 2021 reports the following:

Measure S Budget:	\$143,500,000
Measure AA Budget:	\$295,000,000
Measure V Budget:	\$345,000,000
Income:	\$29,858,053
Other Funding Received:	\$39,898,103
Other Funding Pending:	<u>\$62,809,440</u>
Total Budget:	\$1,076,065,596
Estimate at Completion:	\$1,076,565,596
Bond Funds Remaining:	\$ 257,651,681

- Measure S: Total Measure S Expenditures as of September 30, 2021 were \$142,969,768; total remaining funds are \$530,232. All bonds issued.
- Measure AA: Total Measure AA Expenditures as of September 30, 2021 were \$291,873,746; total remaining funds are \$3,126,254. All bonds issued.
- Measure V: Total Measure V Expenditures as of September 30, 2021 were \$90,998,470; total remaining funds are \$254,001,530. \$165,000,000 bonds to be issued.
- The Bond Sales/Expense Report Indicates total bond amounts, bond issue dates/amounts unsold bond amount and total available as of September 30, 2021.

Total Bond Program:	\$783,500,000
Total Bonds Issued:	\$618,493,686
Total Expenses:	\$525,841,984
Total Available Remaining:	\$ 92,651,702
Total Unsold Bond:	\$165,006,314

C. SMC Bond Program – Contractor List as of September 30, 2021

D. Contractors List as of September 30, 2021

8. SCHEDULE OF MEETINGS, 2021-2022

Wednesdays at 12:00 p.m.

January 26, 2022  
April 20, 2022  
July 20, 2022  
October 19, 2022

9. ADJOURNMENT – 1:15 p.m.

The next meeting of the Citizens’ Bond Oversight Committee will be held on Wednesday, January 26, 2022 (location to be determined).

Current information on all bond construction projects is available at:

<http://smcbondprojects.com> and at <http://www.smc.edu/CBOC>



A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee (CBOC) was held on Wednesday, January 26, 2022. The meeting was conducted via Zoom Conference.

I. **CALL TO ORDER** – 12:02 p.m.

2. **ROLL CALL – Members of the Citizens' Bond Oversight Committee**

Elizabeth Greenwood, Chair – Present  
Bruce Sultan, Vice-Chair – Present  
Patrick Acosta – Absent  
Heather Anderson – Present  
Alfred Barrett – Present  
Anne Plechner – Present  
Elaine Polachek – Present  
Katherine Reuter – Present  
Donald Schort – Present  
Emily Lu – Absent

CBOC Support Staff Present

Chris Bonvenuto, Chief Director, Business Services  
Don Girard, Senior Director, Government Relations/Institutional Communications  
John Greenlee, Director of Facilities Finance  
Olinka Rodriguez, Citizens' Bond Oversight Committee Coordinator  
Charlie Yen, Director of Facilities Planning

3. **APPROVAL OF MINUTES OF CBOC MEETING, October 20, 2021**

Motion was made by Heather Anderson and seconded by Elaine Polachek to approve the minutes of the Citizens' Bond Oversight Committee meeting held on October 20, 2021.  
Elizabeth Greenwood abstained. *Minutes were approved.*

4. **CONFLICT OF INTEREST FORM**

The Committee Members completed and endorsed forms. The forms are on file.

5. **FINANCIAL AND PERFORMANCE AUDIT REPORTS 2020-2021**

Alicia Herrera, Auditor with Eide Bailly, gave summary of financials and assets for each bond. The audit reports are unmodified, which is the highest opinion the auditors can give. The audit reports contain no audit findings and did not identify any deficiencies in internal control. The District expended General Obligation Bond Funds (Measure S, Measure AA and Measure V) only for specific projects approved by the voters in the City of Santa Monica.

6. **REPORTS and DISCUSSION**

Bond Projects Website

<https://www.smc.edu/administration/governance/citizens-bond-oversight-committee/index.php>

A. **Bond Construction Projects**

- Malibu Campus: Construction continues with pouring of the first layer of asphalt in the front and back parking lots. The glass panels/windows in the front of the building as well as a mosaic wall in the interior are being installed. The County of LA will manage the helipad for the Sheriff's Department. The project is delayed due to the impact that covid has had on the construction crew. The estimated completion date is October 2022.

- The Math/Science Project: The rendering images showed the location of the planetarium and observatory. The beam that will house the telescope is a freestanding structure to ensure steady views of the sky. The building's steel framing is 50% complete. The utilities and waterlines are being connected and installed.  
The estimated completion date for this project is July 2024.
- HVAC Project: HVAC lines have been connected to the Cayton Center and the Pavilion/Gym, now they are going into Drescher Hall.  
The estimated completion date for this project is March 2022.
- New Art Building on Pico Boulevard and 14<sup>th</sup> will have renderings of what the project will look like when completed. The plan check will take a couple more months with an approximate groundbreaking date of July 2022.  
The estimated completion date for this project is July 2024.
- John Adams Auditorium was completed in November 2021.  
The community is now enjoying and holding events in the new facilities.

B. Measure S, AA and V Budget Summaries and Bond Sales Expense Reports

The SMC Bond Capital Construction Budget Summary as of December 31, 2021 reports the following:

Measure S Budget:	\$143,500,000
Measure AA Budget:	\$295,000,000
Measure V Budget:	\$345,000,000
Interest:	\$29,858,053
Other Funding Received:	\$39,898,103
Other Funding Pending:	<u>\$62,809,440</u>
Total Budget:	\$1,076,065,596
Estimate at Completion:	\$1,076,065,596
Bond Funds Remaining:	\$ 253,450,510

- Measure S: Total Measure S Expenditures as of December 31, 2021 were \$142,969,766; total remaining funds are \$528,089.
- Measure AA: Total Measure AA Expenditures as of December 31, 2021 were \$292,216,261; total remaining funds are \$2,779,569.
- Measure V: Total Measure V Expenditures as of December 31, 2021 were \$94,857,149; total remaining funds are \$250,142,851.
- The Bond Sales/Expense Report  
Indicates total bond amounts, bond issue dates/amounts unsold bond amount and total available as of December 31, 2021.

Total Bond Program:	\$783,500,000
Total Bonds Issued:	\$618,493,686
Total Expenses:	\$530,043,177
Total Available Remaining:	\$ 88,450,509
Total Unsold Bond:	\$165,006,314

C. SMC Bond Program – Contractor List as of December 31, 2021

D. Contractors List as of December 31, 2021

7. **SCHEDULE OF MEETINGS, 2021-2022**

Wednesdays at 12:00 p.m.

January 26, 2022

April 20, 2022

July 20, 2022

October 19, 2022

8. **ADJOURNMENT** – 1:14 p.m.

The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, April 20, 2022 (location to be determined).

Current information on all bond construction projects is available at:

<http://smcbondprojects.com> and at <http://www.smc.edu/CBOC>



A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee (CBOC) was held on Wednesday, April 20, 2022. The meeting was conducted via Zoom Conference.

1. **CALL TO ORDER** – 12:10 p.m.

2. **ROLL CALL – Members of the Citizens' Bond Oversight Committee**

Elizabeth Greenwood, Chair – Present  
Bruce Sultan, Vice-Chair – Present  
Patrick Acosta – Absent  
Heather Anderson – Absent  
Alfred Barrett – Present  
Anne Plechner – Present  
Elaine Polachek – Present  
Katherine Reuter – Present  
Donald Schort – Present  
Emily Lu – Absent

CBOC Support Staff Present

Chris Bonvenuto, Vice President, Business and Administration  
Don Girard, Senior Director, Government Relations/Institutional Communications  
John Greenlee, Director of Facilities Finance  
Yu-Ngok Lo, Assistant Director of Facilities Planning  
Olinka Rodriguez, Citizens' Bond Oversight Committee Coordinator

3. **APPROVAL OF MINUTES OF CBOC MEETING, January 26, 2022**

Motion was made by Elaine Polachek and seconded by Don Schort to approve the minutes of the Citizens' Bond Oversight Committee meeting held on January 26, 2022. *Minutes were approved.*

4. **INFORMATION – EXPIRING TERM OF MEMBER OF THE CITIZENS' BOND OVERSIGHT COMMITTEE**

The term of the following member of the Citizens' Bond Oversight Committee is expiring effective **June 30, 2022**. They are eligible for reappointment:

- Alfred Barrett

5. **REPORTS and DISCUSSION**

Bond Projects Website

<https://www.smc.edu/administration/governance/citizens-bond-oversight-committee/index.php>

A. Bond Construction Projects

- Malibu Campus: The construction crew waterproofed to begin interior work and are painting and cleaning residual paint in the Sheriff's Department area. The Sheriff's Department lobby is having drywall installed. Aerial photographs of the first-floor multipurpose room, second floor Classroom and Interpretive Center were shared. The estimated completion date is November 2022.
- The Math/Science Project: The topping-off ceremony was held on March 31, 2022. The steel framing, welded and bolted, is complete on the 3-story building. The main electrical room with the electrical conduits is being completed. The metal decking, the location of the elevator, and the steel for the telescope were highlighted.

The estimated completion date for this project is July 2024.

- New Art Building on Pico Boulevard and 14<sup>th</sup> is currently in DSA back check. Construction has not begun. The plan check will take a couple more months with an approximate groundbreaking date of July 2022.

The estimated completion date for this project is August 2024.

**B. Measure S, AA and V Budget Summaries and Bond Sales Expense Reports**

The SMC Bond Capital Construction Budget Summary as of March 31, 2022 reports the following:

Measure S Budget:	\$143,500,000
Measure AA Budget:	\$295,000,000
Measure V Budget:	\$345,000,000
Interest:	\$29,858,053
Other Funding Received:	\$39,898,103
Other Funding Pending:	<u>\$62,809,440</u>
Total Budget:	\$1,076,065,596
Estimate at Completion:	\$1,076,065,596
Bond Funds Remaining:	\$ 232,770,027

- Measure S: Total Measure S Expenditures as of March 31, 2022 were \$143,497,859; total remaining funds are \$0.
- Measure AA: Total Measure AA Expenditures as of March 31, 2022 were \$292,263,808; total remaining funds are \$2,736,192.
- Measure V: Total Measure V Expenditures as of March 31, 2022 were \$114,961,993; total remaining funds are \$230,038,007.
- The Bond Sales/Expense Report  
Indicates total bond amounts, bond issue dates/amounts unsold bond amount and total available as of March 31, 2022.

Total Bond Program:	\$783,500,000
Total Bonds Issued:	\$618,493,688
Total Expenses:	\$550,723,660
Total Available Remaining:	\$ 67,770,028
Total Unsold Bond:	\$165,006,312

**C. SMC Bond Program – Contractor List as of March 31, 2022**

**D. Contractors List as of March 31, 2022**

**6. SCHEDULE OF MEETINGS, 2021-2022**

Wednesdays at 12:00 p.m.

- January 26, 2022
- April 20, 2022
- July 20, 2022
- October 19, 2022

**7. ADJOURNMENT – 12:40 p.m.**

The next meeting of the Citizens’ Bond Oversight Committee will be held on Wednesday, July 20, 2022 (location to be determined).

Current information on all bond construction projects is available at:

<http://smcbondprojects.com> and at <http://www.smc.edu/CBOC>



SANTA MONICA COMMUNITY COLLEGE DISTRICT

Capital Outlay Program

Bond Project Report

July 2022

Prepared by SMC Facilities Planning

## Introduction

---

The District's capital outlay program consists of larger non-maintenance projects that are generally over \$100,000, typically financed by local taxpayer approved bonds. The capital projects include new buildings, replacement buildings, renovations, property acquisition, parking, site work, landscaping, infrastructure, security, and technology.

Over the last several decades, Santa Monica and Malibu voters have approved five safety and modernization bond measures in support of the college's career and academic programs:

Proposition T	1992	\$ 23,000,000
Measure U	2002	\$160,000,000
Measure S	2004	\$135,000,000
Measure AA	2008	\$295,000,000
Measure V	2016	\$345,000,000

By way of background, local bonds financed the original Main Campus, built in the 1950s and 1960s. However, in subsequent years until 1992, the District depended primarily on limited state funding, so only a few large projects were built. After the 1994 Northridge Earthquake and the extensive damage to the Main Campus, the District received federal FEMA support for rebuilding which started the current era of major construction on the campus.

In addition to the local bonds listed above, there has been significant financial support from federal, state and city sources along with the District's own capital funds.

The 1998 Facilities Master plan was a major effort in guiding the modernization and development of the Main Campus after the Northridge earthquake. Additional facility assessments were conducted in 2001, 2002, and 2003. In 2007, a master plan was added for the development of the Bundy Campus. In 2010, an update of the Facilities Master Plan was completed to address other safety and modernization improvements on the Main Campus and to incorporate the satellite campuses.

A new Facilities Master Plan is currently underway and will be completed in 2022-2023 to guide the campus development using the Measure V funds.

Highlights of the completed projects include the purchase of the Bundy Campus and Emeritus College, and the construction of the Theatre Arts, Broad Stage, HSS Building, Campus Quad, Information Technology building, Health-PE-Fitness-Dance-Central Plant building, Center for Media and Design, Early Childhood Lab School, and Student Services building.

### ***Projects started in 2021-2022:***

Drescher Hall HVAC Upgrade  
Math & Science Phase 2

### ***Project completed in 2021-2022***

HVAC Upgrade and Connection to the Campus Central Plant  
Drescher Hall HVAC Upgrade  
Math & Science Phase 1 (Demolition)

### ***Projects expected to start construction in 2022-2023:***

Art Building Replacement

### ***Projects expected to be completed in 2022-2023:***

Malibu Campus - Phase 2  
Main Campus Facilities Master Plan

## Bond Program Overview

Project	Funding Source	Total Cost	Status 6/30/19
Purchase of Bundy Site	U	\$30,280,878	Completed 2002
Emeritus College	U, SMC Foundation	\$9,603,782	Completed 2003
Purchase of 1738 Pearl Street	U	\$749,208	Completed 2003
Library Renovation & Expansion	T, State, FEMA	\$23,600,000	Completed 2003
PE/Dance/Athletics Office Relocation	U	\$2,797,033	Completed 2004
Math Complex	U	\$1,458,690	Completed 2004
Bundy Campus West Building	U	\$23,291,387	Completed 2005
Malibu Storm Water Infrastructure P-I	S	\$2,500,000	Completed 2005
Renovation of Theatre Arts	U	\$19,544,314	Completed 2006
Music Complex - Performing Arts	U	\$4,623,547	Completed 2007
HSS North/South	U, State, FEMA, City	\$29,240,945	Completed 2006/7
Shuttle Parking Acquisition & Constr.	U	\$18,969,509	Completed 2007
Malibu Storm Water Infrastructure P-II	S	\$2,500,000	Completed 2008
Broad Stage - Performing Arts	S, SMC Foundation	\$40,690,201	Completed 2008
Athletic Fields - John Adams	S	\$2,969,807	Completed 2008
Main Campus Quad	U	\$11,388,463	Completed 2008
Bundy New Driveway & Signal	S	\$3,825,841	Completed 2009
Athletic Fields - Corsair Field	S	\$4,440,065	Completed 2009
Pico Phase I - Lot 6 & Structures	S	\$1,018,009	Completed 2009
Infrastructure & Safety Phase I	U	\$4,003,084	Completed 2010
Purchase of 1516 Pico Blvd.	AA	\$1,748,667	Completed 2010
Purchase of 1510 Pico Blvd.	AA	\$4,009,228	Completed 2011
Purchase of 919 Santa Monica Blvd.	AA	\$9,029,287	Completed 2011
Bundy/Airport Classroom Relocations	AA	\$3,162,183	Completed 2012
Library Village Relocation & Bike Park	AA	\$1,448,275	Completed 2013
Bundy/Airport Parking	AA	\$2,035,375	Completed 2013
Information Technology	AA	\$23,160,569	Completed 2015
Purchase of 2019 14 <sup>th</sup> Street	AA	\$5,013,226	Completed 2017
Central Plant Loop Connections	AA	\$10,767,251	Completed 2017
East Wing - Performing Arts Center	AA	\$30,161,852	Completed 2017
Purchase of 1530 Pico Blvd.	AA	\$4,821,600	Completed 2018
Security and Fire Alarm Upgrade	AA	\$11,520,794	Completed 2018
Health, PE, Fitness, Dance, Cent. Plant	S, AA	\$56,240,452	Completed 2018
Center for Media & Design	AA, KCRW Foundation	\$131,149,713	Completed 2018
Student Services	U, S, AA, V	\$130,224,164	Completed 2019
Classroom Relocation	V	\$6,900,000	Completed 2020
Child Development Center	S, V, City of SM	\$30,925,693	Completed 2021
HVAC Upgrade	V	\$10,777,654	Completed 2022
Malibu Campus	S, V	\$61,582,273	Under Construction
Math and Science	AA, V, State	\$124,958,336	Under Construction
Art Building Replacement	V, State	\$34,901,000	State review

## *Projects Under Construction or Recently Completed*

### **Malibu Site Campus**

---

**Project Description:** In the 1970s and early 1980s, Santa Monica College offered about 70 general education classes and several non-credit classes in Malibu throughout the year. Today, the program is limited to a few classes offered in Malibu Unified School District buildings.

The new facility will be a classroom facility offering general education classes, science, art and Emeritus College classes. There will be an interpretive center that highlights the natural environment and history of Malibu and a Sheriff's sub-station within the new facility. The selection and acquisition of the project site, which is located at the Malibu Civic Center, is a collaboration between SMC, the City of Malibu and the County of Los Angeles.

**Current Progress:** Phase 2, which includes the construction of the new water main, the new facility and its associated sitework is currently in construction and it is anticipated to be completed by the end of 2022.

**Project Schedule:** Construction is anticipated to be completed by the end of 2022

**Estimated Project Cost:** \$61,582,273

**Funding Sources:** Measure S, V

### **Drescher Hall HVCA Upgrade and Connection to the Campus Central Plant**

---

This project will connect Drescher Hall to the campus wide central loop. The project provides efficient cooling to these buildings while reducing energy consumption that aligns with SMC's long-term sustainability goals.

**Current Progress:** Project is completed

**Project Schedule:** Construction is completed

**Estimated Project Cost:** \$772,851

**Funding Sources:** Measure V

### **HVCA Upgrade and Connection to the Campus Central Plant**

---

The college successfully implemented Phase 1 of the project in 2017, which includes adding a new air conditioning system to the HSS building and connecting the Business Building, Science Building East Wing, and the HSS Building to the campus wide central plant loop. Phase 2 of the project will include adding new air conditioning systems to the Science Building west wing, gymnasium, Student Activities/Cayton center, and the Madison building at PAC. The project provides efficient cooling to these buildings while reducing energy consumption that aligns with SMC's long-term sustainability goals.

**Current Progress:** Project is completed

**Project Schedule:** Construction is completed

**Estimated Project Cost:** \$8,432,609

**Funding Sources:** Measure V

## Science and Math Extension

---

Santa Monica College is renowned for its science and allied health programs; however, the existing labs for Life, Physical and Earth Sciences are at its maximum capacity. Furthermore, part of the Math Department is currently being housed in temporary trailers that lacks the infrastructure for smart classrooms or support for the use of modern technology for instructional use. Consolidating the Math and Science programs into the new Math and Science building will strengthen the interdisciplinary interaction. The project is qualified for up to \$40 million in State funding, which requires a local match. The building will have a new planetarium and a community lab for all ages, including a nutrition and culinary lab in support of the College's nutrition program.

**Current Progress:** Project is under construction.

**Project Schedule:** Construction started in fall 2019.

**Estimated Project Cost:** \$10,777,654

**Funding Sources:** Measure V

### *Projects in Active Design and Planning Phases*

#### Replacement of Art Building

---

The new Art Complex will replace the existing aging buildings systems and strengthen the interdisciplinary interaction between many different disciplines within the Art Department. The College will receive up to \$10 million in State funding for this project, which requires a local match. The project is currently under State review.

**Current Progress:** Project is approved by DSA and is currently waiting for State Funding approval.

**Project Schedule:** Construction is anticipated to start by the beginning of 2023

**Estimated Project Cost:** \$34,901,000

**Funding Sources:** Measure V

### *Future Projects (Measure V)*

*The following projects were included in the 2016 Measure V Bond language and will be further developed during the Facilities Master Plan process:*

**Replacement of Temporary Classrooms.** Bond proceeds would be used to replace the 1994 temporary trailer Math Village classroom complex with permanent First Year Experience classrooms, student support study spaces and instructional support labs. These trailers were rushed into service following the 1994 Northridge Earthquake and have exceeded their time of usable service. Additionally, proceeds would be used to replace the 1984 modular English as a Second Language classroom building. This modular building lacks a fire sprinkler system, is poorly ventilated and has also exceeded its time of usable service.

**Replacement of Business Building.** The 1981 Business Building will be replaced by a new building with instructional spaces, pending the final adoption of the 2020 Facilities Master Plan.

**Replacement of Campus Police Station.** The current police facility is antiquated and undersized. Applying bond proceeds to the replacement, construction, and relocation of the campus police station and including a public space for community and neighborhood use will improve public and campus safety.

**Landscaping / Water Conservation Improvements and Completing Pico Boulevard Frontage Improvements.** Applying bond proceeds for landscaping improvements, including landscaping improvements to complete the main campus Pico Boulevard frontage, will improve water conservation through water reclamation and installation of drought resistant landscaping.

**Completing Master Plan Improvements at the Santa Monica College Performing Arts Center Campus.** Construction at the Performing Arts Center campus has proceeded in phases, in coordination with available funding. The first phase added the Broad Stage and the Edye Second Space theaters. The second phase has added an East Wing rehearsal hall and music performance labs. The final phase, to be funded from bond proceeds, will include an underground three-level parking structure to replace most of the existing surface parking, along with an above-ground art gallery and green-space plaza. The theaters at the Performing Arts Center are among the most heavily used theaters in Los Angeles County.

**Designing and Installing an Outdoor Classroom.** The design, construction, installation and improvement of a venue for outdoor plays and class lectures.

**Making Environmental Performance Improvements.** Bond funds will be used to upgrade District facilities to achieve energy or resource use efficiency and water conservation and achieve sustainability for District operations.

**Upgrading Technology Infrastructure.** Bond proceeds will be applied to renovate, replace, upgrade, acquire, install and integrate major site, building and utility systems, equipment and related infrastructure, including lighting, electrical, wiring and related infrastructure for modern technology, classroom instructional technology, communications and security technology (including security cameras and monitoring systems), data, voice, public address and audio-visual communication, energy efficiency, management monitoring systems, networks, fixtures, controls and equipment, cable infrastructure, network expansion, wireless access points and other communications and administrative systems.

#### COMMUNITY JOINT USE PROJECTS

**Providing for a Joint Use Project with the City of Santa Monica.** The College will contribute up to \$20 million in bond funds for the expansion of the City of Santa Monica's Memorial Park to accommodate soccer and/or other field sports for use by College students and the general public.

**Providing for a Joint Use Project with the Santa Monica-Malibu Unified School District.** The Johns Adams Middle School Auditorium, adjacent to the College's main campus, has suffered earthquake damage and is no longer in service. The College will contribute up to \$20 million bond funds as needed to assist the School District in renovating or replacing the auditorium with a seating capacity of approximately 750, for joint use. This project is completed.

**Providing for City of Malibu Infrastructure and Community Educational Facilities.** The College will contribute up to \$25 million in funding enhancing its instructional presence in Malibu in partnership with the City of Malibu.

# Citizens' Bond Oversight Committee

*Meeting on October 19<sup>th</sup>, 2022*

June 30<sup>th</sup>, 2022 Report

*12 Months - FY 2021-22 - FINAL*

## **BOND CAPITAL CONSTRUCTION REPORTS**

District Management is responsible for the preparation and fair presentation of the statement of expenditures and bond proceeds in accordance with U.S. generally accepted accounting principles; this includes the design, implementation, and maintenance of internal control relevant to the preparation and fair presentation of the statement of expenditures of bond proceeds that is free from material misstatement, whether due to fraud or error.

This report is prepared in accordance with these requirements and all bond expenditures were made in compliance with all applicable laws.

**Santa Monica College - Bond Capital Construction Budget Summary - 6-30-2022**

Project Number	Project Name	Measure U Budget	Measure S Budget	Measure AA Budget	Measure V Budget	Interest	Other Funding Received *	Other Funding Pending **	Total Budget	Estimate at Completion	Status	Bond Funds Remaining
U-A	Purchase of BAE Airport Site	\$30,280,878							\$30,280,878	\$30,280,878	Completed	\$0
U-B	Emeritus College Facility	\$8,909,940					\$693,842		\$9,603,782	\$9,603,782	Completed	\$0
U-C	Purchase of 1738 Pearl Street	\$749,208							\$749,208	\$749,208	Completed	\$0
U-D	PE Temp. Bldg. Replacement	\$2,797,033							\$2,797,033	\$2,797,033	Completed	\$0
U-E	Remodel Library Village for Math	\$1,458,690							\$1,458,690	\$1,458,690	Completed	\$0
U-F	SM Airport Campus Site Improvements	\$4,170,264							\$4,170,264	\$4,170,264	Completed	\$0
U-G	SM Airport Campus West Building	\$19,709,741							\$19,709,741	\$19,709,741	Completed	\$0
U-H	Theater Arts Renovation	\$19,544,314							\$19,544,314	\$19,544,314	Completed	\$0
U-I	Earthquake Rpl. Liberal Arts North	\$6,011,584					\$6,496,141		\$12,507,725	\$12,507,725	Completed	\$0
U-K	Earthquake Rpl. Liberal Arts South	\$6,108,150					\$10,625,070		\$16,733,220	\$16,733,220	Completed	\$0
U-L	Shuttle Replacement Parking	\$18,969,509							\$18,969,509	\$18,969,509	Completed	\$0
U-M	North Quad Plaza	\$11,388,463							\$11,388,463	\$11,388,463	Completed	\$0
U-Q	Infrastructure & Safety	\$4,003,084							\$4,003,084	\$4,003,084	Completed	\$0
U-R	Restroom Improvements	\$17,501							\$17,501	\$17,501	Completed	\$0
S-1	Athletic Fields Phase I, Corsair Field		\$4,372,535				\$67,530		\$4,440,065	\$4,440,065	Completed	\$0
S-1A	Athletic Fields Phase I, John Adams		\$2,969,807						\$2,969,807	\$2,969,807	Completed	\$0
S-10	Pico Promenade Improvements, Phase I		\$1,018,009						\$1,018,009	\$1,018,009	Completed	\$0
S-13	Adv. Architecture Related Exp for AA		\$0						\$0	\$0	Completed	\$0
AA-114	Community Classroom & Facility Projects			\$3,162,183					\$3,162,183	\$3,162,183	Completed	\$0
U-T	14th and Pico Project	\$319,242							\$319,242	\$319,242	Completed	\$0
U-N	Letters & Sci Demo/Restore	\$0							\$0	\$0	Completed	\$0
AA-108	Renovation of Corsair Stadium			\$35,299					\$35,299	\$35,299	Completed	\$0
S-2	Performing Arts Complex		\$37,697,625				\$2,992,576		\$40,690,201	\$40,690,201	Completed	\$0
U-J	Music Complex	\$2,011,371					\$2,618,113		\$4,629,484	\$4,629,484	Completed	\$0
S-3, AA-109	Career Opportunity Center			\$0					\$0	\$0	Completed	\$0
AA-118	Infrastructure & Technology - Utility			\$27,753					\$27,753	\$27,753	Completed	\$0
AA-111	Business & Facilities Infrastructure			\$1,968,124					\$1,968,124	\$1,968,124	Completed	\$0
AA-117	Infrastructure & Technology - Technology			\$2,434,417					\$2,434,417	\$2,434,417	Completed	\$0
S-7, AA-113	Energy Efficiency Projects		\$293,361	\$3,016,773			\$708,637		\$4,018,771	\$4,018,771	Completed	\$0
S-15	Signage Safety/Information		\$706,713						\$706,713	\$706,713	Completed	\$0
AA-102	Infrastructure & Technology - Information Technology Relocation			\$23,140,771			\$19,798		\$23,160,569	\$23,160,569	Completed	\$0
S-8, AA-116	Satellite Campus Parking Facilities and Roadway		\$3,891,747	\$2,130,670					\$6,022,417	\$6,022,417	Completed	\$0
AA-107	Madison East Wing Seismic Upgrade			\$30,161,852					\$30,161,852	\$30,161,852	Completed	\$0
S-4, AA-104	Replacement Health/PE/Fitness Central Plant Building		\$11,603,383	\$44,428,222			\$208,847		\$56,240,452	\$56,240,452	Completed	\$0
AA-101	Environmental Performance - Central Plant Connections			\$10,767,251					\$10,767,251	\$10,767,251	Completed	\$0
S-14, AA-115	Real Property Acquisition		\$45,597	\$24,638,386					\$24,683,983	\$24,683,983	Completed	\$0
AA-103	Media and Technology Complex - Academy Site			\$124,669,502			\$6,835,391		\$131,504,893	\$131,454,893	Completed	\$6,763
AA-119	Emergency Lighting, Fire Alarm, and Security System			\$11,515,614					\$11,515,614	\$11,515,614	Completed	\$0
15004829	Student Services Building	\$21,131,135	\$45,595,322	\$6,870,490	\$33,624,909	\$21,681,308	\$1,321,000		\$130,224,164	\$130,224,164	Completed	\$9,016,712
S-5, V-104	Early Childhood Development/Childcare		\$8,858,656		\$15,405,517		\$6,661,598		\$30,925,771	\$30,925,771	Completed	\$2,427,305
S-6, AA-110, V-103	Malibu Center and Site Acquisition		\$25,132,568		\$34,287,482	\$2,294,791			\$61,714,841	\$61,582,273	In Construction	\$16,613,325
U-S, S-11, AA-112, V-109	Master Planning	\$2,110,430	\$716,428	\$834,697	\$1,000,000				\$4,661,555	\$4,661,555	In Design	\$268,342
U-P, AA-106, V-101	Replacement Math and Science Extension Building	\$308,336		\$2,244,008	\$82,317,992		\$15,159,528	\$24,928,472	\$124,958,336	\$124,958,336	In Construction	\$58,280,249
AA-105, V-110	Drescher - Academic Modernization, Bookstore, Pico Promenade II			\$5,082	\$13,000,000				\$13,005,082	\$13,005,082	In Planning	\$13,000,000
V-105	Art Building Replacement				\$24,000,000		\$286,093	\$10,614,907	\$34,901,000	\$34,901,000	In Design	\$22,324,300
V-106	Business Building Renovation				\$12,547,000			\$12,470,000	\$25,017,000	\$25,017,000	In Planning	\$12,543,600
V-107	Air Conditioning				\$10,777,654				\$10,777,654	\$10,777,654	In Construction	\$653,573
V-108	ADA				\$4,000,000				\$4,000,000	\$4,000,000	In Planning	\$4,000,000
V-111	Outdoor Classroom				\$321,723				\$321,723	\$321,723	Completed	\$0
V-112	John Adams MS Auditorium (SMMUSD)				\$20,000,000				\$20,000,000	\$20,000,000	Completed	\$0
V-113	City of Santa Monica				\$20,000,000				\$20,000,000	\$20,000,000	In Planning	\$20,000,000
V-114	Classrooms Relocation				\$7,400,000				\$7,400,000	\$7,400,000	Completed	\$113,281
S-12, V-120	Other Bond Related Expenses		\$476,636		\$300,000				\$776,636	\$909,204	In Planning	\$55,446
V-115	TBD				\$39,717,723				\$39,717,723	\$39,717,723	In Planning	\$39,446,785
S-16, AA-121, V-121	Cost of Issuance		\$119,470	\$498,026	\$800,000				\$1,417,496	\$1,417,496	In Planning	\$55,848
AA-122, V-122	Management Reserve			\$2,446,709	\$25,500,000	\$6,152,892			\$34,099,601	\$34,149,601	In Planning	\$27,946,709
U-U, S-17, AA-123, V-123	Unissuable	\$1,127	\$2,143	\$4,171					\$7,441	\$7,441	On-Going	\$0
<b>Project Totals</b>		<b>\$160,000,000</b>	<b>\$143,500,000</b>	<b>\$295,000,000</b>	<b>\$345,000,000</b>	<b>\$30,128,991</b>	<b>\$54,694,164</b>	<b>\$48,013,379</b>	<b>\$1,076,336,534</b>	<b>\$1,076,336,534</b>		<b>\$226,752,238</b>

\* City of SM: \$14,647,889; FEMA: \$2,456,388; State: \$8,363,000; Prop T: \$2,618,113; DWP: \$86,245; SCE: \$844,284; Gas Co.: \$106,262; Madison Foundation: \$2,992,576; KCRW: \$6,803,412; Emeritus College Foundation: \$693,842; Bond Interest and Cost of Issuance Refund: \$29,858,053

\*\* City of SM: \$2,220,533; State: \$60,588,907


**Bond Sales / Expenses Report**

As of June 30, 2022

<b>Measure S Bond \$143,500,000 (1)</b>	
Bond Issue Date	Amount
2005	\$58,000,000
2007	\$8,500,000
2009	\$56,997,859
2017	\$20,000,000
<b>Total Available</b>	<b>\$143,497,859</b>
Expenses as of 6-30-2022	\$143,497,859
<b>Total Available Remaining</b>	<b>\$0</b>
Unsold Bond Amount	\$2,141
<b>Total Available as of 7-1-2022</b>	<b>\$2,141</b>

Total Bond Program (S,AA,V)	\$783,500,000
Total Bonds Issued	\$783,493,688
Total Expenses as of 6-30-22	\$556,741,449
Total Available Remaining	\$226,752,239
Total Unsold Bond	\$6,312

<b>Measure AA Bond \$295,000,000</b>	
Bond Issue Date	Amount
2010	\$100,000,000
2014	\$144,995,829
2017	\$50,000,000
<b>Total Available</b>	<b>\$294,995,829</b>
Expenses as of 6-30-2022	\$292,302,532
<b>Total Available Remaining</b>	<b>\$2,693,297</b>
Unsold Bond Amount	\$4,171
<b>Total Available as of 7-1-2022</b>	<b>\$2,697,468</b>

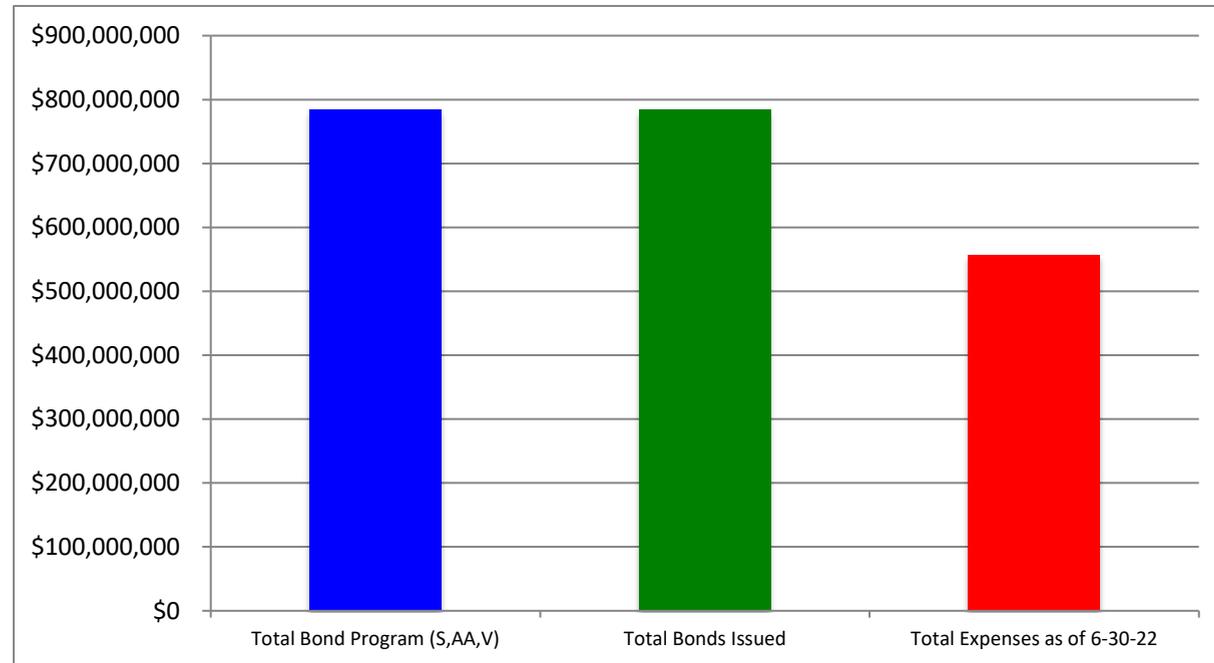

<b>Measure V Bond \$345,000,000</b>	
Bond Issue Date	Amount
2018	\$180,000,000
2022	\$165,000,000
<b>Total Available</b>	<b>\$345,000,000</b>
Expenses as of 6-30-2022	\$120,941,058
<b>Total Available Remaining</b>	<b>\$224,058,942</b>
Unsold Bond Amount	\$0
<b>Total Available as of 7-1-2022</b>	<b>\$224,058,942</b>

Interest	Measure S	Measure AA	Measure V
As of 6-30-22	\$12,148,354	\$6,978,496	\$8,737,900
Expenditure / Arbitrage as of 6-30-22	\$12,148,354	\$5,192,948	\$0
<b>Available Interest as of 7-1-22</b>	<b>\$0</b>	<b>\$1,785,548</b>	<b>\$8,737,900</b>


Cost of Issuance Refund	Measure S
As of 6-30-22	\$35,575
Expenditure as of 6-30-22	\$35,575
<b>Available as of 7-1-22</b>	<b>\$0</b>

(1) Original Bond \$135,000,000, refunding on 2-15-07 received additional \$8,500,000

**Measure S Bond Budget**

As of June 30, 2022

	Project Name	Completion	Project Budget	Measure S Allocation	Other Funding	Measure S Expenditures as of 6/30/22	Measure S Expenditures as of 3/31/22	Measure S Expenditures Last Period	Total Measure S Remaining
1	Athletic Fields Phase I, Corsair Field	Completed	\$4,440,065	\$4,372,535	\$67,530	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	Completed	\$2,969,807	\$2,969,807	\$0	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	Completed	\$40,690,201	\$37,697,625	\$2,992,576	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	Completed	\$58,272,030	\$11,603,383	\$46,668,647	\$11,603,383	\$11,603,383	\$0	\$0
5	Early Childhood Development/Childcare	Completed	\$30,925,771	\$8,858,656	\$22,067,115	\$8,858,656	\$8,858,656	\$0	\$0
6	Malibu Site Acquisition and Center	November 2022	\$61,714,841	\$25,132,568	\$36,582,273	\$25,132,568	\$25,132,568	\$0	\$0
7	Energy Efficiency Projects	Completed	\$510,685	\$293,363	\$217,322	\$293,363	\$293,363	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	Completed	\$7,022,417	\$3,891,747	\$3,130,670	\$3,891,747	\$3,891,747	\$0	\$0
9	Parking Garage, Grounds and Equipment - Student Services	Completed	\$130,224,164	\$45,595,322	\$84,628,842	\$45,595,322	\$45,595,322	\$0	\$0
10	Pico Promenade Improvements	Completed	\$1,018,009	\$1,018,009	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	Completed	\$716,428	\$716,428	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	Completed	\$476,636	\$476,636	\$0	\$476,636	\$476,636	\$0	\$0
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	Completed	\$45,597	\$45,597	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	Completed	\$706,713	\$706,713	\$0	\$706,713	\$706,713	\$0	\$0
16	Cost of Issuance	Completed	\$119,470	\$119,470	\$0	\$119,470	\$119,470	\$0	\$0
17	Unissuable Bond	Completed	\$2,141	\$2,141	\$0	\$0	\$0	\$0	\$2,141
	<b>Project Totals</b>		<b>\$339,852,834</b>	<b>\$143,500,000</b>	<b>\$196,354,975</b>	<b>\$143,497,859</b>	<b>\$143,497,859</b>	<b>\$0</b>	<b>\$2,141</b>

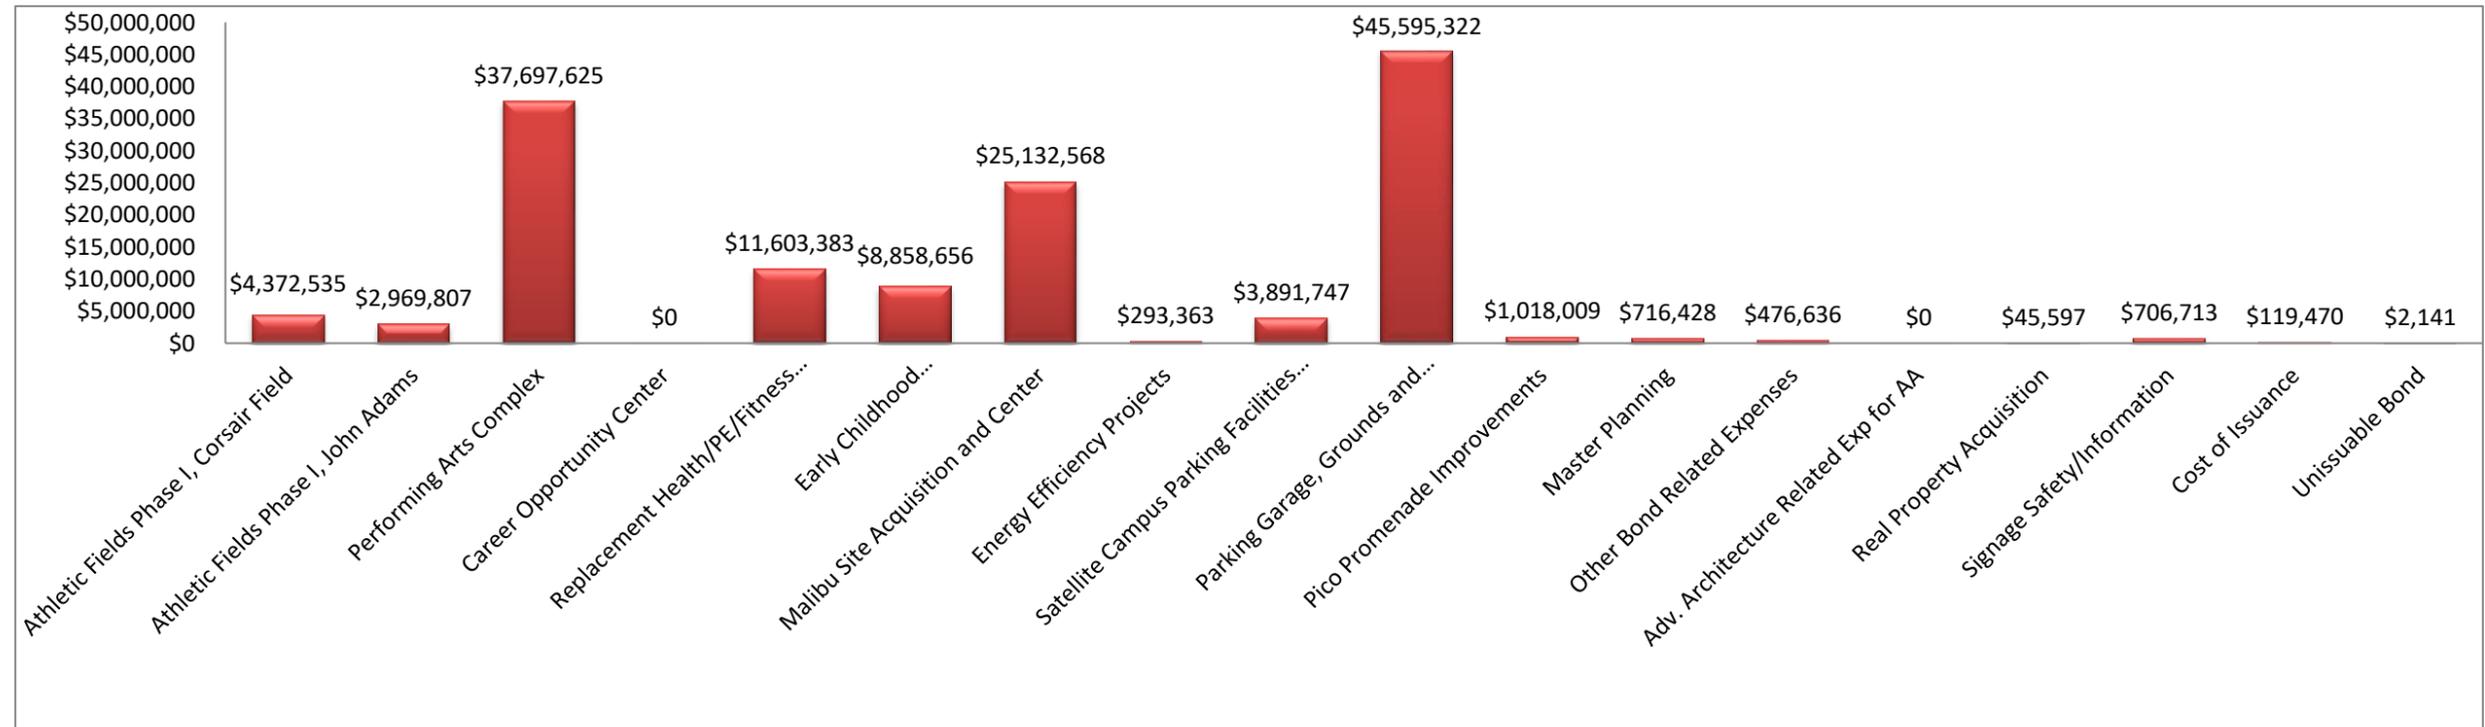

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
**Measure S Bond Budget History**  
as of June 30, 2022

MEASURE S

	Project Name	Completion	Preliminary Measure S Budget	Measure S Budget as of 3/31/22	Measure S Budget as of 6/30/22	Variance	Measure S Remaining as of 6/30/22
1	Athletic Fields Phase I, Corsair Field	<i>Completed</i>	\$1,800,000	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	<i>Completed</i>	\$35,200,000	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	<i>Completed</i>	\$24,000,000	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	<i>Completed</i>	\$20,000,000	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	<i>Completed</i>	\$20,000,000	\$11,603,383	\$11,603,383	\$0	\$0
5	Early Childhood Development/Childcare	<i>Completed</i>	\$7,000,000	\$8,858,656	\$8,858,656	\$0	\$0
6	Malibu Site Acquisition and Center	November 2022	\$25,000,000	\$25,132,568	\$25,132,568	\$0	\$0
7	Energy Efficiency Projects	<i>Completed</i>	\$2,000,000	\$293,363	\$293,363	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	<i>Completed</i>	\$0	\$3,891,747	\$3,891,747	\$0	\$0
9	Parking Garage, Grounds and Equipment - Student Services	<i>Completed</i>	\$0	\$45,595,322	\$45,595,322	\$0	\$0
10	Pico Promenade Improvements, Phase I	<i>Completed</i>	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	<i>Completed</i>	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	<i>Completed</i>	\$0	\$476,636	\$476,636	\$0	\$0
13	Adv. Architecture Related Exp for AA	<i>Completed</i>	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	<i>Completed</i>	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	<i>Completed</i>	\$0	\$706,713	\$706,713	\$0	\$0
16	Cost of Issuance	<i>Completed</i>	\$0	\$119,470	\$119,470	\$0	\$0
17	Unissuable Bond	<i>Completed</i>	\$0	\$2,141	\$2,141	\$0	\$2,141
	<b>Project Totals</b>		<b>\$135,000,000</b>	<b>\$143,500,000</b>	<b>\$143,500,000</b>	<b>\$0</b>	<b>\$2,141</b>

**Measure S Project Schedule**

As of June 30, 2022

	Project Name	Completion	2018	2019	2020	2021	2022
1	Athletic Fields Phase I, Corsair Field	<i>Completed</i>					
1A	Athletic Fields Phase I, John Adams	<i>Completed</i>					
2	Performing Arts Center	<i>Completed</i>					
3	Career Opportunity Center	<i>Completed</i>					
4	Replacement Health/PE/Fitness Building	<i>Completed</i>					
5	Early Childhood Development/Childcare	<i>Completed</i>					
6	Malibu Site Acquisition and Center	November 2022					
7	Energy Efficiency Projects	<i>Completed</i>					
8	Satellite Campus Parking Facilities and Roadway Improvements	<i>Completed</i>					
9	Parking Garage, Grounds and Equipment - Student Services	<i>Completed</i>					
10	Pico Promenade Improvements	<i>Completed</i>					
11	Master Planning	<i>Completed</i>					
12	Other Bond Related Expenses	<i>Completed</i>					
13	Adv. Architecture Related Exp for AA	<i>Completed</i>					
14	Real Property Acquisition	<i>Completed</i>					
15	Signage Safety/Information	<i>Completed</i>					
16	Cost of Issuance	<i>Completed</i>					
17	Unissuable Bond	<i>Completed</i>					

In Planning
In Construction

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
**MEASURE S EXPENDITURES**  
 FUND 42.3  
 As of June 30, 2022

MEASURE S

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<b>S7100019</b>																				
<b>Athletic Field Phase I, Corsair Field (1)</b>																				
Legal		\$0	\$0	\$0	\$301	\$175	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$476
Building & Additions		\$0	\$0	\$0	\$300,380	\$2,579,095	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,879,475
Architect		\$27,332	\$43,815	\$197,557	\$252,736	\$279,173	\$26,563	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$827,176
Inspection & Testing		\$0	\$0	\$0	\$23,411	\$57,585	\$640	\$296	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$81,932
Project Management		\$0	\$0	\$0	\$9,871	\$42,374	\$565	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$52,810
Cap Equipment		\$0	\$0	\$0	\$0	\$483,017	\$35,271	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$518,288
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$2,066	\$10,312	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,378
<b>Total</b>		<b>\$27,332</b>	<b>\$43,815</b>	<b>\$197,557</b>	<b>\$586,699</b>	<b>\$3,443,485</b>	<b>\$73,350</b>	<b>\$296</b>	<b>\$0</b>	<b>\$4,372,535</b>										
Project Budget	\$4,440,065	Received																		
Less Other Funding*	\$67,530	\$67,530																		
Net	\$4,372,535																			
Actual Measure S Expenditures	\$4,372,535																			
Running Balance	\$0																			

\* Other Funding Source:  
 Metropolitan Water District \$67,530 received


**Athletic Field Phase I, Corsair Field**

**Project Description:**  
 Renovation of the Corsair Field, stadium lighting and sound system

**Status:**  
 Completed, 2009

**Architect:**  
 CO Architects

**Contractor:**  
 Byrom Davey, Inc.

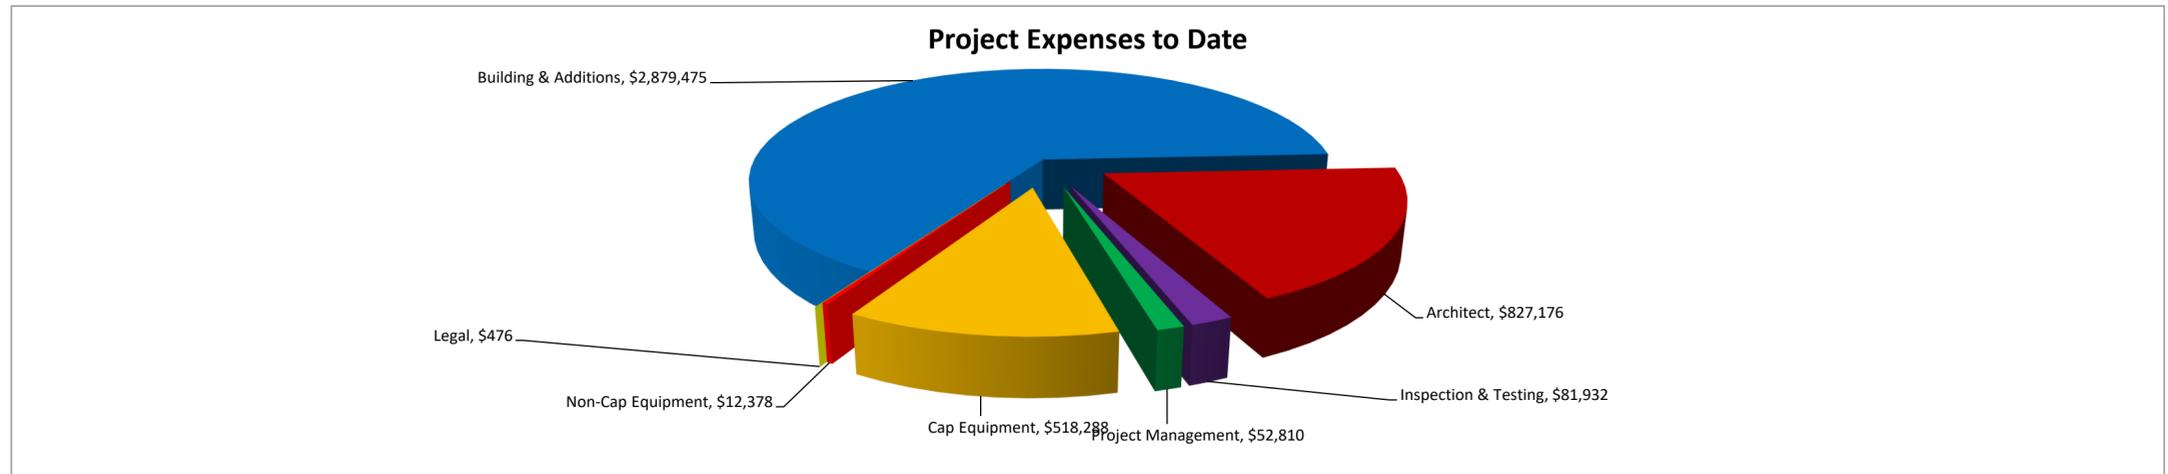

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
**MEASURE S EXPENDITURES**  
 FUND 42.3  
 As of June 30, 2022

MEASURE S

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals	
<b>S7100038</b>																					
<b>Athletic Field Phase I, John Adams (1A)</b>																					
Legal		\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$75
Building & Additions		\$0	\$0	\$0	\$16,556	\$1,395,261	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	\$0	\$49,984	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$56,066
Project Management		\$0	\$0	\$0	\$10,921	\$45,170	\$38	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$56,128
Cap Equipment		\$0	\$0	\$0	\$0	\$1,290,672	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,290,672
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$11,334	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,334
<b>Total</b>		<b>\$0</b>	<b>\$8,681</b>	<b>\$97,148</b>	<b>\$39,701</b>	<b>\$2,824,239</b>	<b>\$38</b>	<b>\$0</b>	<b>\$2,969,807</b>												
Project Budget	\$2,969,807																				
Less Other Funding	\$0																				
Net	\$2,969,807																				
Actual Measure S Expenditures	\$2,969,807																				
Running Balance	\$0																				


**Athletic Field Phase I, John Adams**

**Project Description:**  
Renovation of John Adams Field and lighting

**Status:**  
Completed, 2008

**Architect:**  
Caldwell Architects

**Contractor:**  
Byrom Davey, Inc.

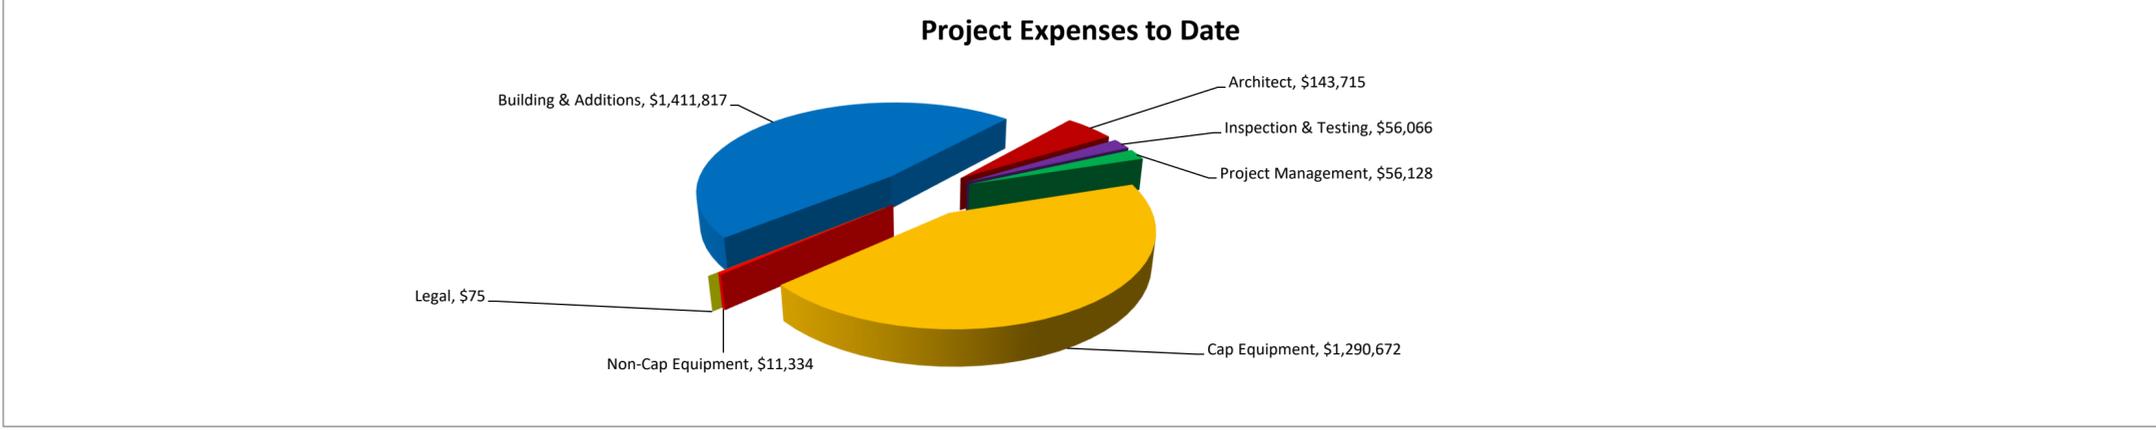

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
**MEASURE S EXPENDITURES**  
 FUND 42.3  
 As of June 30, 2022

MEASURE S

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
S7100012																				
<b>Performing Arts Center (2)</b>																				
Consultants		\$0	\$0	\$0	\$121,790	\$76,639	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$198,429
Other Contract Services		\$0	\$0	\$4,269	\$0	\$22,729	\$22	\$68	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,088
Supplies		\$0	\$0	\$0	\$14,565	\$5,810	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,375
Legal		\$0	\$0	\$34,329	\$275,667	\$492,731	\$15,629	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$818,356
Advertising		\$0	\$0	\$0	\$320	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$320
Building & Additions		\$7,784,151	\$10,292,986	\$8,930,813	\$2,991,903	\$1,629,990	\$50,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$31,679,843
Architect		\$0	\$811,312	\$182,457	\$412,309	\$121,588	\$108	\$1,962	\$0	\$0	\$87,054	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,616,790
Engineering		\$0	\$3,600	\$5,250	\$1,500	\$9,650	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,000
Inspection & Testing		\$104,308	\$722,685	\$411,193	\$210,381	\$22,256	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,470,823
Project Management		\$31,984	\$155,732	\$248,876	\$263,690	\$47,915	\$3,244	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$751,441
Cap Equipment		\$0	\$0	\$130,218	\$292,565	\$342,693	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$765,476
Non-Cap Equipment		\$0	\$0	\$15,124	\$93,106	\$220,455	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$328,685
<b>Total</b>		<b>\$7,920,443</b>	<b>\$11,986,315</b>	<b>\$9,962,528</b>	<b>\$4,677,797</b>	<b>\$2,992,455</b>	<b>\$69,003</b>	<b>\$2,030</b>	<b>\$0</b>	<b>\$0</b>	<b>\$87,054</b>	<b>\$0</b>	<b>\$37,697,625</b>							
Project Budget	\$40,690,201	<b>Received</b>																		
Less Other Funding*	\$2,992,576	\$2,992,576																		
Net	\$37,697,625																			
Actual Measure S Expenditures	\$37,697,625																			
Running Balance	\$0																			

\* Other Funding Source:  
 Madison Project Foundation \$2,992,576 received

**Performing Arts Center**


**Project Description:**  
 Construction of a state-of-the-art 499 seat performing arts theater

**Status:**  
 Completed, 2008

**Architect:**  
 Renzo Zecchetto

**Contractor:**  
 FTR International

**Project Expenses to Date**

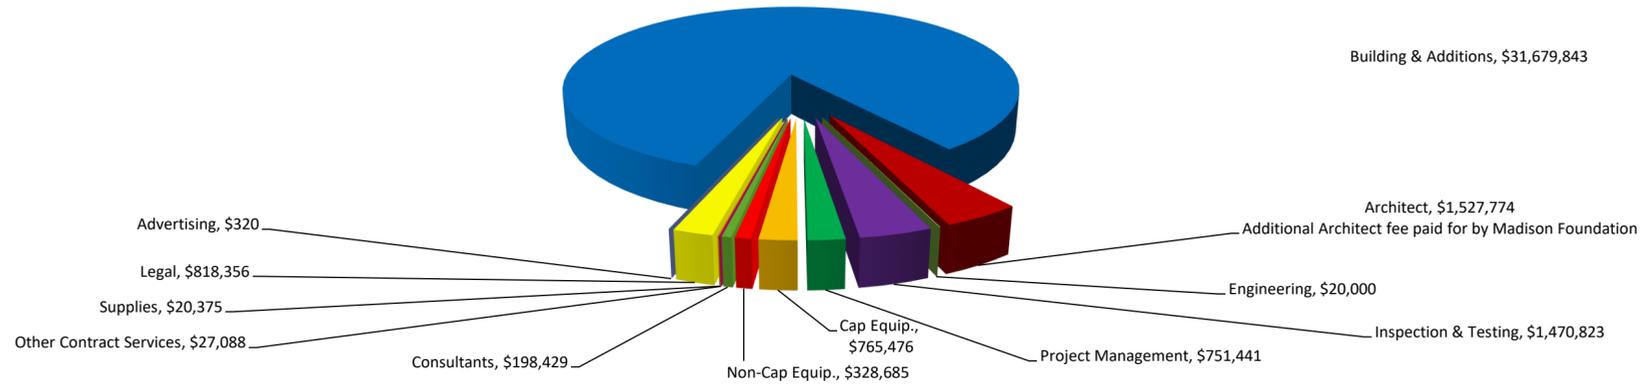

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
**MEASURE S EXPENDITURES**  
 FUND 42.3  
 As of June 30, 2022

MEASURE S

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<i>S710033, S7100144, S7100060</i>																				
<b>Replacement Health/PE/Fitness Building (4)</b>																				
Supplies		\$4,809	\$288	\$0	\$0	\$0	\$163	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,260
Legal		\$0	\$0	\$0	\$0	\$1,413	\$75	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,488
Other Contract Services		\$1,634	\$25,934	\$0	\$0	\$253	\$165	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,985
Repair Facility		\$0	\$4,861	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,861
Building & Additions		\$0	\$0	\$0	\$0	\$112,410	\$526,552	\$0	\$0	\$0	\$6,037,080	\$4,775,714	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,451,757
Architect		\$0	\$0	\$0	\$0	\$0	\$41,044	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$41,044
Inspection & Testing		\$0	\$0	\$0	\$0	\$6,518	\$14,363	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,881
Project Management		\$0	\$0	\$0	\$0	\$9,070	\$23,425	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$32,495
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$17,613	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$17,613
<b>Total</b>		<b>\$6,443</b>	<b>\$31,083</b>	<b>\$0</b>	<b>\$0</b>	<b>\$129,663</b>	<b>\$605,787</b>	<b>\$17,613</b>	<b>\$0</b>	<b>\$0</b>	<b>\$6,037,080</b>	<b>\$4,775,714</b>	<b>\$0</b>	<b>\$11,603,383</b>						
Project Budget	\$58,272,030																			
Less Other Funding*	\$46,668,647																			
Net	\$11,603,383																			
Actual Measure S Expenditures	\$11,603,383																			
Running Balance	\$0																			
* Other Funding Source: Measure AA \$46,459,800 allocated SCE \$190,847.28, Gas Co. \$18,000 received																				

<i>S710045</i>																				
<b>Early Childhood Development/Childcare (5)</b>																				
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$294	\$0	\$0	\$0	\$0	\$294
Consultants		\$0	\$0	\$0	\$9,200	\$0	\$0	\$0	\$0	\$4,800	\$12,930	\$14,078	\$1,388	\$0	\$0	\$0	\$0	\$0	\$0	\$42,395
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,690	\$6,905	\$0	\$0	\$0	\$0	\$0	\$0	\$8,595
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$242	\$747,457	\$5,197,194	\$182,301	\$0	\$0	\$0	\$6,127,193
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$966	\$51,792	\$142,428	\$142,968	\$476,827	\$78,408	\$67,918	\$329,152	\$0	\$0	\$0	\$0	\$1,290,458
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,888	\$0	\$0	\$0	\$0	\$3,888
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$37,796	\$7,475	\$823	\$2,323	\$0	\$4,085	\$296,806	\$2,256	\$0	\$0	\$351,564
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$1,246	\$21,980	\$58,247	\$33,435	\$8,803	\$3,118	\$0	\$307,493	\$599,950	\$0	\$0	\$0	\$1,034,270
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$9,200</b>	<b>\$0</b>	<b>\$0</b>	<b>\$1,246</b>	<b>\$22,946</b>	<b>\$152,635</b>	<b>\$196,268</b>	<b>\$166,670</b>	<b>\$485,344</b>	<b>\$85,555</b>	<b>\$1,127,247</b>	<b>\$6,426,989</b>	<b>\$184,557</b>	<b>\$0</b>	<b>\$0</b>	<b>\$8,858,656</b>
Project Budget	\$30,925,771	<i>Received</i>																		
Less Other Funding*	\$22,067,115	\$4,441,066																		
Net	\$8,858,656																			
Actual Measure S Expenditures	\$8,858,656																			
Running Balance	\$0																			
* Other Funding Source: 1) City of Santa Monica \$6,661,598 committed 2) Measure V \$15,405,517 allocated																				

<i>S710077, S7100015</i>																				
<b>Malibu Site Acquisition and Facilities (6)</b>																				
Consultants		\$0	\$0	\$0	\$0	\$30,000	\$0	\$0	\$72,157	\$68,109	\$30,342	\$66,277	\$60,262	\$3,406	\$17	\$0	\$0	\$0	\$0	\$330,570
Legal		\$0	\$27,722	\$16,787	\$6,159	\$504	\$0	\$0	\$0	\$0	\$1,360	\$78,851	\$40,114	\$7,353	\$6,324	\$0	\$0	\$0	\$0	\$185,174
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,092	\$0	\$0	\$1,820	\$0	\$0	\$0	\$115,267	\$0	\$0	\$0	\$119,178
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$536	\$0	\$0	\$0	\$2,019,660	\$3,136,052	\$2,002,677	\$6,841,303	\$528,091	\$14,528,319
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$966	\$257,584	\$732,891	\$173,610	\$34,753	\$151,772	\$341,307	\$331,426	\$101,080	\$0	\$0	\$2,125,390
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$785	\$562	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,346
Inspection & Testing		\$4,388	\$3,750	\$141,462	\$0	\$0	\$0	\$0	\$98,022	\$15,575	\$22,939	\$10,960	\$0	\$0	\$39,460	\$322,234	\$60,231	\$0	\$0	\$719,020
Project Management		\$0	\$0	\$220	\$0	\$0	\$0	\$2,886	\$55,064	\$53,185	\$47,778	\$118,144	\$97,856	\$46,400	\$431,268	\$747,160	\$485,580	\$38,030	\$0	\$2,123,569
Storm/Waste Water Treatment Center		\$0	\$2,500,000	\$0	\$0	\$2,500,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,000,000
<b>Total</b>		<b>\$4,388</b>	<b>\$2,531,472</b>	<b>\$158,468</b>	<b>\$6,159</b>	<b>\$2,530,504</b>	<b>\$0</b>	<b>\$2,886</b>	<b>\$228,301</b>	<b>\$395,237</b>	<b>\$836,407</b>	<b>\$449,662</b>	<b>\$232,985</b>	<b>\$208,931</b>	<b>\$2,838,036</b>	<b>\$4,652,138</b>	<b>\$2,649,568</b>	<b>\$6,879,333</b>	<b>\$528,091</b>	<b>\$25,132,568</b>
Project Budget	\$61,714,841																			
Less Other Funding*	\$36,582,273																			
Net	\$25,132,568																			
Actual Measure S Expenditures	\$25,132,568																			
Running Balance	\$0																			
* Other Funding Source: 1) Measure V \$34,287,482 2) Interest Allocated \$2,294,791																				

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
**MEASURE S EXPENDITURES**  
 FUND 42.3  
 As of June 30, 2022

MEASURE S

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<i>S7100043, S7100066</i>																				
<b>Energy Efficiency Projects (7)</b>																				
Legal		\$0	\$0	\$0	\$0	\$988	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$988
Building & Additions		\$0	\$0	\$0	\$0	\$106,921	\$355,294	-\$180,342	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$281,873
Engineering		\$0	\$0	\$0	\$10,500	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$10,500
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$10,500</b>	<b>\$107,910</b>	<b>\$355,294</b>	<b>-\$180,342</b>	<b>\$0</b>	<b>\$293,361</b>										
Project Budget	\$510,683	<b>Received</b>																		
Less Other Funding*	\$217,322	\$217,322																		
Net	\$293,361																			
Actual Measure S Expenditures	\$293,361																			
Running Balance	\$0																			
* Other Funding Source: SCE & The Gas Co. \$217,322 received																				

<i>S7100091, S7100092, S7100147</i>																				
<b>Satellite Campus Parking Facilities and Roadway Improvements (8)</b>																				
Legal		\$0	\$0	\$0	\$300	\$175	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$475
Other Contract Services		\$0	\$0	\$0	\$300	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$300
Advertising		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$278,178	\$1,860,152	\$449,543	\$37,777	\$0	\$0	\$64	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,625,714
Architect		\$0	\$0	\$324,919	\$324,864	\$136,911	\$34,490	\$1,397	\$2,289	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$824,871
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$30,896	\$5,470	\$12,165	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$48,531
Inspection & Testing		\$0	\$0	\$0	\$31,100	\$185,947	\$28,218	\$360	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$245,626
Project Management		\$0	\$0	\$0	\$18,288	\$64,880	\$31,137	\$8,659	\$0	\$2,569	\$10,730	\$6,046	\$535	\$0	\$0	\$0	\$0	\$0	\$0	\$142,844
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$3,387	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,387
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$324,919</b>	<b>\$653,031</b>	<b>\$2,248,065</b>	<b>\$546,775</b>	<b>\$48,194</b>	<b>\$2,289</b>	<b>\$2,569</b>	<b>\$41,626</b>	<b>\$11,580</b>	<b>\$12,700</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$3,891,747</b>
Project Budget	\$7,022,417																			
Less Other Funding	\$3,130,670																			
Net	\$3,891,747																			
Actual Measure S Expenditures	\$3,891,747																			
Running Balance	\$0																			
* Other Funding Source: Measure AA \$2,130,670, Measure V \$1,000,000 allocated																				

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
**MEASURE S EXPENDITURES**  
 FUND 42.3  
 As of June 30, 2022

**MEASURE S**

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals	
S7100142																					
<b>Parking Garage and Grounds - Student Services (9)</b>																					
Supplies		\$0	\$0	\$0	\$0	\$1,745	\$0	\$0	\$648	\$0	\$0	\$813	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,206
Consultants		\$0	\$0	\$0	\$0	\$20,700	\$0	\$0	\$0	\$0	\$0	\$0	\$1,740	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$22,440
Legal		\$0	\$0	\$0	\$0	\$2,154	\$17,486	\$4,800	\$2,257	\$17,221	\$0	\$3,570	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$47,488
Other Contract Services		\$0	\$0	\$0	\$0	\$1,508	\$10,952	\$1,986	\$46	\$0	\$12,083	\$5,034	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$31,608
Site Improvement		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,086	\$0	\$1,308	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,394
Building & Additions		\$0	\$0	\$0	\$0	\$2,555,940	\$5,925,152	\$78,717	\$77,320	\$5,509	\$715	\$0	\$3,721	\$11,308,792	\$16,249,515	\$0	\$0	\$0	\$0	\$0	\$36,205,381
Architect		\$0	\$0	\$0	\$2,266,766	\$2,674,054	\$0	\$37,111	\$75,163	\$0	\$0	\$0	\$0	\$0	\$287,176	\$0	\$0	\$0	\$0	\$0	\$5,340,270
Engineering		\$0	\$0	\$0	\$0	\$4,813	\$38,330	\$42,968	\$50,952	\$9,735	\$0	\$0	\$0	\$0	\$49,171	\$0	\$0	\$0	\$0	\$0	\$195,968
Inspection & Testing		\$0	\$0	\$0	\$0	\$131,009	\$161,847	\$54,069	\$32,306	\$30,909	\$4,123	\$22,296	\$38,186	\$516,217	\$851,397	\$0	\$0	\$0	\$0	\$0	\$1,842,359
Project Management		\$0	\$0	\$0	\$0	\$158,766	\$373,559	\$184,088	\$92,118	\$224,994	\$59,525	\$29,714	\$50,380	\$285,057	\$420,233	\$0	\$0	\$0	\$0	\$0	\$1,878,433
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$14,393	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14,393
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,381	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,381
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$2,266,766</b>	<b>\$5,550,689</b>	<b>\$6,541,719</b>	<b>\$403,737</b>	<b>\$342,192</b>	<b>\$289,454</b>	<b>\$76,445</b>	<b>\$62,735</b>	<b>\$94,027</b>	<b>\$12,110,066</b>	<b>\$17,857,492</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$45,595,322</b>
Project Budget	\$130,224,164																				
Less Other Funding*	\$84,628,842																				
Net	\$45,595,322																				
Actual Measure S Expenditures	\$45,595,322																				
Running Balance	\$0																				

\* Other Funding Source:  
 State of California \$1,321,000 received  
 Measure U \$21,131,135, Measure AA \$6,870,490, Measure V \$33,624,909 allocated  
 Measure U, S & AA interests \$21,681,308 allocated

**Parking Garage and Grounds - Student Services**


**Project Description:**  
 Consolidates various student services departments and college administration in a single complex at the front of the campus

**Facility Size:**  
 110,000 sq/ft & 500 cars underground parking structure

**Status:**  
 Phase 1 completed  
 Phase 2 completed

**Architect:**  
 Steinberg Architects, Morris Architects

**Contractor:**  
 Minaco, Bernards

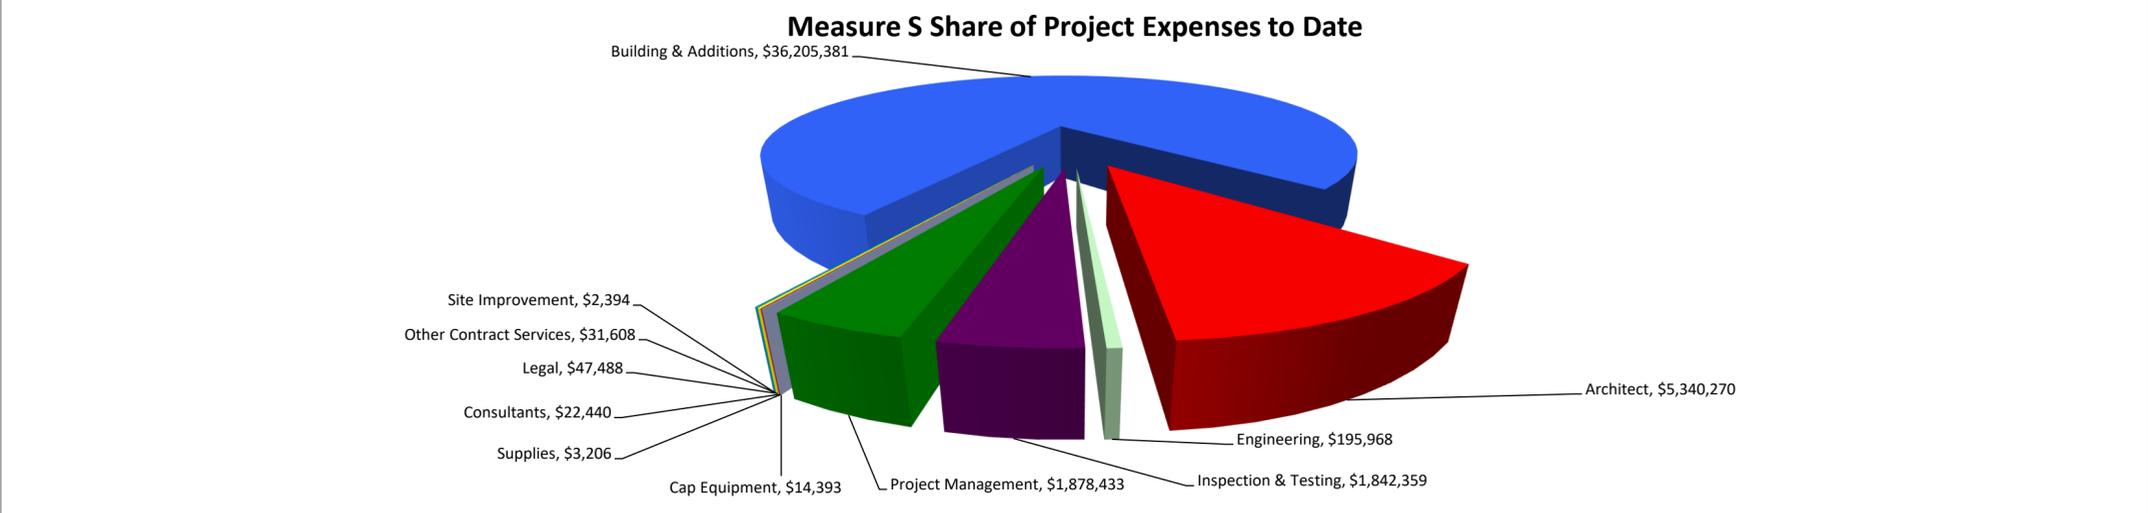

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
**MEASURE S EXPENDITURES**  
 FUND 42.3  
 As of June 30, 2022

**MEASURE S**

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<b>S7100044</b>																				
<b>Pico Promenade Improvements (10)</b>																				
Building & Additions		\$0	\$0	\$0	\$690	\$883,401	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$884,091
Architect		\$0	\$0	\$0	\$69,190	\$28,540	\$864	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$98,595
Inspection & Testing		\$0	\$0	\$0	\$0	\$7,591	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,591
Project Management		\$0	\$0	\$0	\$2,185	\$25,548	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,733
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$72,066</b>	<b>\$945,080</b>	<b>\$864</b>	<b>\$0</b>	<b>\$1,018,009</b>											
Project Budget	\$1,018,009																			
Less Other Funding	\$0																			
Net	\$1,018,009																			
Actual Measure S Expenditures	\$1,018,009																			
Running Balance	\$0																			

<b>S710004</b>																				
<b>Master Planning (11)</b>																				
Consultants		\$0	\$0	\$0	\$0	\$0	\$441,549	\$13,320	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$454,869
Printing		\$0	\$0	\$0	\$0	\$0	\$4,157	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,157
Advertising		\$0	\$0	\$0	\$0	\$0	\$3,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,000
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$442	\$200	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$642
Architect		\$0	\$0	\$0	\$0	\$0	\$192,358	\$24,736	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$217,094
Project Management		\$0	\$0	\$0	\$0	\$0	\$16,638	\$9,341	\$0	\$0	\$7,845	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$33,824
Filing Fees		\$0	\$0	\$0	\$0	\$0	\$0	\$2,842	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,842
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$658,143</b>	<b>\$50,439</b>	<b>\$0</b>	<b>\$0</b>	<b>\$7,845</b>	<b>\$0</b>	<b>\$716,428</b>							
Project Budget	\$716,428																			
Less Other Funding	\$0																			
Net	\$716,428																			
Actual Measure S Expenditures	\$716,428																			
Running Balance	\$0																			

<b>S7100048</b>																				
<b>Other Bond Related Expenses (12)</b>																				
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,971	\$2,524	\$6,239	\$1,354	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$13,089
Lease/Rental		\$0	\$0	\$0	\$0	\$0	\$0	\$11,142	\$15,099	\$15,285	\$14,809	\$13,418	\$13,120	\$16,611	\$17,281	\$23,757	\$0	\$0	\$0	\$140,522
Supplies		\$0	\$0	\$0	\$0	\$0	\$3,638	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,638
Legal		\$0	\$0	\$0	\$0	\$0	\$8,917	\$15,649	\$13,401	\$450	\$503	\$38,130	\$9,186	\$0	\$0	\$0	\$0	\$0	\$0	\$86,236
Software License		\$0	\$0	\$0	\$0	\$0	\$0	\$1,997	\$0	\$3,565	\$0	\$4,200	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$9,762
Advertising		\$0	\$0	\$0	\$0	\$0	\$2,278	\$0	\$0	\$0	\$0	\$0	\$864	\$0	\$0	\$0	\$0	\$0	\$0	\$3,142
Other Contract Services		\$0	\$0	\$0	\$0	\$1,800	\$17,206	\$23,558	\$19,208	\$15,816	\$13,627	\$13,952	\$12,963	\$11,760	\$18,900	\$15,225	\$0	\$0	\$0	\$164,014
Moving Services		\$0	\$0	\$0	\$0	\$0	\$400	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$400
Project Management		\$0	\$0	\$0	\$0	\$0	\$17,747	\$13,179	\$11,963	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$42,888
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$10,086	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$10,086
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$2,860	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,860
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$1,800</b>	<b>\$50,185</b>	<b>\$67,328</b>	<b>\$55,713</b>	<b>\$37,901</b>	<b>\$31,939</b>	<b>\$77,330</b>	<b>\$36,921</b>	<b>\$25,744</b>	<b>\$35,511</b>	<b>\$32,506</b>	<b>\$23,757</b>	<b>\$0</b>	<b>\$0</b>	<b>\$476,636</b>
Project Budget	\$476,636																			
Less Other Funding	\$0																			
Net	\$476,636																			
Actual Measure S Expenditures	\$476,636																			
Running Balance	\$0																			

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
**MEASURE S EXPENDITURES**  
 FUND 42.3  
 As of June 30, 2022

MEASURE S

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<b>S7100049</b>																				
<b>Adv Architecture Related Exp for AA (13)</b>																				
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$45,734</b>	<b>-\$45,734</b>	<b>\$0</b>												
Project Budget	\$0																			
Less Other Funding	\$0																			
Net	\$0																			
Actual Measure S Expenditures	\$0																			
Running Balance	\$0																			

<b>S7100057</b>																				
<b>Real Property Acquisition (14)</b>																				
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$18,721	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$18,721
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$6,336	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,336
Project Management		\$0	\$0	\$0	\$0	\$0	\$20,540	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,540
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$45,597</b>	<b>\$0</b>	<b>\$45,597</b>											
Project Budget	\$45,597																			
Less Other Funding	\$0																			
Net	\$45,597																			
Actual Measure S Expenditures	\$45,597																			
Running Balance	\$0																			

<b>S7100072</b>																				
<b>Campus Signage (15)</b>																				
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$303	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$303
Consultants		\$0	\$0	\$0	\$0	\$0	\$32,225	\$23,725	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$55,950
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$187	\$0	\$836	\$0	\$0	\$0	\$1,051	\$0	\$0	\$0	\$0	\$0	\$2,074
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$638	\$0	\$0	\$1,440	\$1,325	\$416,937	\$0	\$0	\$0	\$0	\$0	\$0	\$420,339
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$22,953	\$0	\$0	\$8,260	\$8,388	\$28,622	\$165	\$0	\$0	\$0	\$0	\$0	\$68,388
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$156,258	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$156,258
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,402	\$0	\$0	\$0	\$0	\$0	\$3,402
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$32,225</b>	<b>\$204,064</b>	<b>\$0</b>	<b>\$836</b>	<b>\$9,700</b>	<b>\$9,712</b>	<b>\$445,559</b>	<b>\$4,618</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$706,713</b>
Project Budget	\$706,713																			
Less Other Funding	\$0																			
Net	\$706,713																			
Actual Measure S Expenditures	\$706,713																			
Running Balance	\$0																			

<b>Measure S</b>																				
<b>Cost of Issuance (16)</b>																				
Cost of Issuance		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$119,470	\$0	\$0	\$0	\$0	\$0	\$119,470
<b>Total</b>		<b>\$0</b>	<b>\$119,470</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$119,470</b>											
Project Budget	\$119,470																			
Less Other Funding	\$0																			
Net	\$119,470																			
Actual Measure AA Expenditures	\$119,470																			
Running Balance	\$0																			


<b>Grand Total</b>		<b>\$7,958,606</b>	<b>\$14,601,366</b>	<b>\$10,740,621</b>	<b>\$8,321,918</b>	<b>\$20,819,624</b>	<b>\$8,933,245</b>	<b>\$617,492</b>	<b>\$651,441</b>	<b>\$878,632</b>	<b>\$1,287,285</b>	<b>\$6,814,769</b>	<b>\$6,083,251</b>	<b>\$12,554,384</b>	<b>\$21,858,285</b>	<b>\$11,111,633</b>	<b>\$2,857,882</b>	<b>\$6,879,333</b>	<b>\$528,091</b>	<b>\$143,497,859</b>
--------------------	--	--------------------	---------------------	---------------------	--------------------	---------------------	--------------------	------------------	------------------	------------------	--------------------	--------------------	--------------------	---------------------	---------------------	---------------------	--------------------	--------------------	------------------	----------------------

<b>Measure S Interest</b>		<b>17/18 Final</b>	<b>18/19 Final</b>
<b>Parking Garage and Grounds - Student Services (9)</b>			
Site Improvement		\$568	\$0
Building & Additions		\$8,224,377	\$629,869
Architect		\$189,078	\$67,105
Engineering		\$11,000	\$15,000
Inspection & Testing		\$125,080	\$0
Project Management		\$171,448	\$0
<b>Total</b>		<b>\$8,721,552</b>	<b>\$711,974</b>
Project Budget	\$9,433,526		
Actual Measure S Interest Expenditures	\$9,433,526		
Running Balance	\$0		

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
**Measure AA Bond Budget**  
 As of June 30, 2022

MEASURE AA

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 6/30/22	Measure AA Expenditures as of 3/31/22	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant Connections	Completed	\$10,767,251	\$10,767,251	\$0	\$10,767,251	\$10,767,251	\$0	\$0
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$23,160,569	\$23,140,771	\$19,798	\$23,140,771	\$23,140,771	\$0	\$0
103	Media and Technology Complex - Academy Site	Completed	\$131,504,893	\$124,669,502	\$6,835,391	\$124,662,739	\$124,624,015	\$38,724	\$6,763
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	Completed	\$56,240,452	\$44,428,222	\$11,812,230	\$44,428,222	\$44,428,222	\$0	\$0
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	Completed	\$13,005,082	\$5,082	\$13,000,000	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	July 2024	\$124,958,336	\$2,244,008	\$122,714,328	\$2,004,184	\$2,004,184	\$0	\$239,824
107	Madison East Wing Seismic Upgrade	Completed	\$30,161,852	\$30,161,852	\$0	\$30,161,852	\$30,161,852	\$0	\$0
108	Renovation of Corsair Stadium	Completed	\$35,299	\$35,299	\$0	\$35,299	\$35,299	\$0	\$0
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
110	Malibu Center	November 2022	\$61,582,273	\$0	\$61,582,273	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$1,968,124	\$1,968,124	\$0	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	Completed	\$834,697	\$834,697	\$0	\$834,697	\$834,697	\$0	\$0
113	Energy Efficiency Projects	Completed	\$3,508,088	\$3,016,773	\$491,315	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$3,162,183	\$3,162,183	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$24,638,386	\$24,638,386	\$0	\$24,638,386	\$24,638,386	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Completed	\$7,022,417	\$2,130,670	\$4,891,747	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$2,434,417	\$2,434,417	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$27,753	\$27,753	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	Completed	\$11,515,614	\$11,515,614	\$0	\$11,515,614	\$11,515,614	\$0	\$0
120	Student Services	Completed	\$130,224,164	\$6,870,490	\$123,353,674	\$6,870,490	\$6,870,490	\$0	\$0
121	Cost of Issuance	Completed	\$498,026	\$498,026	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$2,446,709	\$2,446,709	\$0	\$0	\$0	\$0	\$2,446,709
123	Unissuable Bond	Completed	\$4,171	\$4,171	\$0	\$0	\$0	\$0	\$4,171
	<b>Project Totals</b>		<b>\$637,249,876</b>	<b>\$295,000,000</b>	<b>\$344,700,756</b>	<b>\$292,302,533</b>	<b>\$292,263,809</b>	<b>\$38,724</b>	<b>\$2,697,467</b>

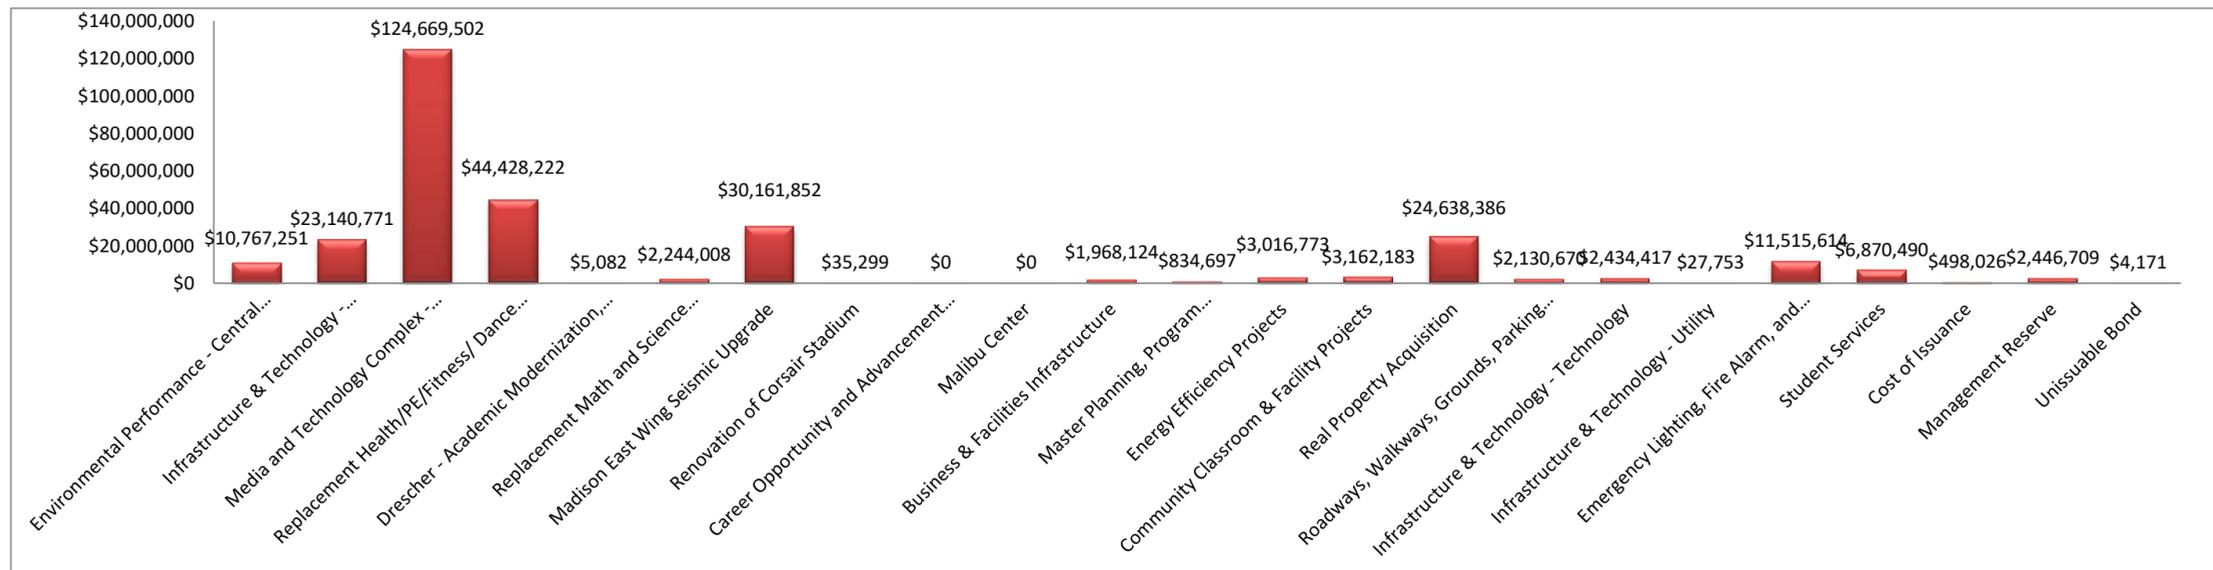

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
**Measure AA Bond Budget History**  
as of June 30, 2022

MEASURE AA

	<b>Project Name</b>	<b>Completion</b>	<b>Preliminary Measure AA Budget</b>	<b>Measure AA Budget as of 3/31/22</b>	<b>Measure AA Budget as of 6/30/22</b>	<b>Variance</b>	<b>Measure AA Remaining as of 6/30/22</b>
101	Environmental Performance - Central Plant Connections	<b>Completed</b>	\$12,034,042	\$10,767,251	\$10,767,251	\$0	\$0
102	Infrastructure & Technology - Information Technology Relocation	<b>Completed</b>	\$13,287,218	\$23,140,771	\$23,140,771	\$0	\$0
103	Media and Technology Complex - Academy Site	<b>Completed</b>	\$57,480,824	\$124,669,502	\$124,669,502	\$0	\$6,763
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	<b>Completed</b>	\$29,232,317	\$44,428,222	\$44,428,222	\$0	\$0
105	Drescher - Academic Modernization, Bookstore, Pico Promenade II	<b>Completed</b>	\$34,026,480	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	July 2024	\$68,259,000	\$2,244,008	\$2,244,008	\$0	\$239,824
107	Madison East Wing Seismic Upgrade	<b>Completed</b>	\$6,146,000	\$30,161,852	\$30,161,852	\$0	\$0
108	Renovation of Corsair Stadium	<b>Completed</b>	\$11,203,000	\$35,299	\$35,299	\$0	\$0
109	Career Opportunity and Advancement Center (Bundy)	<b>Completed</b>	\$32,384,000	\$0	\$0	\$0	\$0
110	Malibu Center	November 2022	\$6,069,031	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	<b>Completed</b>	\$17,506,952	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	<b>Completed</b>	\$2,000,000	\$834,697	\$834,697	\$0	\$0
113	Energy Efficiency Projects	<b>Completed</b>	\$5,371,136	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	<b>Completed</b>	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	<b>Completed</b>	\$0	\$24,638,386	\$24,638,386	\$0	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	<b>Completed</b>	\$0	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	<b>Completed</b>	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	<b>Completed</b>	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	<b>Completed</b>	\$0	\$11,515,614	\$11,515,614	\$0	\$0
120	Student Services	<b>Completed</b>	\$0	\$6,870,490	\$6,870,490	\$0	\$0
121	Cost of Issuance	<b>Completed</b>	\$0	\$498,026	\$498,026	\$0	\$0
122	Management Reserve	On-Going	\$0	\$2,446,709	\$2,446,709	\$0	\$2,446,709
123	Unissuable Bond	<b>Completed</b>	\$0	\$4,171	\$4,171	\$0	\$4,171
	<b>Project Totals</b>		<b>\$295,000,000</b>	<b>\$295,000,000</b>	<b>\$295,000,000</b>	<b>\$0</b>	<b>\$2,697,467</b>

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
**Measure AA Project Schedule**  
 As of June 30, 2022

MEASURE AA

	Project Name	Completion	2020	2021	2022	2023	2024
101	Environmental Performance - Central Plant Connections	<b>Completed</b>					
102	Infrastructure & Technology - Information Technology Relocati	<b>Completed</b>					
103	Media and Technology Complex - Academy Site	<b>Completed</b>					
104	Replacement Health/PE/Fitness/Dance Building with Central Pla	<b>Completed</b>					
105	Drescher - Academic Modernization, Bookstore, Pico Promenad	<b>Completed</b>					
106	Replacement Math and Science Extension Building	July 2024					
107	Madison East Wing Seismic Upgrade	<b>Completed</b>					
108	Renovation of Corsair Stadium	<b>Completed</b>					
109	Career Opportunity and Advancement Center (Bundy)	<b>Completed</b>					
110	Malibu Center	November 2022					
111	Business & Facilities Infrastructure	<b>Completed</b>					
112	Master Planning, Program Management, Overhead	<b>Completed</b>					
113	Energy Efficiency Projects	<b>Completed</b>					
114	Community Classroom & Facility Projects	<b>Completed</b>					
115	Real Property Acquisition	<b>Completed</b>					
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	<b>Completed</b>					
117	Infrastructure & Technology - Technology	<b>Completed</b>					
118	Infrastructure & Technology - Utility	<b>Completed</b>					
119	Emergency Lighting, Fire Alarm, and Security System	<b>Completed</b>					
120	Student Services	<b>Completed</b>					
121	Cost of Issuance	<b>Completed</b>					
122	Management Reserve	On-Going					
123	Unissuable Bond	<b>Completed</b>					

In Planning
In Construction

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
 MEASURE AA EXPENDITURES  
 FUND 42.4  
 As of June 30, 2022

MEASURE AA

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
AA 7100062															
<b>Environmental Performance - Central Plant Connections (101)</b>															
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$125
Other Contract Services		\$0	\$0	\$49,837	\$16,239	\$0	\$0	\$0	\$0	\$9,920	\$0	\$0	\$0	\$0	\$75,996
Consultants		\$0	\$0	\$0	\$0	\$28	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$28
Building & Additions		\$0	\$0	\$0	\$361	\$729	\$640	\$1,328,592	\$6,934,044	\$446,861	\$0	\$0	\$0	\$0	\$8,711,229
Architect		\$0	\$385	\$148,311	\$176,897	\$36,256	\$0	\$0	\$0	\$0	\$15,699	\$0	\$0	\$0	\$377,547
Engineering		\$48,500	\$0	\$4,000	\$0	\$152,010	\$39,638	\$66,918	\$138,887	\$62,883	\$0	\$0	\$0	\$0	\$512,836
Inspection & Testing		\$0	\$0	\$7,688	\$0	\$0	\$0	\$7,310	\$137,150	\$4,382	\$0	\$0	\$0	\$0	\$156,529
Project Management		\$0	\$17,263	\$55,116	\$48,685	\$61,908	\$19,313	\$104,575	\$526,072	\$99,840	\$190	\$0	\$0	\$0	\$932,961
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
<b>Total</b>		<b>\$48,500</b>	<b>\$17,648</b>	<b>\$264,951</b>	<b>\$242,307</b>	<b>\$250,931</b>	<b>\$59,591</b>	<b>\$1,507,396</b>	<b>\$7,736,152</b>	<b>\$623,886</b>	<b>\$15,889</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$10,767,251</b>
Project Budget	\$10,767,251														
Less Other Funding	\$0														
Net	\$10,767,251														
Actual Measure AA Expenditures	\$10,767,251														
Running Balance	\$0														

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
AA 7100063															
<b>Infrastructure &amp; Technology - IT Relocation (102)</b>															
Supplies		\$0	\$0	\$965	\$8,442	\$3,137	\$2,600	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$15,144
Consultants		\$0	\$0	\$0	\$0	\$408	\$0	\$7,800	\$0	\$0	\$0	\$0	\$0	\$0	\$8,208
Maintenance Contract		\$0	\$0	\$0	\$0	\$107,390	\$0	\$77,074	\$79	\$0	\$0	\$0	\$0	\$0	\$184,543
Legal		\$0	\$0	\$0	\$1,363	\$50	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,413
Printing		\$0	\$0	\$0	\$0	\$1,624	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,624
Postage		\$0	\$0	\$0	\$0	\$1,567	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,567
Other Contract Services		\$0	\$0	\$2,163	\$15,259	\$23,356	\$0	\$19,050	\$4,500	\$0	\$0	\$0	\$0	\$0	\$64,328
Moving		\$0	\$0	\$0	\$577	\$266	\$27,655	\$22,618	\$0	\$0	\$0	\$0	\$0	\$0	\$51,116
Site Improvement		\$0	\$0	\$0	\$24	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$24
Building & Additions		\$0	\$0	\$0	\$1,767,083	\$9,667,362	\$4,288,987	\$1,203,916	\$165,229	-\$19,798	\$0	\$0	\$0	\$0	\$17,072,780
Architect		\$105,049	\$482,261	\$505,580	\$183,181	\$287,201	\$236,860	\$120,091	\$0	\$0	\$0	\$0	\$0	\$0	\$1,920,223
Engineering		\$0	\$0	\$10,037	\$11,065	\$17,147	\$19,512	\$25,994	\$1,956	\$0	\$0	\$0	\$0	\$0	\$85,712
Inspection & Testing		\$10,291	\$8,793	\$21,449	\$137,523	\$499,982	\$200,262	\$568	\$0	\$0	\$0	\$0	\$0	\$0	\$878,868
Project Management		\$33,460	\$76,290	\$84,991	\$331,754	\$431,730	\$297,951	\$22,978	\$1,500	\$0	\$0	\$0	\$0	\$0	\$1,280,653
Cap Equipment		\$0	\$0	\$0	\$29,422	\$645,830	-\$29,090	\$589,604	\$9,811	\$0	\$0	\$0	\$0	\$0	\$1,245,576
Non-Cap Equipment		\$0	\$0	\$0	\$18,344	\$10,852	\$277,219	\$1,891	\$20,689	\$0	\$0	\$0	\$0	\$0	\$328,994
<b>Total</b>			<b>\$148,800</b>	<b>\$567,344</b>	<b>\$625,185</b>	<b>\$2,504,035</b>	<b>\$11,697,901</b>	<b>\$5,321,956</b>	<b>\$2,091,584</b>	<b>\$203,764</b>	<b>-\$19,798</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$23,140,771</b>
Project Budget	\$23,160,569	<b>Received</b>													
Less Other Funding	\$19,798	\$19,798		<b>* Other Funding Source:</b>											
Net	\$23,140,771			1) Edison \$19,798 received											
Actual Measure AA Expenditures	\$23,140,771														
Running Balance	\$0														

**Infrastructure & Technology - IT Relocation**


**Project Description:**  
Relocation of IT/Telecom Departments, and renovation of Media Center

**Facility Size:**  
9,230 sq/ft

**Status:**  
Completed

**Architect:**  
Morris Architects

**Contractor:**  
Minco, Bernards Brothers

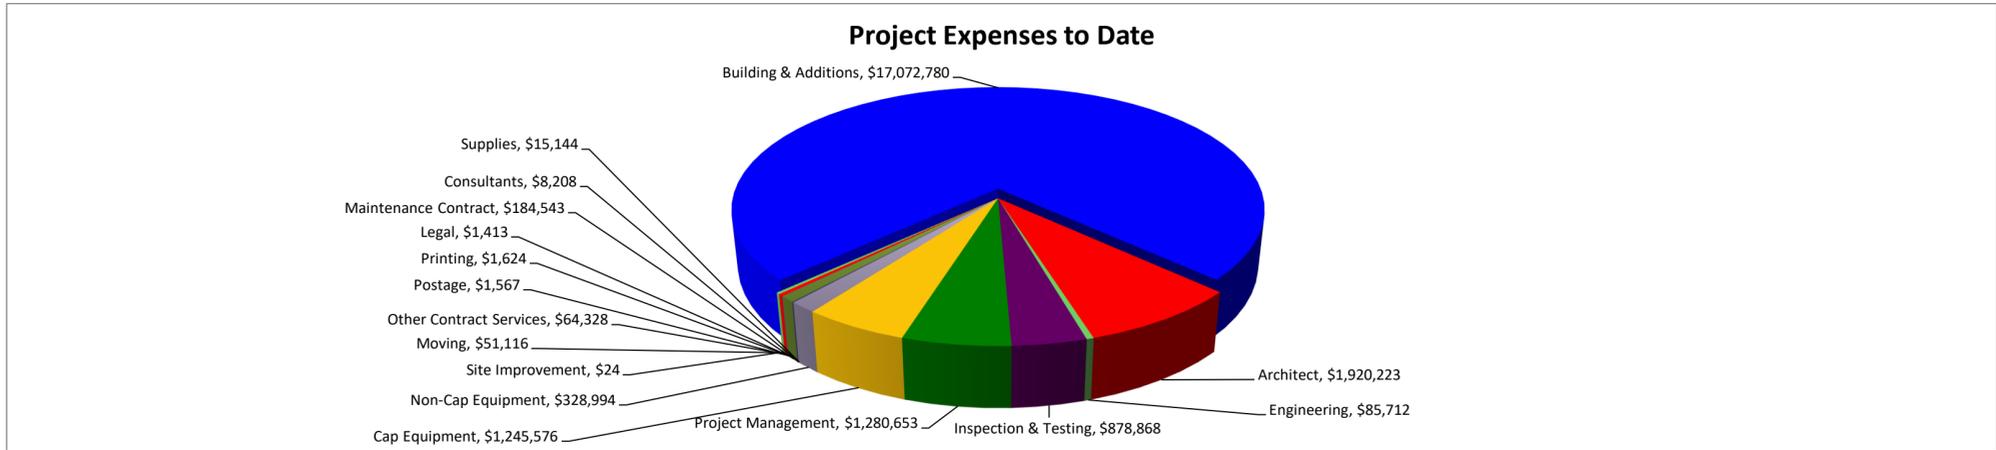

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<b>AA 7100061</b>															
<b>Media and Technology Complex - Academy Site (103)</b>															
Consultants		\$0	\$0	\$20,675	\$12,576	\$9,488	\$7,789	\$2,102	\$0	\$12,922	\$0	\$0	\$0	\$0	\$65,551
Supplies		\$0	\$0	\$0	\$19,481	\$1,048	\$289	\$0	\$9,251	\$40,519	\$937	\$0	\$0	\$0	\$71,525
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$15,922	\$23,561	\$0	\$0	\$0	\$0	\$39,483
Legal		\$16,903	\$0	\$7,958	\$43,363	\$5,066	\$26,186	\$49,155	\$15,435	\$36,221	\$26,991	\$121,256	\$100,053	\$200,783	\$649,368
Software Support		\$0	\$0	\$0	\$1,982	\$0	\$0	\$0	\$6,548	\$6,975	\$0	\$0	\$0	\$0	\$15,505
Service Fee		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$17,000	\$0	\$0	\$0	\$0	\$0	\$17,000
Other Contract Services		\$3,993	\$5,763	\$13,456	\$39,188	\$0	\$0	\$5,853	\$22,622	\$18,628	\$7,690	\$7,550	\$0	\$0	\$124,743
Moving Expenses		\$0	\$0	\$0	\$38,756	\$0	\$0	\$0	\$0	\$97,543	\$17,556	\$0	\$0	\$0	\$153,855
Site Improvement		\$0	\$0	\$0	\$100,505	\$664	\$606	\$476	\$622	\$526	\$0	\$526	\$0	\$0	\$103,925
Building & Additions		\$0	\$538	\$1,498,660	\$3,543,657	\$11,820,615	\$17,734,534	\$23,465,347	\$16,267,550	\$25,548,089	\$219,234	\$626,512	-\$67,164	\$0	\$100,657,570
Architect		\$2,097,553	\$2,508,588	\$295,753	\$265,481	\$778,015	\$517,794	\$1,048,935	\$991,386	\$869,801	\$151,886	\$43,416	\$90,690	\$240,094	\$9,899,392
Engineering		\$16,459	\$29,293	\$9,102	\$29,223	\$8,203	\$72,993	\$118,368	\$72,786	\$51,971	\$37,259	\$0	\$0	\$0	\$445,657
Inspection & Testing		\$64,905	\$27,527	\$123,842	\$235,287	\$563,746	\$1,381,801	\$641,972	\$525,264	\$207,240	\$27,210	\$1,212	\$0	\$0	\$3,800,005
Project Management		\$121,786	\$233,826	\$269,249	\$506,917	\$800,315	\$930,115	\$1,207,850	\$1,121,670	\$859,779	\$50,681	\$27,825	\$2,450	\$0	\$6,132,461
Cap Equipment		\$0	\$0	\$0	\$186,301	\$0	\$0	\$0	\$0	\$1,458,273	\$6,604	\$0	\$0	\$0	\$1,651,178
Non-Cap Equipment		\$0	\$0	\$0	\$10,782	\$0	\$0	\$0	\$326,845	\$490,727	\$7,167	\$0	\$0	\$0	\$835,520
<b>Total</b>		<b>\$2,321,599</b>	<b>\$2,805,534</b>	<b>\$2,238,694</b>	<b>\$5,033,499</b>	<b>\$13,987,159</b>	<b>\$20,672,105</b>	<b>\$26,540,059</b>	<b>\$19,392,902</b>	<b>\$29,722,772</b>	<b>\$553,215</b>	<b>\$828,296</b>	<b>\$126,029</b>	<b>\$440,877</b>	<b>\$124,662,739</b>
Project Budget	\$131,504,893	<b>Received</b>													
Less Other Funding*	\$6,835,391	<b>* Other Funding Source:</b>													
Net	\$124,669,502	1) KCRW Foundation \$6,803,412 received													
Actual Measure AA Expenditures	\$124,662,739	2) Edison \$31,979.48 received													
Running Balance	\$6,763														

**Media and Technology Complex - Academy Site**


**Project Description:**  
 Renovation and new extension to the existing building, new building for KCRW, and a new parking structure

**Facility Size:**  
 Building - 116,000 sq/ft  
 Parking Structure - 450 spaces

**Status:**  
 Completed

**Architect:**  
 Clive Wilkinson Architects

**Contractor:**  
 H.B. Parkco Construction  
 Fast Track Construction  
 CW Driver

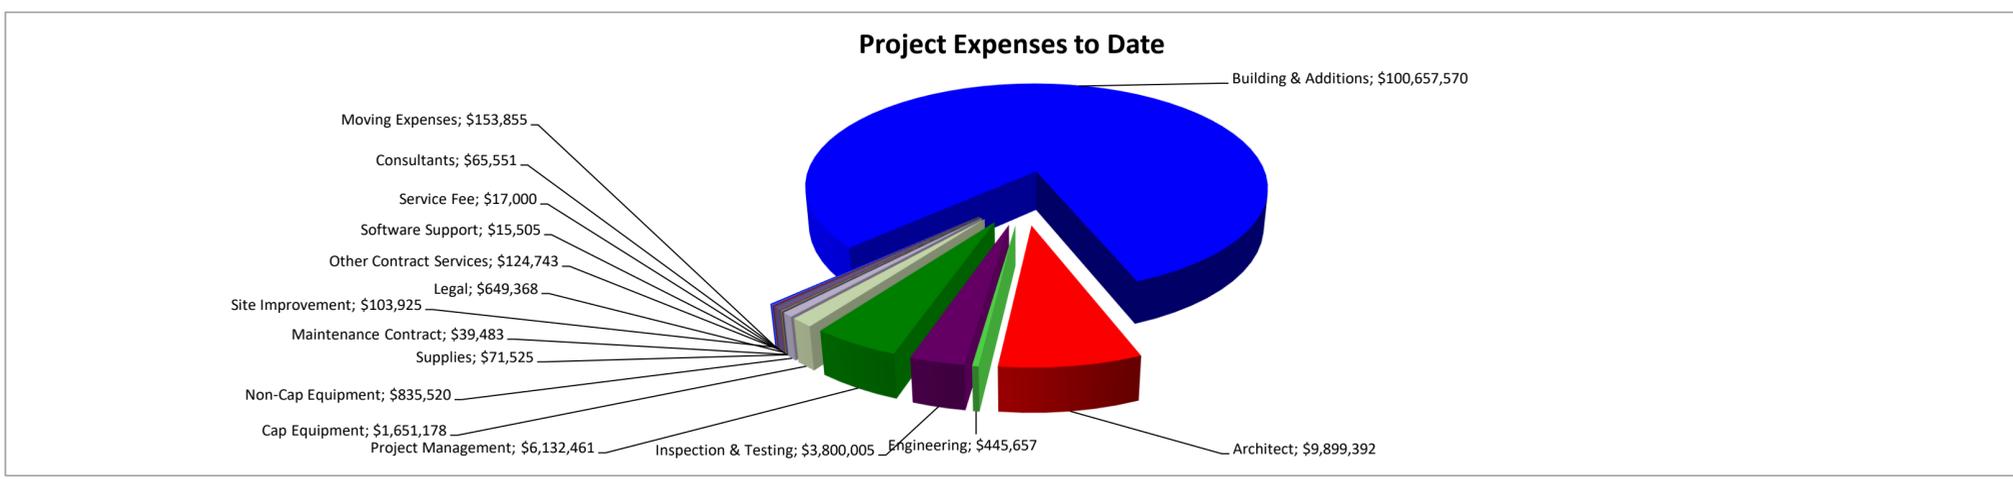

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
AA 7100060															
<b>Repl. Health/PE/Fitness/Dance Building with Central Plant (104)</b>															
Consultants		\$0	\$0	\$0	\$14	\$62	\$2,304	\$184	\$0	\$0	\$0	\$0	\$0	\$0	\$2,564
Supplies		\$0	\$0	\$0	\$0	\$7,089	\$195	\$484	\$20,947	\$0	\$0	\$0	\$0	\$0	\$28,715
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$663	\$80	\$0	\$0	\$0	\$0	\$0	\$742
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,209	\$0	\$0	\$0	\$0	\$0	\$1,209
Site Improvement		\$0	\$0	\$0	\$0	\$0	\$559	\$440	\$575	\$0	\$0	\$0	\$0	\$0	\$1,574
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$2,165	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,165
Postage		\$0	\$0	\$0	\$0	\$0	\$1,505	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,505
Other Contract Services		\$120	\$38	\$112	\$32,634	\$0	\$1,019	\$581	\$0	\$2,644	\$0	\$0	\$0	\$0	\$37,147
Building & Additions		\$0	\$0	\$0	\$817	\$4,188	\$1,623	\$13,783,023	\$14,880,829	\$5,315,393	-\$148,184	\$0	\$0	\$0	\$33,837,688
Architect		\$256,076	\$1,568,564	\$1,790,207	\$518,973	\$177,583	\$364,853	\$585,900	\$373,345	\$210,312	\$108,264	\$0	\$0	\$0	\$5,954,078
Engineering		\$0	\$8,507	\$31,650	\$7,871	\$6,529	\$9,276	\$76,712	\$51,025	\$11,318	\$2,900	\$0	\$0	\$0	\$205,788
Inspection & Testing		\$36,892	\$490	\$21,150	\$1,285	\$360	\$133,756	\$846,765	\$358,724	\$60,826	\$1,330	\$0	\$0	\$0	\$1,461,579
Project Management		\$34,968	\$113,379	\$118,783	\$94,768	\$108,528	\$463,418	\$564,240	\$487,065	\$312,539	\$20,242	\$0	\$0	\$0	\$2,317,928
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$164,793	\$68,425	\$0	\$0	\$0	\$0	\$233,218
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$9,015	\$0	\$206,229	\$127,078	\$0	\$0	\$0	\$0	\$342,322
<b>Total</b>		<b>\$328,056</b>	<b>\$1,690,978</b>	<b>\$1,961,901</b>	<b>\$656,362</b>	<b>\$304,338</b>	<b>\$989,689</b>	<b>\$15,858,991</b>	<b>\$16,544,820</b>	<b>\$6,108,535</b>	<b>-\$15,448</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$44,428,222</b>
Project Budget	\$56,240,452														
Less Other Funding*	\$11,812,230														
Net	\$44,428,222														
Actual Measure AA Expenditures	\$44,428,222														
Running Balance	\$0														

**\* Other Funding Source:**  
 1) Measure S - \$11,603,383 allocated  
 2) SCE \$190,847.28, Gas Co. \$18,000 received

**Repl. Health/PE/Fitness/Dance Building with Central Plant**


**Project Description:**  
 Replacement of locker rooms, fitness center, dance studios, and new central plant

**Facility Size:**  
 62,000 sq/ft

**Status:**  
 Completed

**Architect:**  
 Gensler Architects

**Contractor:**  
 Bernards Brothers

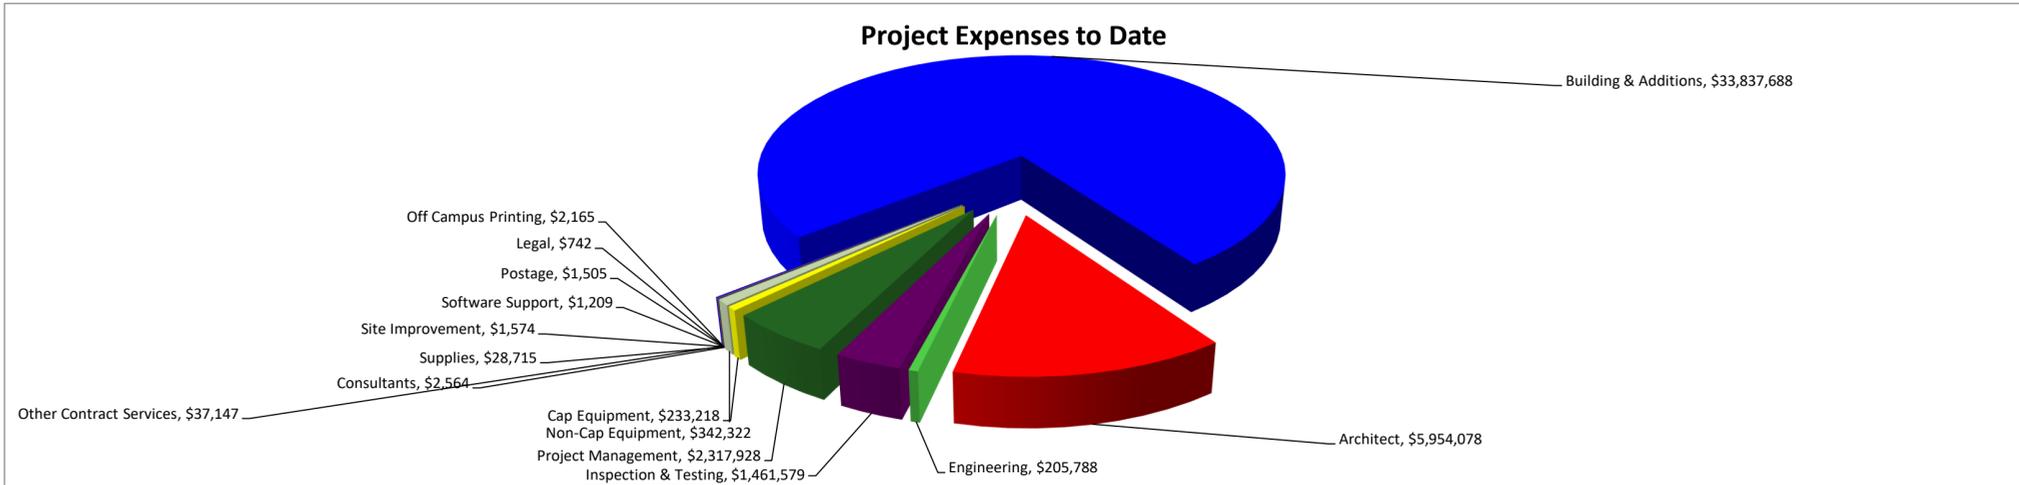

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
 MEASURE AA EXPENDITURES  
 FUND 42.4  
 As of June 30, 2022

MEASURE AA

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<b>AA 7100065</b>															
<b>Drescher - Academic Modernization, Bookstore, Pico Promenade (105)</b>															
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Site Acquisition		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,082
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$5,082</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$5,082</b>
Project Budget	\$13,005,082														
Less Other Funding	\$13,000,000														
Net	\$5,082														
Actual Measure AA Expenditures	\$5,082														
Running Balance	\$0														
* Other Funding Source: 1) Measure V 13,000,000 allocated															
<b>AA 7100090</b>															
<b>Replacement Math and Science Extension Building (106)</b>															
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,525	\$0	\$0	\$0	\$0	\$1,525
Site Acquisition		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,796	\$0	\$0	\$0	\$0	\$4,796
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,787,824	-\$94,695	\$0	\$0	\$0	\$1,693,130
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$70,223	\$0	\$0	\$0	\$0	\$70,223
Project Management		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$800	\$228,760	\$0	\$0	\$0	\$0	\$234,510
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$4,950</b>	<b>\$0</b>	<b>\$0</b>	<b>\$800</b>	<b>\$2,093,128</b>	<b>-\$94,695</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$2,004,184</b>
Project Budget	\$124,958,336	<b>Received</b>													
Less Other Funding	\$122,714,328	\$17,743,528													
Net	\$2,244,008														
Actual Measure AA Expenditures	\$2,004,184														
Running Balance	\$239,824														
* Other Funding Source: 1) Measure U \$308,336 2) Measure V \$82,317,992 allocated 3) State of California \$40,088,000 allocated															

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<b>AA 7100047</b>															
<b>Madison East Wing Seismic Upgrade (107)</b>															
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,197	\$0	\$0	\$0	\$0	\$0	\$6,197
Consultants		\$0	\$0	\$0	\$0	\$135	\$28	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$163
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$285	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$285
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$357	\$0	\$0	\$0	\$0	\$0	\$357
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,579	\$11,822	\$8,263	\$950	\$0	\$0	\$28,613
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$806	\$0	\$0	\$0	\$0	\$0	\$806
Other Contract Services		\$0	\$364	\$997	\$0	\$0	\$1,328	\$711	\$0	\$0	\$0	\$0	\$0	\$0	\$3,400
Building & Additions		\$0	\$656	\$312,643	\$0	\$4,248	\$6,030,371	\$8,829,626	\$4,949,223	\$3,967,591	\$0	\$0	\$0	\$0	\$24,094,358
Architect		\$76,073	\$398,050	\$550,589	\$65,444	\$57,480	\$199,100	\$404,764	\$122,764	\$103,824	\$0	\$0	\$0	\$0	\$1,978,088
Engineering		\$0	\$0	\$10,707	\$778	\$0	\$13,792	\$33,184	\$37,491	\$90	\$0	\$0	\$0	\$0	\$96,042
Inspection & Testing		\$0	\$19,848	\$16,752	\$3,036	\$5,851	\$676,323	\$405,443	\$112,876	\$4,703	\$0	\$0	\$0	\$0	\$1,244,832
Project Management		\$5,557	\$128,878	\$112,573	\$67,447	\$118,242	\$494,874	\$481,165	\$322,379	\$31,230	\$11,286	\$0	\$0	\$0	\$1,773,629
Cap Equipment		\$0	\$0	\$30,603	\$0	\$0	\$0	\$0	\$537,627	\$0	\$0	\$0	\$0	\$0	\$568,230
Non-Cap Equipment		\$0	\$0	\$71,827	\$9,788	\$0	\$0	\$0	\$285,236	\$0	\$0	\$0	\$0	\$0	\$366,851
<b>Total</b>		<b>\$81,630</b>	<b>\$547,796</b>	<b>\$1,106,691</b>	<b>\$146,492</b>	<b>\$185,956</b>	<b>\$7,416,101</b>	<b>\$10,154,894</b>	<b>\$6,382,534</b>	<b>\$4,119,259</b>	<b>\$19,549</b>	<b>\$950</b>	<b>\$0</b>	<b>\$0</b>	<b>\$30,161,852</b>
Project Budget	\$30,161,852														
Less Other Funding	\$0														
Net	\$30,161,852														
Actual Measure AA Expenditures	\$30,161,852														
Running Balance	\$0														

**Madison East Wing Seismic Upgrade**


**Project Description:**  
 Replacement of east wing with a new multipurpose room and additional classrooms

**Facility Size:**  
 20,838 sq/ft

**Status:**  
 Completed

**Architect:**  
 DLR Group WWCOT

**Contractor:**  
 Bernards Brothers

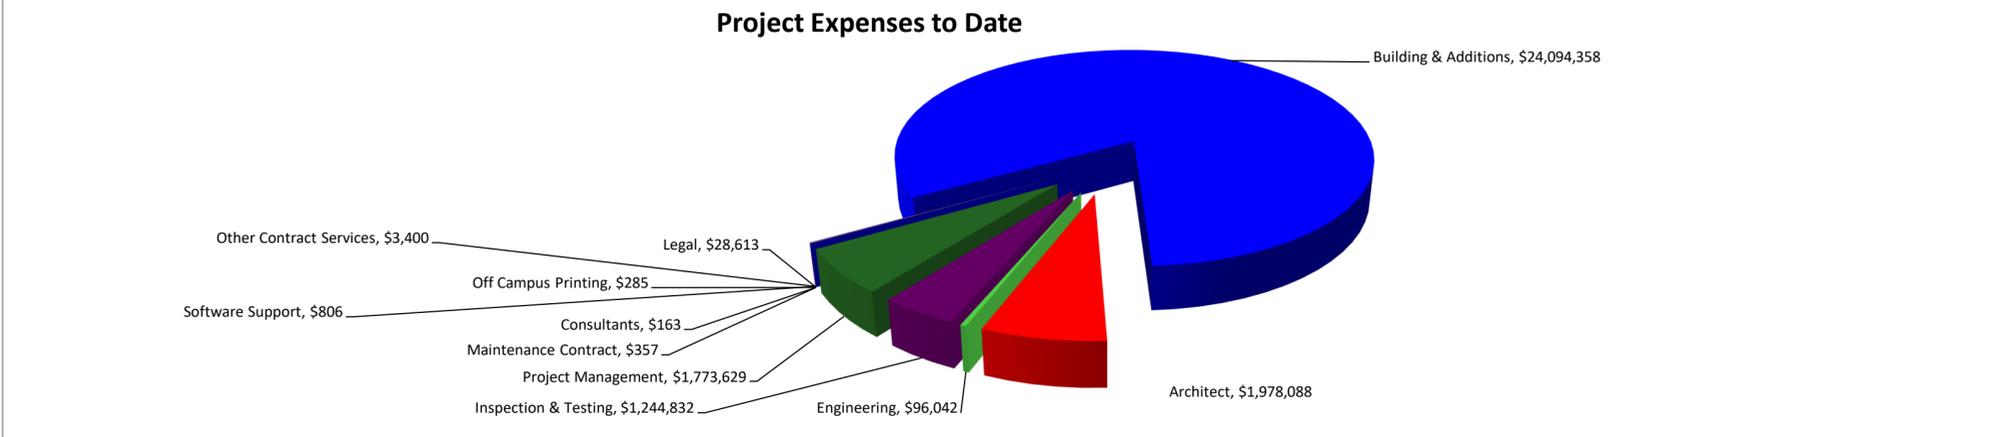

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<b>AA 7100068</b>															
<b>Renovation to Corsair Stadium (108)</b>															
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$30,759	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$30,759
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$4,540	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,540
<b>Total</b>		<b>\$0</b>	<b>\$35,299</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$35,299</b>
Project Budget	\$35,299														
Less Other Funding	\$0														
Net	\$35,299														
Actual Measure AA Expenditures	\$35,299														
Running Balance	\$0														
<b>AA 7100067, 7100152, 7100155, 7100157</b>															
<b>Business &amp; Facilities Infrastructure (111)</b>															
Supplies		\$0	\$0	\$0	\$1,493	\$4,840	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,333
Service Fee		\$0	\$0	\$0	\$12,885	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,885
Consultants		\$0	\$0	\$0	\$0	\$14	\$8	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$22
Maintenance Contract		\$0	\$0	\$0	\$0	\$1,366	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,366
Legal		\$0	\$0	\$75	\$0	\$0	\$0	\$1,105	\$0	\$0	\$0	\$0	\$0	\$0	\$1,180
Software License		\$0	\$0	\$0	\$0	\$375	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$375
Other Contract Services		\$0	\$6,289	\$6,988	\$750	\$0	\$2,209	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,236
Moving Services		\$0	\$0	\$0	\$395	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$395
Building & Additions		\$0	\$34,672	\$198,667	\$200,585	\$284,668	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$718,592
Architect		\$0	\$0	\$80,626	\$170,132	\$37,906	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$288,664
Engineering		\$0	\$0	\$0	\$3,705	\$9,735	\$6,840	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,280
Inspection & Testing		\$0	\$0	\$8,142	\$10,938	\$10,500	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$29,580
Project Management		\$0	\$3,073	\$154,904	\$87,291	\$139,821	\$3,571	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$388,659
Cap Equipment		\$0	\$0	\$0	\$35,892	\$80,090	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$115,982
Non-Cap Equipment		\$0	\$89,204	\$0	\$84,590	\$193,782	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$367,576
<b>Total</b>		<b>\$0</b>	<b>\$133,238</b>	<b>\$449,401</b>	<b>\$608,656</b>	<b>\$763,095</b>	<b>\$12,628</b>	<b>\$1,105</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$1,968,124</b>
Project Budget	\$1,968,124														
Less Other Funding	\$0														
Net	\$1,968,124														
Actual Measure AA Expenditures	\$1,968,124														
Running Balance	\$0														
<b>AA 7100004</b>															
<b>Master Planning, Program Management, Overhead (112)</b>															
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$139,302	\$187,927	\$245,329	\$1,270	\$0	\$0	\$0	\$573,828
Project Management		\$0	\$0	\$0	\$0	\$76,015	\$150	\$0	\$49,170	\$135,533	\$0	\$0	\$0	\$0	\$260,868
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$76,015</b>	<b>\$150</b>	<b>\$139,302</b>	<b>\$237,097</b>	<b>\$380,863</b>	<b>\$1,270</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$834,697</b>
Project Budget	\$834,697														
Less Other Funding	\$0														
Net	\$834,697														
Actual Measure AA Expenditures	\$834,697														
Running Balance	\$0														

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<b>AA 7100154</b>															
<b>Energy Efficiency Projects (113)</b>															
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$189	\$2,108,853	\$990,389	-\$97,621	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,001,810
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$4,020	\$0	\$10,118	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14,138
Project Management		\$0	\$0	\$0	\$0	\$0	\$825	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$825
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$189</b>	<b>\$2,112,873</b>	<b>\$990,389</b>	<b>-\$86,678</b>	<b>\$0</b>	<b>\$3,016,773</b>						
Project Budget	\$3,508,088														
Less Other Funding	\$491,315														
Net	\$3,016,773														
Actual Measure AA Expenditures	\$3,016,773														
Running Balance	\$0														
		<b>* Other Funding Source:</b>													
		1) DWP \$18,715.00 received													
		2) SCE \$446,519.77 received													
		3) Gas Co. \$26,080 received													

<b>AA 7100064</b>															
<b>Community Classroom &amp; Facility Projects (114)</b>															
Supplies		\$0	\$0	\$0	\$124	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$124
Legal		\$0	\$0	\$1,867	\$1,418	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,285
Other Contract Services		\$0	\$3,720	\$1,869	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,588
Building & Additions		\$0	\$434,578	\$1,369,441	\$408,696	-\$1,003	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,211,712
Architect		\$0	\$263,833	\$48,120	\$1,318	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$313,272
Engineering		\$0	\$3,220	\$3,143	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,363
Inspection & Testing		\$0	\$41,002	\$80,885	\$1,495	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$123,382
Project Management		\$135	\$117,247	\$143,780	\$27,570	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$288,732
Non-Cap Equipment		\$0	\$0	\$209,726	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$209,726
<b>Total</b>		<b>\$135</b>	<b>\$863,599</b>	<b>\$1,858,831</b>	<b>\$440,621</b>	<b>-\$1,003</b>	<b>\$0</b>	<b>\$3,162,183</b>							
Project Budget	\$3,162,183														
Less Other Funding	\$0														
Net	\$3,162,183														
Actual Measure AA Expenditures	\$3,162,183														
Running Balance	\$0														

<b>AA 7100057</b>															
<b>Real Property Acquisition (115)</b>															
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$659	\$0	\$0	\$0	\$0	\$659
Other Contract Services		\$0	\$39	\$7,000	\$0	\$15,800	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$22,839
Site Acquisition		\$1,739,979	\$4,001,204	\$9,022,207	\$0	\$0	\$0	\$5,013,226	\$4,821,600	\$0	\$0	\$0	\$0	\$0	\$24,598,214
Inspection & Testing		\$8,689	\$7,986	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,674
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
<b>Total</b>		<b>\$1,748,667</b>	<b>\$4,009,228</b>	<b>\$9,029,207</b>	<b>\$0</b>	<b>\$15,800</b>	<b>\$0</b>	<b>\$5,013,226</b>	<b>\$4,822,259</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$24,638,386</b>
Project Budget	\$24,638,386														
Less Other Funding	\$0														
Net	\$24,638,386														
Actual Measure AA Expenditures	\$24,638,386														
Running Balance	\$0														

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
 MEASURE AA EXPENDITURES  
 FUND 42.4  
 As of June 30, 2022

MEASURE AA

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<b>AA 7100058, 7100151, 7100156, 7100059</b>															
<b>Roadways, Walkways, Grounds, Parking Lots, and Garages (116)</b>															
Supplies		\$0	\$0	\$0	\$0	\$4,616	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,616
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$125
Consultants		\$0	\$0	\$0	\$48,090	\$5,018	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$53,108
Other Contract Services		\$218	\$770	\$122	\$25,249	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$26,358
Building & Additions		\$185,345	\$6,731	\$113,784	\$321,603	\$975,401	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,602,864
Architect		\$0	\$0	\$0	\$103,569	\$19,225	\$1,240	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$124,035
Engineering		\$0	\$0	\$0	\$1,095	\$1,445	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,540
Inspection & Testing		\$13,380	\$7,865	\$13,553	\$20,126	\$42,865	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$97,787
Project Management		\$24,404	\$12,439	\$21,945	\$54,095	\$104,943	\$1,411	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$219,237
<b>Total</b>		<b>\$223,347</b>	<b>\$27,804</b>	<b>\$149,403</b>	<b>\$573,951</b>	<b>\$1,153,512</b>	<b>\$2,652</b>	<b>\$0</b>	<b>\$2,130,670</b>						
Project Budget	\$7,022,417														
Less Other Funding	\$4,891,747														
Net	\$2,130,670														
Actual Measure AA Expenditures	\$2,130,670														
Running Balance	\$0														
		<b>* Other Funding Source:</b>													
		1) Measure S: \$3,891,747													
		2) Measure V: \$1,000,000 allocated													

<b>AA 7100069</b>															
<b>Infrastructure &amp; Technology - Technology (117)</b>															
Software		\$0	\$0	\$0	\$0	\$0	\$218	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$218
Supplies		\$0	\$0	\$13,646	\$7,587	\$0	\$16,966	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$38,200
Maintenance Contract		\$0	\$9,472	\$46,300	\$210,581	\$18,944	\$42,415	\$9,472	\$0	\$0	\$0	\$0	\$0	\$0	\$337,186
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$49,589	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$49,589
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$207,423	\$33,063	\$576,294	\$0	\$1,145,668	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,962,449
Non-Cap Equipment		\$0	\$0	\$42,827	\$500	\$0	\$3,447	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$46,775
<b>Total</b>		<b>\$0</b>	<b>\$216,896</b>	<b>\$135,838</b>	<b>\$794,963</b>	<b>\$18,944</b>	<b>\$1,258,304</b>	<b>\$9,472</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$2,434,417</b>
Project Budget	\$2,434,417														
Less Other Funding	\$0														
Net	\$2,434,417														
Actual Measure AA Expenditures	\$2,434,417														
Running Balance	\$0														

<b>AA 7100150</b>															
<b>Infrastructure &amp; Technology - Utility (118)</b>															
Software License		\$0	\$12,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,000
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$4,979	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,979
Project Management		\$0	\$3,240	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,240
Cap Equipment		\$0	\$0	\$7,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,534
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
<b>Total</b>		<b>\$0</b>	<b>\$20,219</b>	<b>\$7,534</b>	<b>\$0</b>	<b>\$27,753</b>									
Project Budget	\$27,753														
Less Other Funding	\$0														
Net	\$27,753														
Actual Measure AA Expenditures	\$27,753														
Running Balance	\$0														

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<b>AA 7100153</b>															
<b>Emergency Lighting, Fire Alarm, and Security System (119)</b>															
Supplies		\$0	\$0	\$0	\$0	\$2,348	\$0	\$0	\$2,671	\$0	\$0	\$0	\$0	\$0	\$5,020
Consultants/Legal		\$0	\$0	\$0	\$0	\$0	\$16	\$0	\$0	\$0	\$442	\$0	\$0	\$0	\$458
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$800	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$800
Maintenance Contract		\$0	\$0	\$648	\$0	\$39,700	\$0	\$2,700	\$0	\$0	\$0	\$0	\$0	\$0	\$43,048
Software Support		\$0	\$0	\$24,765	\$0	\$106,367	\$0	\$2,232	\$0	\$0	\$0	\$0	\$0	\$0	\$133,365
Other Contract Services		\$0	\$0	\$0	\$0	\$47,695	\$0	\$4,643	\$1,560	\$0	\$0	\$0	\$0	\$0	\$53,897
Building & Additions		\$0	\$0	\$0	\$0	\$110	\$2,648,866	\$4,129,145	\$1,308,230	\$763,170	\$26,375	\$79,172	\$0	\$0	\$8,955,068
Architect		\$0	\$0	\$0	\$0	\$0	\$18,925	\$0	\$0	\$5,047	\$0	\$0	\$0	\$0	\$23,972
Engineering		\$0	\$0	\$0	\$0	\$211,030	\$389,013	\$156,247	\$255,798	\$358,560	\$114,585	\$0	\$0	\$0	\$1,485,233
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$58,831	\$4,800	\$0	\$0	\$0	\$0	\$0	\$63,631
Project Management		\$0	\$0	\$0	\$0	\$51,008	\$52,044	\$79,285	\$16,500	\$49,738	\$240	\$0	\$0	\$0	\$248,814
Cap Equipment		\$0	\$0	\$0	\$0	\$89,415	\$0	\$5,871	\$0	\$0	\$0	\$0	\$0	\$0	\$95,286
Non-Cap Equipment		\$0	\$0	\$6,087	\$0	\$392,586	\$8,348	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$407,022
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$31,500</b>	<b>\$0</b>	<b>\$940,259</b>	<b>\$3,118,012</b>	<b>\$4,438,953</b>	<b>\$1,589,560</b>	<b>\$1,176,515</b>	<b>\$141,642</b>	<b>\$79,172</b>	<b>\$0</b>	<b>\$0</b>	<b>\$11,515,614</b>
Project Budget	\$11,515,614														
Less Other Funding	\$0														
Net	\$11,515,614														
Actual Measure AA Expenditures	\$11,515,614														
Running Balance	\$0														

<b>AA 7100142</b>															
<b>Student Services (120)</b>															
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,165,626	\$3,704,864	\$0	\$0	\$0	\$6,870,490
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
<b>Total</b>		<b>\$0</b>	<b>\$3,165,626</b>	<b>\$3,704,864</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$6,870,490</b>							
Project Budget	\$6,870,490														
Less Other Funding	\$0														
Net	\$6,870,490														
Actual Measure AA Expenditures	\$6,870,490														
Running Balance	\$0														
<b>* Other Funding Source:</b>															
1) State of California \$1,321,000 received															
2) Measure U \$21,131,135, Measure S \$45,595,322, Measure V \$33,624,909 allocated															
3) Measure U, S & AA interests \$21,681,308 allocated															

<b>Cost of Issuance (121)</b>															
Cost of Issuance		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$0	\$0	\$0	\$0	\$0	\$498,026
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$285,000</b>	<b>\$0</b>	<b>\$213,026</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$498,026</b>
Project Budget	\$498,026														
Less Other Funding	\$0														
Net	\$498,026														
Actual Measure AA Expenditures	\$498,026														
Running Balance	\$0														

<b>Grand Total</b>		<b>\$4,900,734</b>	<b>\$10,935,584</b>	<b>\$17,864,407</b>	<b>\$13,113,759</b>	<b>\$30,388,248</b>	<b>\$39,049,510</b>	<b>\$60,741,756</b>	<b>\$57,313,878</b>	<b>\$52,193,046</b>	<b>\$4,326,286</b>	<b>\$908,418</b>	<b>\$126,029</b>	<b>\$440,877</b>	<b>\$292,302,532</b>
--------------------	--	--------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	---------------------	--------------------	------------------	------------------	------------------	----------------------


Measure AA Interest		<b>18/19 Final</b>
<b>Parking Garage and Grounds - Student Services (9)</b>		
Site Improvement	\$0	
Building & Additions	\$5,192,948	
Architect	\$0	
Engineering	\$0	
Inspection & Testing	\$0	
Project Management	\$0	
<b>Total</b>	<b>\$5,192,948</b>	
Project Budget	\$5,192,948	
Actual Measure S Interest Expenditures	\$5,192,948	
Running Balance	\$0	

**Measure V Bond Budget**

As of June 30, 2022

	Project Name	Completion	Project Budget	Measure V Allocation	Other Funding	Measure V Expenditures as of 6/30/22	Measure V Expenditures as of 3/31/22	Measure V Expenditures Last Period	Total Measure V Remaining
101	Replacement Math and Science Extension Build	July 2024	\$124,958,336	\$82,317,992	\$42,640,344	\$24,277,567	\$23,546,506	\$731,061	\$58,040,425
102	Student Services	<b>Completed</b>	\$130,224,164	\$33,624,909	\$96,599,255	\$24,608,197	\$24,586,482	\$21,715	\$9,016,712
103	Malibu Center	November 2022	\$61,714,841	\$34,558,420	\$27,156,421	\$17,945,095	\$13,573,520	\$4,371,575	\$16,613,325
104	Early Childhood Development/Childcare	<b>Completed</b>	\$30,925,771	\$15,405,517	\$15,520,254	\$12,978,212	\$12,975,968	\$2,244	\$2,427,305
105	Art Building Replacement	August 2024	\$34,901,000	\$24,000,000	\$10,901,000	\$1,675,700	\$1,611,228	\$64,472	\$22,324,300
106	Business Building Renovation	December 2026	\$25,017,000	\$12,547,000	\$12,470,000	\$3,400	\$3,400	\$0	\$12,543,600
107	Air Conditioning	<b>Completed</b>	\$10,777,654	\$10,777,654	\$0	\$10,124,081	\$9,836,959	\$287,122	\$653,573
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$0	\$0	\$0	\$0	\$4,000,000
109	Master Planning	June 2022	\$1,000,000	\$1,000,000	\$0	\$731,658	\$683,658	\$48,000	\$268,342
110	Drescher Hall Modernization	On-Going	\$13,005,082	\$13,000,000	\$5,082	\$0	\$0	\$0	\$13,000,000
111	Outdoor Classroom	On-Going	\$321,723	\$321,723	\$0	\$321,723	\$321,723	\$0	\$0
112	John Adams MS Auditorium (SMMUSD)	<b>Completed</b>	\$20,000,000	\$20,000,000	\$0	\$20,000,000	\$20,000,000	\$0	\$0
113	City of Santa Monica	On-Going	\$20,000,000	\$20,000,000	\$0	\$0	\$0	\$0	\$20,000,000
114	Classrooms Relocation	<b>Completed</b>	\$7,400,000	\$7,400,000	\$0	\$7,286,719	\$7,286,719	\$0	\$113,281
115	TBD	On-Going	\$39,446,785	\$39,446,785	\$0	\$0	\$0	\$0	\$39,446,785
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$0	\$244,554	\$244,554	\$0	\$55,446
121	Cost of Issuance	On-Going	\$800,000	\$800,000	\$0	\$744,152	\$291,277	\$452,875	\$55,848
122	Management Reserve	On-Going	\$25,500,000	\$25,500,000	\$0	\$0	\$0	\$0	\$25,500,000
123	Unissuable Bond	On-Going	\$0	\$0	\$0	\$0	\$0	\$0	\$0
<b>Project Totals</b>			<b>\$550,292,356</b>	<b>\$345,000,000</b>	<b>\$205,292,356</b>	<b>\$120,941,058</b>	<b>\$114,961,994</b>	<b>\$5,979,064</b>	<b>\$224,058,942</b>

**Measure V Allocation**

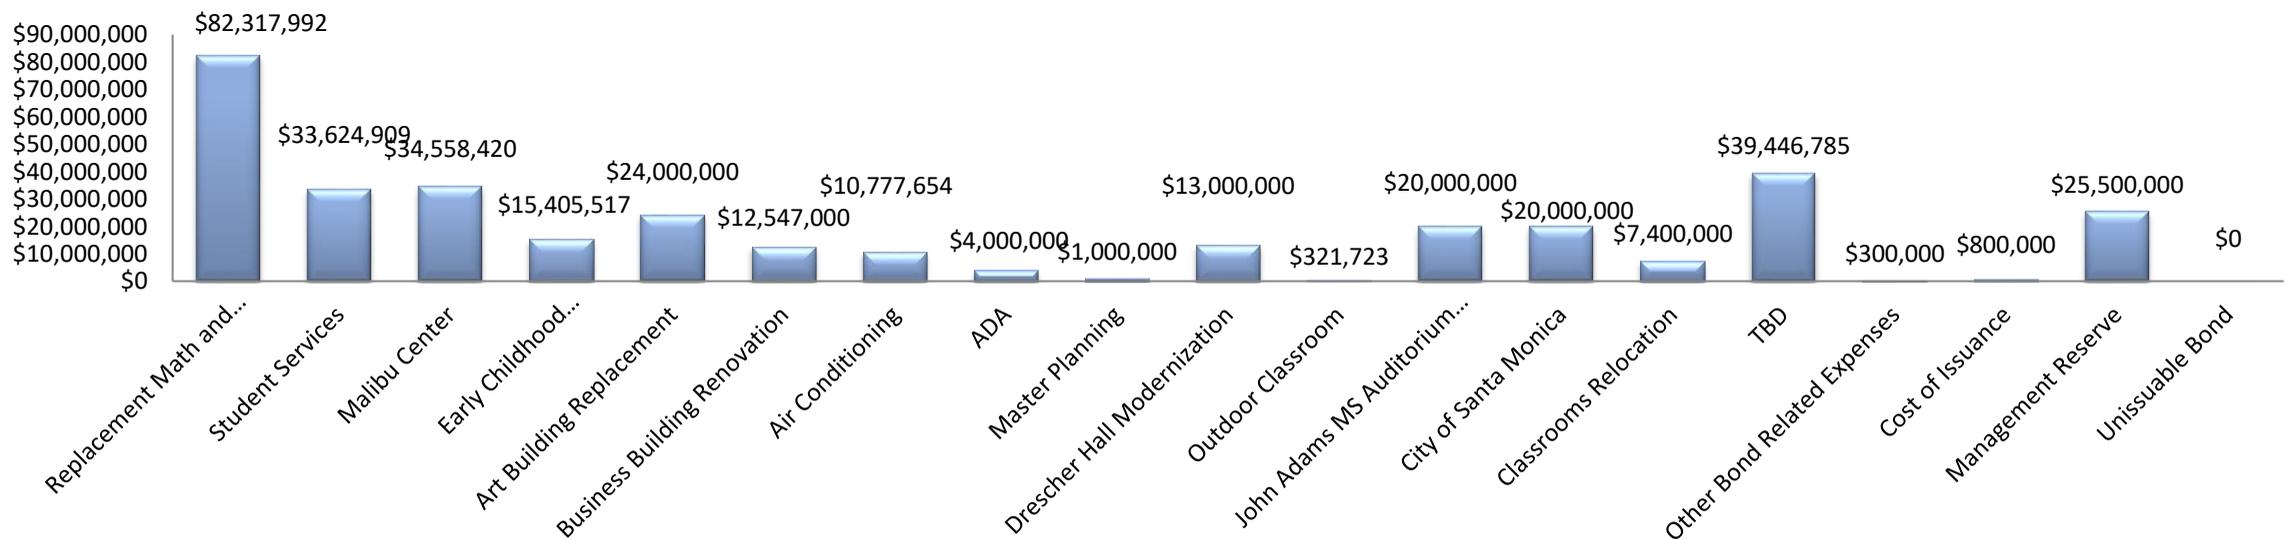

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
**Measure V Bond Budget History**  
as of June 30, 2022

MEASURE V

	Project Name	Completion	Preliminary Measure V Budget	Measure V Budget as of 3/31/22	Measure V Budget as of 6/30/22	Variance	Measure V Remaining as of 6/30/22
101	Replacement Math and Science Extension Building	July 2024	\$82,317,992	\$82,317,992	\$82,317,992	\$0	\$58,040,425
102	Student Services	<b>Completed</b>	\$21,130,252	\$33,624,909	\$33,624,909	\$0	\$9,016,712
103	Malibu Center	November 2022	\$25,000,000	\$34,558,420	\$34,558,420	\$0	\$16,613,325
104	Early Childhood Development/Childcare	<b>Completed</b>	\$15,405,517	\$15,405,517	\$15,405,517	\$0	\$2,427,305
105	Art Building Replacement	August 2024	\$24,000,000	\$24,000,000	\$24,000,000	\$0	\$22,324,300
106	Business Building Renovation	December 2026	\$12,547,000	\$12,547,000	\$12,547,000	\$0	\$12,543,600
107	Air Conditioning	<b>Completed</b>	\$10,777,654	\$10,777,654	\$10,777,654	\$0	\$653,573
108	ADA	On-Going	\$4,000,000	\$4,000,000	\$4,000,000	\$0	\$4,000,000
109	Master Planning	December 2022	\$450,000	\$1,000,000	\$1,000,000	\$0	\$268,342
110	Drescher Hall Modernization	On-Going	\$13,000,000	\$13,000,000	\$13,000,000	\$0	\$13,000,000
111	Outdoor Classroom	On-Going	\$10,000,000	\$321,723	\$321,723	\$0	\$0
112	John Adams MS Auditorium (SMMUSD)	<b>Completed</b>	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$0
113	City of Santa Monica	On-Going	\$20,000,000	\$20,000,000	\$20,000,000	\$0	\$20,000,000
114	Classrooms Relocation	<b>Completed</b>	\$0	\$7,400,000	\$7,400,000	\$0	\$113,281
115	TBD	On-Going	\$57,271,585	\$39,446,785	\$39,446,785	\$0	\$39,446,785
120	Other Bond Related Expenses	On-Going	\$300,000	\$300,000	\$300,000	\$0	\$55,446
121	Cost of Issuance	On-Going	\$800,000	\$800,000	\$800,000	\$0	\$55,848
122	Management Reserve	On-Going	\$28,000,000	\$25,500,000	\$25,500,000	\$0	\$25,500,000
123	Unissuable Bond	On-Going	\$0	\$0	\$0	\$0	\$0
	<b>Project Totals</b>		<b>\$345,000,000</b>	<b>\$345,000,000</b>	<b>\$345,000,000</b>	<b>\$0</b>	<b>\$224,058,942</b>

**Measure V Project Schedule**

As of March 31, 2022

	Project Name	Completion	2020	2021	2022	2023	2024
101	Replacement Math and Science Extension Building	July 2024					
102	Student Services	<b>Completed</b>					
103	Malibu Center	November 2022					
104	Early Childhood Development/Childcare	<b>Completed</b>					
105	Art Building Replacement	August 2024					
106	Business Building Renovation	December 2026					
107	Air Conditioning	<b>Completed</b>					
108	ADA	On-Going					
109	Master Planning	November 2022					
110	Drescher Hall Modernization	On-Going					
111	Outdoor Classroom	On-Going					
112	John Adams SMMUSD	<b>Completed</b>					
113	City of Santa Monica	On-Going					
114	Classrooms Relocation	<b>Completed</b>					
115	TBD	On-Going					
120	Other Bond Related Expenses	On-Going					
121	Cost of Issuance	On-Going					
122	Management Reserve	On-Going					
123	Unissuable Bond	On-Going					

In Planning In Construction

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
MEASURE V EXPENDITURES  
FUND 42.5  
As of June 30, 2022

MEASURE V

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<b>V 710090</b>							
<b>Replacement Math and Science Extension Building (101)</b>							
Legal		\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$67,242	\$0	\$0	\$67,242
Building & Additions		\$675	\$12,987	\$2,633	\$3,697,529	\$13,243,628	\$16,957,452
Architect		\$2,047,911	\$14,446	\$229,267	\$653,770	\$552,565	\$3,497,959
Engineering		\$0	\$0	\$19,622	\$6,966	\$10,940	\$37,529
Inspection & Testing		\$30,804	\$44,077	\$60,666	\$225,542	\$919,688	\$1,280,776
Project Management		\$130,874	\$617,805	\$347,350	\$474,483	\$866,097	\$2,436,609
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0
<b>Total</b>		<b>\$2,210,264</b>	<b>\$689,315</b>	<b>\$726,781</b>	<b>\$5,058,290</b>	<b>\$15,592,919</b>	<b>\$24,277,567</b>
Project Budget	\$124,958,336	<b>Received</b>					
Less Other Funding	\$42,640,344	\$17,711,872	<b>* Other Funding Source:</b>				
Net	\$82,317,992	1) Measure U \$308,336 2) Measure AA \$2,244,008 allocated					
Actual Measure V Expenditures	\$24,277,567	3) State of California \$40,088,000 allocated					
Running Balance	\$58,040,425						

<b>V 7100142</b>							
<b>Student Services Building (102)</b>							
Supplies		\$0	\$71,445	\$38,162	\$0	\$0	\$109,607
Other Contract Services		\$0	\$0	\$59,784	\$6,935	\$0	\$66,719
Consultants		\$0	\$0	\$687	\$0	\$0	\$687
Software Support		\$0	\$189,120	\$0	\$0	\$0	\$189,120
Moving Services		\$0	\$55,062	\$9,056	\$0	\$0	\$64,118
Building & Additions		\$0	\$12,355,060	\$4,201,966	\$355,441	\$0	\$16,912,467
Architect		\$0	\$419,829	\$530,797	\$186,296	\$27,836	\$1,164,758
Engineering		\$0	\$140,458	\$67,481	\$0	\$0	\$207,939
Inspection & Testing		\$55,202	\$296,732	\$131,128	\$21,146	\$0	\$504,208
Project Management		\$0	\$900,333	\$219,425	\$85,310	\$13,020	\$1,218,088
Cap Equipment		\$0	\$1,565,928	\$90,915	\$0	\$0	\$1,656,844
Non-Cap Equipment		\$0	\$2,279,541	\$196,313	\$37,790	\$0	\$2,513,644
<b>Total</b>		<b>\$55,202</b>	<b>\$18,273,508</b>	<b>\$5,545,714</b>	<b>\$692,918</b>	<b>\$40,856</b>	<b>\$24,608,197</b>
Project Budget	\$130,224,164	<b>* Other Funding Source:</b>					
Less Other Funding	\$96,599,255	1) State of California \$1,321,000 received					
Net	\$33,624,909	2) Measure U \$21,131,135 3) Measure S 45,595,322,					
Actual Measure V Expenditures	\$24,608,197	4) Measure AA \$6,870,490 allocated					
Running Balance	\$9,016,712	5) Measure U, S & AA interests \$21,681,308 allocated					

<b>V 7100015</b>							
<b>Malibu Site Acquisition and Center (103)</b>							
Legal		\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$2,713	\$38,163	\$0	\$40,876
Consultants		\$0	\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$2,642,861	\$3,388,666	\$8,734,478	\$14,766,005
Architect		\$0	\$0	\$0	\$155,448	\$493,355	\$648,803
Engineering		\$0	\$0	\$8,482	\$0	\$15,268	\$23,750
Inspection & Testing		\$0	\$0	\$51,754	\$633,723	\$511,002	\$1,196,478
Project Management		\$0	\$0	\$49,588	\$581,175	\$626,405	\$1,257,168
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$12,015	\$12,015
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$2,755,398</b>	<b>\$4,797,174</b>	<b>\$10,392,522</b>	<b>\$17,945,095</b>
Project Budget	\$61,714,841	<b>* Other Funding Source:</b>					
Less Other Funding	\$27,427,359	1) Measure S \$25,132,568					
Net	\$34,287,482	2) Interest Allocated \$2,294,791					
Actual Measure V Expenditures	\$17,945,095						
Running Balance	\$16,342,387						

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
MEASURE V EXPENDITURES  
FUND 42.5  
As of June 30, 2022

MEASURE V

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<i>V 7100104</i>							
<b>Early Childhood Development/Childcare (104)</b>							
Supplies		\$0	\$0	\$35,150	\$5,332	-\$500	\$39,982
Other Contract Services		\$0	\$0	\$35,344	\$15,128	\$0	\$50,472
Consultants		\$0	\$0	\$16	\$0	\$0	\$16
Software Support		\$0	\$0	\$6,158	\$0	\$5,677	\$11,835
Legal		\$0	\$0	\$96	\$0	\$0	\$96
Building & Additions		\$0	\$0	\$8,879,770	\$1,603,432	\$0	\$10,483,202
Architect		\$0	\$0	\$262,660	\$275,924	\$105,158	\$643,742
Engineering		\$0	\$0	\$19,448	\$0	\$15,550	\$34,998
Inspection & Testing		\$0	\$0	\$349,661	\$135,767	\$3,700	\$489,128
Project Management		\$0	\$0	\$384,279	\$384,714	\$2,144	\$771,137
Cap Equipment		\$0	\$0	\$32,448	\$0	\$0	\$32,448
Non-Cap Equipment		\$0	\$0	\$328,242	\$92,913	\$0	\$421,155
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$10,333,272</b>	<b>\$2,513,210</b>	<b>\$131,730</b>	<b>\$12,978,212</b>
Project Budget	\$30,925,771	<b>Received</b>					
Less Other Funding	\$15,520,254	\$6,661,598		<b>* Other Funding Source:</b>			
Net	\$15,405,517			1) City of Santa Monica \$6,661,598 committed			
Actual Measure V Expenditures	\$12,978,212			2) Measure S \$8,858,656 allocated			
Running Balance	\$2,427,305						

<i>V 7100240</i>							
<b>Art Complex (105)</b>							
Legal		\$0	\$0	\$14,811	\$0	\$0	\$14,811
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$20,991	\$40,710	\$1,344	\$63,045
Moving Services		\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$184	\$407,369	\$3,040	\$0	\$1,791	\$412,383
Architect		\$0	\$0	\$39,542	\$569,178	\$28,572	\$637,292
Engineering		\$0	\$0	\$0	\$0	\$40,750	\$40,750
Inspection & Testing		\$0	\$35,495	\$25,052	\$43,653	\$45,227	\$149,427
Project Management		\$0	\$1,600	\$85,708	\$85,978	\$184,706	\$357,992
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0
<b>Total</b>		<b>\$184</b>	<b>\$444,464</b>	<b>\$189,143</b>	<b>\$739,518</b>	<b>\$302,390</b>	<b>\$1,675,700</b>
Project Budget	\$34,901,000	<b>Received</b>					
Less Other Funding	\$10,901,000	\$506,957		<b>* Other Funding Source:</b>			
Net	\$24,000,000			1) State of California \$10,901,000 pending			
Actual Measure V Expenditures	\$1,675,700						
Running Balance	\$22,324,300						

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
MEASURE V EXPENDITURES  
FUND 42.5  
As of June 30, 2022

MEASURE V

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<i>V 7100243</i>							
<b>Business Building Replacement (106)</b>							
Legal		\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$3,400	\$0	\$0	\$3,400
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$3,400</b>	<b>\$0</b>	<b>\$0</b>	<b>\$3,400</b>
Project Budget	\$25,017,000	<b>* Other Funding Source:</b> 1) State Funding \$12,470,000					
Less Other Funding	\$12,470,000						
Net	\$12,547,000						
Actual Measure V Expenditures	\$3,400						
Running Balance	\$12,543,600						
<i>V 7100188</i>							
<b>Air Conditioning (107)</b>							
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$2,451	\$7,537,201	\$733,457	\$8,273,110
Architect		\$0	\$79,000	\$0	\$0	\$39,872	\$118,872
Engineering		\$417,960	\$217,966	\$26,992	\$81,868	\$109,823	\$854,609
Inspection & Testing		\$0	\$54,810	\$776	\$253,936	\$125,639	\$435,160
Project Management		\$4,370	\$4,570	\$35,700	\$365,350	\$32,340	\$442,330
<b>Total</b>		<b>\$422,330</b>	<b>\$356,346</b>	<b>\$65,919</b>	<b>\$8,238,355</b>	<b>\$1,041,132</b>	<b>\$10,124,081</b>
Project Budget	\$10,777,654	<b>* Other Funding Source:</b> 1) State Funding \$12,470,000					
Less Other Funding	\$0						
Net	\$10,777,654						
Actual Measure V Expenditures	\$10,124,081						
Running Balance	\$653,573						

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
 MEASURE V EXPENDITURES  
 FUND 42.5  
 As of June 30, 2022

MEASURE V

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<i>V 710004</i>							
<b>Master Plan (109)</b>							
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$48,000	\$48,000
Advertising		\$0	\$641	\$0	\$0	\$0	\$641
Architect		\$0	\$112,073	\$528,182	\$37,861	\$0	\$678,116
Engineering		\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$3,800	\$1,100	\$0	\$0	\$4,900
<b>Total</b>		<b>\$0</b>	<b>\$116,515</b>	<b>\$529,282</b>	<b>\$37,861</b>	<b>\$48,000</b>	<b>\$731,658</b>
Project Budget	\$1,000,000						
Less Other Funding	\$0						
Net	\$1,000,000						
Actual Measure V Expenditures	\$731,658						
Running Balance	\$268,342						
<i>V 7100237</i>							
<b>Outdoor Classroom (111)</b>							
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$100,000	\$102,023	\$102,495	\$0	\$0	\$304,518
Engineering		\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$17,205	\$0	\$0	\$0	\$17,205
<b>Total</b>		<b>\$100,000</b>	<b>\$119,228</b>	<b>\$102,495</b>	<b>\$0</b>	<b>\$0</b>	<b>\$321,723</b>
Project Budget	\$321,723						
Less Other Funding	\$0						
Net	\$321,723						
Actual Measure V Expenditures	\$321,723						
Running Balance	\$0						

SANTA MONICA COMMUNITY COLLEGE DISTRICT  
MEASURE V EXPENDITURES  
FUND 42.5  
As of June 30, 2022

MEASURE V

Projects	Budget	17/18 Final	18/19 Final	19/20 Final	20/21 Final	21/22 Final	Combined Totals
<b>V 7100243</b>							
<b>Classrooms Relocation (114)</b>							
Supplies		\$0	\$0	\$0	\$0	\$11,963	\$11,963
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$3,467	\$5,709,329	\$391,967	\$0	\$6,104,763
Supplies		\$0	\$0	\$4,982	\$0	\$0	\$4,982
Architect		\$0	\$184,434	\$78,179	\$92,082	\$0	\$354,695
Engineering		\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$16,795	\$115,194	\$25,996	\$0	\$157,985
Project Management		\$0	\$61,520	\$476,831	\$55,650	\$0	\$594,001
Non-Cap Equipment		\$0	\$0	\$58,331	\$0	\$0	\$58,331
<b>Total</b>		<b>\$0</b>	<b>\$266,216</b>	<b>\$6,442,846</b>	<b>\$565,695</b>	<b>\$11,963</b>	<b>\$7,286,719</b>
Project Budget	\$7,400,000						
Less Other Funding	\$0						
Net	\$7,400,000						
Actual Measure V Expenditures	\$7,286,719						
Running Balance	\$113,281						
<b>V 7100255</b>							
<b>John Adams MS Auditorium - SMMUSD (112)</b>							
Building and Additions		\$0	\$0	\$0	\$15,000,000	\$5,000,000	\$20,000,000
<b>Total</b>		<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$15,000,000</b>	<b>\$5,000,000</b>	<b>\$20,000,000</b>
Project Budget	\$20,000,000						
Less Other Funding	\$0						
Net	\$20,000,000						
Actual Measure V Expenditures	\$20,000,000						
Running Balance	\$0						
<b>S7100048</b>							
<b>Other Bond Related Expenses (116)</b>							
Consultants		\$0	\$0	\$0	\$0	\$0	\$0
Lease/Rental		\$0	\$13,590	\$18,171	\$6,814	\$0	\$38,576
Supplies		\$0	\$0	\$0	\$0	\$0	\$0
Legal		\$0	\$0	\$0	\$0	\$0	\$0
Software License		\$0	\$0	\$0	\$0	\$0	\$0
Advertising		\$0	\$0	\$0	\$770	\$900	\$1,670
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$184	\$191,065	\$0	\$0	\$0	\$191,249
Inspection & Testing		\$0	\$13,060	\$0	\$0	\$0	\$13,060
Project Management		\$0	\$0	\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0
<b>Total</b>		<b>\$184</b>	<b>\$217,715</b>	<b>\$18,171</b>	<b>\$7,584</b>	<b>\$900</b>	<b>\$244,554</b>
Project Budget	\$300,000						
Less Other Funding	\$0						
Net	\$300,000						
Actual Measure V Expenditures	\$244,554						
Running Balance	\$55,446						
<b>Cost of Issuance (117)</b>							
Cost of Issuance		\$291,277	\$0	\$0	\$0	\$452,875	\$744,152
<b>Total</b>		<b>\$291,277</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$452,875</b>	<b>\$744,152</b>
Project Budget	\$800,000						
Less Other Funding	\$0						
Net	\$800,000						
Actual Measure V Expenditures	\$744,152						
Running Balance	\$55,848						
<b>Grand Total</b>		<b>\$3,079,439</b>	<b>\$20,483,307</b>	<b>\$26,712,421</b>	<b>\$37,650,605</b>	<b>\$33,015,286</b>	<b>\$120,941,058</b>

**SMC Bond Program**  
**Contractor List as of 6-30-2022**

---

**Student Services (Measure U #0, Measure S #9, Measure AA #120, Measure V #102):**

---

Architect – Steinberg Architects, Morris Architects, SVA Architects  
Contractor – Minco, Bernards Brothers, Spinitar  
Engineering – IVA, Cogent Energy Engineering, XL Fire  
Inspection & Testing – Geo Labs, BTC Labs - Vertical V, Peak Survey, LPI  
Rango Inc., Twining, AGE  
Project Management – LPI, YNL, Vanir

**Replacement Health/PE/Fitness/Dance Building (Measure S #4, Measure AA #104):**

---

Architect – Gensler Architects  
Contractor – Bernards Brothers  
Engineering – IVA, Glumac  
Inspection & Testing – Geo Labs, Ellis Environmental, Twining, Rango Inc.  
Project Management – LPI

**Early Childhood Development (Measure S #5, Measure V #104):**

---

Architect – Carde Ten Architects  
Consultant – Child Educational Center  
Contractor – The Nazerian Group  
Engineering – Jacobs  
Inspection & Testing – Geo Labs, Rango Inc., Twining  
Project Management – LPI, Vanir, YNL

**Malibu Site (Measure S #6, Measure AA #110, Measure V #103):**

---

Architect – Quatro Design Group  
Contractor – Master Contracting, Icon West  
Consultant – m2 Strategic, Parker Environmental  
Engineering – Ensitu Services, Jacobs  
Inspection & Testing – Peak Surveys, Ellis Environmental, JL Inspection, Ninyo  
& Moore, JL Inspection  
Project Management – LPI, m6 Strategic, Vanir, YNL

**Energy Efficiency Projects (Measure S #7, Measure AA #113):**

---

Architect – N/A  
Contractor – Compass Energy Solutions, Johnson Controls  
Engineering – Compass Energy Solutions, Johnson Controls  
Inspection & Testing – Ellis Environmental

**Environmental Performance (Measure AA #101):**

---

Architect – Kishimoto Architects  
Contractor – SJ Amoroso Construction  
Engineering – P2S Engineering  
Inspection & Testing – Cannon, Peak Surveys  
Project Management – LPI

**Information Technology Relocation (Measure AA #102):**

---

Architect – Morris Architects  
Contractor – Minco, Bernards Brothers, Eidim AV Technology  
Engineering – IVA, P2S Engineering  
Inspection & Testing – Cannon, Peak Surveys, Geo Labs, Ellis Environmental,  
Twining, JL Inspection, Rango Inc.  
Project Management – LPI, CCS Presentation

**Media and Technology Complex (Measure AA #103):**

---

Architect – Clive Wilkinson Architects, Morris Architects  
Contractor – H.B. Parkco Construction, Fast Track Construction, CW  
Driver, Dimension Data, Key Code Media, Omega  
Construction  
Consultant – EEG Services  
Engineering – IVA, P2S Engineering  
Inspection & Testing – Twining, Geo Labs, BTC Labs – Vertical V,  
JL Inspection, EEG Services, Ellis Environmental, Rango  
Inc., Cannon  
Project Management – LPI

**Madison East Wing Seismic Upgrade (Measure AA #107):**

---

Architect – DLR Group – WWCOT, LPI  
Contractor – Trimax, Bernards Brothers, Dimension Data  
Engineering – IVA, Glumac  
Inspection & Testing – Twining, Peak Surveys, LPI, All Group Engineering, EEG  
Services, Ellis Environmental  
Project Management – LPI

**Business & Facilities Infrastructure (Measure AA #111):**

---

Architect – LPI, Gwynne Pugh Urban Studio  
Contractor – REC+S, Inc., Omega Construction,  
Concept Consultant, Inc.  
Engineering – N/A  
Inspection & Testing – Ellis Environmental, JL Inspection  
Project Management – LPI

**Community Classroom & Facility Project (Measure AA #114)**

---

Architect – Morris Architects  
Contractor – Waisman Construction, Spinitar, Trimax  
Engineering – IVA  
Inspection & Testing – LPI, Twining  
Project Management – LPI

**Satellite Campus Parking Facilities and Roadway Improvements (Measure S #8)**

---

Architect – N/A  
Contractor – N/A  
Engineering – MK Engineering Group  
Inspection & Testing – N/A  
Project Management – LPI

**Roadways, walkways, Grounds, Parking Lots, and Garages (Measure AA #116)**

---

Architect – LPI, DLR Group - WWCOT  
Contractor – Trimax, Pub Construction  
Consultant – Walker Parking  
Engineering – MK Engineering  
Inspection & Testing – Ellis Environmental, Peak Surveys, LPI  
Project Management – LPI

**Emergency Lighting, Fire Alarm, and Security System (Measure AA #119)**

---

Contractor – Red Hawk Fire and Security, Nexus  
Engineering – MDC Engineers  
Inspection & Testing – Rango Inc.  
Project Management – LPI

**Signage Safety/Information (Measure S #15)**

---

Contractor – Sign Excellence  
Consultant – APCO  
Project Management – LPI

**Math and Science Addition (Measure AA #106/Measure V #101)**

---

Architect – Cannon Design  
Contractor – Icon West, The Nazerian Group  
Consultant – N/A  
Engineering – Arup  
Inspection & Testing – AGE  
Project Management – Vanir, YNL

**Classrooms Relocation (Measure V #114)**

---

Architect – Gwynne Pugh  
Contractor – The Nazerian Group  
Inspection & Testing – AGE  
Project Management – Vanir, YNL

**Art Building Replacement (Measure V #105)**

---

Architect – Little Architects  
Contractor – N/A  
Engineering – tk1sc  
Inspection & Testing – B2 Environmental, Geolabs, CNA  
Project Management – Vanir, YNL

**Air Conditioning (Measure V #107)**

---

Architect - P2S

Contractor - A&B Construction, Inc

Engineering - tk1sc, P2S

Inspection & Testing - Rango Inc., Koury, B2 Environmental

Project Management - Vanir, YNL

## Vendors and Contractors List

*(Received Payments from Bond Funds)*

For the 12 month period July 1, 2021 to June 30, 2022 (FY 2021-22)

---

A&B Construction  
All Group Engineering (AGE)  
Arup Engineering  
B2 Environmental  
Cannon Design  
Chris Nelson and Assoc Consultants (CNA)  
Design Services Inc  
Division of State Architect  
Fagen Friedman & Fulfrost LLP  
Fehr and Peers Consultants  
GeoLabs  
Grainger  
Icon West Construction Company  
Jacobs Engineering  
JL Inspection  
Koury Engineering  
Little Architects  
P2S Engineers  
QDG Architecture  
Rango Inspection  
Santa Monica Daily Press  
Santa Monica- Malibu USD  
Southern Cal Gas Company  
TK1SC  
Twining  
Vanir Construction Management  
YNL Architects
